

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल बिहारशरीफ

पत्रांक 5/1/2023 बिहारशरीफ, दिनांक 24-4-23

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ ।

सेवा में,

नोडल पदाधिकारी 3054
ग्रामीण कार्य विभाग, बिहार, पटना

विषय:— नई अनुरक्षण नीति-2018 अन्तर्गत आवंटन उपलब्ध करने के संबंध में।
महाशय,

उपर्युक्त विषयक से संबंधित नई अनुरक्षण नीति-2018 अन्तर्गत इस प्रमंडल द्वारा कराये जा रहे पथों के निर्माण कार्य के लिये आवंटन उपलब्ध करने हेतु अधियाचना पत्र समर्पित की जा रही है।

अतः अनुरोध है कि पथ में कराये गये कार्यों के विरुद्ध भुगतान हेतु संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक को भुगतान किया जा सके।

अनु०:— यथोक्त।

विश्वासभाजन


24/4/2023


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ
24/04/23

(See Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate up to the month of-20.04.2023

(New Maintenance Policy 2018)

PIU- BIHARSHARIF

Year-2023-2024


Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	ltr-54 Dt-28.03.2023	3285.00186	Certified that out of Rs 3285.00186 received & balance during the years 2023-24 in favour of Ex. Engineer, R.W.D. Works Division Biharsharif, sum of Rs 3134.21643 has been utilized for the purpose of New Maintenance Policy 2018 scheme as given in the margin for which it was sanctioned and that the balance of Rs 150.78543 lacs remaining unutilized at the end of the period under -20.04.2023
	Total Rs.		3285.00186	

2 Certified that I have satisfied myself that the conditions on which the grants-in- aid was
Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant .
- All other codal formalities have been observed.

3 Physical Progress achieved:

- Construction of Road Works.
- Construction of CD works


Divisional Accounts Officer
Rwd, Works Division
Biharsharif


Executive Engineer
Rwd, Works Division
Biharsharif
24/04/23

Position Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Works Division :-Bihar Sharif

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Amount Alloted (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Increase In Allotment	Remains
					Length (In km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/NA/ BHH/23/ 0005	Masuma More To Masuma	10200612004	1405 07 Sep 2022	0.744	33.0400	32.75689	7.28251	01/12/2023- 24 19-04-2023	04-05-2023	0	2393	25.00	5.2	0	0	30.00607	
TOTAL																		30.00607

Total = 30.00607

- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.


24/04/23
Divisional Accounts Officer

Rwd,works Division Biharsharif

Executive Engineer


24/04/23
Rwd,works Division Biharsharif

Head-New MR
Road Name-Masuma More to Masuma
Con-Kumud Ranjan Sarkar


Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	ATEGOR ROAD	Latitude	Longitude	Event	$Y = 0 * X^2 + 0.816 * X + 249$	
4/12/22	16:18:38	29	0.1	290	20.2	2900	2615	G	25.29347	85.75522	Normal	X = 2400	
4/12/22	16:19:13	29	0.1	200	20.2	2000	1880	G	25.29359	85.75625	Normal	Y = 2207	
4/12/22	16:19:13	29	0.1	290	20.2	2900	2615	G	25.29302	85.7569	Normal		
4/12/22	16:21:34	29	0.1	220	20.2	2200	2044	G	25.28893	85.75577	Normal		
4/12/22	16:21:34	29	0.1	280	20.2	2800	2533	G	25.28911	85.75476	Normal	RURAL ROAD	
4/12/22	16:22:0	29	0.1	320	20.2	3200	2860	G	25.28921	85.75374	Curve	Good	Average
4/12/22	16:22:9	29	0.1	240	10.1	2400	2207	G	25.29007	85.75369	Normal	<4000	4001-5000
Total-							16754						Poor
IRI Value-							2393						

24/10/23
AETM

24.4.2023
A E

24/10/23
C/S

File : E:\Krishna Kumar ITM\Bump Reading And Software\Bump Reading\Kumud Ranjan Sarkar\04121743.Xls,
Name of Customer :Kumud Ranjan Sarkar, Name of Work/ Road :Masuma More to Masuma, Lab Job number :

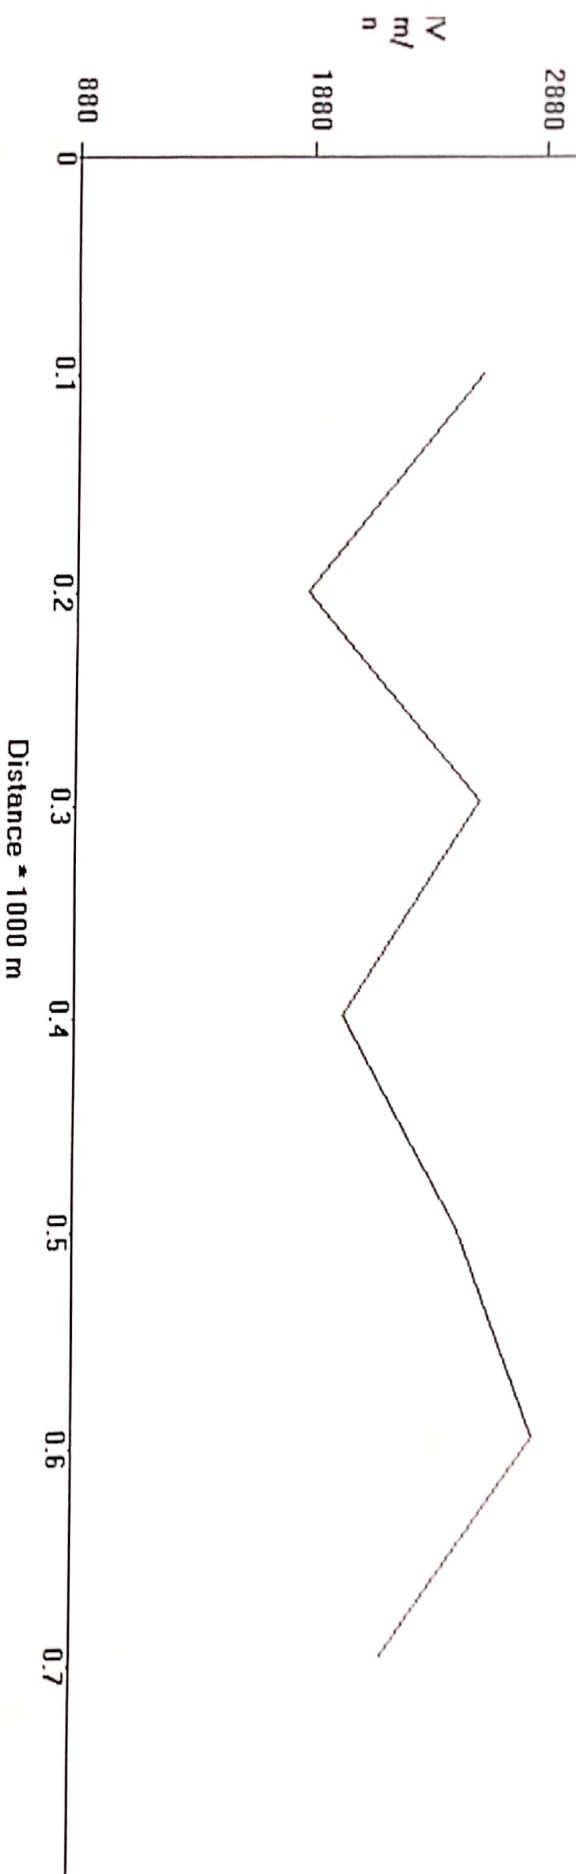

24/10/23
A27m

24.7.2023
A-E

1
24 4 | 23
AE

$$\begin{array}{r} 24 \overline{) 24123} \\ \underline{24} \\ 0 \end{array}$$

Name of Work-
 Situation of Work-
 Agency by which work is executed-
 Date of Measurement-
 No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1st					
Name of work -	Mansuwar Musre				
to Mansuwar					
Agency -	Kumud Panjan Sarkar				
Block -	Sarmere				
Agreement No. -	01/F2/23-24				
work started date -	19/04/23				
Date of Completion -					
Actual date of Completion -					
1	Cleaning & grubbing road				
land do do all Complete					
	$2 \times 1 \times 25 \times 1.00 =$				50.00
	$2 \times 2 \times 30 \times 1.00 =$				120.00
	$2 \times 6 \times 30 \times 1.00 =$				360.00
	$2 \times 5 \times 30 \times 1.00 =$				300.00
	$2 \times 7 \times 30 \times 1.00 =$				420.00
	$2 \times 1 \times 13 \times 1.00 =$				26.00
					1276.00 m^2
					= 0.128 Ha

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Material Statement					
Earthwork - 631.75 m ³					
G.S.B - 76.11 m ³					
Local sand - 47.43 m ³					
Stone material Gr-II + Gr-III - 261.58 m ³					
Stone screening - 62.70 m ³					
Emulsion (SS-1) - 1.840 M.T.					
Emulsion (RS-1) - 1.192 M.T.					
Bitumen (S-90) - 10.55 M.T.					
Stone chips - 174.20 m ³					
Sand - 20.21 m ³					
					

Abstract of Cost-					
1. Clearing & grubbing road					
Land do do all complete					
0.128 Ha	Pg No. - (1)				
@ Rs 48479 = 00 / Ha - Rs 6205 = 00					
2. Scrubbing Ex. stop bituminous					
Surface do do all complete					
299.05 m ²	Pg No. - (2)				
@ Rs 15.84 / m ² - Rs 4737 = 00					
3. Cont ⁿ of embankment with					
material obtained from borrow					
pits lead upto 1000 do do					
all complete					
631.750 m ³	Pg No. - (3)				
@ Rs 203.80 / m ³ - Rs 128751 = 00					
Continuation					
@ Rs 139693 = 00					

Scanned with CamScanner
