

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, रजौली।

Mob No.: 8986915851.

Email I.D.: - eerwdrajauli@gmail.com

पत्रांक....1457-अ.प्र.

रजौली / दिनांक...03/8/23

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, रजौली।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
भूमि विकास बैंक भवन, बुद्ध मार्ग रोड पटना-1।


विषय :- नई अनुरक्षण नीति-2018 योजनान्तर्गत आवंटित राशि का उपयोगिता प्रमाण पत्र तथा आवंटन अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है, कि इस प्रमण्डल के अधीन नई अनुरक्षण नीति-2018 योजनान्तर्गत चल रहे कार्यों के भुगतान हेतु विहित प्रपत्र में माँग पत्र एवं उपयोगिता प्रमाण पत्र संलग्न करते हुए आग्रह है, कि आवंटन उपलब्ध कराने की कृपा की जाय ताकि कराये गए कार्यों का भुगतान किया जा सके।

अनु० :- यथोक्त।

विश्वासभाजन,


31-07-23
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, रजौली।

Requisition for Scheme Head :- MR (3054) under Bihar Rural Road Maintenance Policy 2018
(Initial Rectification and Surface Renewal)

Name of Works Division: RWD (W) Division, Rajauli

SL NO	Package No-	Name Of Road	Project Id as Per MIS	Administrative Approval (AA) Letter No- & Date	Administrative Approval (AA)		Agreement Amount		Agreement No- & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in percentage	Previous Total allotted Amount (in Lakh)	upto date expenditure as per MIS (in Lakh)	Requisition against work done (in lakh)	Remarks
					Length (in km)	Amount (in lakh)	Initial Rectification with surface Renewal (in lakh)	5 years routine Maintenance (in Lakh)										
1	RMNARAJ 230008	Budhwara To Alipur	15271036414	LT. 851/ 18.02.22	4.105	147.06000	90.36200	34.89945	01/MBD/MR 3054/2022-23	11-01-2024	-	3320	25	5.01	0.00000	0.00000	81.32580	
2	RMNARAJ 230008	Fatehpur - Govindpur Road To Bhargawan	15271036416	LT. 851/ 18.02.22	2.260	77.84800	47.31710	19.50780	01/MBD/MR 3054/2022-23	11-01-2024	-	1923	25	5.02	0.00000	0.00000	42.56539	
3	RMNARAJ 230001	NH31- Phulwarya Dam Road to Bhaur	15271034357	LT. 851/ 18.02.22	0.855	47.98000	30.34157	8.01420	04/MBD/MR 3054/2022-23	19-11-2023	-	3259	25	5.01	0.00000	0.00000	27.30741	
					7.220	272.88800	168.02067	62.42145	0.00000	-	-	-			0.00000	0.00000	151.21860	

In Word One Crore Fifty One Lakh Twenty One Thousand Eight Hundred Sixty only)


 Executive Engineer,
 Rural Works Department,
 Works Division- Rajauli.

FORM GFR 19-A

(See Government of India's Decision (1) below Rule 150)
Form of Utilization Certificate up to the Month of **31-JULY-2023**.

S. No	Name of Scheme	Sanction No. & Date with Amount (In Rs.lacs)	Amount Received (In Rs.Lacs)	Decrease (in Lacs)	Particulars
1	Bihar Rural Roads New Maint. Policy 2018	As on 25-MARCH-2023	3787.76798	0	Certified that out of Rs. 5093.19846 Lakh received during the Financial Year 2023-24 (31-JULY-23) in favour of Executive Engineer, RWD (W) Division, Rajauli, Bihar out of which a sum of Rs. 4803.20871 Lacs has been utilized for the purpose of New Maintenance Policy 2018 Under MR3054 Scheme as given in the margin for which it was sanctioned and Rs. 0.00 has been surrendered and that the balance of Rs. 289.98975 Lacs remaining unutilized at the end of the said period.
2		Lt. 63 Dt 13.04.23	20.97956		
3		Lt. 31 Dt 31.05.23	89.44542		
4		Lt. 78 Dt 24.05.23	198.63594		
5		Lt. 84 Dt 08.06.23	126.74006		
6		Lt. 85 Dt 14.06.23	129.82321		
		Lt. 92 Dt 28.06.23	613.59155		
		Lt. 100 Dt 14.07.23	126.21474		
			5093.19846	0.00000	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineers/Superintending Engineer.
- Periodic inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

Physical Progress achieved :-

- Construction of Road Works
- Construction of CD Works

31/7/23


Executive Engineer,
Rural Works Department,
Works Division, Rajauli.

Name of Road- Fatehpur - Govindpur Road To Bhargawan													
Batch No- RM/NA/RAJ/23/0008													
Name of Contractor-Sujay Bhan Singh													
Date	Time	Section	Length	Bumps	Speed	OR	U/V	REGORY	IRI	Latitude	Longitude	Event	
		No.	in km	in mm	Rate	mm/km		ROAD					
26/7/23	11:16:0	41	0.1	360	10.1	2600	2450	G	4.56	24.78954	85.64414	Normal	$Y = 0 * X \wedge 2 + 0.854 * X + 376.5$
26/7/23	11:16:0	41	0.1	290	30.3	2900	2853	G	3.85	24.79036	85.64424	Normal	$Y = 1530$
26/7/23	11:16:30	41	0.1	390	10.1	2700	2707	G	4.86	24.79123	85.64463	Normal	
26/7/23	11:17:0	41	0.1	240	20.2	2400	2426	G	3.33	24.79166	85.64387	Normal	
26/7/23	11:17:4	41	0.1	210	40.4	2100	2169	G	3.01	24.79212	85.64298	Normal	(R) RURAL ROAD
26/7/23	11:17:4	41	0.1	180	30.3	1800	1913	G	2.69	24.79253	85.64219	Normal	Good
26/7/23	11:17:4	41	0.1	100	30.3	1000	1230	G	1.82	24.79278	85.6413	Normal	Average
26/7/23	11:17:39	41	0.1	120	30.3	1200	1401	G	2.04	24.7932	85.6403	Normal	Poor
26/7/23	11:18:0	41	0.1	140	30.3	1400	1572	G	2.26	24.79401	85.6386	Normal	
26/7/23	11:18:0	41	0.1	140	30.3	1400	1572	G	2.26	24.79466	85.63796	Normal	
26/7/23	11:18:0	41	0.1	260	30.3	2600	2596	G	3.54	24.7953	85.63731	Normal	
26/7/23	11:18:25	41	0.1	250	30.3	2500	2511	G	3.43	24.7959	85.63648	Normal	
26/7/23	11:19:0	41	0.1	460	10.1	2600	2504	G	5.55	24.79663	85.63623	Normal	
26/7/23	11:19:0	41	0.1	240	10.1	2400	2426	G	3.33	24.79697	85.63534	Normal	
26/7/23	11:19:0	41	0.1	130	30.3	1300	1486	G	2.15	24.79723	85.63448	Normal	
26/7/23	11:19:36	41	0.1	210	30.3	2100	2169	G	3.01	24.7977	85.63362	Normal	
26/7/23	11:19:36	41	0.1	120	40.4	1200	1401	G	2.04	24.79809	85.63266	Normal	
26/7/23	11:20:0	41	0.1	110	30.3	1100	1315	G	1.93	24.79851	85.63173	Normal	
26/7/23	11:20:11	41	0.1	140	40.4	1400	1572	G	2.26	24.79879	85.63103	Normal	
26/7/23	11:20:15	41	0.1	140	40.4	1400	1572	G	2.26	24.79879	85.63103	Normal	
26/7/23	11:20:18	41	0.1	140	40.4	1400	1572	G	2.26	24.79879	85.63103	Normal	
26/7/23	11:20:35	41	0.1	130	40.4	1300	1486	G	2.15	24.79919	85.63002	Normal	
26/7/23	11:20:45	41	0.06	50	70.7	1351	1530	G	2.21	24.79937	85.62965	Normal	
Total		2.260	4550.000	707.000	42151.00	44233.00							
Average		197.83	30.74	1832.65	1923.17								

punjpur
 26/7/23
 SR

26/7/23
 31-07-23
 EC

File : E:\Manish\Maintenance Bump Data of Rajauli\Surey Bhan Singh\26071520.Xls, Section No. : 41, Eqn : $Y = 0$
 Name of Customer : Sujay Bhan Singh, Name of Work/ Road : Jathepur Govindpur Road to Bhargawan, Lab Job

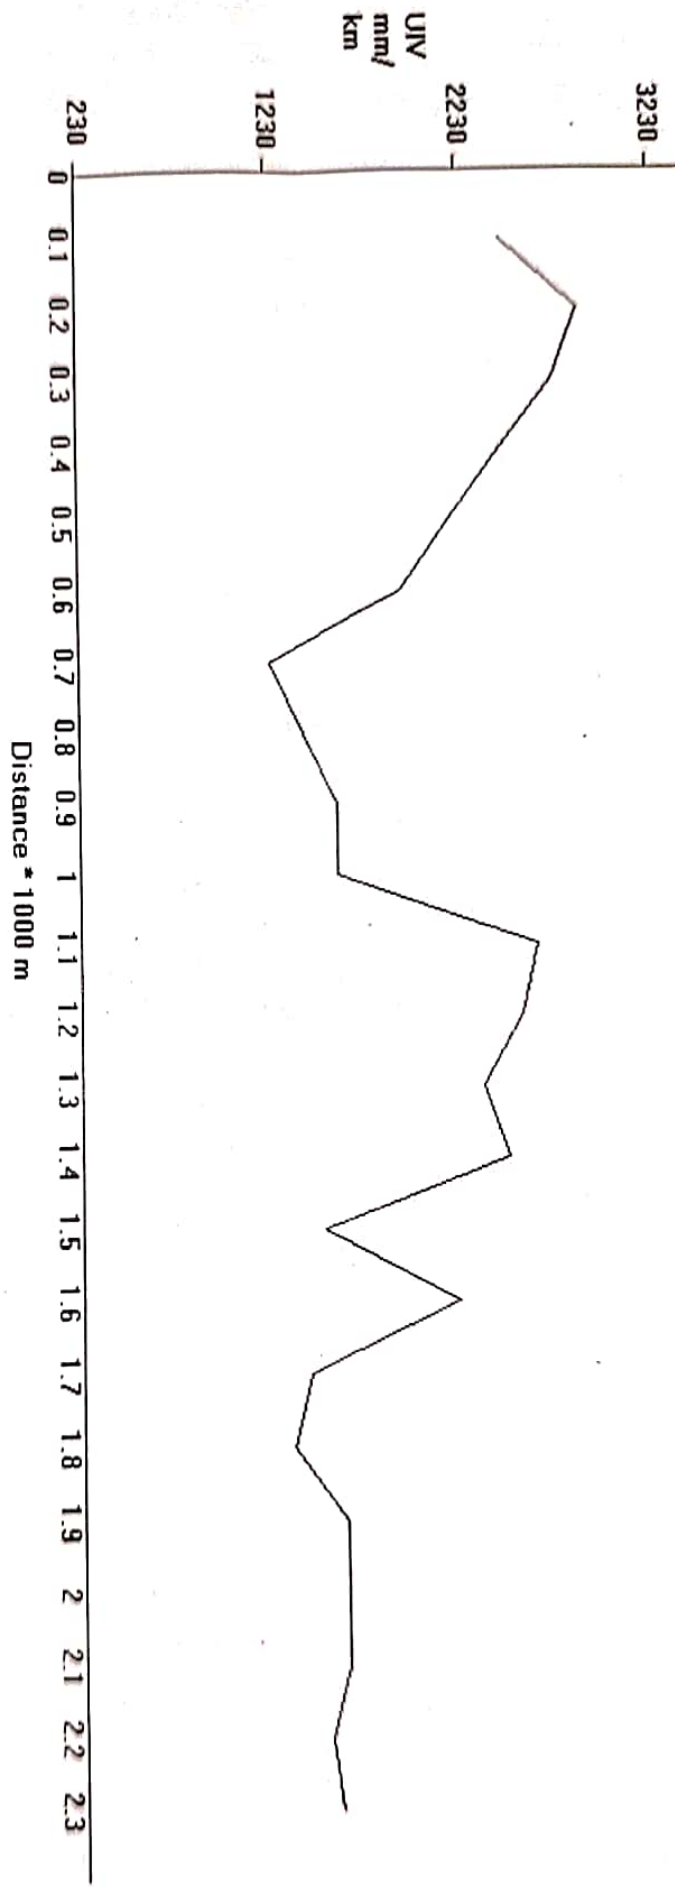

26/7/23
 SP

26/7/23
 SP

31.07.23
 ECE

Name of Road - Budhwara To Alipur

Batch No- RM/NA/RA/J23/0008

Name of Contractor-Sujay Bhan Singh										Name of Road - Budhwara To Alipur									
Date	Time	Section	Length	Bumps	Speed	OR	REGORY	IRI	Latitude	Longitude	Event								
No.		in km	in mm	Rate	mm/km	UIV	ROAD												
26/7/23	10:39:0	36	0.1	380	0	2800	3421 G	4.76	24.76186	85.645	Normal								
26/7/23	10:39:0	36	0.1	330	20.2	2300	3194 G	4.25	24.76188	85.64594	Normal								
26/7/23	10:39:0	36	0.1	320	30.3	2200	3109 G	4.15	24.76124	85.64655	Normal								
26/7/23	10:39:36	36	0.1	410	40.4	2100	3277 G	5.06	24.7605	85.647	Normal								
26/7/23	10:39:36	36	0.1	540	30.3	2400	3188 G	6.33	24.75962	85.64736	Normal								
26/7/23	10:40:0	36	0.1	330	40.4	2500	3365 G	4.46	24.75887	85.64774	Normal								
26/7/23	10:40:11	36	0.1	320	40.4	2200	3109 G	4.15	24.758	85.64786	Normal								
26/7/23	10:40:11	36	0.1	330	20.2	2300	3194 G	4.25	24.75725	85.64832	Normal								
26/7/23	10:40:11	36	0.1	510	30.3	2100	3331 G	6.04	24.75644	85.64852	Normal								
26/7/23	10:40:46	36	0.1	350	40.4	2500	3365 G	4.46	24.75547	85.64859	Normal								
26/7/23	10:40:46	36	0.1	380	40.4	2800	3621 G	4.76	24.75461	85.64857	Normal								
26/7/23	10:41:0	36	0.1	270	30.3	2700	2682 G	3.64	24.75381	85.64827	Normal								
26/7/23	10:41:0	36	0.1	340	40.4	2400	3380 G	4.56	24.75297	85.64808	Normal								
26/7/23	10:41:21	36	0.1	450	40.4	2500	3319 G	5.45	24.75202	85.64803	Normal								
26/7/23	10:41:21	36	0.1	360	30.3	2600	3450 G	4.56	24.75118	85.64806	Normal								
26/7/23	10:41:21	36	0.1	420	10.1	2200	3563 G	5.16	24.7502	85.64818	Normal								
26/7/23	10:42:0	36	0.1	1320	10.1	2400	3649 G	13.49	24.74948	85.64859	Normal								
26/7/23	10:42:32	36	0.1	1200	20.2	2000	3424 G	12.43	24.74888	85.64931	Normal								
26/7/23	10:43:0	36	0.1	1270	10.1	2700	3222 G	13.05	24.74813	85.64988	Normal								
26/7/23	10:43:7	36	0.1	1360	10.1	2600	3490 G	13.85	24.7476	85.65057	Normal								
26/7/23	10:44:0	36	0.1	1600	10.1	2000	3040 G	15.94	24.74715	85.65141	Normal								
26/7/23	10:44:17	36	0.1	1000	20.2	2500	3216 G	10.63	24.74628	85.65152	Normal								
26/7/23	10:44:17	36	0.1	690	10.1	2324	3339 G	10.01	24.74566	85.65187	Normal								
26/7/23	11:4:15	36	0.1	800	0	2000	3208 G	8.79	24.77693	85.63983	Normal								
26/7/23	11:4:15	36	0.1	480	20.2	2800	3475 G	5.75	24.7717	85.64051	Normal								
26/7/23	11:4:50	36	0.1	280	30.3	2800	2767 G	3.74	24.77801	85.64079	Normal								
26/7/23	11:5:0	36	0.1	400	40.4	2000	3792 G	4.96	24.77885	85.64071	Normal								
26/7/23	11:5:0	36	0.1	290	20.2	2900	2653 G	3.85	24.77957	85.64008	Normal								
26/7/23	11:5:25	36	0.1	370	20.2	2700	3536 G	4.66	24.77934	85.63918	Normal								
26/7/23	11:5:25	36	0.1	510	10.1	2100	3131 G	6.04	24.77891	85.63835	Normal								
26/7/23	11:6:36	36	0.1	430	0	2773	3422 G	10.42	24.77873	85.63791	Normal								
26/7/23	11:11:0	36	0.1	510	0	2100	3631 G	6.04	24.77939	85.63921	Normal								
26/7/23	11:11:16	36	0.1	380	20.2	2800	3621 G	4.76	24.77961	85.6401	Normal								
26/7/23	11:11:16	36	0.1	590	10.1	2900	3415 G	6.81	24.7804	85.64032	Normal								
26/7/23	11:11:52	36	0.1	450	30.3	2500	3219 G	5.45	24.78124	85.64039	Normal								
26/7/23	11:12:0	36	0.1	340	30.3	2400	3280 G	4.66	24.78213	85.64052	Normal								
26/7/23	11:12:0	36	0.1	380	30.3	2800	3621 G	4.76	24.78301	85.64066	Normal								

26/7/23
20/7/23
5/2

26/7/23
26/7/23
26/7/23

26/7/23
26/7/23
26/7/23


26/7/23	11:12:0	36	0.1	320	30.3	2200	3109	G	4.15	24.78392	85.64077	Normal					
26/7/23	11:13:8	36	0.1	420	10.1	2200	3563	G	5.16	24.78601	85.64234	Normal					
26/7/23	11:13:8	36	0.1	370	20.2	2700	3247	G	4.66	24.78679	85.6429	Normal					
26/7/23	11:13:8	36	0.1	370	20.2	2200	3456	G	4.66	24.78679	85.6429	Normal					
26/7/23	11:13:8	36	0.005	370	20.2	2400	3152	G	4.66	24.78679	85.6429	Normal					
	Total	4.105	22560.00	939.30	102397.00	139446.00											
	Average		537.14	22.36	2438.02	3320.14											

Drummond
26/7/23
 JE

Drummond
27/07/23
 A.C.

Drummond
31-07-23
 JE

File : E:\Manish\Maintenance Bump Data of Rajauli\Surey Bhan Singh\26071520.Xls, Section No. :36, Eqn : $Y = 0$
 Name of Customer : Sujay Bhan Singh, Name of Work/ Road : Budwera to Alipur, Lab Job number :36

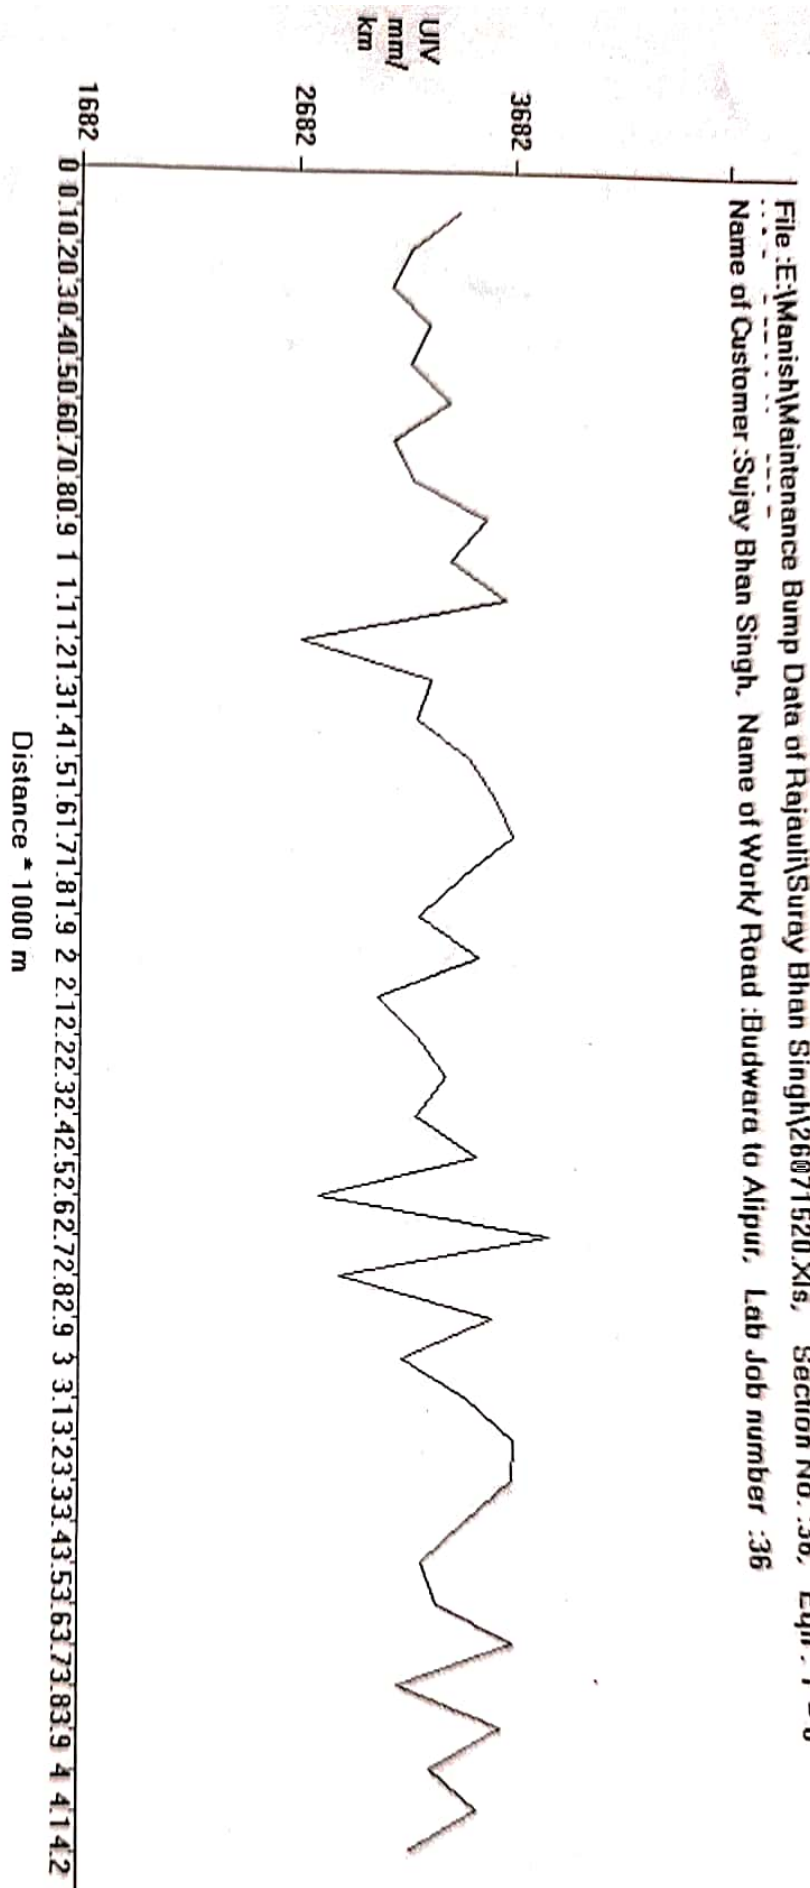

Sum
26/7/23
R

Sum
26/7/23
R

Sum
26/7/23
R
