

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल पकड़ीदयाल।**

पत्रांक.....1525 8/8/23 पकड़ीदयाल दिनांक.....24.8.23

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पकड़ीदयाल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।



विषय :- **(New Maintenance Policy 2018)** अन्तर्गत चयनित पथों के लिए
प्राप्त राशि का उपयोगिता प्रमाण-पत्र एवं अधियाचना के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि (New Maintenance Policy 2018)
अन्तर्गत चयनित पथों के लिए उपयोगिता प्रमाण-पत्र एवं अधियाचना विहित प्रपत्र में तैयार
कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

- अनु०- 1. उपयोगिता प्रमाण-पत्र Form GFR 19A
2. अधियाचना पत्र।
3. प्रतिवेदन की छायाप्रति।

विश्वासभाजन


24.8.23
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पकड़ीदयाल

24/8/23

Form.GFR 19-A Form.

(See Government of India's Decision (1) below Rule 150)

Form Of Utilisation Certificate up to the Month Of August 2023

(New Maintenance Policy 2018)

वर्ष 2018-19, 2019-20 एवं 2020-21 में चयनित पथों के लिए उपयोगिता प्रमाण पत्र

PIU -

SL. No.	Name Of Scheme	Sanction No. & Date With Amount	Amount Received (InRs.)	Particulars
1	Construction Of Rural roads Under (New Maintenance Policy 2018)	Lt. 37 (We) Dt. 27.05.2020 Rs. 75,00,000.00 Lt. 45 (We) Dt. 18.06.2020 Rs. 01,04,50,000.00 Lt. 47 (We) Dt. 24.06.2020 Rs. 96,00,000.00 Lt. 72 (We) Dt. 07.10.2020 Rs. 01,03,00,000.00 Lt. 77 (We) Dt. 14.10.2020 Rs. 01,45,00,000.00 Lt. 80 (We) Dt. 05.11.2020 Amount. Rs. 01,36,50,000.00 Lt. 82 (We) Dt. 13.11.2020 Amount. Rs. 01,35,50,000.00 Lt. 84 (We) Dt. 26.11.2020 Amount. Rs. 01,16,00,000.00 Lt. 86 (We) Dt. 11.12.2020 Amount. Rs. 04,71,14,000.00 Lt. 05 (We) Dt. 12.01.2021 Amount. Rs. 04,88,72,500.00 Lt. 17 (We) Dt. 26.02.2021 Amount. Rs. 04,47,26,500.00 Lt. 20 (We) Dt. 19.03.2021 Amount. Rs. 06,09,42,938.00 Lt. 20 (We) Dt. 19.03.2021 Amount. Rs. 06,09,42,938.00 Lt. 35 (We) Dt. 14.03.2023 Amount. Rs. 06,09,42,938.00 Lt. 60 (We) Dt. 07.04.2023 Amount. Rs. 01,49,00,000.00 Lt. 67 (We) Dt. 27.04.2023 Amount. Rs. 01,77,87,000.00 Lt. 72 (We) Dt. 10.05.2023 Amount. Rs. 11,18,55,000.00 Lt. 81 (We) Dt. 31.05.2023 Amount. Rs. 07,06,59,000.00 Lt. 84 (We) Dt. 08.06.2023 Amount. Rs. 03,02,73,000.00 Lt. 92 (We) Dt. 28.06.2023 Amount. Rs. 05,25,84,000.00 Lt. 100 (We) Dt. 14.07.2023 Amount. Rs. 01,25,59,000.00	89,05,85,852.00	Certified that out of Rs. 89,05,85,852.00 received during the year 2017-18 in favour of EX. Engineer, R.W.D W.D Pakridayal sum of Rs. 80,54,75,099.00 has been utilized for the purpose of New Maintenance Policy 2018) schemes as given in the margin for which it was sanctioned and that the balance of Rs 08,51,10,753.00 remaining Unutilized at the end of the period under.
		89,05,85,852.00	89,05,85,852.00	

2. Certified that I have satisfied myself that the conditions on which the grant in aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was Sanctioned.

Kind Of Checks Exercised :-

- xxxvi) Works have been supervised by Executive Engineer/Superintending Engineer.
- xxxvii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- xxxviii) Construction material have been tested.
- xxxix) Measurements have been recorded in the MB'S and test check conducted by the Assistant.
- xl) All other codal Formalities have been Observed.

3. Physical Progress Achieved:

- i) Construction Of Road Works.
- ii) Construction Of CD works.

D.A.O., Pakridayal,

Rural Works Department,
Works Division Pakridayal.

 Executive Engineer,
 Rural Works Department,
 Works Division Pakridayal.

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Pakriddayal.**

Name of Works Division : Pakriddayal

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

SI No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification (in lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
		Punas To Kajarah.	31708702030	Latter No. 1956 Date- 31.03.2023	11.700	679.93000	537.30005	168.376	06-MBD/2023-24 Date- 27.06.2023	26.03.2024	In Progress	3439	25	5.00	0.00000	0.00000	537.00000	
																	537.00000	

1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2 Update Physical Progress has been uploaded in MIS.
24.08.23
J.E

[Signature]
A.E

D.A.O, Grade-I,
R.W.D, Pakriddayal

[Signature]
24.08.23

[Signature]
24.08.23
Executive Engineer,
Rural Works Department,
Works Division, Pakriddayal

Name of Customer : Priyanka Kumari
 Name of Work/ Road : T01 Purnas To Kajrahan (VR1)
 Lab Job number :
 Date : 23-08-2023
 Section No. : 64

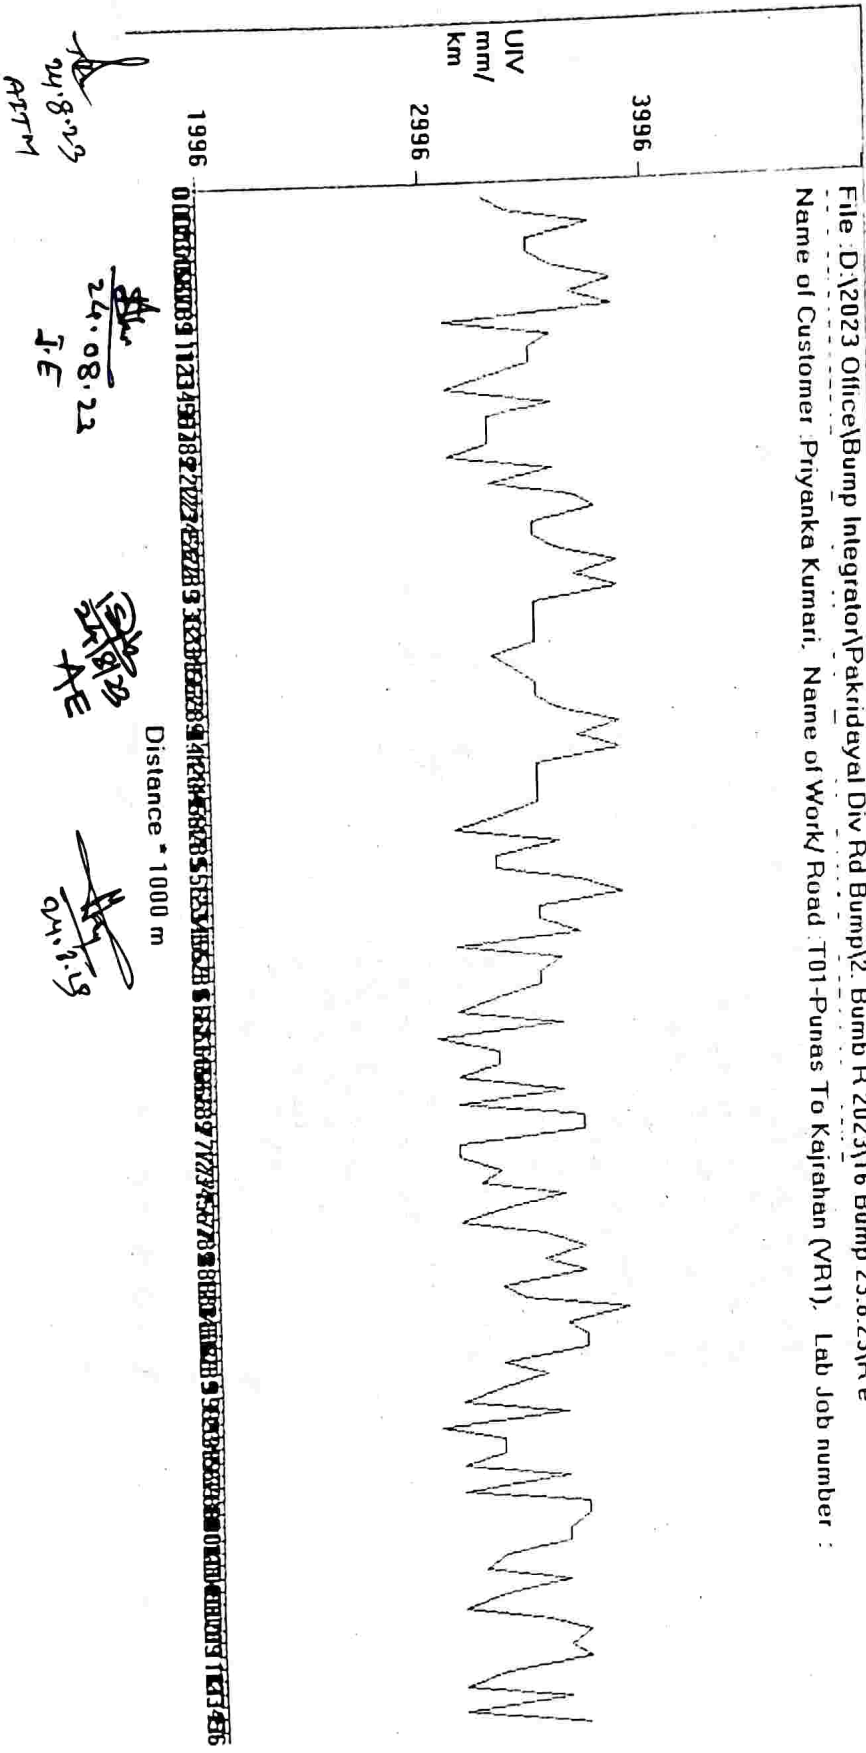
Test Date : 23-08-2023
 Road Name : T01 Purnas To Kajrahan (VR1)
 Machine No : 437
 Road Type : (R) RURAL ROAD
 Start S No :
 Side :
 Start E No :
 Interval :
 Weather : Normal
 UIV Range : 1996 To 5000 mm/km
 Dist Range : 0 To 11.8 0.1 1000 m
 Start Location :
 End Location :
 Equation : $Y = 0 * X^2 + 0.954 * X + 1345$

Print Generate Report and Graph

Redraw Graph

Map View

File : D:\2023 Office\Bump Integrator\Pakridyal Div Rd Bump\2. Bump R 2023\16 Bump 23.8.23\Re
 Name of Customer : Priyanka Kumari, Name of Work/ Road : T01 Purnas To Kajrahan (VR1), Lab Job number :



Name of Road :- T01-Punas To Kajrahan (VRI)

Contractor Name:- Priyanka Kumari

Scheme:- MR New Maintenance Policy

Division:- Pakridayal

Date	Time	Section	Length in km	Bumps in mm	Speed Rate mm/km	OR	IRI mm/km ROAD	CATEGORY	Latitude	Longitude	Event	
23/8/23	12:43:20	64	0.1	330	0	3300	3282 G		26.39866	85.129601	Normal	$Y = 0 * X^2 - 0.954 * X + 134.5$
23/8/23	12:44:0	64	0.1	340	20.2	3400	3378 G		26.398233	85.130697	Normal	$X = 11695$
23/8/23	12:44:0	64	0.1	380	20.2	3800	3759 G		26.397865	85.131777	Normal	$Y = 11291$
23/8/23	12:44:31	64	0.1	350	10.1	3500	3473 G		26.398551	85.132735	Normal	
23/8/23	12:45:0	64	0.1	350	10.1	3500	3473 G		26.397454	85.133063	Normal	(R) RURAL ROAD
23/8/23	12:45:5	64	0.1	360	10.1	3600	3568 G		26.397194	85.133621	Normal	Good
23/8/23	12:45:6	64	0.1	390	10.1	3900	3855 G		26.396806	85.134728	Normal	Average
23/8/23	12:45:6	64	0.1	370	10.1	3700	3664 G		26.396655	85.135367	Normal	Poor
23/8/23	12:45:41	64	0.1	390	10.1	3900	3855 G		26.396263	85.136336	Normal	
23/8/23	12:46:0	64	0.1	310	20.2	3100	3091 G		26.39609	85.136935	Normal	
23/8/23	12:46:17	64	0.1	360	10.1	3600	3568 G		26.395945	85.137671	Normal	
23/8/23	12:46:17	64	0.1	350	20.2	3500	3473 G		26.395616	85.138439	Normal	
23/8/23	12:47:0	64	0.1	350	20.2	3500	3473 G		26.395108	85.139191	Normal	
23/8/23	12:47:27	64	0.1	330	30.3	3300	3282 G		26.394387	85.139455	Normal	
23/8/23	12:47:27	64	0.1	310	20.2	3100	3091 G		26.393407	85.139463	Normal	
23/8/23	12:47:27	64	0.1	360	10.1	3600	3568 G		26.392889	85.140735	Normal	
23/8/23	12:48:2	64	0.1	330	30.3	3300	3282 G		26.392756	85.141599	Normal	
23/8/23	12:48:2	64	0.1	310	20.2	3100	3091 G		26.392148	85.141967	Normal	
23/8/23	12:48:2	64	0.1	330	30.3	3300	3282 G		26.391134	85.142147	Normal	
23/8/23	12:48:38	64	0.1	360	10.1	3600	3568 G		26.390547	85.142587	Normal	
23/8/23	12:48:38	64	0.1	330	30.3	3300	3282 G		26.390751	85.143638	Normal	
23/8/23	12:49:0	64	0.1	370	10.1	3700	3664 G		26.390706	85.144437	Normal	
23/8/23	12:49:13	64	0.1	380	20.2	3800	3759 G		26.390836	85.145353	Normal	
23/8/23	12:49:13	64	0.1	350	10.1	3500	3473 G		26.391003	85.146272	Normal	
23/8/23	12:49:13	64	0.1	350	10.1	3500	3473 G		26.39087	85.147073	Normal	
23/8/23	12:49:48	64	0.1	360	10.1	3600	3568 G		26.390159	85.147232	Normal	
23/8/23	12:50:0	64	0.1	390	10.1	3900	3855 G		26.389115	85.147502	Normal	
23/8/23	12:50:0	64	0.1	370	10.1	3700	3664 G		26.387993	85.149513	Normal	
23/8/23	12:50:24	64	0.1	390	10.1	3900	3855 G		26.387782	85.150444	Normal	
23/8/23	12:50:24	64	0.1	350	10.1	3500	3473 G		26.387585	85.15135	Normal	
23/8/23	12:50:24	64	0.1	350	10.1	3500	3473 G		26.387294	85.152353	Normal	
23/8/23	12:50:24	64	0.1	350	20.2	3500	3473 G		26.386889	85.153344	Normal	
23/8/23	12:51:0	64	0.1	350	20.2	3500	3473 G		26.386614	85.154078	Normal	
23/8/23	12:51:0	64	0.1	350	20.2	3500	3473 G		26.386588	85.155194	Normal	
23/8/23	12:51:34	64	0.1	330	30.3	3300	3282 G		26.38646	85.15565	Normal	
23/8/23	12:52:0	64	0.1	340	30.3	3400	3378 G		26.385636	85.156417	Normal	
23/8/23	12:52:9	64	0.1	350	10.1	3500	3473 G		26.38504	85.157307	Normal	
23/8/23	12:53:0	64	0.1	350	10.1	3500	3473 G		26.384728	85.157722	Normal	
23/8/23	12:53:20	64	0.1	360	10.1	3600	3568 G		26.38391	85.158046	Normal	
23/8/23	12:53:20	64	0.1	390	10.1	3900	3855 G		26.38364	85.1589	Normal	

24.8.23
42mm24.08.23
5E24.8.23
4E

24.8.19

23/8/23	12:53:20	64	0.1	370	10.1	3700	3664 G	26.383148	85.159962 Normal
23/8/23	12:54:0	64	0.1	390	10.1	3900	3855 G	26.38274	85.159914 Normal
23/8/23	12:54:0	64	0.1	350	10.1	3500	3473 G	26.381992	85.159576 Normal
23/8/23	12:54:30	64	0.1	350	20.2	3500	3473 G	26.381514	85.159359 Normal
23/8/23	12:54:30	64	0.1	350	20.2	3500	3473 G	26.38108	85.159101 Normal
23/8/23	12:55:0	64	0.1	350	20.2	3500	3473 G	26.380212	85.159196 Normal
23/8/23	12:55:5	64	0.1	330	30.3	3300	3282 G	26.379935	85.160278 Normal
23/8/23	12:55:40	64	0.1	310	20.2	3100	3091 G	26.379711	85.161058 Normal
23/8/23	12:55:40	64	0.1	360	10.1	3600	3568 G	26.379532	85.161857 Normal
23/8/23	12:56:0	64	0.1	330	30.3	3300	3282 G	26.379366	85.162718 Normal
23/8/23	12:56:0	64	0.1	370	10.1	3700	3664 G	26.37911	85.163713 Normal
23/8/23	12:56:15	64	0.1	390	10.1	3900	3855 G	26.378994	85.16449 Normal
23/8/23	12:56:15	64	0.1	350	10.1	3500	3473 G	26.378675	85.165891 Normal
23/8/23	12:56:15	64	0.1	350	20.2	3500	3473 G	26.37855	85.166448 Normal
23/8/23	12:56:51	64	0.1	370	30.3	3700	3664 G	26.378271	85.167632 Normal
23/8/23	12:57:0	64	0.1	310	20.2	3100	3091 G	26.378325	85.168567 Normal
23/8/23	12:57:0	64	0.1	360	10.1	3600	3568 G	26.378561	85.168513 Normal
23/8/23	12:57:0	64	0.1	350	20.2	3500	3473 G	26.378876	85.170209 Normal
23/8/23	12:57:26	64	0.1	350	20.2	3500	3473 G	26.378953	85.170962 Normal
23/8/23	12:57:26	64	0.1	330	30.3	3300	3282 G	26.37922	85.171857 Normal
23/8/23	12:58:1	64	0.1	310	20.2	3100	3091 G	26.379485	85.17284 Normal
23/8/23	12:58:1	64	0.1	360	10.1	3600	3568 G	26.37999	85.173728 Normal
23/8/23	12:58:37	64	0.1	330	30.3	3300	3282 G	26.38044	85.1743 Normal
23/8/23	12:58:37	64	0.1	310	20.2	3100	3091 G	26.380563	85.174743 Normal
23/8/23	12:59:0	64	0.1	360	10.1	3600	3568 G	26.380737	85.175155 Normal
23/8/23	12:59:12	64	0.1	310	20.2	3100	3091 G	26.380926	85.176205 Normal
23/8/23	13:0:0	64	0.1	370	30.3	3700	3664 G	26.38119	85.177233 Normal
23/8/23	13:0:22	64	0.1	310	10.1	3100	3091 G	26.381532	85.177979 Normal
23/8/23	13:1:0	64	0.1	310	20.2	3100	3091 G	26.382166	85.178355 Normal
23/8/23	13:1:33	64	0.1	330	20.2	3300	3282 G	26.382537	85.178562 Normal
23/8/23	13:2:8	64	0.1	360	10.1	3600	3568 G	26.382412	85.178493 Normal
23/8/23	13:2:8	64	0.1	330	20.2	3300	3282 G	26.383468	85.179403 Normal
23/8/23	13:2:44	64	0.1	310	20.2	3100	3091 G	26.383826	85.180113 Normal
23/8/23	13:4:29	64	0.1	350	20.2	3500	3473 G	26.384272	85.180702 Normal
23/8/23	13:11:32	64	0.1	370	30.3	3700	3664 G	26.384355	85.180856 Normal
23/8/23	13:12:41	64	0.1	350	20.2	3500	3473 G	26.385087	85.1818 Normal
23/8/23	13:13:0	64	0.1	370	30.3	3700	3664 G	26.385457	85.182396 Normal
23/8/23	13:13:17	64	0.1	330	20.2	3300	3282 G	26.385782	85.182769 Normal
23/8/23	13:13:52	64	0.1	340	30.3	3400	3378 G	26.386501	85.183291 Normal
23/8/23	13:14:0	64	0.1	390	10.1	3900	3855 G	26.387345	85.183609 Normal
								26.387953	85.183858 Normal
								26.388994	85.184217 Normal
								26.38987	85.184507 Normal
								26.390704	85.18485 Normal

24.8.23
ATM

24.8.23
FE

24.8.23
AC

24.8.23

23/8/23	13:14:27	64	0.1	360	20.2	3600	3568 G	26.391557	85.185139 Normal
23/8/23	13:15:3	64	0.1	370	10.1	3700	3664 G	26.393215	85.185815 Normal
23/8/23	13:16:0	64	0.1	370	10.1	3700	3664 G	26.394668	85.186403 Normal
23/8/23	13:16:13	64	0.1	330	30.3	3300	3282 G	26.395603	85.186835 Normal
23/8/23	13:16:48	64	0.1	350	20.2	3500	3473 G	26.395961	85.187112 Normal
23/8/23	13:17:0	64	0.1	330	30.3	3300	3282 G	26.396161	85.187136 Normal
23/8/23	13:17:24	64	0.1	310	20.2	3100	3091 G	26.396325	85.187268 Normal
23/8/23	13:18:0	64	0.1	360	10.1	3600	3568 G	26.410117	85.19417 Normal
23/8/23	13:18:34	64	0.1	300	30.3	3000	2996 G	26.411165	85.19438 Normal
23/8/23	13:19:0	64	0.1	330	20.2	3300	3282 G	26.41153	85.194177 Normal
23/8/23	13:19:10	64	0.1	330	30.3	3300	3282 G	26.412382	85.194642 Normal
23/8/23	13:19:45	64	0.1	310	20.2	3100	3091 G	26.413399	85.185076 Normal
23/8/23	13:20:0	64	0.1	360	10.1	3600	3568 G	26.414317	85.195104 Normal
23/8/23	13:20:20	64	0.1	310	20.2	3100	3091 G	26.415157	85.195331 Normal
23/8/23	13:20:20	64	0.1	370	30.3	3700	3664 G	26.415662	85.196031 Normal
23/8/23	13:21:0	64	0.1	370	30.3	3700	3664 G	26.415973	85.19659 Normal
23/8/23	13:21:31	64	0.1	360	10.1	3600	3568 G	26.416582	85.197086 Normal
23/8/23	13:21:31	64	0.1	360	10.1	3600	3568 G	26.416969	85.197228 Normal
23/8/23	13:22:6	64	0.1	330	20.2	3300	3282 G	26.417804	85.1976 Normal
23/8/23	13:22:6	64	0.1	320	20.2	3200	3187 G	26.383448	85.160076 Normal
23/8/23	13:22:41	64	0.1	360	10.1	3600	3568 G	26.38339	85.161285 Normal
23/8/23	13:22:41	64	0.1	330	20.2	3300	3282 G	26.38321	85.162642 Normal
23/8/23	13:23:0	64	0.1	310	20.2	3100	3091 G	26.382876	85.163803 Normal
23/8/23	13:23:16	64	0.1	350	20.2	3500	3473 G	26.382261	85.165361 Normal
23/8/23	13:23:16	64	0.1	370	30.3	3700	3664 G	26.382007	85.166176 Normal
23/8/23	13:24:0	64	0.1	360	10.1	3600	3568 G	26.3823	85.166809 Normal
23/8/23	13:24:0	64	0.1	370	30.3	3700	3664 G	26.382319	85.16787 Normal
23/8/23	13:24:27	64	0.1	330	20.2	3300	3282 G	26.380216	85.158898 Normal
23/8/23	13:24:27	64	0.1	310	20.2	3100	3091 G	26.378796	85.158741 Normal
23/8/23	13:25:2	64	0.1	360	10.1	3600	3568 G	26.377454	85.15871 Normal
23/8/23	13:25:2	64	0.1	310	20.2	3100	3091 G	26.376447	85.1547 Normal
23/8/23	13:26:13	64	0.1	370	30.3	3700	3664 G	26.377474	85.14531 Normal
Total:-				402323					
Avg IRI:-				3439					

24.8.23
927M

24.8.23
J-E

24.8.23
J-E

24.8.23
J-E
