

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रोसड़ा

पत्रांक:- 2225/ 12 रोसड़ा, दिनांक:- 12 / 12 / 2023

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रोसड़ा।

सेवामें,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- नई अनुक्षण नीति 2018 शीर्ष MR-3054 योजना अंतर्गत राशि की अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष-नई अनुक्षण नीति 2018 शीर्ष MR-3054 योजना मद अंतर्गत व्यय हेतु विहित प्रपत्र में अधियाचना पत्र संलग्न कर भेजी जा रही है।

अतः अनुरोध है कि संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा किया जाय।

अनु0- यथोक्त।

विश्वासभाजन


12/12/23

कार्यपालक अभियंता,

ग्रामीण कार्य विभाग, कार्य प्रमंडल, रोसड़ा।


12/12/23

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Rosera

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)			Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	1st Year			
					Length (In km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)	9				1st Quarter	2nd Quarter	3rd Quarter	4th Quarter
	2	3	4	5	6	7	8	9		10	11	12	13	14	15	16
1	RM/SA/ROS/19/0009	MDR - Patori	32010302056	2166, 06.07.2019	1.550	30.31112	26.79800	14.07800		06(MBD)2019-20	3/3/2021	27/06/2021	0.70389			
2	RM/SA/ROS/19/0009	T03 - Nakuni	32010302031	2166, 06.07.2019	1.300	35.92835	31.37600	12.22600		06(MBD)2019-20	3/3/2021	27/06/2021	0.61130			
3	RM/SA/ROS/19/0009	Kurban-Baliyar-Rahibi-Bhagaut Road (2007-08)	32010301017	2166, 06.07.2019	2.900	98.84600	54.51900	27.65950		06(MBD)2019-20	3/3/2021	27/06/2021	1.38298			
4	RM/SA/ROS/19/0009	Utkramit middle school paroriya north-east parri paswan tola road	32010301030	2166, 06.07.2019	1.000	35.36979	19.55800	9.44292		06(MBD)2019-20	3/3/2021	27/06/2021	0.47215			
5	RM/SA/ROS/19/0009	BITHAN - JAGMOHRA	NEA22000554	2166, 06.07.2019	9.500	286.8581	150.70300	83.65006		05(MBD)2019-20	24/01/2021	15/02/2021	4.18250	4.18250	4.18250	0.0
Total													7.35282	4.18250	4.18250	0.0

- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.

Sapna Singh

Divisional Account Officer
Works Division, Rosera

Sapna Singh
12/12/2023
Executive Engineer
RWD (W) Division, Rosera

(परिशिष्ट - 'H')

FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of utilization Certificate up to the month of Up to Dec. 23
Scheme **MR 3054 Maintenance**

PIU - Rosera

Sl no.	Name of Scheme	Section No. & Date with Amount (In Lacks)	Amount Received (In Lacks)	Particulars
1	Construction of Rural roads under Scheme MR 3054 Maintenance	BRRDA's Memo No. 165 dt. 7-12-23 Rs. 785308=	32329416=	Certified that out of Rs 32329416= lacks received during the years 23-24... in favor of EX. Engineer, RWD Bihar, 29031834= lacks has been utilized for the purpose of 3054 NMP main Schemes as given in the margin for which it was sanctioned and that the balance of 4377532= lacks remaining unutilized at the end of the period under.

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


Kinds of Checks exercised:-

- Works have been supervised by executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other caudal formalities have been observed.

3. Physical Progress achieved:

- Construction of road works.
- Construction of CD works.


D.A.O.
Works Division,
Rural Works Department


Executive Engineer
Works Division,
Rural Works Department


1st Quarter of 1 st Year											
Government of Bihar OM01			ORDINARY MAINTENANCE INSPECTION REPORT Form OM01							Form:- 27/06/2021	
Rural Works Department Road From : Kurban-Baliyar-Rahthi-Bhagaut Road (20/7-08) Length of Road:- 2.9 km Period:- From...26.09.2021 Inspector :- J.E., RWD Sub- Division Hasanpur, Works Section Rosera			To:- Executive Engineer RWD, Works Division Rosera (Samastipur) Position :- E.E.								Date :-26.09.2021
Standard Work Item			Unit of Work required in each Kilometre								
No	Name	Work Units	1	2	3	4	5	6	10	Comments	
OM101	Pothote Patching	m ²	Nil	Nil	Nil					No pothole found	
OM102	Surface Depression and Rut Patching	m ²	Nil	Nil	Nil					No Surface Depression and Rut Patching found	
OM103	Crack Sealing	Lm	Nil	Nil	Nil					No Crack Sealing Found	
OM104	Surface Treatment										
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil					No Loss of Aggregate (Surface Ravelling) Found.	
	(b) Bleeding/Flushing	m ²	Nil	Nil	Nil					No Bleeding / Flushing required.	
OM105	(c) Crocodile Cracking	m ²	Nil	Nil	Nil					No Crocodile Cracking Found.	
	Edge Repair	m ²	Nil	Nil	Nil					No Edge Repair Required.	
	Digouts	m ²	N.A	N.A	N.A						
OM107	Concrete Pavement	m ³	N.A	N.A	N.A						
OM 200 Shoulder	Other Activities										
	Unsealed Shoulder										
	(a) Edge Drop-off	Lm	Nil	Nil	Nil					No Edge Drop-off Required	
OM 201	(b) Roughness, Scouring of Potholes	Lm	Nil	Nil	Nil					No Roughness, Scouring of Potholes Required.	
	(c) Holding water	Lm	Nil	Nil	Nil					No Holding water found.	
OM 202	Embankment Repair	m ³	Nil	Nil	Nil					No Embankment Repair Required.	
	Other activities		N.A	N.A	N.A						
OM 300 Drainage including culverts major											
MO 301	Surface Drains & Verge	Lm	N.A	N.A	N.A						
MO 302	Culvert Cleaning	No	Nil	Nil	Nil					Not Required	
MO 303	Culvert and Pit Repair	m ³	Nil	Nil	Nil					Not Required	
Other activities (White Washing)			Nil	Nil	Nil					Not Required	

Executive Engineer, Works Division
Rosera (Samastipur)

A.E. RWD

J.E. RWD(w)

Appendix

Bidder

Standard Work Item		Work Units	Unit of Work required in each Kilometre										Comments
No	Name		1	2	3	4	5	6	7	8	9	10	
OM 400 Vegetation													
OM 401	Grass Control												
	(a) Roadside-General Tidy	Ha	Nil	Nil	Nil								Not Required
	(b) Clear near Safety signs, Kilometre posts and Roadside furniture	Ha	Nil	Nil	Nil								Not Required
	Tree and Shrub Management	No	100%	100%	100%								Cutting of Trees and shrubs within time period.
OM402	(Cutting Trees)	No	100%	100%	100%								Trimming of Grass within time period.
	(Cutting Shrubs)	No	100%	100%	100%								
	Other activation (Trimming of Grass)	m ²	Nil	Nil	Nil								Not Required.
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No	Nil	Nil	Nil								Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A								Not Required
OM503	Distance Stones	No	N.A	N.A	N.A								Not Required
OM504	Road Marking	m ²	Nil	Nil	Nil					Nil	Nil	Nil	Not Required
Other Activities													

रमेश देवी

(Signature of Contractor/Authorized Representative)

Date

Time

Place

12/19/23

A.E.RWD

Executive Engineer, Works Division
Roseria (Samastipur)

12/19/23

A.E.RWD(w)

Note:- Enclose photographs with the report.

STANDRAD FORMAT FOR ROADS QUARTERLY

PIU Name :- R.W.D Works Division Rosera

1	Name of the Road	Kurban-Baliyar-Rahthi-Bhagaut Road (2007-08)		
2	Batch No.	RM/SA/ROS/19/0009		
3	Project Id	32010301017		
4	Total Length of Road (in Km)	2.9		
5	Length of Road to Meet Required Service Level	2.9		
6	No. of Total Quarter (ie3 Months as a unit in 5 years)	1st Quarter		
7	Ordinary Maintenance Cost as per Schedule	27.65950		
8	Quarterly Payment : 1/20 of Ordinary Maintenance	1.38298		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]= [3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGATAION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh [6]				1.38298

Date of inpection by E/I or his agent

Prepared by Contractor's Self Control Unit

[Signature]
12/9/23
A.E

[Signature]
12/9/23
Name and Designation of person inspection road

Date

(Signature)


Executive Engineer
R.W.D. (W) Division,
Rosera

Signature of person inspecting Road

Certify by E/I [signature] Date:-

[Signature]
12/9/23
cc

me of Customer: M/S Jain Construction, Pro-Ram Suresh Mandal, Machine no: 19209, Road: Kurban-Baliyar-Rahthi-Bhagaut Road (2007-08), Date: 12-09-23, Section No: 18, Equation: $Y=0.926X+9$

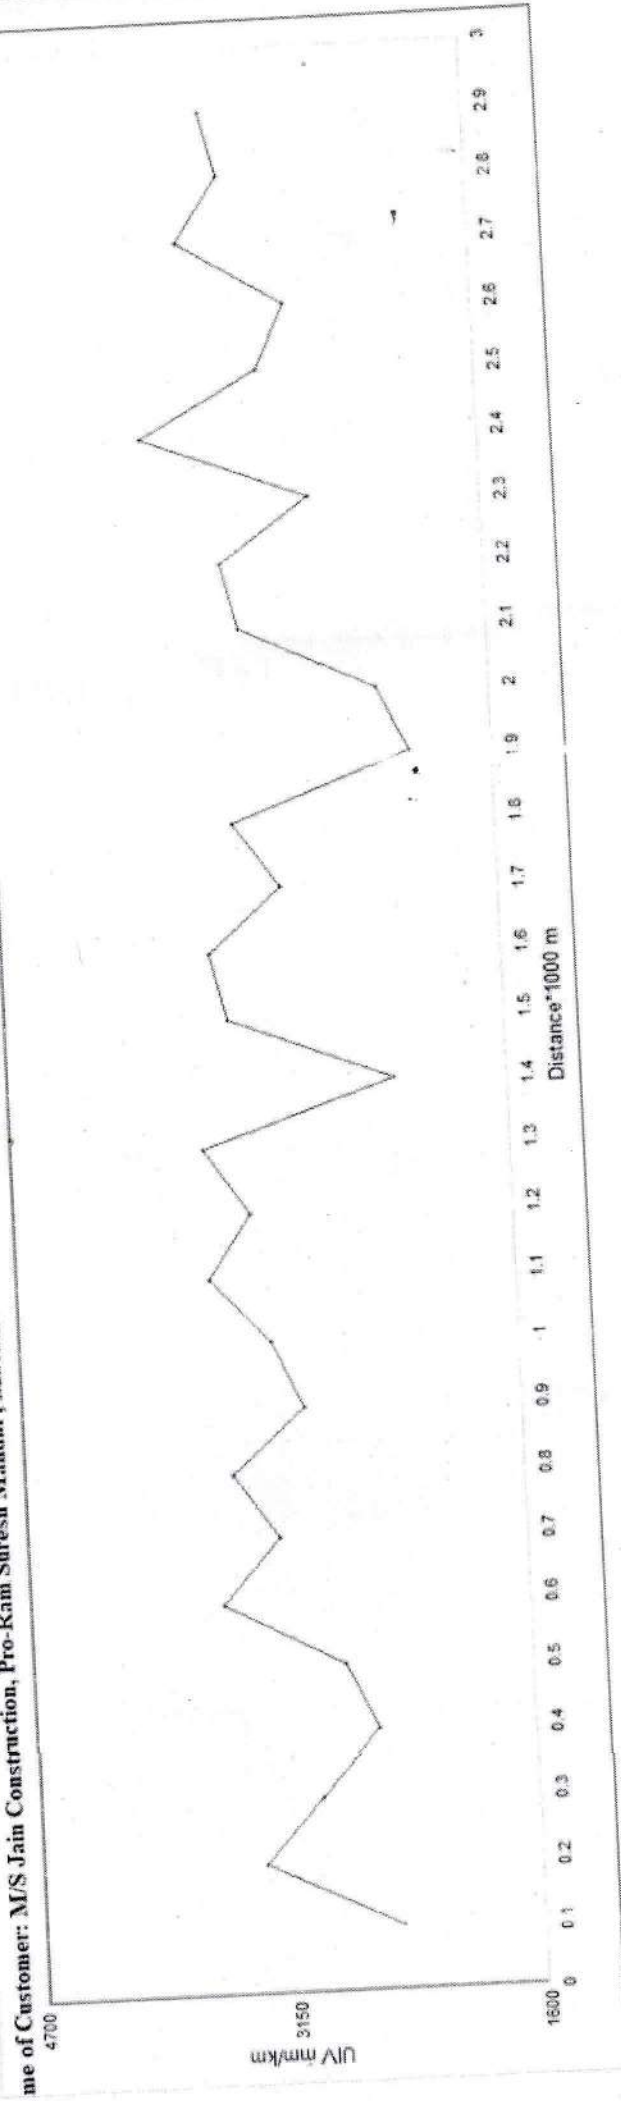

12/9/23
A.E

12/9/23

12/9/23

Name of work : Kurban-Baliyar-Ranathi-Bhagaut Road (2007-08)															
Name of customer : M/S Jain Construction, Pro-Ram Suresh Mandal															
(R)Rural Road															
Good		Average				Poor									
< 4000		4001 - 5000				> 5000									
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
12/09/23	15:44:06	18	100	100	26.0 cm	15.7 Km/Hr	2600.0 mm/Km	2498	3.42	Good	25.757673	N	86.228601	E	Normal
12/09/23	15:44:21	18	100	200	35.0 cm	22.7 Km/Hr	3500.0 mm/Km	3332	4.42	Good	25.755639	N	86.227823	E	Normal
12/09/23	15:44:34	18	100	300	31.0 cm	28.5 Km/Hr	3100.0 mm/Km	2962	3.98	Good	25.755639	N	86.227823	E	Normal
12/09/23	15:44:47	18	100	400	27.0 cm	27.0 Km/Hr	2700.0 mm/Km	2591	3.53	Good	25.754250	N	86.227212	E	Normal
12/09/23	15:45:01	18	100	500	29.0 cm	27.0 Km/Hr	2900.0 mm/Km	2776	3.76	Good	25.753407	N	86.228617	E	Normal
12/09/23	15:45:13	18	100	600	37.0 cm	30.0 Km/Hr	3700.0 mm/Km	3517	4.64	Good	25.753407	N	86.228617	E	Normal
12/09/23	15:45:24	18	100	700	33.0 cm	31.3 Km/Hr	3300.0 mm/Km	3147	4.2	Good	25.752771	N	86.229703	E	Normal
12/09/23	15:45:35	18	100	800	36.0 cm	32.7 Km/Hr	3600.0 mm/Km	3425	4.53	Good	25.752463	N	86.230715	E	Normal
12/09/23	15:45:45	18	100	900	31.0 cm	36.7 Km/Hr	3100.0 mm/Km	2962	3.98	Good	25.752463	N	86.230715	E	Normal
12/09/23	15:45:58	18	100	1000	33.0 cm	27.9 Km/Hr	3300.0 mm/Km	3147	4.2	Good	25.750583	N	86.230208	E	Normal
12/09/23	15:46:14	18	100	1100	37.0 cm	22.2 Km/Hr	3700.0 mm/Km	3517	4.64	Good	25.750583	N	86.230208	E	Normal
12/09/23	15:46:27	18	100	1200	34.0 cm	28.5 Km/Hr	3400.0 mm/Km	3239	4.31	Good	25.749694	N	86.229472	E	Normal
12/09/23	15:46:41	18	100	1300	37.0 cm	25.4 Km/Hr	3700.0 mm/Km	3517	4.64	Good	25.749694	N	86.229472	E	Normal
12/09/23	15:46:58	18	100	1400	24.0 cm	21.1 Km/Hr	2400.0 mm/Km	2313	3.19	Good	25.747616	N	86.226931	E	Normal
12/09/23	15:47:17	18	100	1500	35.0 cm	19.2 Km/Hr	3500.0 mm/Km	3332	4.42	Good	25.746111	N	86.225864	E	Normal
12/09/23	15:47:41	18	100	1600	36.0 cm	14.5 Km/Hr	3600.0 mm/Km	3425	4.53	Good	25.745718	N	86.225928	E	Normal
12/09/23	15:48:10	18	100	1700	31.0 cm	12.8 Km/Hr	3100.0 mm/Km	2962	3.98	Good	25.745718	N	86.225928	E	Normal
12/09/23	15:48:34	18	100	1800	34.0 cm	14.1 Km/Hr	3400.0 mm/Km	3239	4.31	Good	25.745587	N	86.227091	E	Normal
12/09/23	15:48:48	18	100	1900	22.0 cm	24.4 Km/Hr	2200.0 mm/Km	2128	2.96	Good	25.745587	N	86.227091	E	Normal
12/09/23	15:49:02	18	100	2000	24.0 cm	28.0 Km/Hr	2400.0 mm/Km	2313	3.19	Good	25.744337	N	86.226975	E	Normal
12/09/23	15:49:15	18	100	2100	33.0 cm	26.4 Km/Hr	3300.0 mm/Km	3147	4.2	Good	25.744337	N	86.226975	E	Normal

12/9/23

Name of work : Kurban-Baliyar-Rahthi-Bhagaut Road (2007-08)

Name of customer : M/S Jain Construction, Pro-Ram Suresh Mandal

(R)Rural Road									
Good			Average			Poor			
< 4000			4001 - 5000			> 5000			

12/09/23	15:49:33	18	100	2200	34.0 cm	19.8 Km/Hr	3400.0 mm/Km	3239	4.31	Good	25.744337	N	86.226975	E	Normal
12/09/23	15:49:50	18	100	2300	28.0 cm	20.9 Km/Hr	2800.0 mm/Km	2684	3.65	Good	25.743728	N	86.227397	E	Normal
12/09/23	15:50:05	18	100	2400	39.0 cm	24.9 Km/Hr	3900.0 mm/Km	3702	4.86	Good	25.743091	N	86.228191	E	Normal
12/09/23	15:50:21	18	100	2500	31.0 cm	21.8 Km/Hr	3100.0 mm/Km	2962	3.98	Good	25.742209	N	86.229609	E	Normal
12/09/23	15:50:40	18	100	2600	29.0 cm	19.0 Km/Hr	2900.0 mm/Km	2776	3.76	Good	25.741479	N	86.229872	E	Normal
12/09/23	15:51:01	18	100	2700	36.0 cm	17.1 Km/Hr	3600.0 mm/Km	3425	4.53	Good	25.740528	N	86.229642	E	Normal
12/09/23	15:51:18	18	100	2800	33.0 cm	20.9 Km/Hr	3300.0 mm/Km	3147	4.2	Good	25.739955	N	86.229792	E	Normal
12/09/23	15:51:32	18	100	2900	34.0 cm	25.4 Km/Hr	3400.0 mm/Km	3239	4.31	Good	25.739692	N	86.230162	E	Normal

12/9/23
A.E

12/9/23
A.E

12/9/23
A.E

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रोसड़ा

Name of Road -	Kurban-Baliyar-Rahthi-Bhagaut Road (2007-08)
Name of Scheme -	MR 3054 (New Maintenance Policy - 2018)
Name of Contractor/Agency-	M/S Jain Construction
Length of Road	- 2.9 km
Project ID	- 32010301017
Package No.	- RM/SA/ROS/19/0009
Name of Block	- Hasanpur

Certified that all item
wise 100% Measurement
has been checked by me




Junior Engineer RWD
Work Section Rosera
Works Division, **Hasanpur**

Certified that all item
wise 50% Measurement
has been checked by me



Assistant Engineer RWD
Work Section Rosera
Works Division, **Hasanpur**

Certified that all item
wise 10% Measurement
has been checked by me



Executive Engineer
RWD Works Division,
Rosera
