

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सहरसा

पत्रांक-1939-मु/

सहरसा, दिनांक 26.12.23 /

प्रेषक:-

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सहरसा।

सेवा में,

नोडल पदाधिकारी,
3054 (M.R) कोषांग,
बिहार, पटना।

विषय:- शीर्ष 3054 नई अनुरक्षण नीति-2018 अंतर्गत Initial Rectification and Surface renewal. कराये गये कार्य हेतु अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक कहना है कि विहित प्रपत्र में संलग्न विवरणी के अनुसार शीर्ष Mr 3054 New Maintenance Policy-2018. अन्तर्गत Repair of Road KNR Navhatta to Bonoba path & Muradpur पथ का Initial Rectification and Surface renewal. कराये गये कार्य हेतु राशि Rs.120.47804/- (रुपये एक करोड़ बीस लाख सैंतालीस हजार आठ सौ चार मात्र) राशि की आवश्यकता है।

अतः कार्यहित में अनुरोध है कि उक्त अधियाचित राशि Rs.120.47804/- (रुपये एक करोड़ बीस लाख सैंतालीस हजार आठ सौ चार मात्र) उपलब्ध कराने की कृपा की जाय ताकि कराये जा रहे कार्यों का विपत्र भुगतान किया जा सके।

- अनु०:- (1) अधियाचना प्रपत्र
(2) IRI Value Report
(3) Map
(4) प्रमाण-पत्र।

विश्वासभाजून

26-12-2023

कार्यपालक अभियन्ता

ग्रा०का०वि०, कार्य प्रमण्डल,

सहरसा

Rural Works Department

MR NEW MAINTENANCE POLICY-2018. ALLOTMENT REQUISITION

Name of Division:- RWD Works Division Saharsa

SL. No.	Year	Name of Road	Name of Contractor (In English)	Project Id	Administrative		Agreement Amount		Value of IRU (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Allotment Received (in Lacs)	Total Expenditure as per MIS (in Lacs)	Value of Measurement (in Lacs)	Current Demand (in Lacs)	Remarks
					Sanction	Amount (in Lacs)	Main Work	Maintenance								
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
65	2019-20	Repair of Road KNR Navhata to Bonoba path & Muradpur	Yeshar Construction Private Limited	20904308069	5.470	194.10600	120.47804	49.65695	2694	25	5%	0.00000	0.00000	120.47804	120.47804	Complete

D.A.O.
RWD Works Division
Saharsa

26-12-2023

B.L.

Executive Engineer
RWD Works Division
Saharsa

26/12/23

26-12-2023

**OFFICE OF THE EXECUTIVE ENGINEER
RWD WORKS DIVISION SAHARSA.**

**Name of Scheme:- Repair of Road KNR Navhatta to Bonoba path & Muradpur ,PACKAGE No-
RM/SA/SAH/20/0001, Project ID- 20904308069.**

**Certified that all item wise 100%
Measurement has been taken by me**


21/12/23


Junior Engineer
RWD Work section Nauhatta
Works Division Saharsa

**Certified that all item wise 50%
Measurement has been cheked by me**


21/12/23

Assistant Engineer
RWD Work Section Nauhatta
Works Division Saharsa

**Certified that all item wise 10%
Measurement has been cheked by me**


26-12-2023

Executive Engineer
Rural work Department
Works Division Saharsa

Name of Road - Repair of Road KNR Navhatta to Bonoba path & Muradpur

Name of Contractor Yeshar Construction Private Limited						Batch Name -RM/SA/SAH/20/0001					
Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGOR	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	Y			
21-12-2023	11:53:55	74	0.000	0	0.0	0	0	G	25.996655	86.488391	Normal
21-12-2023	11:54:34	74	0.100	270	10.1	2700	3167	G	25.996060	86.488842	Normal
21-12-2023	11:55:00	74	0.100	210	10.1	2100	2577	G	25.994411	86.487855	Normal
21-12-2023	11:55:14	74	0.100	180	10.1	2000	2478	G	25.993783	86.487668	Normal
21-12-2023	11:55:25	74	0.100	270	10.1	2700	3167	G	25.994324	86.487868	Normal
21-12-2023	11:56:00	74	0.100	180	10.1	2000	2478	G	25.992334	86.486824	Normal
21-12-2023	11:56:34	74	0.100	200	10.1	2000	2478	G	25.991461	86.486443	Normal
21-12-2023	11:57:09	74	0.100	180	10.1	2000	2478	G	25.990947	86.486785	Normal
21-12-2023	11:57:21	74	0.100	270	10.1	2700	3167	G	25.989843	86.485975	Normal
21-12-2023	11:58:02	74	0.100	180	10.1	2000	2478	G	25.989253	86.485495	Normal
21-12-2023	11:58:37	74	0.100	200	10.1	2000	2478	G	25.988234	86.485528	Normal
21-12-2023	11:59:08	74	0.100	270	10.1	2700	3167	G	25.987073	86.485468	Normal
21-12-2023	11:59:45	74	0.100	180	10.1	2000	2478	G	25.986315	86.485474	Normal
21-12-2023	12:00:04	74	0.100	270	10.1	2700	3167	G	25.986320	86.485687	Normal
21-12-2023	12:00:29	74	0.100	210	10.1	2100	2577	G	25.985342	86.485720	Normal
21-12-2023	12:01:07	74	0.100	190	10.1	1900	2380	G	25.983014	86.485645	Normal
21-12-2023	12:01:48	74	0.100	210	10.1	2100	2577	G	25.982039	86.485738	Normal
21-12-2023	12:01:57	74	0.100	180	10.1	2000	2478	G	25.981051	86.485500	Normal
21-12-2023	12:02:15	74	0.100	270	10.1	2700	3167	G	25.980246	86.485145	Normal
21-12-2023	12:02:38	74	0.100	180	10.1	2000	2478	G	25.979372	86.484606	Normal
21-12-2023	12:02:51	74	0.100	200	10.1	2000	2478	G	25.979437	86.484323	Normal
21-12-2023	12:03:05	74	0.100	180	10.1	2000	2478	G	25.978055	86.484181	Normal
21-12-2023	12:03:25	74	0.100	270	10.1	2700	3167	G	25.977199	86.483703	Normal
21-12-2023	12:03:41	74	0.100	180	10.1	2000	2478	G	25.976785	86.482715	Normal
21-12-2023	12:03:59	74	0.100	210	10.1	2100	2577	G	25.975634	86.482703	Normal
21-12-2023	12:04:35	74	0.100	180	10.1	2000	2478	G	25.975138	86.482646	Normal
21-12-2023	12:05:45	74	0.100	270	10.1	2700	3167	G	25.974198	86.482110	Normal

$$Y = 0 * X^2 + 0.984 * X + 510.7$$

$$X =$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

21/12/23

21/12/23

21/12/2023

21-12-2023	12:06:15	74	0.100	180	10.1	2000	2478	G	25.973786	86.482190	Normal
21-12-2023	12:06:51	74	0.100	200	10.1	2000	2478	G	25.972617	86.481271	Normal
21-12-2023	12:07:14	74	0.100	180	10.1	2000	2478	G	25.971591	86.481394	Normal
21-12-2023	12:07:31	74	0.100	270	10.1	2700	3167	G	25.970826	86.480966	Normal
21-12-2023	12:07:51	74	0.100	180	10.1	2000	2478	G	25.970245	86.480238	Normal
21-12-2023	12:08:15	74	0.100	210	10.1	2100	2577	G	25.970247	86.480393	Normal
21-12-2023	12:08:34	74	0.100	180	10.1	2000	2478	G	25.969777	86.478405	Normal
21-12-2023	12:08:56	74	0.100	270	10.1	2700	3167	G	25.967928	86.479726	Normal
21-12-2023	12:09:15	74	0.100	180	10.1	2000	2478	G	25.966241	86.479908	Normal
21-12-2023	12:09:57	74	0.100	200	10.1	2000	2478	G	25.965471	86.479568	Normal
21-12-2023	12:10:13	74	0.100	180	10.1	2000	2478	G	25.965523	86.480197	Normal
21-12-2023	12:10:35	74	0.100	270	10.1	2700	3167	G	25.965309	86.479354	Normal
21-12-2023	12:10:47	74	0.100	180	10.1	2000	2478	G	25.963597	86.478913	Normal
21-12-2023	12:10:53	74	0.100	200	10.1	2000	2478	G	25.965300	86.479455	Normal
21-12-2023	12:11:01	74	0.100	270	10.1	2700	3167	G	25.962760	86.478829	Normal
21-12-2023	12:11:05	74	0.100	180	10.1	2000	2478	G	25.961814	86.478549	Normal
21-12-2023	12:11:34	74	0.100	270	10.1	2700	3167	G	25.960967	86.477958	Normal
21-12-2023	12:11:57	74	0.100	180	10.1	2000	2478	G	25.960180	86.477676	Normal
21-12-2023	12:12:19	74	0.100	210	10.1	2100	2577	G	25.959652	86.477000	Normal
21-12-2023	12:12:47	74	0.100	180	10.1	2000	2478	G	25.958602	86.476975	Normal
21-12-2023	12:12:59	74	0.100	270	10.1	2700	3167	G	25.957114	86.475525	Normal
21-12-2023	12:13:16	74	0.100	180	10.1	2000	2478	G	25.956513	86.474219	Normal
21-12-2023	12:13:39	74	0.100	270	10.1	2700	3167	G	25.955559	86.474716	Normal
21-12-2023	12:13:54	74	0.100	180	10.1	2000	2478	G	25.954819	86.473980	Normal
21-12-2023	12:14:26	74	0.100	210	10.1	2100	2577	G	25.953793	86.473790	Normal
21-12-2023	12:14:47	74	0.100	180	10.1	2000	2478	G	25.953117	86.473426	Normal
21-12-2023	12:15:21	74	0.070	180	10.1	2000	2478	G	25.952841	86.473128	Normal
21-12-2023	12:15:22	74									
Total							148204.0				
Average							2694.62				

21/12/23
JE

21/12/23
Kc

21-12-2023

Name of Customer :	har Construction Private Limited
Name of Work/ Road :	Itita to Bonoba path & Muradpur
Lab Job number	
Date :	12/21/2023
Section No.	74

Test Date :	12/21/2023	Road Name :	Itita to Bonoba path & Muradpur
Machine No :	403	Road Type :	(A) ASPHALTIC
Start S No :		Side :	
Start E No :		Interval	
Weather :		UIV Range :	1380 To 4000 mm/km
Start Location :		Dist Range :	0 To 5.6 0.1 * 1000 m
End Location :		Equation :	test

Print


Generate Report and Graph

Redraw Graph

Map View

File : E:\BUMP INDICATOR\Saharsa\21122023.xls, Section No. : 74, Eqn. test

Name of Customer : Yeshar Construction Private Limited, Name of Work/ Road : Repair of Road KNR Navhatta to

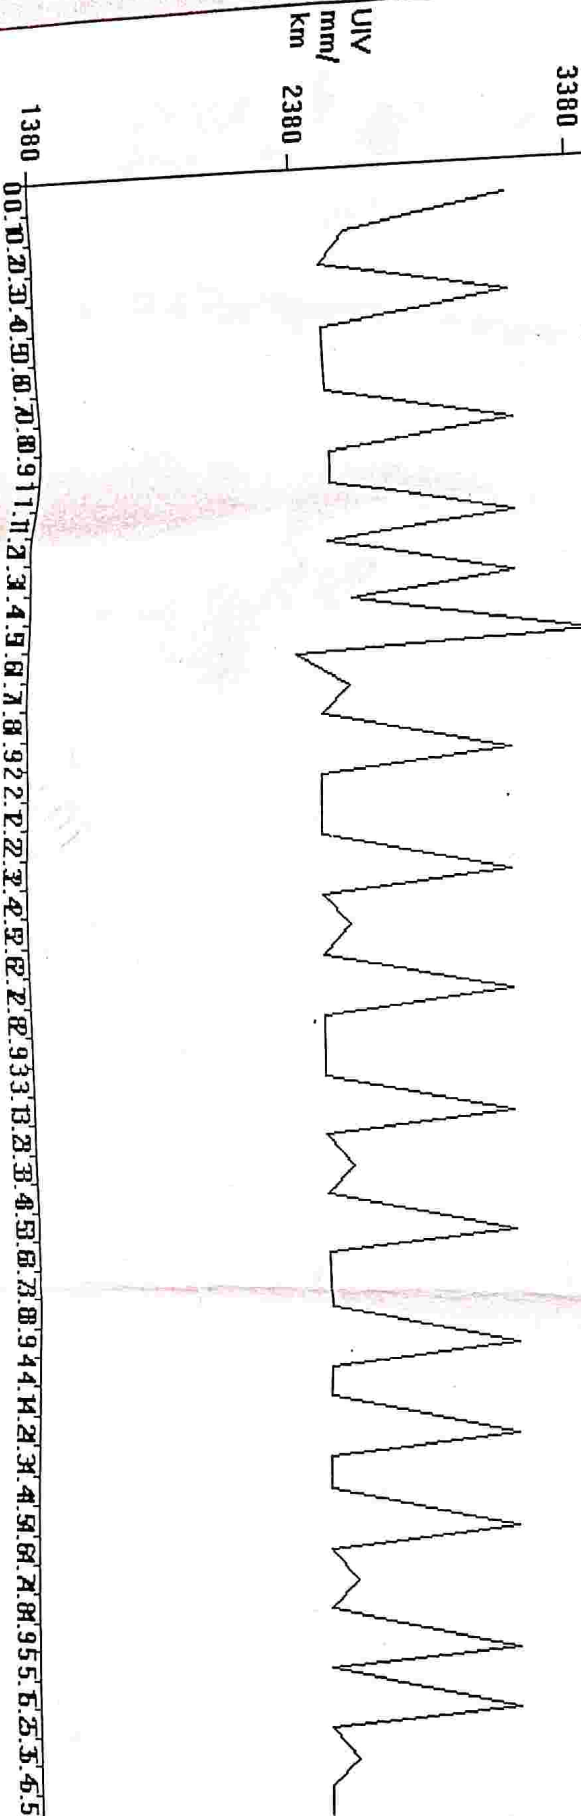

Distance * 1000 m

21/12/23

21/12/23

21/12/23
