

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिमरी बख्तियारपुर।

Email ID :- ee.simribakhtiyarpur@gmail.com (Mob-8986915464)

पत्रांक 2590 Ans/
प्रेषक,

सिमरी बख्तियारपुर, दिनांक- 01/12/2022

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल सिमरी बख्तियारपुर।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी
—सह—सचिव BRRDA
बिहार, पटना।

विषय :- MR-3054 (New Maintenance Policy 2018) के अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण हेतु अधियाचना के संबंध में।

प्रसंग :- अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार पटना के पत्रांक मु०अ०-4 (मु०) 3054-04-229/229/2021- 2021- 1135 अनु०, दिनांक 09.03.2022


महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः MR-3054(New Maintenance Policy 2018) के अन्तर्गत (MR-N/19-20 SimriBakhtiyarpur/11) 1. “Daini Tola to PWD Road” 2. “MDR T01 to Tegraha” पथ के अनुरक्षण हेतु अधियाचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद है। उक्त पथों में ए०टी०आर० लंबित नहीं है।

अनु० :- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिमरी बख्तियारपुर।

Requisition Formet for Scheme Head MR (3054) Under Bihar Rural Road Maintenance Policy 2018(Initial Rectification, and Surface Renewal)

Name of work Division:-Simri Bakhtiyarpur
Government Of Bihar
OM01Q

1st year(2nd Quarter)

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Rural Works Department

Road From: Daini Tola to PWD road

Package No.-MR-N/19-20 SimriBakhtiyarpur/11

Length of Road :-3.378KM

Period:-From 24/07/2021 To 23/10/2021

Inspector : JE RWD Sub Division Banma itahari

To

Executive Engineer

RWD, Works Division Simri Bakhtiyarpur

Date:-.....

Position:-JE

No.	Standard work item	Work Units	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed Pavement												
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil	Nil						No Pothole Found
OM102	Surface Depression and Rut Patching	m3	Nil	Nil	Nil	Nil	Nil						Not Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil						No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil	Nil						No Loss of Aggregate (Surface Ravelling) Found
	(b) Bleeding / Flushing	m2	Nil	Nil	Nil	Nil	Nil						No Bleeding / Flushing required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil	Nil						No Crocodile Cracking Found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil	Nil						NO Edge Repair required
OM106	Digouts	m2	Nil	Nil	Nil	Nil	Nil						Not required
OM107	Concrete Pavement	m3	Nil	Nil	Nil	Nil	Nil						Not required
	Other activities	m2	Nil	Nil	Nil	Nil	Nil						Not required
OM200	Shoulder												
OM201	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil						No Edge Drop-off found
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil						Not required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil						NO Holding Water Found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil	Nil						Not required
	Other activities(rain cuts)												
OM 300	Drainage including culverts major and												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A	N.A						Not required
OM302	Culvert Cleaning	Lm	4	6		1							Defects Rectified within
OM303	Culvert and Pit Repair	m2	Nil	Nil	Nil	Nil	Nil						Not required
	Other activities	m2	Nil	Nil	Nil	Nil	Nil						Not required

25/11/22
25-11-2022
PE

25/11/22
25-11-2022
PE

Standard work item No.	Name	Work Units	Units of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation													
OM401	Grass Control												
	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	b) Clear near safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and shrub Management	Ha	Nil	Nil	Nil	Nil							Not Required
	Other activities	M2	Nil	Nil	Nil	Nil							Not Required
OM500	Signage and Road Safety												
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard stones	LM	Nil	Nil	Nil	Nil							Not Required
OM503	Distance stones	No	Nil	Nil	Nil	Nil							Not Required
OM504	Road marking	M2	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Signature of Contractor/ Authorized representative

Date

Time

Place

Note :- Enclose Photographs with this report.

AB
25/11/22
SE.

shaj
25-11-2022
AB

shaj
01/12/22
Executive Engineer
R.W.D. Works Division
Simabakhtiyarpur

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1st year (end quarter)
TU Name :- Rural Works Department Works Division Simri Bakhtiyarpur

1	Name of the Road	Daini Tola to PWD road		
2	Batch No.	RM/SA/SIM/19/0013		
3	Project ID	20904302030		
	Total Length of Road (in Km)	3.378		
5	Length of Road to meet Required Service Level [Completed length] (in Km) [1]	3.378		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	41.32251		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.06612		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATAION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TO BE PAID FOR THE QUARTER/ DEMAND (IN Lakh) [6]				2.06612

Date of inspection by E/I or his agent
prepared by Contractor's self Control unit

Name and Designation of person inspecting road

(Signature)
Executive Engineer
R.W.D. Works Division
Simri Bakhtiyarpur

Date


Signature of person inspection road

25/11/22

25-11-2022
AE

Certify by E/I [signature] Date:-

Name of work : Dani Tola - PWD Road															
Name of customer : Prasar Remodelling & Construction Pvt Ltd															
(R)Rural Road															
GoodAveragePoor															
< 40004001 - 5000> 5000															
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	Ul(mm/Km)	Corrected Ul (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
10/11/22	14:38:02	55	100	100	34.0 cm	5.4 Km/Hr	3400.0 mm/Km	3264	4.34	Good	25.6915891	N	86.617997751	E	Breaker
10/11/22	14:38:39	55	100	200	25.0 cm	10.0 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:38:55	55	100	300	35.0 cm	20.0 Km/Hr	3500.0 mm/Km	3357	4.45	Good	25.6912813	N	86.61177716	E	Curve
10/11/22	14:39:11	55	100	400	36.0 cm	22.9 Km/Hr	3600.0 mm/Km	3451	4.57	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:39:28	55	100	500	15.0 cm	22.0 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.6912813	N	86.61177716	E	Breaker
10/11/22	14:39:44	55	100	600	23.0 cm	22.0 Km/Hr	2300.0 mm/Km	2237	3.1	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:39:58	55	100	700	21.0 cm	25.4 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:40:12	55	100	800	23.0 cm	25.9 Km/Hr	2300.0 mm/Km	2237	3.1	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:40:33	55	100	900	25.0 cm	16.9 Km/Hr*	2500.0 mm/Km	2423	3.33	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:40:49	55	100	1000	21.0 cm	22.9 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:41:05	55	100	1100	14.0 cm	22.2 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.6912813	N	86.61177716	E	Breaker
10/11/22	14:41:22	55	100	1200	13.0 cm	20.8 Km/Hr	1300.0 mm/Km	1303	1.91	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:41:39	55	100	1300	16.0 cm	21.1 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:41:53	55	100	1400	12.0 cm	25.4 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.6912813	N	86.61177716	E	Curve
10/11/22	14:42:07	55	100	1500	17.0 cm	26.2 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:42:21	55	100	1600	19.0 cm	24.9 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:42:36	55	100	1700	18.0 cm	24.5 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.6912813	N	86.61177716	E	Breaker
10/11/22	14:42:53	55	100	1800	22.0 cm	21.6 Km/Hr	2200.0 mm/Km	2143	2.98	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:43:06	55	100	1900	17.0 cm	26.7 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:43:25	55	100	2000	38.0 cm	19.0 Km/Hr	3800.0 mm/Km	3638	4.79	Good	25.6912813	N	86.61177716	E	Normal
10/11/22	14:43:39	55	100	2100	24.0 cm	24.6 Km/Hr	2400.0 mm/Km	2330	3.21	Good	25.6912813	N	86.61177716	E	Normal

 25/11/22
 25-11-2022
 R.W.D. Works Division
 Simsbaktiyanpur

Name of work : Dani Tola - PWD Road															
Name of customer : Prasara Remodelling & Construction Pvt Ltd															
(R)Rural Road															
Good		Average				Poor									
< 4000		4001 - 5000				> 5000									
10/11/22	14:43:56	55	100	2200	15.0 cm	22.0 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.6912813	N	86.6117716	E	Brekar
10/11/22	14:44:12	55	100	2300	12.0 cm	22.2 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.6912813	N	86.6117716	E	Normal
10/11/22	14:44:31	55	100	2400	25.0 cm	20.0 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.6912813	N	86.6117716	E	Brekar
10/11/22	14:45:02	55	100	2500	36.0 cm	11.3 Km/Hr	3600.0 mm/Km	3451	4.57	Good	25.7037535	N	86.6223993	E	Normal
10/11/22	14:45:23	55	100	2600	21.0 cm	16.5 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.7037535	N	86.6223993	E	Normal
10/11/22	14:45:53	55	100	2700	25.0 cm	12.8 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.7037535	N	86.6223993	E	Normal
10/11/22	14:46:31	55	100	2800	22.0 cm	9.5 Km/Hr	2200.0 mm/Km	2143	2.98	Good	25.7037535	N	86.6223993	E	Normal
10/11/22	14:46:58	55	100	2900	31.0 cm	13.8 Km/Hr	3100.0 mm/Km	2984	4.01	Good	25.7037535	N	86.6223993	E	Normal
10/11/22	14:47:21	55	100	3000	20.0 cm	13.5 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7037535	N	86.6223993	E	Corve
10/11/22	14:47:54	55	100	3100	35.0 cm	11.8 Km/Hr	3500.0 mm/Km	3357	4.45	Good	25.7005453	N	86.6270380	E	Normal
10/11/22	14:48:16	55	100	3200	19.0 cm	16.0 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.7005453	N	86.6270380	E	Brekar
10/11/22	14:48:30	55	100	3300	18.0 cm	25.2 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.7005453	N	86.6270380	E	Normal


25/11/22
25/11/22

25-11-2022
AS

48/11/22
01/11/22
Engineer

25-11-2022
AE

25/11/22
Executive Engineer
R.W.D. Works Division
Sagaribhivarpur

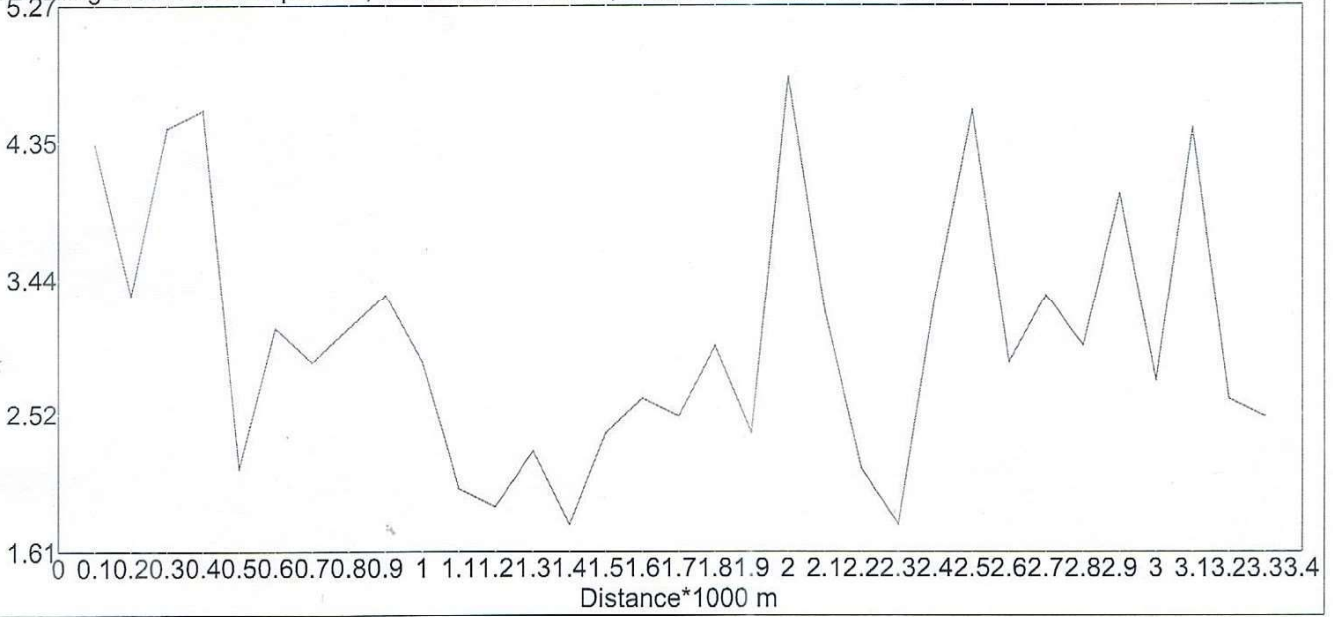

AP
25/11/22
SE

S. H. J.
25-11-2022
AE

SV
01/12/22
Executive Engineer
R.W.D. Works Division
Simr Bakhtiyarnur
