

कार्यपालक अभियंता का कार्यालय,

ग्रामीण कार्य विभाग, कार्य प्रमण्डल, धमदाहा।

पत्रांक.....54.....

धमदाहा/दिनांक.....09-01-2023

प्रेषक:-

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, धमदाहा।

सेवा में,

नोडल पदाधिकारी MR(3054),
ग्रामीण कार्य विभाग,
बिहार पटना।

विषय:- शीर्ष MR(3054) नई अनुरक्षण निति 2018 मरम्मति एवं सम्पोषण योजना मद में राशि आवंटित करने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष MR(3054) नई अनुरक्षण निति 2018 मरम्मति एवं सम्पोषण योजना मद में इस प्रमण्डल अन्तर्गत राशि की आवश्यकता है।

अतः अनुरोध है कि अधियाचित राशि आवंटित करने की कृपा की जाय।

अनु० यथोक्त।

विश्वासभाजन

अधियाचना कि प्रति(मुल में)

09-01-23

कार्यपालक अभियंता

ग्रामीण कार्य

विभाग,

कार्य प्रमण्डल, धमदाहा

09/01/23

Name of Works Division-EXECUTIVE ENGINEER RWD WORKS DIVISION DHAMDAHIA

Sl No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval Length (in m)	Administrative Approval Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)	Agreement No & Date	Date of Completion as per Agreement	Actual date of Completion	Value OF IRI (in mm/m)	Thickness of Bitumen Layer (in MM)	Value of Bitumen Content in Percent	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	MR-N22.23	Barhara kothi To Harirahi	21105308072	1304/23.03.22	4.7	229.4	151.08787	46.90812	37/MBD/202	03.05.23	09.01.23	2.905	25mmstdbc	5.0stdbc	0.000000	0.000000	150.68787	150.68787
2																		
TOTAL RS. One crore fifty lakh sixty eight thousand seven hundred eighty seven only.																		

1 SIGNED HARD COPY & SOFT COPY (IN EXCEL) OF RECORDED IRI IS ENCLOSED
2 UP-TO-DATE PHYSICAL PROGRESS HAS BEEN UPLOADED IN MIS

SR DIVISIONAL ACCOUNTS OFFICER,
RURAL WORKS DEPARTMENT
WORKS DIVISION DHAMDAHIA, PURNEA

EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION DHAMDAHIA, PURNEA

09/01/23

Lab Job number :01(2023)

Date :08-01-23

Name of Customer :DHANANJAY KUMAR SINGH

Name of Work/ Road :BARAHARA KOTHI TO HARARAH

Sr.no Location of Corrected U.I Road category
test(in km) value(mm/km)

174	0	2478 G
175	0	2970 G
176	0	2577 G
177	0	2773 G
178	0	2380 G
179	0	3069 G
180	0	2380 G
181	0	2577 G
182	0	2872 G
183	0	2380 G
184	0	2183 G
185	0	2872 G
186	0	2970 G
187	0	3364 G
188	0	3167 G
189	0	2970 G
190	0	2872 G
191	0	2872 G
192	0	2085 G
193	0	2577 G
194	0	3069 G
195	0	3167 G
196	0	3462 G
197	0	3069 G
198	0	3069 G
199	0	3069 G
200	0	3561 G
201	0	2675 G
202	0	3167 G
203	0	3167 G
204	0	2675 G
205	0	2773 G
206	0	3069 G
207	0	3069 G
208	0	2773 G
209	0	2970 G
210	0	2675 G
211	0	2478 G
212	0	2970 G
213	0	2773 G
214	0	2773 G
215	0	3561 G
216	0	3167 G
217	0	3364 G
218	0	3265 G
219	0	3364 G
220	0	2970 G
AVERAGE		2905.362

144mm/km
09/01/23
JB

9/1/23
JB

9.1.23

Date	Time	Section	Length	Bumps	Speed	OR	ROAD	IRI	Latitude	Longitude	Event
No.		In km	In mm	Rate	mm/km	UV					
8/1/23	12:56:0	76	0.1	200	0	2000	2478 G	3.39	25.77366	87.10808	Normal
8/1/23	12:56:0	76	0.1	250	20.2	2500	2970 G	3.99	25.77324	87.10897	Normal
8/1/23	12:56:24	76	0.1	210	10.1	2100	2577 G	3.51	25.77257	87.10961	Normal
8/1/23	12:56:24	76	0.1	230	20.2	2300	2773 G	3.75	25.77271	87.11045	Normal
8/1/23	12:57:0	76	0.1	190	20.2	1900	2380 G	3.27	25.77317	87.11113	Normal
8/1/23	12:57:0	76	0.1	260	20.2	2600	3069 G	4.11	25.77316	87.11209	Normal
8/1/23	12:57:33	76	0.1	190	20.2	1900	2380 G	3.27	25.773	87.1131	Normal
8/1/23	12:57:33	76	0.1	210	20.2	2100	2577 G	3.51	25.77254	87.11384	Normal
8/1/23	12:58:0	76	0.1	240	20.2	2400	2872 G	3.87	25.77249	87.11448	Normal
8/1/23	12:58:8	76	0.1	190	20.2	1900	2380 G	3.27	25.77232	87.11564	Normal
8/1/23	12:58:8	76	0.1	170	20.2	1700	2183 G	3.03	25.77146	87.11588	Normal
8/1/23	12:58:44	76	0.1	240	20.2	2400	2872 G	3.87	25.77109	87.11665	Normal
8/1/23	12:59:0	76	0.1	250	10.1	2500	2970 G	3.99	25.77156	87.11736	Normal
8/1/23	12:59:19	76	0.1	290	20.2	2900	3364 G	4.46	25.77232	87.11766	Normal
8/1/23	12:59:19	76	0.1	270	20.2	2700	3167 G	4.22	25.77307	87.11816	Normal
8/1/23	12:59:54	76	0.1	250	20.2	2500	2970 G	3.99	25.77357	87.1188	Normal
8/1/23	13:0:0	76	0.1	240	20.2	2400	2872 G	3.87	25.77339	87.1198	Normal
8/1/23	13:0:0	76	0.1	240	20.2	2400	2872 G	3.87	25.77325	87.12076	Normal
8/1/23	13:0:29	76	0.1	160	20.2	1600	2085 G	2.91	25.77292	87.12165	Normal
8/1/23	13:0:29	76	0.1	210	20.2	2100	2577 G	3.51	25.77282	87.12264	Normal
8/1/23	13:1:5	76	0.1	260	20.2	2600	3069 G	4.11	25.77273	87.12357	Normal
8/1/23	13:1:5	76	0.1	270	20.2	2700	3167 G	4.22	25.77269	87.12455	Normal
8/1/23	13:1:5	76	0.1	300	20.2	3000	3462 G	4.57	25.77288	87.12547	Normal
8/1/23	13:3:0	76	0.1	260	10.1	2600	3069 G	4.11	25.77453	87.12936	Normal
8/1/23	13:3:26	76	0.1	260	20.2	2600	3069 G	4.11	25.77435	87.13034	Normal
8/1/23	13:3:26	76	0.1	260	20.2	2600	3069 G	4.11	25.77417	87.13125	Normal
8/1/23	13:4:36	76	0.1	310	20.2	3100	3561 G	4.69	25.77425	87.13399	Normal
8/1/23	13:5:0	76	0.1	220	20.2	2200	2675 G	3.63	25.7747	87.13487	Normal
8/1/23	13:5:12	76	0.1	270	20.2	2700	3167 G	4.22	25.77515	87.13567	Normal
8/1/23	13:5:12	76	0.1	270	20.2	2700	3167 G	4.22	25.77584	87.13638	Normal
8/1/23	13:5:47	76	0.1	220	10.1	2200	2675 G	3.63	25.77656	87.1369	Normal
8/1/23	13:6:0	76	0.1	230	20.2	2300	2773 G	3.75	25.77739	87.13715	Normal
8/1/23	13:6:22	76	0.1	260	20.2	2600	3069 G	4.11	25.77822	87.13746	Normal
8/1/23	13:6:22	76	0.1	260	10.1	2600	3069 G	4.11	25.77885	87.13806	Normal
8/1/23	13:6:22	76	0.1	260	10.1	2600	3069 G	3.75	25.77819	87.13746	Normal
8/1/23	13:10:0	76	0.1	230	10.1	2300	2773 G	3.99	25.77734	87.13715	Normal
8/1/23	13:10:29	76	0.1	250	20.2	2500	2970 G	3.63	25.77643	87.13687	Normal
8/1/23	13:11:0	76	0.1	220	10.1	2200	2675 G	3.39	25.77577	87.13631	Normal
8/1/23	13:11:4	76	0.1	200	10.1	2000	2478 G	3.99	25.77512	87.13564	Normal
8/1/23	13:11:40	76	0.1	250	20.2	2500	2970 G	3.75	25.77467	87.1348	Normal
8/1/23	13:11:40	76	0.1	230	20.2	2300	2773 G	3.75	25.77423	87.13394	Normal
8/1/23	13:12:0	76	0.1	230	20.2	2300	2773 G	4.69	25.77383	87.1331	Normal
8/1/23	13:12:15	76	0.1	310	20.2	3100	3561 G	4.22	25.77437	87.13024	Normal
8/1/23	13:13:0	76	0.1	290	20.2	2900	3364 G	4.46	25.77454	87.12928	Normal
8/1/23	13:13:26	76	0.1	280	20.2	2800	3265 G	4.34	25.77452	87.1283	Normal
8/1/23	13:15:11	76	0.1	290	20.2	2900	3364 G	4.46	25.77268	87.12449	Normal
8/1/23	13:15:11	76	0.1	250	20.2	2500	2970 G	3.99	25.77275	87.12345	Normal
AVERAGE							2905.362				

$$Y = 0 \cdot X^2 + 0.984 \cdot X + 510.70$$
$$X = 1800$$
$$Y = 2281$$

(R) RURAL ROAD
Good Average Poor
4001-5000 >5001

141M/hour
29/01/23
513


25.77453
87.13687

9.1.23

Name of Customer: Subash Kumar Singh
 Name of Work: Indrapada Kotih To Haradahl
 Road: 0123
 Lab Job number: 0123
 Date: 06/01/23
 Section No: 7

Test Date:	06/01/23	Road Name:	KANAKOTHI TO HARADAH
Machine No:	300	Road Type:	(R) RURAL ROAD
Sheet No:		Side:	
Sheet E. No:		Interval:	
Weather:		UTV Range:	1005 To 5000 mm/Km
Start Location:		Dial Range:	0 To 48 0.1 1000 m
End Location:		Equation:	$Y = 0.0002 \times X + 510.70$

Print Generate Report and Graph Redraw Graph Map View

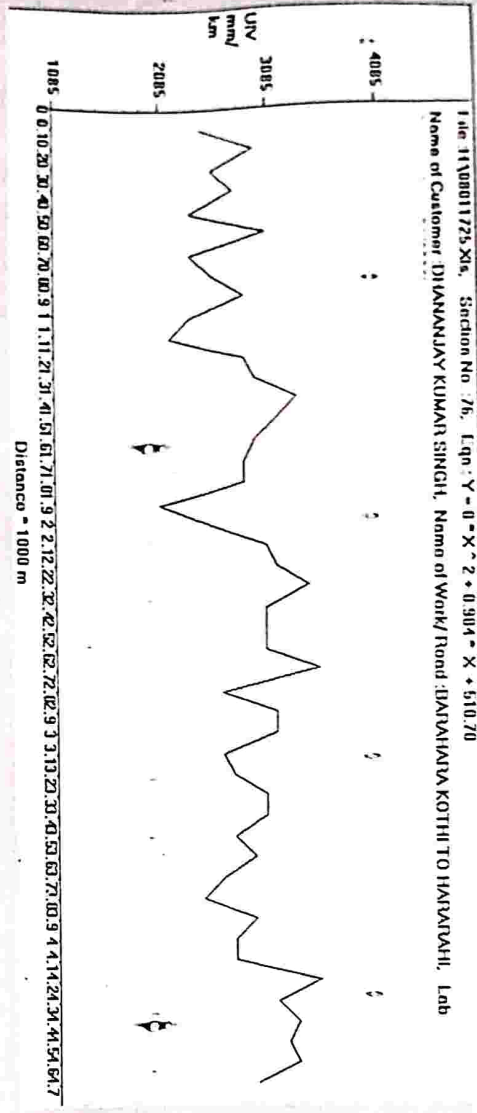


1011/1011
 09/01/23
 712

09/01/23
 09/11/23

09.1.23

File 11 N00011726.k16, Elevation File, 76, Equ 1' = 0.24" = 0.5084" = 2' = 610.70
 Name of Customer: DIAMANTZ KUMAR SINGH, Name of Work/ Road: MATHANAKOTTA TO MATHANAKOTTA, Lab

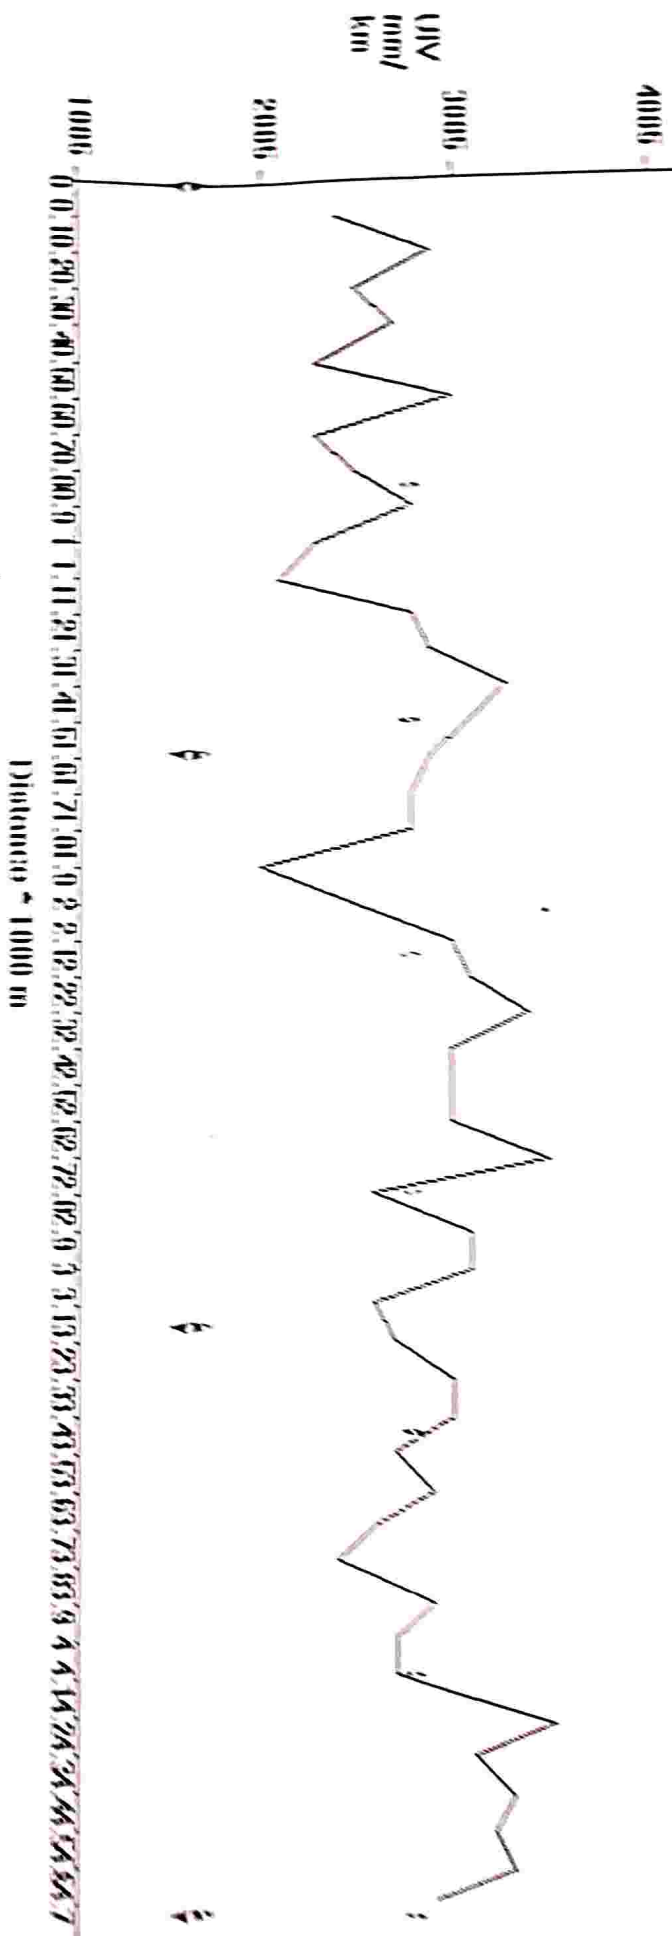

10/10/23
 10/10/23

10/10/23
 10/10/23

10/10/23
 10/10/23

कार्यपालक अभियंता, का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल धमदाहा, पूर्णियाँ।

ईमेल आईडी - cerwddhamdaha@gmail.com

पत्रांक.....55...../

धमदाहा / दिनांक...9/01/23

प्रमाणित किया जाता है कि Barhara Kothi to Harrahi Project id-21105308072 का सभी अवयवों की जाँच शत प्रतिशत कनीय अभियंता द्वारा किया गया है। सहायक अभियंता द्वारा सभी अवयवों की 50 प्रतिशत से अधिक जाँच किया गया है। अधोहस्ताक्षरी द्वारा 10 प्रतिशत अवयवों की जाँच की गई है।

14m/w
29/01/23
कनीय अभियंता

29/01/2023
सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, बी० कोठी

29/01/23
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल धमदाहा, पूर्णियाँ।
