

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, महुआ।

Email Id-cerwd.mahua@gmail.com

Mobile No-8986915790

पत्रांक.....166.7...../

महुआ/दिनांक.....17...../07/2023

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महुआ।

सेवा में,

नोडल पदाधिकारी,
एम0आर0 3054 नई अनुरक्षण नीति 2018,
विश्वेश्वरैया भवन,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय : शीर्ष एम0आर0 3054 नई अनुरक्षण नीति 2018 अन्तर्गत पथ में कराये गए कार्य के विरुद्ध अधियाचना भेजने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष एम0आर0 3054 नई अनुरक्षण नीति 2018 अन्तर्गत पथ में कराये गए कार्य के विरुद्ध अधियाचना इस पत्र के साथ समर्पित की जा रही है।

विश्वासभाजन,

Lamian
17.7.23

कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
महुआ।

7/07/23

Requisition Formate for Scheme Head- MR-3054 Under Bihar Rural Road Maintenance Policy 2018 (In Rectification and Surface Renewal)

Division Name:- Rural Works Department, Works Division, Mahua

S.No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA)	Administrative Approval (AA)	Agreement Amount (In Lacs)	Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of FRI (In Km)	Thickness of Bitumen Layer (In mm)	Value of Bitumen Content in %	Previous Total Allocated Amount (In Lacs)	Upto date Expenditure as per MIS (In Lacs)	Requisition against Work Done (in Lacs)	Remarks	
1	MR-N/22-23 Mahua/11	T04 - Akabarpur naya tola	31507602053	169/13.06.2022	3.310	251.530	201.10436	25.75087	16/MBD/2022-23	09.10.2023	25.75	25.00	5.00	0	0	201.10000	Work Completed
																201.10000	

Executive Engineer
R.W.D, Works Division, Mahua

Sanjay Kumar
14.9.23

17/09/23

17/09/23



Form GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month- 17.07.2023

STATE- BIHAR

SL. No	Name of Scheme	Sanction No. & Date With Amount (In Rs. Lacs)	Amount Received (In Rs.Lacs)	Particulars
1	Construction of Rural Roads under MR New Maintenance Policy 2018	Lt-84 Dated- 08-06-2023 Amount- 20.38879	6652.54164	Certified that out of Rs.6652.54164 Lacs of grants-in-aid sanctioned upto 12/2017 in favour of E-in-C, REO Bihar, Patna a sum of Rs.6582.82681 lacs has been utilized for the purpose of MR New Maintenance Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs- 69.71483 lacs remaining unutilized at the end of the period under.
	Total:		6652.54164	

- 2 Certified that I have satisfied myself that the conditions on which the gram-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised:-

- Works has been supervised by Executive Engineer/Superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/Superintending
 - Construction materials have been tested.
 - Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer
 - All other codal formalities have been observed.
- 3 Physical Progress achived:-
- Construction of Road Works.
 - Construction of CD Works.

[Signature]
Divisional Account Officer
RWD. Works Division, Mahua

[Signature] 17.7.23
Executive Engineer
RWD. Works Division, Mahua

[Signature]
17/07/23


प्रमाण-पत्र

पथ का नाम - T04 - Akabarpur naya tola.
योजना - एम0आर0 (3054) नई अनुरक्षण नीति 2018
कार्य प्रमंडल - महुआ।
प्रखंड - पातेपुर।


उक्त पथ में कराये गये सभी अवयवों के अवयववार कार्य निम्नलिखित पदाधिकारी द्वारा मापी पुस्तिका से सत्यापन किया गया।

क्र0	पदनाम	कराये गये कार्य के मापी पुस्तिका से सत्यापन की प्रतिशत	अभ्युक्ति
1	कनीय अभियंता	100 प्रतिशत	
2	सहायक अभियंता	50 प्रतिशत	
3	कार्यपालक अभियंता	10 प्रतिशत	


17.07.2023
कनीय अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रशाखा-पातेपुर।


17.07.23
सहायक अभियंता,
ग्रामीण कार्य विभाग,
कार्य अवर प्रमंडल, पातेपुर।


17.7.23
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महुआ।

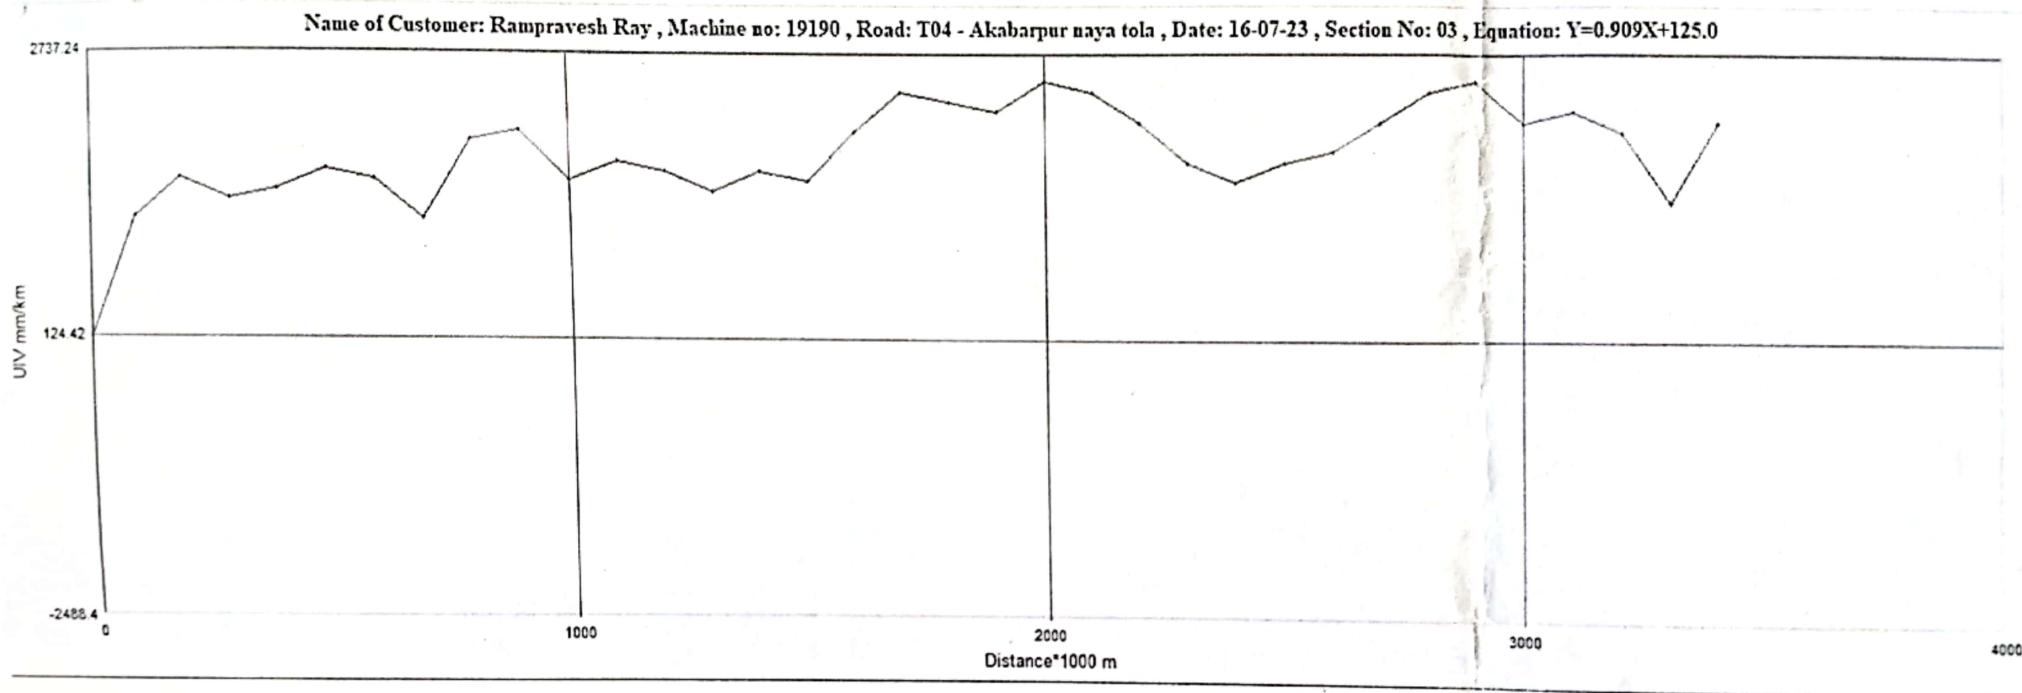

[Signature]
17.07.2023
S.E.

[Signature]
17.07.23
AE

[Signature] 17.7.23
Executive Engineer
P. W. Works Division
District



Date	Time	Test No	Distance(meter)	Total Distance(meter)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI(mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction 1	Remarks
16-07-2023	12:39:28	3	0	0	0.0 cm	13.8 Km/Hr	0.0 mm/Km	125	0.236	Good	25.9002696	N	85.5430384	E	Normal
16-07-2023	13:36:38	3	100	100	12.0 cm	6.3 Km/Hr	1200.0 mm/Km	1215.8	1.799	Good	25.8497324	N	85.5522165	E	Normal
16-07-2023	13:37:02	3	100	200	16.0 cm	15.6 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.8497324	N	85.5522165	E	Normal
16-07-2023	13:37:23	3	100	300	14.0 cm	16.5 Km/Hr	1400.0 mm/Km	1397.6	2.037	Good	25.8507662	N	85.5508814	E	Normal
16-07-2023	13:37:59	3	100	400	15.0 cm	10.2 Km/Hr	1500.0 mm/Km	1488.5	2.155	Good	25.8511401	N	85.5498896	E	Normal
16-07-2023	13:38:19	3	100	500	17.0 cm	18.0 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.8511477	N	85.5495768	E	Normal
16-07-2023	13:38:38	3	100	600	16.0 cm	18.0 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.8510542	N	85.5478067	E	Normal
16-07-2023	13:38:52	3	100	700	12.0 cm	25.4 Km/Hr	1200.0 mm/Km	1215.8	1.799	Good	25.8513117	N	85.5469599	E	Normal
16-07-2023	13:39:05	3	100	800	20.0 cm	28.2 Km/Hr	2000.0 mm/Km	1943	2.734	Good	25.851636	N	85.5458994	E	Normal
16-07-2023	13:39:17	3	100	900	21.0 cm	29.1 Km/Hr	2100.0 mm/Km	2033.9	2.847	Good	25.851779	N	85.5452509	E	Normal
16-07-2023	13:39:37	3	100	1000	16.0 cm	18.3 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.851861	N	85.5439768	E	Normal
16-07-2023	13:39:59	3	100	1100	18.0 cm	16.5 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.8519221	N	85.542985	E	Normal
16-07-2023	13:40:20	3	100	1200	17.0 cm	17.1 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.8520556	N	85.5421534	E	Normal
16-07-2023	13:40:39	3	100	1300	15.0 cm	18.5 Km/Hr	1500.0 mm/Km	1488.5	2.155	Good	25.8522139	N	85.5412302	E	Normal
16-07-2023	13:40:58	3	100	1400	17.0 cm	19.8 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.8522139	N	85.5401697	E	Normal
16-07-2023	13:41:16	3	100	1500	16.0 cm	19.8 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.8521739	N	85.5396357	E	Normal
16-07-2023	13:41:41	3	100	1600	21.0 cm	14.4 Km/Hr	2100.0 mm/Km	2033.9	2.847	Good	25.8518763	N	85.5382624	E	Normal
16-07-2023	13:42:01	3	100	1700	25.0 cm	18.1 Km/Hr	2500.0 mm/Km	2397.5	3.298	Good	25.851161	N	85.5386896	E	Normal
16-07-2023	13:42:18	3	100	1800	24.0 cm	20.9 Km/Hr	2400.0 mm/Km	2306.6	3.186	Good	25.8508921	N	85.5388193	E	Normal
16-07-2023	13:42:34	3	100	1900	23.0 cm	22.2 Km/Hr	2300.0 mm/Km	2215.7	3.074	Good	25.8502379	N	85.5404978	E	Normal
16-07-2023	13:42:51	3	100	2000	26.0 cm	21.0 Km/Hr	2600.0 mm/Km	2488.4	3.409	Good	25.8494807	N	85.5408564	E	Normal
16-07-2023	13:43:08	3	100	2100	25.0 cm	21.8 Km/Hr	2500.0 mm/Km	2397.5	3.298	Good	25.8491335	N	85.5413294	E	Normal
16-07-2023	13:43:24	3	100	2200	22.0 cm	22.2 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.8483935	N	85.5421076	E	Normal
16-07-2023	13:44:27	3	100	2300	18.0 cm	6.0 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.8479796	N	85.5425272	E	Normal
16-07-2023	13:44:50	3	100	2400	16.0 cm	15.3 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.8476782	N	85.5435877	E	Normal
16-07-2023	13:45:09	3	100	2500	18.0 cm	18.7 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.8481017	N	85.5439463	E	Normal
16-07-2023	13:45:27	3	100	2600	19.0 cm	20.4 Km/Hr	1900.0 mm/Km	1852.1	2.619	Good	25.8480921	N	85.545495	E	Normal
16-07-2023	13:45:42	3	100	2700	22.0 cm	22.5 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.8480273	N	85.5461283	E	Normal
16-07-2023	13:46:17	3	100	2800	25.0 cm	11.1 Km/Hr	2500.0 mm/Km	2397.5	3.298	Good	25.8478442	N	85.5474482	E	Normal
16-07-2023	13:47:15	3	100	2900	26.0 cm	6.0 Km/Hr	2600.0 mm/Km	2488.4	3.409	Good	25.8478874	N	85.5472345	E	Normal
16-07-2023	13:47:34	3	100	3000	22.0 cm	19.8 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.8480406	N	85.5456552	E	Normal
16-07-2023	13:47:53	3	100	3100	23.0 cm	18.6 Km/Hr	2300.0 mm/Km	2215.7	3.074	Good	25.8480406	N	85.5456552	E	Normal
16-07-2023	13:48:14	3	100	3200	21.0 cm	17.3 Km/Hr	2100.0 mm/Km	2033.9	2.847	Good	25.8481341	N	85.5442209	E	Normal
16-07-2023	13:48:37	3	100	3300	14.0 cm	15.7 Km/Hr	1400.0 mm/Km	1397.6	2.037	Good	25.8474951	N	85.5431147	E	Normal
16-07-2023	13:49:01	3	100	3400	22.0 cm	14.7 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.8468428	N	85.5422831	E	Normal

16-07-2023
J.E.

Khish
17-07-23
AB

Sanjay
17-7-23
Executive Engineer
New Work Division
Main

IRI Value 2573
Machine No. 19190

