

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, औरंगाबाद

पत्रांक.....384..... अनु0

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, औरंगाबाद।

सेवा में,

नोडल पदाधिकारी, (MR304
ग्रामीण कार्य विभाग, पटना, बिहार।

औरंगाबाद, दिनांक.....18/11/23

विषय:- नई अनुरक्षण नीति-2018 MR(3054) योजना के अन्तर्गत पाँच वर्षीय रख-रखाव पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR(3054) योजना के अन्तर्गत पाँच वर्षीय रख-रखाव पथ में कराये गये कार्य के लिए सम्वेदक को भुगतान करने हेतु अधिचाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु0:-आवंटन माँग पत्र की प्रति संलग्न।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल औरंगाबाद।

Sr Divisional Account Officer
RWD, Works Division, Durgabad

Executive Engineer
R.W.D. (W) Division, Aurangabad

Kishore

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

Project Name: RWD (W) Div. Aurangabad
1st Aug-19

1	Name of the Road	XXX <u>6th Road to Nax Road</u>		
2	Batch No.	XXX <u>RM/AU/AUR/19/0032</u>		
3	Project ID	XXX <u>10602902016</u>		
4	Total Length of Road (in Km)	0.00 <u>3.85km</u>		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	0 <u>3.85km</u>		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	0 <u>36.2152 Lakh</u>		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0 <u>1.81078 Lakh</u>		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00 0.00
II	SHOULDERS AND EMBANKMENTS	0.00	10%	0.00 0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00 0.00
IV	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00 0.00
V	VEGETATION	0.00	5%	0.00 0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]		0.00 0.00		
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]		0.00 <u>1.81078 Lakh</u>		

Date of inspection by E/I or his agent
Prepared by Contractor's self Control unit

Name and Designation of person inspecting road

Date

Signature of person inspecting road

(Signature)

Certify by E/I [signature] Date:-

10/21/21
Executive Engineer
R.W.D. (W) Division
Aurangabad

Name of Contractor : Kishore Kumar Singh

Name of Road : GT Road se Narkapi

Date	Time	Section	Length	Bumps	Speed	OR		CATEG ORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	UJV	ROAD				
15/3/22	11:22:24	57	0.1	170	0	1700	2063	G	2.88	24.704532	84.55347	Normal
15/3/22	11:24:9	57	0.1	260	0	2600	3086	G	4.13	24.705407	84.55367	Normal
15/3/22	11:24:44	57	0.1	220	10.1	2200	2631	G	3.58	24.70635	84.55372	Normal
15/3/22	11:25:0	57	0.1	290	10.1	2900	3426	G	4.53	24.707035	84.553147	Normal
15/3/22	11:25:19	57	0.1	280	20.2	2800	3313	G	4.4	24.707212	84.552153	Normal
15/3/22	11:26:0	57	0.1	290	10.1	2900	3426	G	4.53	24.707357	84.55116	Normal
15/3/22	11:26:30	57	0.1	290	10.1	2900	3426	G	4.53	24.707832	84.550337	Normal
15/3/22	11:27:5	57	0.1	250	10.1	2500	2972	G	3.99	24.708225	84.549177	Normal
15/3/22	11:27:5	57	0.1	260	10.1	2600	3086	G	4.13	24.70844	84.548502	Normal
15/3/22	11:27:40	57	0.1	250	10.1	2500	2972	G	3.99	24.709053	84.547912	Normal
15/3/22	11:28:0	57	0.1	290	10.1	2900	3426	G	4.53	24.709073	84.546985	Normal
15/3/22	11:28:16	57	0.1	280	10.1	2800	3313	G	4.4	24.709912	84.547087	Normal
15/3/22	11:28:51	57	0.1	270	20.2	2700	3199	G	4.26	24.71066	84.547037	Normal
15/3/22	11:29:0	57	0.1	290	10.1	2900	3426	G	4.53	24.711497	84.547222	Normal
15/3/22	11:29:26	57	0.1	270	10.1	2700	3199	G	4.26	24.712347	84.547542	Normal
15/3/22	11:30:2	57	0.1	220	10.1	2200	2631	G	3.58	24.712997	84.548047	Normal
15/3/22	11:30:2	57	0.1	260	20.2	2600	3086	G	4.13	24.713038	84.548922	Normal
15/3/22	11:30:37	57	0.1	260	20.2	2600	3086	G	4.13	24.71345	84.549747	Curve
15/3/22	11:30:37	57	0.1	300	20.2	3000	3540	G	4.66	24.713515	84.550572	Normal
15/3/22	11:31:12	57	0.1	260	10.1	2600	3086	G	4.13	24.71338	84.551347	Speed Breaker
15/3/22	11:31:12	57	0.1	280	10.1	2800	3313	G	4.4	24.714282	84.551312	Normal
15/3/22	11:31:47	57	0.1	220	20.2	2200	2631	G	3.58	24.715108	84.551565	Normal
15/3/22	11:32:0	57	0.1	190	20.2	1900	2290	G	3.16	24.71588	84.5518	Normal
15/3/22	11:32:23	57	0.1	250	20.2	2500	2972	G	3.99	24.716047	84.552077	Normal
15/3/22	11:32:23	57	0.1	260	20.2	2600	3086	G	4.13	24.71594	84.55367	Normal
15/3/22	11:32:23	57	0.1	280	20.2	2800	3313	G	4.4	24.715842	84.554045	Normal
15/3/22	11:33:0	57	0.1	220	20.2	2200	2631	G	3.58	24.715607	84.555638	Normal
15/3/22	11:33:0	57	0.1	240	20.2	2400	2858	G	3.85	24.715302	84.556615	Normal
15/3/22	11:33:33	57	0.1	260	10.1	2600	3086	G	4.13	24.714442	84.556582	Normal
15/3/22	11:34:0	57	0.1	260	20.2	2600	3086	G	4.13	24.7135	84.556532	Normal
15/3/22	11:34:9	57	0.1	270	20.2	2700	3199	G	4.26	24.712627	84.55672	Normal
15/3/22	11:34:44	57	0.1	260	10.1	2600	3086	G	4.13	24.71258	84.557558	Normal
15/3/22	11:35:0	57	0.1	230	20.2	2300	2745	G	3.72	24.712842	84.558552	Normal
15/3/22	11:35:19	57	0.1	320	10.1	3200	3767	G	4.93	24.71294	84.559493	Normal
15/3/22	11:35:54	57	0.1	290	10.1	2900	3426	G	4.53	24.713362	84.560302	Speed Breaker
15/3/22	11:36:0	57	0.1	270	10.1	2700	3199	G	4.26	24.713068	84.56116	Normal
15/3/22	11:37:5	57	0.1	180	0	1800	2177	G	3.02	24.713103	84.56207	Normal
15/3/22	11:37:40	57	0.1	290	10.1	2900	3426	G	4.53	24.71364	84.56293	Normal

$$Y = 0.2 \times 2 + 1.136 \times X + 1$$

$$X = 1700$$

$$Y = 3700$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5000

Executive Engineer

R.W.D. (Works) Division

Aurangabad

Name of Contractor : Kishore Kumar Singh
Name of Road : GT Road se Narkapi

Sieco Analyzer

Name of Customer : Kishore Kumar Singh
Name of Work/ Road : GT Road se Narkapi
Lab Job number : 57
Date : 15-Mar-22
Section No. : 57

Test Date : 15-Mar-22
Machine No : 377
Start S No : 3
Start E No : 40
Weather : Normal
Start Location : 24.704532, 84.124713643, 84.1
End Location : 24.713643, 84.1
Road Name : GT Road se Narkapi
Road Type : (R) RURAL ROAD
Side : Madanpur
Interval :
U/V Range : 1063 To 5000
Dist Range : 0 To 39
Equation : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Print


Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\RWDD\Desktop\57.Xls, Section No. : 57, Eqn : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Name of Customer : Kishore Kumar Singh, Name of Work/ Road : GT Road se Narkapi, Lab Job number : 57

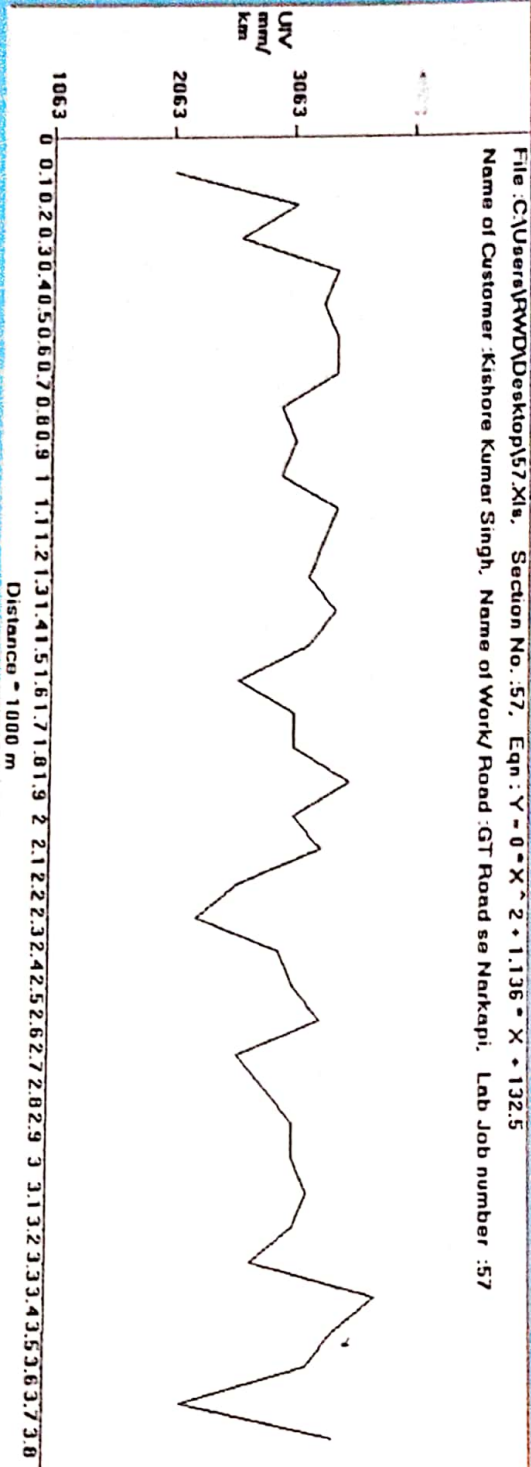

[Signature]
JE

[Signature]
AE

[Signature]
Executive Engineer
R.W.D. (Works) Division
Aurangabad
