

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, चकिया, (पूर्वी चम्पारण)।

पत्रांक-347/अनु0 / चकिया, दिनांक:- 06/06/2023

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, चकिया।

सेवामे,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए निधि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए पथवार मांगी जाने वाली आवंटन की सूची पत्र के साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय।

- अनु0:- 1. आवंटन की सूची।
2. मापी पुस्त की छाया प्रति।

विश्वासभाजन,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

ज्ञापांक-347 दिनांक-06-06-2023

प्रतिलिपि-नोडल पदाधिकारी (3054), ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

- अनु0:- 1. आवंटन की सूची।
2. मापी पुस्त की छाया प्रति।

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Chakia.**

Rectification Format for Scheme Head-MRI(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Chakia

SI No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in lakh)	up-to-date expenditure as per MIS (in Lakh)	Requestion against work done. (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/EA/CHA/22/0007	Mehal Kataha RWD Road Mandir to Purni Mehal Tolia	317841035649	Letter No.105 Date-03.06.2022	1.600	84.71	63.91619	14.34599	10 MBD/2022-23 Date-16.09.2022	15.06.2023	In Progress	2870	25	05.00	0.00000	0.00000	63.76500	Work In Progress
					1.600	84.713	63.91619	14.34599							0.00000	0.00000	63.76500	

- 1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.


 कार्यपालक अभियंता
 ग्रामीण कार्य विभाग
 कसं प्रमडल, चकिया
 06/06/23

Form GER 19-A
(See Government of India's decision (1) below Rule - 150)
Form of utilization certificate up to the month up to 06/2023
M.R. (3054) New maintenance Policy-2018

PIU - RWD, W.D- CHAKIA

Sl. NO	Name of Scheme	Sanction No. / Date with Amount (in RS. Lacks)	Amount Received (in RS. Lacks)	particulars
1	M.R. (3054) New maintenance Policy-2018	9346.23493	9346.23493	Certified that out of Rs 9346.23493 Lacs Receive upto the year.2023-24 executive engineer RWD, (W) DIV, chakia a sum of RS 9192.72655 Lacs has been utilized for the perpose of M.R. (3054) New maintenance Policy-2018 'CFMS' Schemes given in the margin for which it was sanctioned and that the balance of Rs 153.50838 lacks remaining unutilized at this end of the (up to 06/2023)

2. Certificate that I have satisfied myself that the conditions on which the grand's-in-aid was sanctioned have been duly fulfilled/ate being fulfilled and that have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned kinds of cheks exercised:-


- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.

3. Physical Progress achieved :-

- Construction of M.R. (3054) New maintenance Policy-2018 (Details in Progress report)
- Construction of Road Works. (.....Do.....)
- GSB entered in MB has been badly damage due to flood in Dekha Bandh to Ajit Singh ke Tola Tak Path

EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT
WORKS DIVISION-CHAKIA.

Name of Customer: Prabhat Kumar, Machine no: 19191, Road: Mehshi Kataha RWD Road Mandir to Purani Mehshi Tola, Date: 04-06-23, Section No: 30, Equation: $Y = 0.927 X + 204.3$

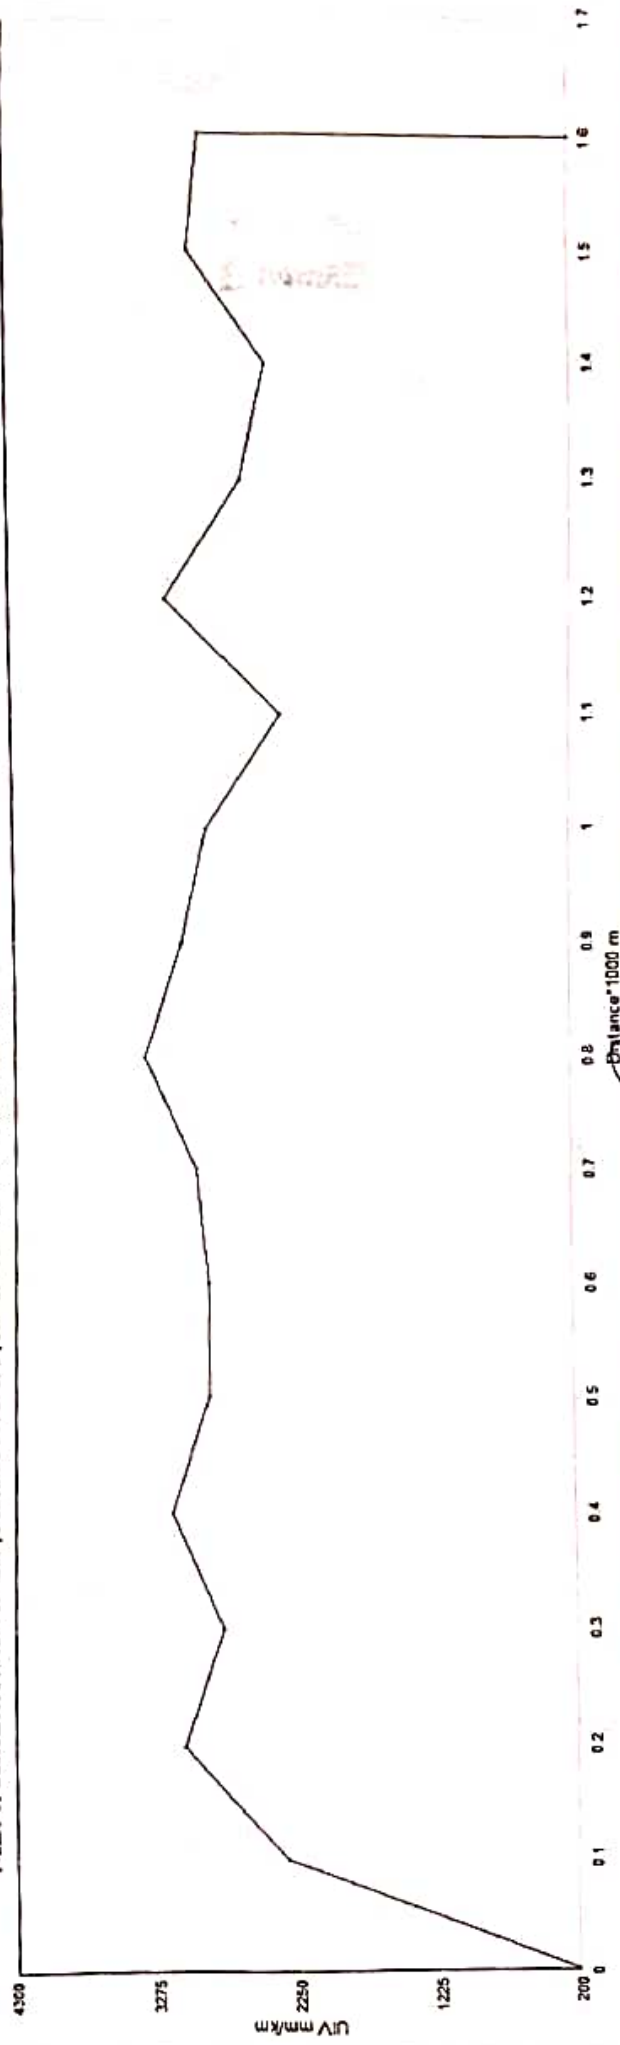

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, चकिया

5/6/23
5/6/23

5/6/23
5/6/23

Name of work : Mehshi Kalaha RWD Road Mandir to Purani Mehshi Tola	
Name of customer : Prabhat Kumar	
(R) Rural Road	
Good	Average
< 4000	4001 - 5000
	Poor
	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
04/06/23	10:40:10	80	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	205	0.37	Good	26.3579557	N	85.1081311	E	Normal
04/06/23	10:41:30	80	100	100	23.0 cm	13.8 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.3582275	N	85.1083184	E	Normal
04/06/23	10:41:51	80	100	200	31.0 cm	17.0 Km/Hr	3100.0 mm/Km	3079	4.12	Good	26.3583148	N	85.1084131	E	Normal
04/06/23	10:42:05	80	100	300	28.0 cm	25.4 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.3587791	N	85.1088373	E	Normal
04/06/23	10:42:19	80	100	400	32.0 cm	26.7 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.3592857	N	85.1095813	E	Normal
04/06/23	10:42:35	80	100	500	29.0 cm	22.5 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3595298	N	85.1094984	E	Normal
04/06/23	10:42:55	80	100	600	29.0 cm	18.2 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3601672	N	85.1082894	E	Normal
04/06/23	10:43:16	80	100	700	30.0 cm	16.6 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.3603392	N	85.1076398	E	Normal
04/06/23	10:43:55	80	100	800	34.0 cm	19.6 Km/Hr	3400.0 mm/Km	3357	4.45	Good	26.3607951	N	85.1066254	E	Normal
04/06/23	10:44:15	80	100	900	31.0 cm	17.4 Km/Hr	3100.0 mm/Km	3079	4.12	Good	26.3611948	N	85.1058861	E	Normal
04/06/23	10:44:40	80	100	1000	29.0 cm	15.0 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3618624	N	85.1052257	E	Normal
04/06/23	10:45:02	80	100	1100	23.0 cm	15.8 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.3624967	N	85.1048087	E	Normal
04/06/23	10:45:33	80	100	1200	32.0 cm	11.5 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.3625626	N	85.1046914	E	Normal
04/06/23	10:45:56	80	100	1300	26.0 cm	16.0 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.3631531	N	85.1039374	E	Normal
04/06/23	10:46:17	80	100	1400	24.0 cm	17.2 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.3636222	N	85.1026979	E	Normal
04/06/23	10:46:40	80	100	1500	30.0 cm	15.6 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.3641665	N	85.1018312	E	Normal
04/06/23	10:47:09	80	100	1600	29.0 cm	12.6 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3655122	N	85.0966692	E	Normal
			0	1600				205	0.37	Good					

Lab
04/06/23
JE

Prabhat
04/06/2023
1075

AVG IRI-2870

कार्यपालक सभियता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, चकिया
