

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल खड़गपुर-तारापुर

पत्रांक-.....815 (अनु०)
मो०-8986915854

दिनांक-.....08/06/23
ई मेल - ee.kh.tarapur.rwd2@gmail.com

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, खड़गपुर-तारापुर।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति 2018" (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) "नई अनुरक्षण नीति 2018" योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) "नई अनुरक्षण नीति 2018" योजनान्तर्गत पथों का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन


08/06/2023

कार्यपालक अभियंता
ग्रामीण कार्य विभाग

कार्य प्रमंडल खड़गपुर-तारापुर



08/06/23

**Office Of The Executive Engineer
Rural Works Department
Works Division, Kharagpur-Tarapur**

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative Length (in Km)	Administrative Amount	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	RM/MU/KHA/ 21/0002	PWD Road Kharagpur Jamui (Banhara) - Ganali, Teen Mile	NEA230001768	3976 27.09.2021	12.500	995.85000	20MBD/2022-23 29.09.2022	28.06.2023	-	2687	SDBC-25mm, Thickness of PCC Layer in 160 mm	SDBC-5.0	315.00000	315.00000	571.53475	Surface Complete
2	RM/MU/KHA/ 22/0002	L056-P.W.D.ROAD GANGTAMORE SANGRAMPUR TO LAURIA DHANADIH (TRACK56)	20803802072	1304 23.03.2022	9.400	82.76000	13MBD/2022-23 31.08.2022	30.05.2023	08.05.2023	3131	SDBC-25mm, Thickness of PCC Layer in 160 mm	SDBC-5.0	0.00000	0.00000	70.72952	Completed
3	RM/MU/KHA/ 22/0004	L023-P.W.D.ROAD TARAPUR TO NAWADA (VR23)	20803802033	1304 23.03.2022	2.050	109.40000	24MBD/2022-23 30.08.2023	29.05.2023	s	3021	SDBC-25mm, Thickness of PCC Layer in 160 mm	SDBC-5.0	0.00000	0.00000	78.59538	Surface Complete
4	RM/MU/KHA/ 23/0001	L029-T02 GANELI BANAHARA ROAD TO ADABASI TOLA BANARKOLA (TRACK29)	20803802043	463 04.07.2022	2.220	123.46100	26MBD/2022-23 15.12.2022	14.09.2023	-	3268	SDBC-25mm, Thickness of PCC Layer in 160 mm	SDBC-5.0	0.00000	0.00000	85.97802	Surface Complete
5	RM/MU/KHA/ 23/0001	L026-T02 GANALI BANHARA TO BARDIHA (TRACK26)	20803802037	463 04.07.2022	1.600	97.06700	26MBD/2022-23 15.12.2022	14.09.2023	-	3113	SDBC-25mm, Thickness of PCC Layer in 160 mm	SDBC-5.0	0.00000	0.00000	80.01317	Surface Complete
6	RM/MU/KHA/ 23/0001	L045-T04 RAJARANI TALAB TETIYA TO JAGATPURA (TRACK45)	20803802060	463 04.07.2022	1.900	120.30000	26MBD/2022-23 15.12.2022	14.09.2023	-	3101	SDBC-25mm, Thickness of PCC Layer in 160 mm	SDBC-5.0	0.00000	0.00000	89.91565	Surface Complete
7	RM/MU/KHA/ 23/0004	P.W.D ROAD KHARAGPUR JAMUI VIA KHUTATAR T01 - GANGTA	20803802016	463 04.07.2022	2.700	201.46400	31MBD/2022-23 14.01.2023	13.10.2023	29-05-23	3217	SDBC-25mm, Thickness of PCC Layer in 160 mm	SDBC-5.0	0.00000	0.00000	156.29304	Surface Complete


Divisional Account Officer
Rural Works Department
Works Division Kharagpur-Tarapur


Executive Engineer
Rural Works Department
Work(s) Division Kharagpur-Tarapur

EXECUTIVE ENGINEER, WORK DEPARTMENT, WORKS DIVISION ,KHARAGPUR-TARAPUR,(MUNGER)

FORM GFR19 A

(See Government Of India'S Decesion (1) Below Rule 150)


(Form Of Utilization Certificate up To The Month Of Up To June .2023)

(MR New Maintenance Policy 2018)

1	Name Of Scheme/Purpose	Sanctioned with Date	Sanctioned Amounts(In Lacs-Rs.)	Amount Recived(IN Rs. Lacs)	Particulars
	Construction of Rural Road & Bridge underMR New Maintenance Policy 2018	Ltr. No. 35 Dt. 13.10.2022 Ltr. No.47 dt 24.11.2022 Ltr. No.04 dt 10.01.2023 Ltr. No.10 dt 27.01.2023 Ltr. No.21 dt 20.02.2023 Ltr. No.33 dt 07.03.2023 Ltr. No.56 dt 28.03.2023 Ltr.No.78 dt 24.05.2023	7501.52493	7501.52493	Certified that Out of Rs.7501.52493 lakh received up to date In Favour Of Executive Engineer , RWD, Kharagpur-Tarapur Sum of Rs. 7318.22342 lakh has been utilized for the purpose of MR New Maintenance Policy 2018 Program Fund scheme as given in the margin for which it was sanctioned and that the balance Of Rs. 183.30151 lakh remaining unutilized amount at the end of the period under.

2 Certified that I have satisfied myself that the condition on which the grants in aid was sanctioned have been duly fulfilled /are being fulfilled And that I have exercised the checks to see that the money was actually utilized for which it was sanctioned.


 05/06/23
 Divisional Accounts Officer
 R.W.D. (W) Div, Kharagpur-Tarapur (Munger)


 05/06/2023
 Executive Engineer
 R.W.D. (W) Div, Kharagpur-Tarapur (Munger)

Name of work : PWD Road Kharagpur Jamui (Banhara) - Ganaili Teen Mile

Name of customer : S B Engicon Private Limited

(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
24/05/23	17:35:43	79	100	100	23.0 cm	33.6 Km/Hr	2300.0 mm/Km	2454	3.37	Good	25.0400286	N	86.5929728	E	Normal
24/05/23	17:35:56	79	100	200	15.0 cm	27.0 Km/Hr	1500.0 mm/Km	1678	2.4	Good	25.0400286	N	86.5929728	E	Normal
24/05/23	17:36:10	79	100	300	21.0 cm	25.7 Km/Hr	2100.0 mm/Km	2260	3.13	Good	25.0400286	N	86.5929728	E	Normal
24/05/23	17:36:24	79	100	400	25.0 cm	25.7 Km/Hr	2500.0 mm/Km	2647	3.6	Good	25.0400286	N	86.5929728	E	Normal
24/05/23	17:36:38	79	100	500	22.0 cm	26.4 Km/Hr	2200.0 mm/Km	2357	3.25	Good	25.0400286	N	86.5929728	E	Normal
24/05/23	17:36:52	79	100	600	21.0 cm	24.4 Km/Hr	2100.0 mm/Km	2260	3.13	Good	25.0400286	N	86.5929728	E	Normal
24/05/23	17:37:07	79	100	700	19.0 cm	24.6 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0400286	N	86.5929728	E	Normal
24/05/23	17:37:21	79	100	800	21.0 cm	25.9 Km/Hr	2100.0 mm/Km	2260	3.13	Good	25.0400286	N	86.5929728	E	Normal
24/05/23	17:37:45	79	100	900	32.0 cm	34.4 Km/Hr	3200.0 mm/Km	3326	4.42	Good	25.0400286	N	86.5929728	E	Normal
24/05/23	17:37:59	79	100	1000	15.0 cm	26.2 Km/Hr	1500.0 mm/Km	1678	2.4	Good	25.0400286	N	86.5929728	E	Normal
24/05/23	17:38:12	79	100	1100	17.0 cm	26.7 Km/Hr	1700.0 mm/Km	1872	2.64	Good	25.0466394	N	86.5672083	E	Normal
24/05/23	17:38:26	79	100	1200	18.0 cm	26.2 Km/Hr	1800.0 mm/Km	1969	2.77	Good	25.0463438	N	86.5681620	E	Normal
24/05/23	17:38:43	79	100	1300	20.0 cm	22.0 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0463438	N	86.5681620	E	Normal
24/05/23	17:38:58	79	100	1400	20.0 cm	22.9 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0452890	N	86.5695658	E	Normal
24/05/23	17:39:13	79	100	1500	19.0 cm	24.6 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0450449	N	86.5702829	E	Normal
24/05/23	17:39:27	79	100	1600	18.0 cm	24.6 Km/Hr	1800.0 mm/Km	1969	2.77	Good	25.0450449	N	86.5702829	E	Normal
24/05/23	17:39:43	79	100	1700	20.0 cm	23.8 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0450449	N	86.5702829	E	Normal
24/05/23	17:39:58	79	100	1800	28.0 cm	23.8 Km/Hr	2800.0 mm/Km	2938	3.95	Good	25.0450449	N	86.5702829	E	Normal
24/05/23	17:40:13	79	100	1900	19.0 cm	23.4 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0450449	N	86.5702829	E	Normal
24/05/23	17:40:28	79	100	2000	21.0 cm	24.6 Km/Hr	2100.0 mm/Km	2260	3.13	Good	25.0450449	N	86.5702829	E	Normal
24/05/23	17:40:54	79	100	2100	14.0 cm	34.4 Km/Hr	1400.0 mm/Km	1582	2.27	Good	25.0427542	N	86.5759134	E	Normal

8/6/23

8/6/23

Name of work : PWD Road Kharagpur Jamui (Banhara) - Ganaili Teen Mile

Name of customer : S B Engicon Private Limited

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

24/05/23	17.41.24	79	100	2200	11.0 cm	32.0 Km/Hr	1100.0 mm/Km	1291	1.9	Good	25.0424414	N	86.5768900	E	Normal
24/05/23	17.41.42	79	100	2300	19.0 cm	20.2 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0422258	N	86.5777369	E	Normal
24/05/23	17.42.04	79	100	2400	20.0 cm	36.3 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0421762	N	86.5787439	E	Normal
24/05/23	17.42.27	79	100	2500	33.0 cm	35.2 Km/Hr	3300.0 mm/Km	3423	4.53	Good	25.0422010	N	86.5789423	E	Normal
24/05/23	17.42.56	79	100	2600	30.0 cm	32.6 Km/Hr	3000.0 mm/Km	3132	4.19	Good	25.0418215	N	86.5806360	E	Normal
24/05/23	17.43.18	79	100	2700	13.0 cm	36.6 Km/Hr	1300.0 mm/Km	1485	2.15	Good	25.0415449	N	86.5814447	E	Normal
24/05/23	17.43.37	79	100	2800	17.0 cm	18.4 Km/Hr	1700.0 mm/Km	1872	2.64	Good	25.0415697	N	86.5823908	E	Normal
24/05/23	17.43.56	79	100	2900	20.0 cm	19.4 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0414114	N	86.5828104	E	Normal
24/05/23	17.44.14	79	100	3000	23.0 cm	20.0 Km/Hr	2300.0 mm/Km	2454	3.37	Good	25.0410414	N	86.5842981	E	Normal
24/05/23	17.44.30	79	100	3100	20.0 cm	21.8 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0409117	N	86.5852213	E	Normal
24/05/23	17.44.50	79	100	3200	35.0 cm	18.3 Km/Hr	3500.0 mm/Km	3616	4.76	Good	25.0406866	N	86.5862284	E	Normal
24/05/23	17.45.21	79	100	3300	37.0 cm	31.0 Km/Hr	3700.0 mm/Km	3810	4.99	Good	25.0405779	N	86.5873194	E	Breaker
24/05/23	17.45.43	79	100	3400	34.0 cm	36.6 Km/Hr	3400.0 mm/Km	3520	4.65	Good	25.0405168	N	86.5883646	E	Normal
24/05/23	17.46.02	79	100	3500	38.0 cm	19.2 Km/Hr	3800.0 mm/Km	3907	5.1	Good	25.0404501	N	86.5892267	E	Breaker
24/05/23	17.46.19	79	100	3600	23.0 cm	20.2 Km/Hr	2300.0 mm/Km	2454	3.37	Good	25.0407934	N	86.5901346	E	Normal
24/05/23	17.46.37	79	100	3700	25.0 cm	20.8 Km/Hr	2500.0 mm/Km	2647	3.6	Good	25.0407362	N	86.5911493	E	Normal
24/05/23	17.46.54	79	100	3800	22.0 cm	21.1 Km/Hr	2200.0 mm/Km	2357	3.25	Good	25.0406332	N	86.5921106	E	Normal
24/05/23	17.47.11	79	100	3900	26.0 cm	21.0 Km/Hr	2600.0 mm/Km	2744	3.72	Good	25.0403814	N	86.5931635	E	Normal
24/05/23	17.47.29	79	100	4000	19.0 cm	20.0 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0398493	N	86.5939264	E	Normal
24/05/23	17.47.48	79	100	4100	28.0 cm	19.2 Km/Hr	2800.0 mm/Km	2938	3.95	Good	25.0391359	N	86.5941401	E	Normal
24/05/23	17.48.12	79	100	4200	38.0 cm	35.0 Km/Hr	3800.0 mm/Km	3907	5.1	Good	25.0380144	N	86.5944147	E	Normal
24/05/23	17.48.37	79	100	4300	18.0 cm	34.1 Km/Hr	1800.0 mm/Km	1969	2.77	Good	25.0375776	N	86.5944376	E	Normal

316123
08

08-06-23

Name of work : PWD Road Kharapur Jamui (Barhara) - Garaili Teen Mile

Name of customer : S B Engicon Private Limited

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

24/05/23	17:48:58	79	100	4400	13.0 cm	37.1 Km/Hr	1300.0 mm/Km	1485	2.15	Good	25.0375776	N	86.5944376	E	Normal
24/05/23	17:49:16	79	100	4500	20.0 cm	20.4 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0375776	N	86.5944376	E	Normal
24/05/23	17:49:33	79	100	4600	26.0 cm	21.6 Km/Hr	2600.0 mm/Km	2744	3.72	Good	25.0375776	N	86.5944376	E	Normal
24/05/23	17:49:50	79	100	4700	24.0 cm	20.7 Km/Hr	2400.0 mm/Km	2550	3.49	Good	25.0375776	N	86.5944376	E	Normal
24/05/23	17:50:05	79	100	4800	21.0 cm	23.6 Km/Hr	2100.0 mm/Km	2260	3.13	Good	25.0339003	N	86.5965662	E	Normal
24/05/23	17:50:20	79	100	4900	19.0 cm	23.4 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0330419	N	86.5965357	E	Normal
24/05/23	17:50:35	79	100	5000	19.0 cm	23.9 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0321951	N	86.5963221	E	Normal
24/05/23	17:50:52	79	100	5100	22.0 cm	21.6 Km/Hr	2200.0 mm/Km	2357	3.25	Good	25.0312910	N	86.5963526	E	Normal
24/05/23	17:51:08	79	100	5200	18.0 cm	22.5 Km/Hr	1800.0 mm/Km	1969	2.77	Good	25.0311289	N	86.5978861	E	Normal
24/05/23	17:51:24	79	100	5300	19.0 cm	23.4 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0305223	N	86.5985193	E	Normal
24/05/23	17:51:38	79	100	5400	25.0 cm	24.3 Km/Hr	2500.0 mm/Km	2647	3.6	Good	25.0301123	N	86.5989923	E	Normal
24/05/23	17:51:53	79	100	5500	21.0 cm	24.1 Km/Hr	2100.0 mm/Km	2260	3.13	Good	25.0296431	N	86.5998239	E	Normal
24/05/23	17:52:08	79	100	5600	21.0 cm	23.8 Km/Hr	2100.0 mm/Km	2260	3.13	Good	25.0291681	N	86.6006021	E	Normal
24/05/23	17:52:24	79	100	5700	19.0 cm	23.1 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0290327	N	86.6014948	E	Normal
24/05/23	17:52:40	79	100	5800	23.0 cm	22.5 Km/Hr	2300.0 mm/Km	2454	3.37	Good	25.0292768	N	86.6029596	E	Normal
24/05/23	17:52:56	79	100	5900	27.0 cm	22.2 Km/Hr	2700.0 mm/Km	2841	3.84	Good	25.0296316	N	86.6036768	E	Normal
24/05/23	17:53:18	79	100	6000	21.0 cm	36.3 Km/Hr	2100.0 mm/Km	2260	3.13	Good	25.0304003	N	86.6040201	E	Normal
24/05/23	17:53:35	79	100	6100	19.0 cm	20.7 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0313902	N	86.6043329	E	Normal
24/05/23	17:53:51	79	100	6200	20.0 cm	22.7 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0321341	N	86.6046076	E	Normal
24/05/23	17:54:32	79	100	6300	18.0 cm	39.1 Km/Hr	1800.0 mm/Km	1969	2.77	Good	25.0333624	N	86.6059122	E	Normal
24/05/23	17:54:49	79	100	6400	22.0 cm	20.9 Km/Hr	2200.0 mm/Km	2357	3.25	Good	25.0332766	N	86.6063318	E	Normal
24/05/23	17:55:24	79	100	6500	20.0 cm	30.6 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0340471	N	86.6075830	E	Normal

8/6/23
S.B.C.N

Name of customer :	S B Engicon Private Limited
---------------------------	-----------------------------

Good

Average

Poor

< 4000

4001 - 5000

> 5000

24/05/23	17:55:42	79	100	6600	21.0 cm	20.7 Km/Hr	2100.0 mm/Km	2260	3.13	Good	25.0340471	N	86.6075830	E	Normal
24/05/23	17:57:10	79	100	6700	23.0 cm	34.2 Km/Hr	2300.0 mm/Km	2454	3.37	Good	25.0340586	N	86.6105280	E	Normal
24/05/23	17:57:34	79	100	6800	34.0 cm	34.6 Km/Hr	3400.0 mm/Km	3520	4.65	Good	25.0349703	N	86.6107264	E	Breaker
24/05/23	17:58:02	79	100	6900	32.0 cm	32.9 Km/Hr	3200.0 mm/Km	3326	4.42	Good	25.0356092	N	86.6114893	E	Normal
24/05/23	17:58:24	79	100	7000	36.0 cm	16.3 Km/Hr	3600.0 mm/Km	3713	4.87	Good	25.0360613	N	86.6116877	E	Normal
24/05/23	17:58:42	79	100	7100	34.0 cm	19.6 Km/Hr	3400.0 mm/Km	3520	4.65	Good	25.0370417	N	86.6121073	E	Normal
24/05/23	17:59:03	79	100	7200	38.0 cm	17.8 Km/Hr	3800.0 mm/Km	3907	5.1	Good	25.0377245	N	86.6123209	E	Breaker
24/05/23	17:59:23	79	100	7300	36.0 cm	17.6 Km/Hr	3600.0 mm/Km	3713	4.87	Good	25.0386152	N	86.6131372	E	Normal
24/05/23	17:59:41	79	100	7400	32.0 cm	20.0 Km/Hr	3200.0 mm/Km	3326	4.42	Good	25.0392256	N	86.6135111	E	Normal
24/05/23	17:59:57	79	100	7500	18.0 cm	22.2 Km/Hr	1800.0 mm/Km	1969	2.77	Good	25.0397425	N	86.6138163	E	Normal
24/05/23	18:00:18	79	100	7600	37.0 cm	17.8 Km/Hr	3700.0 mm/Km	3810	4.99	Good	25.0409441	N	86.6145487	E	Normal
24/05/23	18:00:37	79	100	7700	35.0 cm	18.3 Km/Hr	3500.0 mm/Km	3616	4.76	Good	25.0420008	N	86.6151895	E	Normal
24/05/23	18:01:02	79	100	7800	37.0 cm	34.7 Km/Hr	3700.0 mm/Km	3810	4.99	Good	25.0420008	N	86.6157236	E	Normal
24/05/23	18:01:21	79	100	7900	31.0 cm	18.1 Km/Hr	3100.0 mm/Km	3229	4.3	Good	25.0428438	N	86.6164408	E	Normal
24/05/23	18:02:46	79	100	8000	29.0 cm	34.4 Km/Hr	2900.0 mm/Km	3035	4.07	Good	25.0436773	N	86.6170130	E	Normal
24/05/23	18:03:20	79	100	8100	30.0 cm	30.3 Km/Hr	3000.0 mm/Km	3132	4.19	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:03:39	79	100	8200	29.0 cm	18.8 Km/Hr	2900.0 mm/Km	3035	4.07	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:07:04	79	100	8300	36.0 cm	31.7 Km/Hr	3600.0 mm/Km	3713	4.87	Good	25.0442953	N	86.6174784	E	Breaker
24/05/23	18:07:25	79	100	8400	30.0 cm	16.6 Km/Hr	3000.0 mm/Km	3132	4.19	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:07:46	79	100	8500	33.0 cm	17.1 Km/Hr	3300.0 mm/Km	3423	4.53	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:08:09	79	100	8600	35.0 cm	35.7 Km/Hr	3500.0 mm/Km	3616	4.76	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:08:29	79	100	8700	32.0 cm	18.3 Km/Hr	3200.0 mm/Km	3326	4.42	Good	25.0442953	N	86.6174784	E	Normal

8/6/23
D.E.

08-06-23
Rahay

Name of work : PWD Road Kharagpur Jamui (Banhara) - Ganaili Teen Mile

Name of customer : S B Engicon Private Limited

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

24/05/23	18:08:52	79	100	8800	36.0 cm	15.3 Km/Hr	3600.0 mm/Km	3713	4.87	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:09:14	79	100	8900	35.0 cm	16.3 Km/Hr	3500.0 mm/Km	3616	4.76	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:09:39	79	100	9000	37.0 cm	34.7 Km/Hr	3700.0 mm/Km	3810	4.99	Good	25.0442953	N	86.6174784	E	Breaker
24/05/23	18:10:00	79	100	9100	32.0 cm	17.4 Km/Hr	3200.0 mm/Km	3326	4.42	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:10:20	79	100	9200	29.0 cm	17.2 Km/Hr	2900.0 mm/Km	3035	4.07	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:10:38	79	100	9300	32.0 cm	20.2 Km/Hr	3200.0 mm/Km	3326	4.42	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:10:56	79	100	9400	37.0 cm	19.8 Km/Hr	3700.0 mm/Km	3810	4.99	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:11:14	79	100	9500	34.0 cm	19.4 Km/Hr	3400.0 mm/Km	3520	4.65	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:11:32	79	100	9600	27.0 cm	20.8 Km/Hr	2700.0 mm/Km	2841	3.84	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:11:48	79	100	9700	23.0 cm	21.8 Km/Hr	2300.0 mm/Km	2454	3.37	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:12:04	79	100	9800	22.0 cm	22.9 Km/Hr	2200.0 mm/Km	2357	3.25	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:12:19	79	100	9900	32.0 cm	23.1 Km/Hr	3200.0 mm/Km	3326	4.42	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:12:34	79	100	10000	31.0 cm	24.1 Km/Hr	3100.0 mm/Km	3229	4.3	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:12:52	79	100	10100	24.0 cm	19.9 Km/Hr	2400.0 mm/Km	2550	3.49	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:13:09	79	100	10200	33.0 cm	21.3 Km/Hr	3300.0 mm/Km	3423	4.53	Good	25.0442953	N	86.6174784	E	Normal
24/05/23	18:13:28	79	100	10300	36.0 cm	19.0 Km/Hr	3600.0 mm/Km	3713	4.87	Good	25.0536585	N	86.6316080	E	Normal
24/05/23	18:13:47	79	100	10400	34.0 cm	19.4 Km/Hr	3400.0 mm/Km	3520	4.65	Good	25.0541105	N	86.6317377	E	Normal
24/05/23	18:14:03	79	100	10500	26.0 cm	22.5 Km/Hr	2600.0 mm/Km	2744	3.72	Good	25.0548353	N	86.6318521	E	Normal
24/05/23	18:14:18	79	100	10600	25.0 cm	23.6 Km/Hr	2500.0 mm/Km	2647	3.6	Good	25.056326	N	86.6319666	E	Normal
24/05/23	18:14:33	79	100	10700	25.0 cm	23.4 Km/Hr	2500.0 mm/Km	2647	3.6	Good	25.0564585	N	86.6321650	E	Normal
24/05/23	18:14:48	79	100	10800	19.0 cm	24.6 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0569353	N	86.6335611	E	Normal
24/05/23	18:15:02	79	100	10900	23.0 cm	25.2 Km/Hr	2300.0 mm/Km	2454	3.37	Good	25.0567808	N	86.6345530	E	Normal

86/23
B.E.

Name of work : PWD Road Kharagpur Jamui (Banhara) - Ganaili Teen Mile

Name of customer : S B Engicon Private Limited

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

24/05/23	18:15:17	79	100	11000	20.0 cm	24.0 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0567808	N	86.6345530	E	Normal
24/05/23	18:15:32	79	100	11100	37.0 cm	24.6 Km/Hr	1700.0 mm/Km	1872	2.64	Good	25.0568495	N	86.6368341	E	Normal
24/05/23	18:15:48	79	100	11200	22.0 cm	22.5 Km/Hr	2200.0 mm/Km	2357	3.25	Good	25.0568495	N	86.6368341	E	Normal
24/05/23	18:16:03	79	100	11300	23.0 cm	24.5 Km/Hr	2300.0 mm/Km	2454	3.37	Good	25.0568495	N	86.6368341	E	Normal
24/05/23	18:16:17	79	100	11400	21.0 cm	24.9 Km/Hr	2100.0 mm/Km	2260	3.13	Good	25.0568495	N	86.6368341	E	Normal
24/05/23	18:16:30	79	100	11500	19.0 cm	27.3 Km/Hr	1900.0 mm/Km	2066	2.89	Good	25.0568495	N	86.6368341	E	Normal
24/05/23	18:16:38	79	100	11600	34.0 cm	40.3 Km/Hr	1400.0 mm/Km	1582	2.27	Good	25.0568495	N	86.6368341	E	Normal
24/05/23	18:16:47	79	100	11700	20.0 cm	43.2 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.0568495	N	86.6368341	E	Breaker
24/05/23	18:17:14	79	100	11800	38.0 cm	33.8 Km/Hr	3800.0 mm/Km	3907	5.1	Good	25.0568495	N	86.6435556	E	Normal
24/05/23	18:17:54	79	100	11900	36.0 cm	17.0 Km/Hr	3600.0 mm/Km	3713	4.87	Good	25.0542784	N	86.6435556	E	Normal
24/05/23	18:17:54	79	100	12000	34.0 cm	20.0 Km/Hr	3400.0 mm/Km	3520	4.65	Good	25.0542784	N	86.6435556	E	Normal
24/05/23	18:17:54	79	100	12100	30.0 cm	35.0 Km/Hr	3000.0 mm/Km	3132	4.19	Good	25.0542784	N	86.6435556	E	Normal
24/05/23	18:17:54	79	100	12200	27.0 cm	35.0 Km/Hr	2700.0 mm/Km	2841	3.84	Good	25.0542784	N	86.6435556	E	Normal
24/05/23	18:17:54	79	100	12300	25.0 cm	32.0 Km/Hr	2500.0 mm/Km	2647	3.6	Good	25.0542784	N	86.6435556	E	Normal
24/05/23	18:17:54	79	100	12400	27.0 cm	30.0 Km/Hr	2700.0 mm/Km	2841	3.84	Good	25.0542784	N	86.6435556	E	Normal
24/05/23	18:17:54	79	100	12500	30.0 cm	30.0 Km/Hr	3000.0 mm/Km	3132	4.19	Good	25.0542784	N	86.6435556	E	Normal

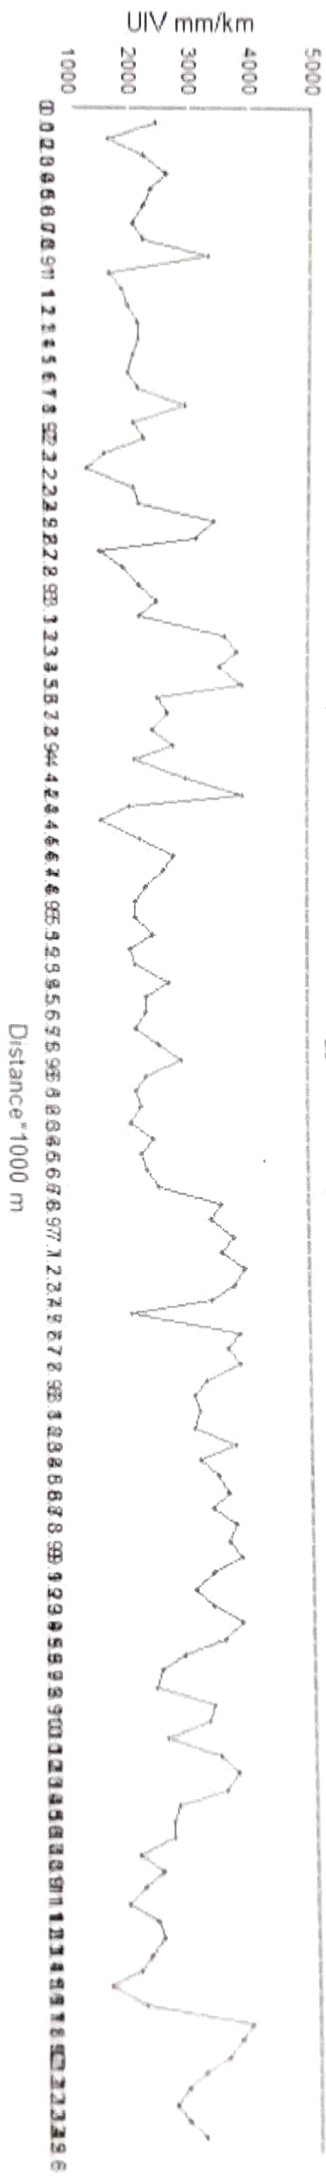
Average - 2687.

28/06/23

28/06/23

28/06/23

ier: S B Engicon Private Limited , Machine no: 19213 , Road: PVD Road Kharagpur Jamui (Baulhara) - Ganaili Teen Mile , Date: 24-05-23 , Section No: 79 , Equation: Y=



[Signature]
24/05/23

[Signature]
24/05/23

[Signature]
08-06-23
PN

[Signature]
25/06/2023
