

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, जयनगर

पत्रांक.....782...

जयनगर, दिनांक.....07/06/23

प्रेषक :- कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जयनगर

सेवा में,
नोडल पदाधिकारी (3054)
ग्रामीण कार्य विभाग
ब्राडा, पटना।


विषय :- **MR-3054 (NMP)** योजनान्तर्गत चल रहे योजनाओं हेतु आवंटन उपलब्ध कराने के सम्बंध में।


महाशय,

उपर्युक्त विषयक के सम्बंध में कहना है कि **MR-3054 (NMP)** योजना हेतु अधियाचना विहित प्रपत्र में आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु0- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जयनगर


7.6.23

R(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division. Jaynagar

Sl No	Package No	Name of the Road (English)	Project ID as per MIS	Administrative Approval (AA) Letter no Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No & Date	Date Completion as per Agreement	Actual Date of Completion	Value of IRI (In mm/Km)	Thickness of Bitumen Layer (In mm)	Value of Bitumen Content in Percentage	Previous Total Amount Allotted (In Lakh)	Up to Date Expenditure as per MIS	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of Lakh	Initial Rectification and Surface Renewal (in Lakh)	Five Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/MA/JA Y/19/0005	Narkatiya - Chacharaha	31910002050	Lt-1862 Dt-24.06.2019	3.080	127.50900	98.28309	22.94154	67/MIBD/21-22 03.01.2022	02.01.2023	-	2983	25 mm	5.16%	0.00000	0.00000	98.12260	
2	RM/MA/JA Y/19/0005	T03 - Narkatiya	31910002083	Lt-1862 Dt-24.06.2019	3.300	83.41800	58.91993	22.70013	67/MIBD/21-22 03.01.2022	02.01.2023	-	2816	25 mm	5.16%	0.00000	0.00000	58.76328	

Executive Engineer
RWD, Works Division, Jaynagar

74/15
7.6.23

FORM GFR -19 -A

(see Govt. of India's decision (i) below rule 150)
Form of Utilisation Certificate upto June - 2023

Rural Road Maintenance policy-2018

PIU:- R.W.D. Works, Division , Jaynagar


Sl. No.	Name of Scheme	Sanction No.& Date with amount (in Rs. Lakh)	Amount Received (in Rs. Lakh)	Particulars
1	2	3	4	5
1	Construction of Road Under Rural Road Maintenance policy-2018	3207.35417	3207.35417	Certified that out of Rs.3207.35417 Lakh received till date in favour of Ex.Engineer, R.W.D. Works Division, Jaynagar a sum of Rs.3148.47149 Lakh has been utilized for the purpose of Rural Road Maintenance policy-2018 Scheme as given in the margine for which it was sanctioned and that the balance of Rs.58.88268 Lakh remaining unutilized at the end of the period under the time of completion.
		3207.35417	3207.35417	

- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the propose for which it was sanctioned.

Kind of Checks Exercised :-

- (i) Workers have been supervised by Executive Engineer/ Superintending Engineer
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer
- (iii) Construction materials have been tested.
- (iv) Measurments have been recorded in the MB's and test check conducted by the Assistant
- (v) All other codal formalities have overserved


Executive Engineer
Rural works Department
Works Division, Jaynagar


7.6.23





प्रमाण-पत्र


शीर्ष :- 3054 एम0 आर0 (बिहार ग्रामीण पथ अनुरक्षण निति-2018)

योजना :- T03 To Narkatiya (Package No.- RM/MA/JAY/19/0005)

1. मपीपुस्त पर इस आशय का प्रमाण-पत्र दर्ज है कि कार्य गुणवत्तापूर्ण कराया गया है।
2. कराये गये कार्यों के सभी अवयवों के अवयववार 100 प्रतिशत कार्य का दर्ज मापी का सत्यापन कनीय अभियंता, 50 प्रतिशत मापी का सत्यापन सहायक अभियंता एवं 10 प्रतिशत मापी का सत्यापन कार्यपालक अभियंता द्वारा किया गया है।


कनीय अभियंता
कार्य प्रशाखा, बासोपट्टी


सहायक अभियंता
कार्य अवर प्रमंडल, बासोपट्टी


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जयनगर

Name of work : T03 to Narkatiya

Name of customer : Ramchandra Yadav

(R) Rural Road

Good

Average

< 4000

4001 - 5000

Poor

> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(P/cm)	Speed(Km/Hr)	Ultrasonic(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
02/06/23	15:37:25	21	0	0	0.0 cm	7.8 Km/Hr	0.0 mm/Km	196	0.35	Good	26.5320562	N	86.0224441	E	Normal
02/06/23	16:18:51	21	100	100	26.0 cm	15.8 Km/Hr	2600.0 mm/Km	2607	3.55	Good	26.5321456	N	86.0234629	E	Normal
02/06/23	16:19:17	21	100	200	22.0 cm	14.1 Km/Hr	2200.0 mm/Km	2236	3.1	Good	26.5324339	N	86.0245598	E	Normal
02/06/23	16:19:52	21	100	300	27.0 cm	11.3 Km/Hr	2700.0 mm/Km	2699	3.67	Good	26.5329145	N	86.0250237	E	Normal
02/06/23	16:20:28	21	100	400	23.0 cm	11.9 Km/Hr	2300.0 mm/Km	2328	3.21	Good	26.5331125	N	86.0260009	E	Normal
02/06/23	16:20:56	21	100	500	31.0 cm	12.3 Km/Hr	3100.0 mm/Km	3070	4.11	Good	26.5332635	N	86.0269389	E	Normal
02/06/23	16:21:16	21	100	600	25.0 cm	21.3 Km/Hr	2500.0 mm/Km	2514	3.44	Good	26.5331455	N	86.0280029	E	Normal
02/06/23	16:21:35	21	100	700	32.0 cm	18.9 Km/Hr	3200.0 mm/Km	3163	4.22	Good	26.5330275	N	86.0290169	E	Normal
02/06/23	16:21:54	21	100	800	31.0 cm	23.8 Km/Hr	3100.0 mm/Km	3070	4.11	Good	26.5329465	N	86.0299689	E	Normal
02/06/23	16:22:14	21	100	900	29.0 cm	18.1 Km/Hr	2900.0 mm/Km	2865	3.89	Good	26.5332365	N	86.0306789	E	Normal
02/06/23	16:22:42	21	100	1000	26.0 cm	13.1 Km/Hr	2600.0 mm/Km	2607	3.55	Good	26.5331264	N	86.0315604	E	Normal
02/06/23	16:23:01	21	100	1100	28.0 cm	18.8 Km/Hr	2800.0 mm/Km	2792	3.78	Good	26.5333224	N	86.0329614	E	Normal
02/06/23	16:23:19	21	100	1200	32.0 cm	19.0 Km/Hr	3200.0 mm/Km	3163	4.22	Good	26.5335045	N	86.0334274	E	Normal
02/06/23	16:23:39	21	100	1300	34.0 cm	18.1 Km/Hr	3400.0 mm/Km	3348	4.44	Good	26.5336686	N	86.0344238	E	Normal
02/06/23	16:23:58	21	100	1400	22.0 cm	19.0 Km/Hr	2200.0 mm/Km	2236	3.1	Good	26.5336744	N	86.0353576	E	Normal
02/06/23	16:24:16	21	100	1500	30.0 cm	25.8 Km/Hr	3000.0 mm/Km	2977	4	Good	26.5342647	N	86.0362203	E	Normal
02/06/23	16:24:34	21	100	1600	34.0 cm	20.0 Km/Hr	3400.0 mm/Km	3348	4.44	Good	26.5347517	N	86.0377543	E	Normal
02/06/23	16:24:52	21	100	1700	35.0 cm	20.6 Km/Hr	3500.0 mm/Km	3441	4.55	Good	26.5352257	N	86.0386993	E	Normal
02/06/23	16:25:09	21	100	1800	31.0 cm	21.4 Km/Hr	3100.0 mm/Km	3070	4.11	Good	26.5353437	N	86.0397313	E	Normal
02/06/23	16:25:26	21	100	1900	26.0 cm	21.3 Km/Hr	2600.0 mm/Km	2607	3.55	Good	26.5354427	N	86.0406325	E	Normal
02/06/23	16:25:45	21	100	2000	30.0 cm	20.0 Km/Hr	3000.0 mm/Km	2977	4	Good	26.5355496	N	86.0415842	E	Normal

End of report

20/6/23

20/6/23

कार्यपालक अभियंता
आशीष कार्य विभाग
कार्य प्रमण्डल, जयनगर

Name of work : T03 to Narkatiya

Name of customer : Ramchandra Yadav

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

02/06/23	16.26.17	21	100	2100	37.0 cm	11.4 Km/Hr	3700.0 mm/Km	3526	4.77	Good	26.5356022	N	86.0426412	E	Normal
02/06/23	16.26.42	21	100	2200	36.0 cm	14.8 Km/Hr	3600.0 mm/Km	3534	4.66	Good	26.5355132	N	86.0436802	E	Normal
02/06/23	16.27.03	21	100	2300	29.0 cm	16.3 Km/Hr	2900.0 mm/Km	2885	3.89	Good	26.5354330	N	86.0445109	E	Normal
02/06/23	16.27.24	21	100	2400	32.0 cm	17.6 Km/Hr	3200.0 mm/Km	3163	4.22	Good	26.5353637	N	86.0454286	E	Normal
02/06/23	16.28.01	21	100	2500	34.0 cm	21.9 Km/Hr	3400.0 mm/Km	3348	4.44	Good	26.5355407	N	86.0464693	E	Normal
02/06/23	16.28.27	21	100	2600	27.0 cm	13.3 Km/Hr	2700.0 mm/Km	2699	3.67	Good	26.5354785	N	86.0473915	E	Normal
02/06/23	16.28.55	21	100	2700	25.0 cm	12.8 Km/Hr	2500.0 mm/Km	2514	3.44	Good	26.5355203	N	86.0484038	E	Normal
02/06/23	16.29.26	21	100	2800	24.0 cm	11.5 Km/Hr	2400.0 mm/Km	2421	3.33	Good	26.5357155	N	86.0493295	E	Normal
02/06/23	16.29.54	21	100	2900	33.0 cm	13.3 Km/Hr	3300.0 mm/Km	3255	4.33	Good	26.5356752	N	86.0498456	E	Normal
02/06/23	16.30.34	21	100	3000	23.0 cm	22.8 Km/Hr	2300.0 mm/Km	2328	3.21	Good	26.5434874	N	86.0489771	E	Normal
02/06/23	16.31.11	21	100	3100	30.0 cm	16.7 Km/Hr	3000.0 mm/Km	2977	4	Good	26.5357197	N	86.0511718	E	Normal
02/06/23	16.31.42	21	100	3200	32.0 cm	11.2 Km/Hr	3200.0 mm/Km	3163	4.22	Good	26.5360079	N	86.0524075	E	Normal
02/06/23	16.32.08	21	100	3300	25.0 cm	14.2 Km/Hr	2500.0 mm/Km	2514	3.44	Good	26.5360079	N	86.0524075	E	Normal

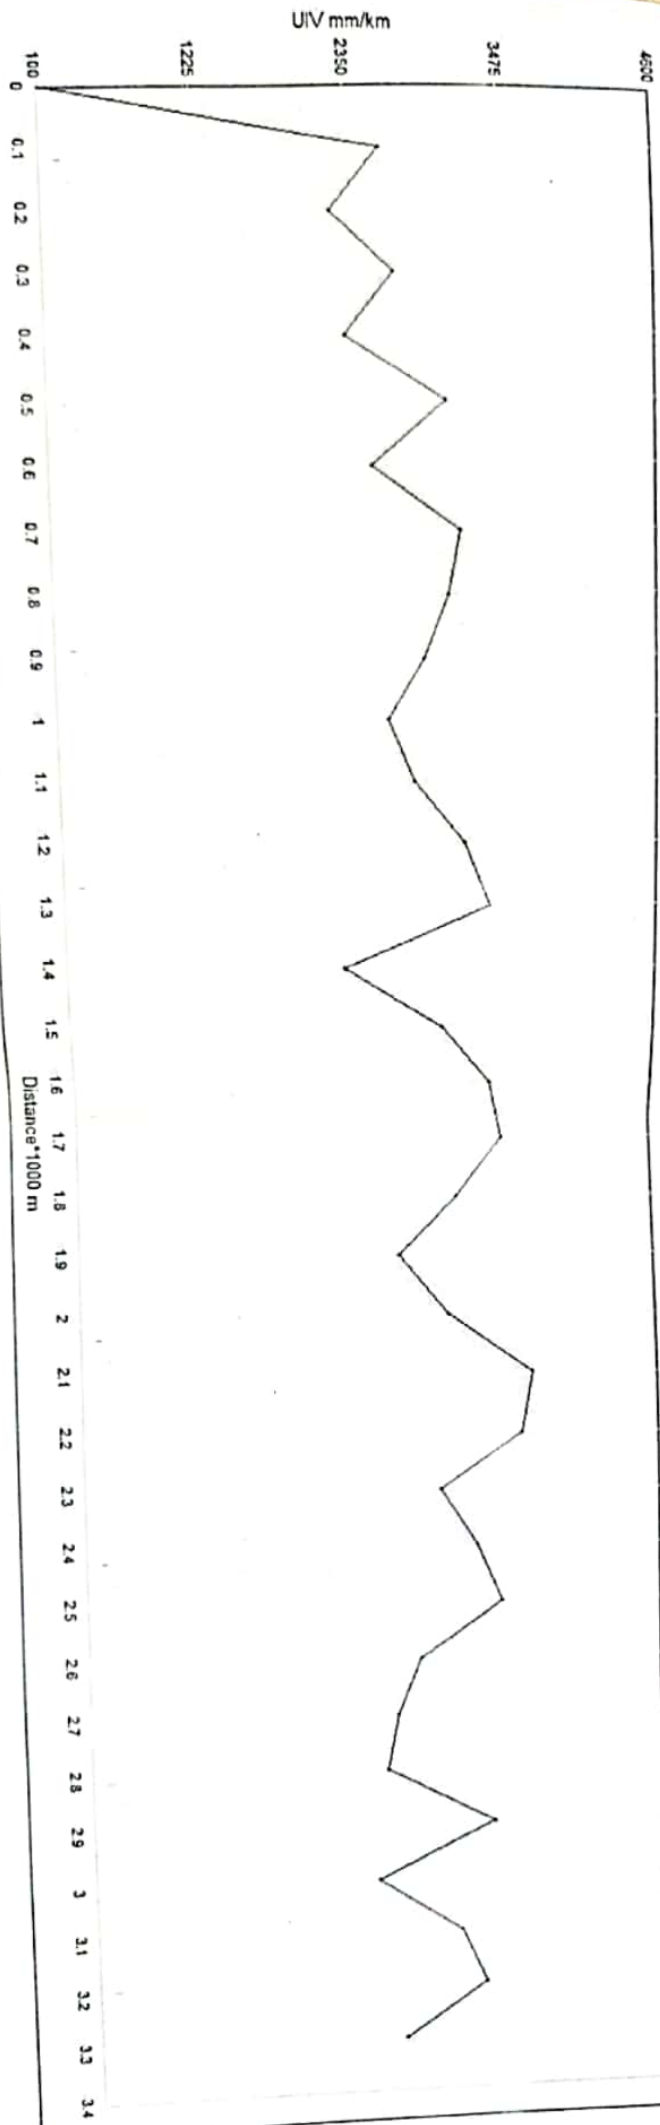
Ave:-2816

02/06/23

02/06/23

कार्यपालक अभियंता
श्रीमणि कार्यालय
कार्य प्रमण्डल, अयनगर

Name of Customer: Ramchandra Yadav, Machine no: 19195, Road: 103 to Narkatiya, Date: 02/06/23, Section No: 21, Equation: $Y = 0.927 X + 196.3$



02/06/23

02/06/23

02/06/23

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जयनगर

OFFICE OF THE EXECUTIVE ENGINEER, REGIONAL LABORATORY, R.W.D, DARBHANGA (BIHAR)
BITUMEN PERCENTAGE TEST

Name of the Scheme Canal. of. Nandakanya. To. Nandakanya
 Package No 62. MED. 21-22
 Sample collected by Lab.
 Date of sample collection 24.05.22
 Name of the works Division R.W.D. Darbhanga
 Name of the work circle Darbhanga
 Name of Agency Sri. Ram. Chandra. Yadav
 Date of test 31.05.22

CH = 1400MS.D.B.C

Sl No	Sample No	1	2	3
1	Wt. of mix taken before extraction (A) gm	500.210		
2	Wt. of filter paper before extraction (B) gm	4.920		
3	Wt. of mix after extraction (C) gm	471.040		
4	Wt. of filter paper after extraction (D) gm	5.960		
5	Wt. of filler collected from extract after allowing for setting (E) gm	2.310		
6	Wt. of filler collected in filter paper (D-B)=F gm	1.040		
7	Wt. of aggregate + filter paper (C+E+F)=G gm	474.390		
8	Percentage of Bitumen (in the mix) [(A-G)×100/A]	5.16%		

M. S. S.
21/05/22
 Laboratory Assistant
 R.W.D, Regional Laboratory
 Darbhanga (Bihar)

Nandakanya
31/05/22
 Assistant Engineer
 R.W.D, Regional Laboratory
 Darbhanga (Bihar)

S. S. S.
31/05/22
 Executive Engineer
 R.W.D, Regional Laboratory
 Darbhanga (Bihar)
