

कार्यालय
कार्यपालक अभियंता, ग्रामीण कार्य विभाग
कार्य प्रमंडल, दलसिंहसराय, समस्तीपुर

पत्राक 796 दलसिंहसराय / दिनांक 27/06/2023

प्रेषक, कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दलसिंहसराय

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
सचिव –सह– प्राधिकृत पदाधिकारी, बिहार
ग्रामीण पथ विकास ऐजेंसी पटना।

विषय– **New Maintenance Policy 2018** योजनान्तर्गत पथ में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि **New Maintenance Policy 2018** योजनान्तर्गत चल रहे पथ के निर्माणधीन कार्य के विरुद्ध चल रहे योजनाओं का भुगतान हेतु मो0- 113.43612 लाख की आवश्यकता है। अधियाचना का निर्माण कार्य विशिष्टियों के अनुरूप है तथा कार्य संतोषप्रद है।


अतः अनुरोध है कि अधियाचना पत्र के आधार पर आवंटन हेतु मो0- 113.43612 लाख उपलब्ध कराने की कृपा की जाय।

अनु0- 1) अधियाचना प्रपत्र।

2) 19ए फॉर्म।

3) IRI Report. की छायाप्रति संलग्न

विश्वासभाजन



कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल, दलसिंहसराय

FROM GFR-19-A

(See Govt. of India's decision(i) below rule 150)

Form of Utilisation Certificate upto June.-2023

New Maintenance Policy 2018(MR New)

PIU;- RWD Works Division Dalsinghsarai

Sl No	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lakh)	Amount Received (in Lakh)	Particulars
1	2	3	4	5
1	New Maintenance Policy 2018 (MR New)	3916.49472	3916.49472	Certified that out of Rs-3916.49472 Lakh received till date in favour of Executive Engineer, RWD Works Division Dalsinghsarai a Sum of Rs-3847.02997 Lakh has been utilized for the New Maintenance Policy 2018(MR New) Scheme as given in the margin for which it was Sanctioned and that the Balance of Rs-69.46475 1 Lakh remaining unutilized at the end of period under the time of completion
		3916.49472	3916.49472	


2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was

Kind of Checks Exercised:-

- Workers have been supervised by Executive Engineer/ Superintending Engineer
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer
- Construction materials have been tested
- Measurements have been recorded in the MB's and test check conducted by the
- All other codal formalities have observed

3. Physical Progress Achieved

- Construction of Road Works
- Construction of CD Works


Sr.DAO
Rural Works Department,
Works Division Dalsinghsarai


Executive Engineer
Rural Works Department,
Works Division Dalsinghsarai


Rural Works Department, Works Division Dalsinghsarai
Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018
(Initial Rectification and Surface Renewal)

Name of Division : PIU(Dalsinghsarai)


Sl No	Package no	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allotted Amount (Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (In lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (In lac)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/SA/DAL/22/0005	L032 To Damodarpur Manika Tola	32010412001	1424/26.03.22	2.600	101.25000	78.55847	25.49447	05MBD/2023-24 12.05.2023	11.02.2024	-	3508	25mm	5.10%	0.00000	0.00000	62.84678	
2	RM/SA/DAL/22/0005	L042-T03 to Vishwaspur (VR42)	32010402064	1424/26.03.22	1.780	82.36000	63.23668	21.78070	05MBD/2023-24 12.05.2023	11.02.2024	-	3508	25mm	5.10%	0.00000	0.00000	50.58934	
TOTAL					4.380	183.610	141.795	47.275							0.00000	0.00000	113.43612	

- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed
- 2 Up-to date Physical Progress has been uploaded in MIS


 Sr Divisional Account Officer
 Rural Works Department,
 Works Division Dalsinghsarai


 Executive Engineer
 Rural Works Department,
 Works Division Dalsinghsarai



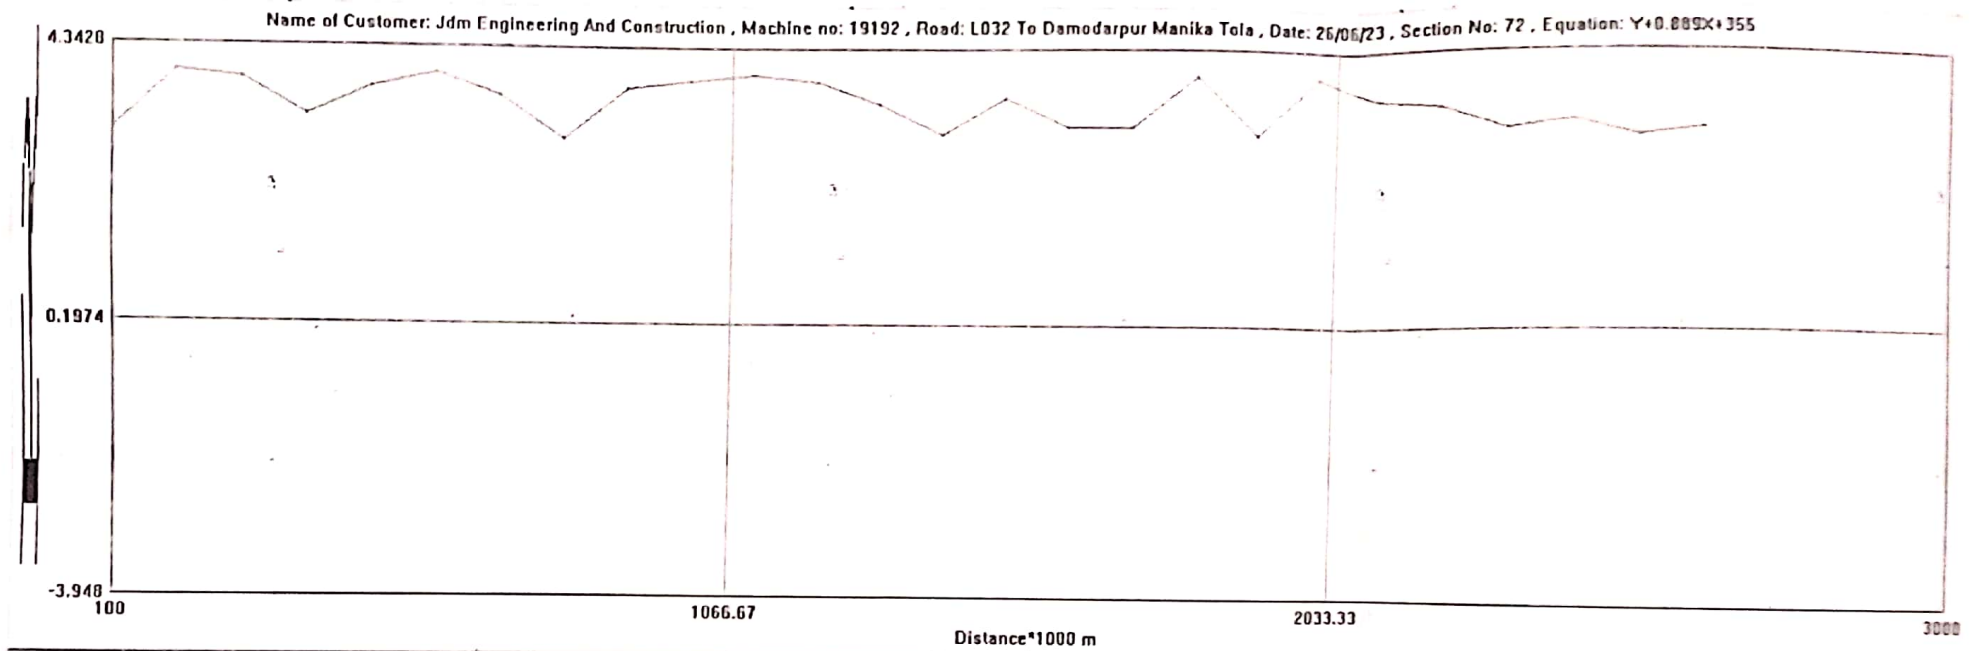

[Handwritten signature]
27/06/23

[Handwritten signature]
27/06/23

[Handwritten signature]
27/06/23



Name of the work: L032 To Damodarpur Manika Tola


Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed (Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
26/06/2023	11:22:45	72	100	100	21.0 cm	14.7 Km/Hr	2100.0 mm/Km	2221.9	3.08	Good	25.68023	N	85.78933	E	Normal
26/06/2023	11:23:31	72	100	200	29.0 cm	17.9 Km/Hr	2900.0 mm/Km	2933.1	3.95	Good	25.68023	N	85.78933	E	Normal
26/06/2023	12:11:29	72	100	300	28.0 cm	10.4 Km/Hr	2800.0 mm/Km	2844.2	3.84	Good	25.68027	N	85.78931	E	Normal
26/06/2023	12:11:48	72	100	400	23.0 cm	18.4 Km/Hr	2300.0 mm/Km	2399.7	3.3	Good	25.68109	N	85.78935	E	Normal
26/06/2023	12:12:08	72	100	500	27.0 cm	18.9 Km/Hr	2700.0 mm/Km	2755.3	3.73	Good	25.68184	N	85.78901	E	Normal
26/06/2023	12:12:39	72	100	600	29.0 cm	11.4 Km/Hr	2900.0 mm/Km	2933.1	3.95	Good	25.68257	N	85.78873	E	Normal
26/06/2023	12:12:59	72	100	700	26.0 cm	17.4 Km/Hr	2600.0 mm/Km	2666.4	3.63	Good	25.68354	N	85.78881	E	Normal
26/06/2023	12:13:19	72	100	800	20.0 cm	18.0 Km/Hr	2000.0 mm/Km	2133	2.97	Good	25.68431	N	85.78893	E	Normal
26/06/2023	12:13:51	72	100	900	27.0 cm	11.7 Km/Hr	2700.0 mm/Km	2755.3	3.73	Good	25.68517	N	85.78901	E	Normal
26/06/2023	12:14:25	72	100	1000	28.0 cm	10.2 Km/Hr	2800.0 mm/Km	2844.2	3.84	Good	25.68602	N	85.78914	E	Normal
26/06/2023	12:14:51	72	100	1100	29.0 cm	14.2 Km/Hr	2900.0 mm/Km	2933.1	3.95	Good	25.6869	N	85.78928	E	Normal
26/06/2023	12:15:15	72	100	1200	28.0 cm	15.0 Km/Hr	2800.0 mm/Km	2844.2	3.84	Good	25.68768	N	85.7895	E	Normal
26/06/2023	12:15:38	72	100	1300	25.0 cm	15.0 Km/Hr	2500.0 mm/Km	2577.5	3.52	Good	25.68782	N	85.7885	E	Normal
26/06/2023	12:16:00	72	100	1400	21.0 cm	16.8 Km/Hr	2100.0 mm/Km	2221.9	3.08	Good	25.68801	N	85.78751	E	Normal
26/06/2023	12:16:36	72	100	1500	26.0 cm	10.5 Km/Hr	2600.0 mm/Km	2666.4	3.63	Good	25.68816	N	85.78676	E	Normal
26/06/2023	12:17:30	72	100	1600	22.0 cm	12.5 Km/Hr	2200.0 mm/Km	2310.8	3.19	Good	25.68827	N	85.78571	E	Normal
26/06/2023	12:17:50	72	100	1700	22.0 cm	13.2 Km/Hr	2200.0 mm/Km	2310.8	3.19	Good	25.68821	N	85.78392	E	Normal
26/06/2023	12:18:30	72	100	1800	29.0 cm	12.0 Km/Hr	2900.0 mm/Km	2933.1	3.95	Good	25.68738	N	85.78411	E	Normal
26/06/2023	12:18:10	72	100	1900	21.0 cm	10.5 Km/Hr	2100.0 mm/Km	2221.9	3.08	Good	25.68646	N	85.78404	E	Normal
26/06/2023	12:19:20	72	100	2000	29.0 cm	11.2 Km/Hr	2900.0 mm/Km	2933.1	3.95	Good	25.68565	N	85.78389	E	Normal
26/06/2023	12:19:50	72	100	2100	26.0 cm	13.9 Km/Hr	2600.0 mm/Km	2666.4	3.63	Good	25.68482	N	85.78388	E	Normal
26/06/2023	12:20:08	72	100	2200	25.0 cm	10.5 Km/Hr	2500.0 mm/Km	2577.5	3.52	Good	25.68391	N	85.78379	E	Normal
26/06/2023	12:20:59	72	100	2300	22.0 cm	10.2 Km/Hr	2200.0 mm/Km	2310.8	3.19	Good	25.68316	N	85.78375	E	Normal
26/06/2023	12:21:01	72	100	2400	23.0 cm	13.7 Km/Hr	2300.0 mm/Km	2399.7	3.3	Good	25.68239	N	85.78416	E	Normal
26/06/2023	12:21:35	72	100	2500	21.0 cm	17.5 Km/Hr	2100.0 mm/Km	2221.9	3.08	Good	25.6819	N	85.78487	E	Normal
26/06/2023	12:22:10	72	100	2600	22.0 cm	12.5 Km/Hr	2200.0 mm/Km	2310.8	3.19	Good	25.6813	N	85.78543	E	Normal

IRI Value 3511
Machine ID 19192

27/6/23
CV

27/06/23

27/06/23

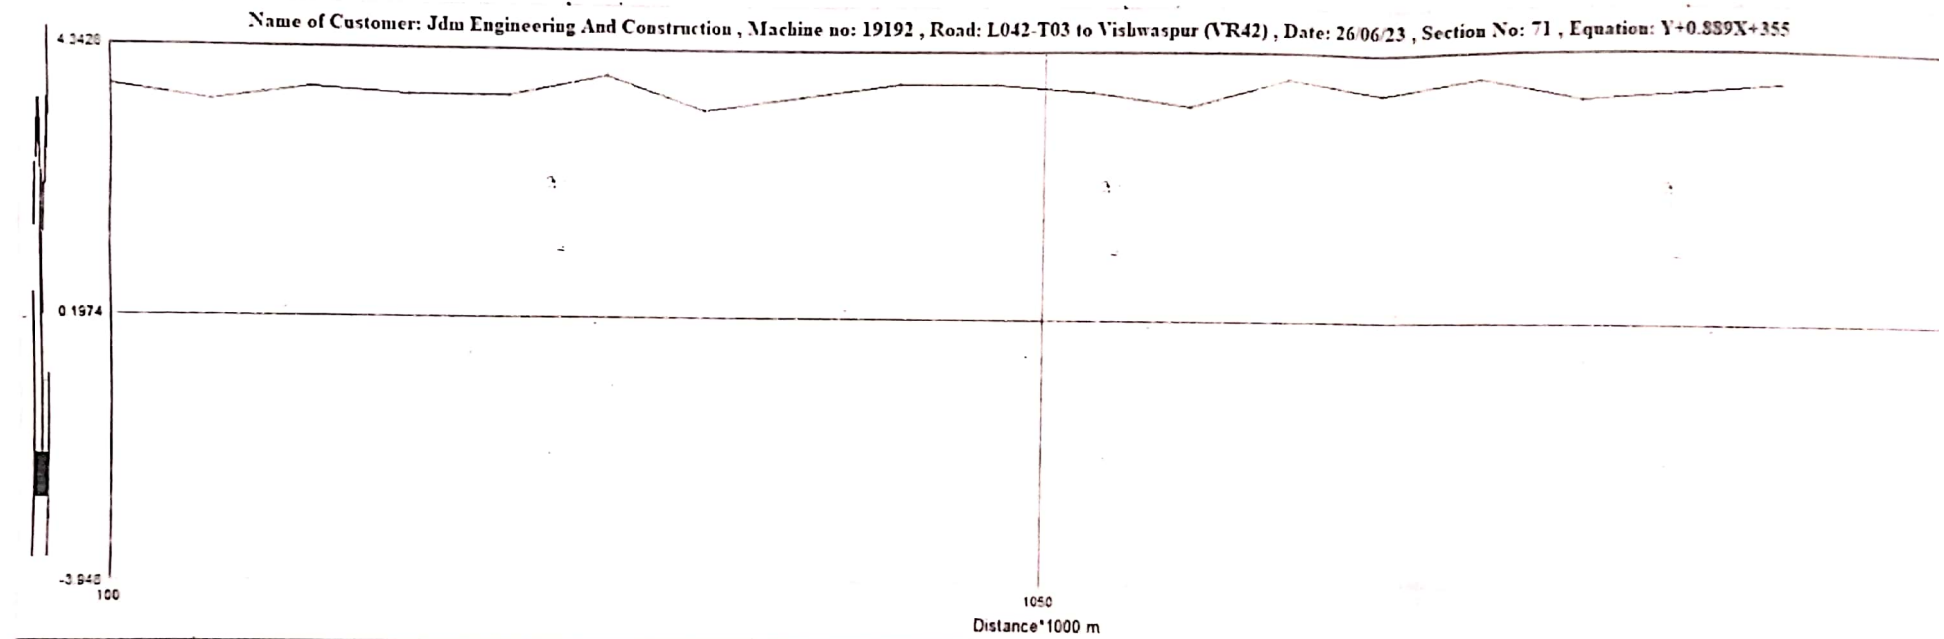

Handwritten signature
27/6/23
SE

Handwritten signature
27/06/23
AB

Handwritten signature
27/06/23



Name of the work: L042-T03 to Vishwaspur (VR42)

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed (Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
26/06/2023	10:00:16	71	100	100	27.0 cm	10.7 Km/Hr	2700.0 mm/Km	2755.3	3.734	Good	25.63375	N	85.79479	E	Normal
26/06/2023	10:05:03	71	100	200	25.0 cm	17.0 Km/Hr	2500.0 mm/Km	2577.5	3.518	Good	25.63425	N	85.79468	E	Normal
26/06/2023	10:05:21	71	100	300	27.0 cm	22.4 Km/Hr	2700.0 mm/Km	2755.3	3.734	Good	25.63504	N	85.79443	E	Normal
26/06/2023	10:06:39	71	100	400	26.0 cm	20.6 Km/Hr	2600.0 mm/Km	2666.4	3.626	Good	25.63587	N	85.79443	E	Normal
26/06/2023	10:06:54	71	100	500	26.0 cm	24.3 Km/Hr	2600.0 mm/Km	2666.4	3.626	Good	25.63644	N	85.79517	E	Normal
26/06/2023	10:07:12	71	100	600	28.0 cm	29.8 Km/Hr	2900.0 mm/Km	2933.1	3.948	Good	25.63726	N	85.79545	E	Normal
26/06/2023	10:07:32	71	100	700	24.0 cm	16.4 Km/Hr	2400.0 mm/Km	2488.6	3.41	Good	25.63806	N	85.79567	E	Normal
26/06/2023	10:08:49	71	100	800	26.0 cm	21.1 Km/Hr	2600.0 mm/Km	2666.4	3.626	Good	25.63892	N	85.79562	E	Normal
26/06/2023	10:08:56	71	100	900	28.0 cm	17.9 Km/Hr	2800.0 mm/Km	2844.2	3.841	Good	25.63972	N	85.79526	E	Normal
26/06/2023	10:09:21	71	100	1000	28.0 cm	14.2 Km/Hr	2800.0 mm/Km	2844.2	3.841	Good	25.6401	N	85.79526	E	Normal
26/06/2023	10:09:54	71	100	1100	27.0 cm	11.3 Km/Hr	2700.0 mm/Km	2755.3	3.734	Good	25.63231	N	85.78969	E	Normal
26/06/2023	10:10:21	71	100	1200	25.0 cm	13.0 Km/Hr	2500.0 mm/Km	2577.5	3.518	Good	25.63317	N	85.78961	E	Normal
26/06/2023	10:10:49	71	100	1300	29.0 cm	10.1 Km/Hr	2900.0 mm/Km	2933.1	3.948	Good	25.6341	N	85.78956	E	Normal
26/06/2023	10:11:29	71	100	1400	27.0 cm	13.6 Km/Hr	2700.0 mm/Km	2755.3	3.734	Good	25.63493	N	85.78964	E	Normal
26/06/2023	10:11:49	71	100	1500	29.0 cm	12.3 Km/Hr	2900.0 mm/Km	2933.1	3.948	Good	25.63579	N	85.78993	E	Normal
26/06/2023	10:12:24	71	100	1600	26.0 cm	19.1 Km/Hr	2600.0 mm/Km	2666.4	3.626	Good	25.63673	N	85.79022	E	Normal
26/06/2023	10:12:59	71	100	1700	27.0 cm	20.2 Km/Hr	2700.0 mm/Km	2755.3	3.734	Good	25.63743	N	85.7906	E	Normal
26/06/2023	10:13:08	71	100	1800	28.0 cm	19.4 Km/Hr	2800.0 mm/Km	2844.2	3.841	Good	25.63801	N	85.79118	E	Normal

IRI Value 3721
Machine ID 19192

27/6/23
65

27/06/23

27/06/23

