

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक 421/अनु० पालीगंज/दिनांक 16/03/23

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी -सह- सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, पटना।

विषय:-

शीर्ष MR 3054 Under Bihar Rural Road Maintenance Policy-2018 योजना अंतर्गत
आवंटन का अधियाचना के संबंध में।

महाशय,


उपर्युक्त विषय के संबंध में कहना है कि शीर्ष MR 3054 Under Bihar Rural Road Maintenance Policy-2018 योजना अंतर्गत पथों का अधियाचना का माँग विहित प्रपत्र में तैयार कर भेजी जा रही है।

अतः अनुरोध है कि उक्त योजना का आवंटन उपलब्ध करने की कृपा की जाय, ताकि संवेदक का भुगतान हो सकें।


अनु०:- यथोक्त।

विश्वासभाजन


16/3/23


16/03/23

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।


16.3.23

Requisition Format for Scheme Head-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Division : Paliganj

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of Road IRI (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Alloted Amount (in Lakh)	Up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Amount (In Lakh)	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	20	21
1	RM/PA/PAL/22/0002	CHIRAURA NH 98 - BADIPUR	10100102100	457/04.07.2022	2.2	117.297	87.82796	23.8889	05 MBD/NEW MR 2018/2022-23 & Dt 05.01.2023	04.10.2023	—	2903.045	25mm SDBC	5%	0		87.82796	कमरे गये कार्य गुणवत्तापूर्ण एवं विधिचिदों के अनुसार है एवं सहायक अभियन्ताओं द्वारा 50 प्रतिशत एवं अग्रोहस्तवरी द्वारा 10 प्रतिशत कार्य का सत्यापन कर लिया गया है।
2	RM/PA/PAL/22/0002	DARIPUR MAIN ROAD - Majhanpura Via Mushari Tola	10100102107	457/04.07.2022	3.7	185.225	146.27403	31.25670	05 MBD/NEW MR 2018/2022-23 & Dt 05.01.2023	04.10.2023	—	2893.783	25mm SDBC	5%	0		146.27403	


16/3/23
 Executive Engineer
 RWD Works Division, Paliganj

16.3.23



Name of The Road : CHIRAURA NH 98 - BADIPUR

Length : 2.200 KM

Package No. : RM/PA/PAL/22/0002

Division : Paliganj

Block : Naubatpur

Contractor Name : Patliputra Infra Construction Pvt Ltd

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD				$Y = 0 * X^2 + 0.936 * X + 278.4$		
16/03/23	9:45:29	44	0.1	280	30.3	2800	2899	G	25.528528	84.995212	Normal	X = 2900		
16/03/23	9:46:0	44	0.1	290	30.3	2900	2992	G	25.529349	84.994722	Normal	Y = 2992		
16/03/23	9:46:4	44	0.1	250	30.3	2500	2618	G	25.53022	84.994623	Normal			
16/03/23	9:46:4	44	0.1	220	30.3	2200	2337	G	25.530769	84.993904	Normal			
16/03/23	9:47:4	44	0.1	260	30.3	2600	2712	G	25.53136	84.993068	Normal	(R) RURAL ROAD		
16/03/23	9:47:39	44	0.1	320	30.3	3200	3273	G	25.531785	84.992213	Normal	Good	Average	Poor
16/03/23	9:48:0	44	0.1	280	30.3	2800	2899	G	25.53225	84.991574	Normal	<4000	4001-5000	>5001
16/03/23	9:48:13	44	0.1	250	30.3	2500	2618	G	25.53261	84.990701	Normal			
16/03/23	9:48:13	44	0.1	290	20.2	2900	2992	G	25.533074	84.990471	Curve			
16/03/23	9:49:22	44	0.1	330	30.3	3300	3367	G	25.533357	84.989585	Normal			
16/03/23	9:49:49	44	0.1	320	30.3	3200	3273	G	25.533939	84.989118	Normal			
16/03/23	9:50:0	44	0.1	350	20.2	3500	3554	G	25.534228	84.988236	Curve			
16/03/23	9:50:21	44	0.1	290	30.3	2900	2992	G	25.534532	84.987278	Normal			
16/03/23	9:50:49	44	0.1	260	30.3	2600	2712	G	25.534812	84.986348	Normal			
16/03/23	9:51:24	44	0.1	260	30.3	2600	2712	G	25.535195	84.985353	Normal			
16/03/23	9:51:24	44	0.1	290	30.3	2900	2992	G	25.535544	84.984523	Normal			
16/03/23	9:52:0	44	0.1	260	30.3	2600	2712	G	25.535928	84.983555	Normal			
16/03/23	9:52:19	44	0.1	250	30.3	2500	2618	G	25.536273	84.982642	Normal			
16/03/23	9:52:42	44	0.1	280	20.2	2800	2899	G	25.536652	84.981818	Curve			
16/03/23	9:53:9	44	0.1	280	20.2	2800	2899	G	25.537046	84.980881	Normal			
16/03/23	9:53:29	44	0.1	270	30.3	2700	2805	G	25.537433	84.979991	Normal			
16/03/23	9:54:11	44	0.1	290	30.3	2900	2992	G	25.537504	84.979677	Normal			
Total			2.2	6170	626.2	61700	63867		561.742388	1869.735493				
Average						2804.545	2903.045							

82/16/03/2023
OE

SEL
16/3/23
ee



Name of Customer : Pattiputra Infra Construction Pvt
 Name of Work/ Road : CHIRAUURA NH 98 - BADIPUR
 Lab Job number :
 Date : 16-03-2023
 Section No. : 44

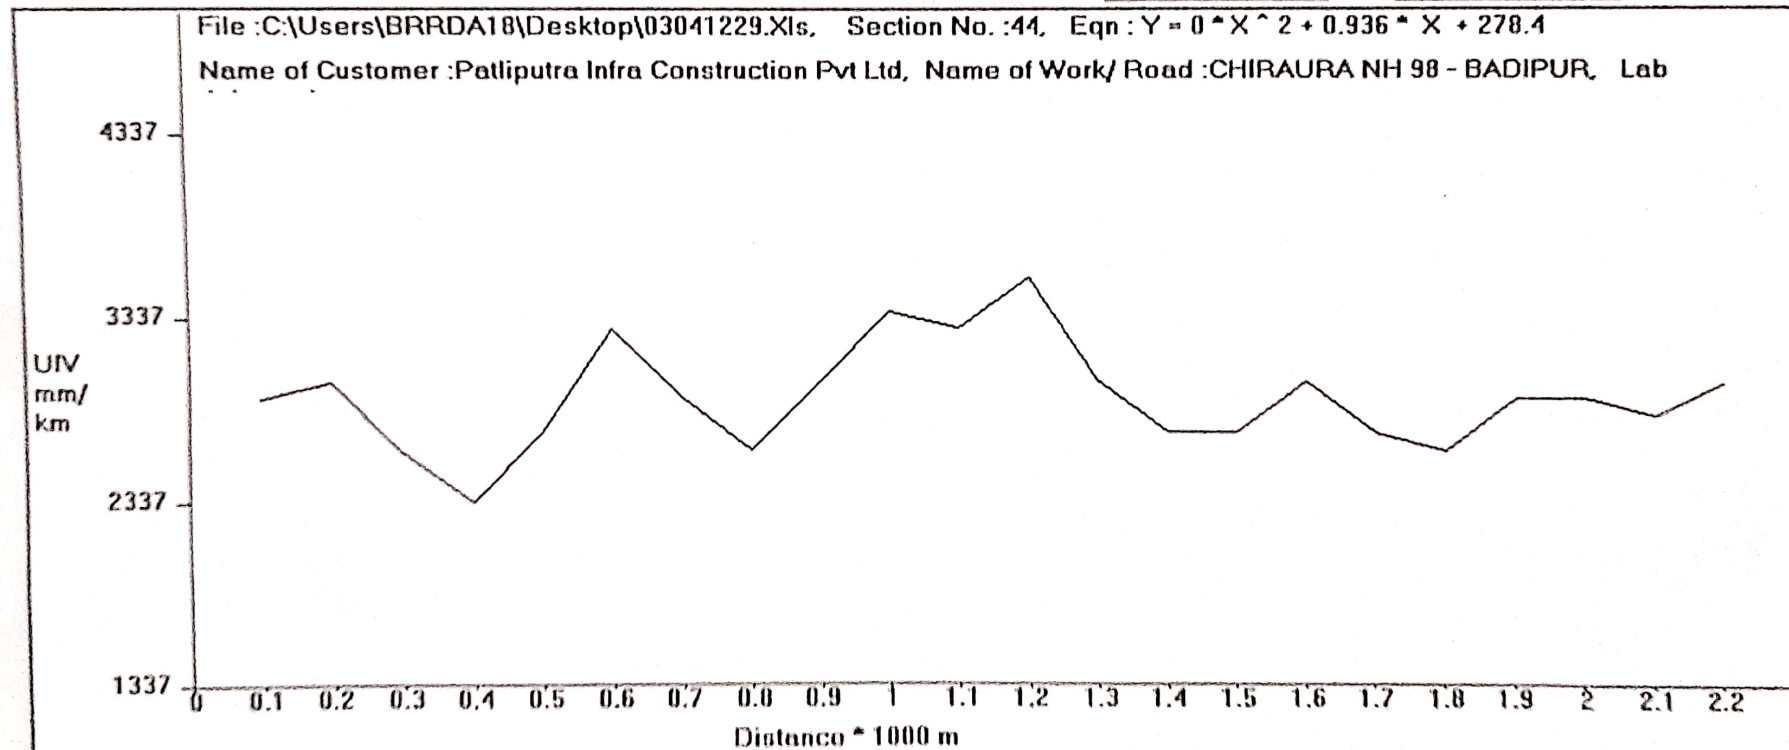
Test Date : 16-03-2023 Road Name : CHIRAUURA NH 98 - BADIPUR
 Machine No : 374 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : UIV Range : 1337 To 5000 1000 mm/km
 Start Location : Dist Range : 0 To 2.3 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 0.936 * X + 278.4$

Print

Generate Report and Graph

Redraw Graph

Map View



16/03/2023
 OC

RC
 16/3/23
 GG
