

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक 421/अनु० पालीगंज/दिनांक 16/03/23

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी -सह- सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, पटना।

विषय:-

शीर्ष MR 3054 Under Bihar Rural Road Maintenance Policy-2018 योजना अंतर्गत
आवंटन का अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष MR 3054 Under Bihar Rural Road Maintenance Policy-2018 योजना अंतर्गत पथों का अधियाचना का माँग विहित प्रपत्र में तैयार कर भेजी जा रही है।

अतः अनुरोध है कि उक्त योजना का आवंटन उपलब्ध करने की कृपा की जाय, ताकि संवेदक का भुगतान हो सकें।


अनु०:- यथोक्त।

विश्वासभाजन


16/3/23


16/03/23


कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।


16.3.23

Requisition Format for Scheme Head-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Division : Paliganj

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of Road IRI (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Alloted Amount (in Lakh)	Up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Amount (In Lakh)	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	20	21
1	RM/PA/PAL/22/0002	CHIRAURA NH 98 - BADIPUR	10100102100	457/04.07.2022	2.2	117.297	87.82796	23.8889	05 MBD/NEW MR 2018/2022-23 & Dt 05.01.2023	04.10.2023	—	2903.045	25mm SDBC	5%	0		87.82796	ऊपर दिये गए कार्य पूर्णतः पूर्ण एवं विभिन्न चरणों के अनुसार है एवं सहायक अभियन्ताओं द्वारा 50 प्रतिशत एवं अग्रोहस्तवरी द्वारा 10 प्रतिशत कार्य का सत्यापन कर लिया गया है।
2	RM/PA/PAL/22/0002	DARIPUR MAIN ROAD - Majhanpura Via Mushari Tola	10100102107	457/04.07.2022	3.7	185.225	146.27403	31.25670	05 MBD/NEW MR 2018/2022-23 & Dt 05.01.2023	04.10.2023	—	2893.783	25mm SDBC	5%	0		146.27403	


16/3/23
 Executive Engineer
 RWD Works Division, Paliganj

16.3.23



Name of The Road :DARIPUR MAIN ROAD - Majhanpura Via Mushari Tola

Length : 3.700 Km

Package No. : RM/PA/PAL/22/0002

Division : Paliganj

Block : Naubatpur

Contractor Name : Patliputra Infra Construction Pvt Ltd

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	$Y = 0 * X^2 + 0.936 * X + 278.4$		
16/03/23	8:45:29	45	0.1	280	0	2800	2899	G	25.40944	84.93365	Normal	X = 3000		
16/03/23	8:46:0	45	0.1	230	30.3	2300	2431	G	25.40953	84.93273	Normal	Y = 3086		
16/03/23	8:46:4	45	0.1	200	30.3	2000	2150	G	25.40961	84.93182	Normal			
16/03/23	8:46:4	45	0.1	230	30.3	2300	2431	G	25.40975	84.93086	Normal			
16/03/23	8:46:4	45	0.1	350	20.2	3500	3554	G	25.41003	84.92984	Normal	RURAL ROAD		
16/03/23	8:46:39	45	0.1	260	30.3	2600	2712	G	25.41062	84.9294	Normal	Good	Average	Poor
16/03/23	8:47:0	45	0.1	330	20.2	3300	3367	G	25.41155	84.92932	Normal	<4000	4001-5000	>5001
16/03/23	8:47:13	45	0.1	220	30.3	2200	2337	G	25.41232	84.92966	Normal			
16/03/23	8:47:13	45	0.1	330	20.2	3300	3367	G	25.41322	84.92949	Curve			
16/03/23	8:47:13	45	0.1	210	30.3	2100	2244	G	25.41385	84.92902	Normal			
16/03/23	8:47:49	45	0.1	370	20.2	3700	3741	G	25.41386	84.92804	Normal			
16/03/23	8:48:0	45	0.1	260	30.3	2600	2712	G	25.41384	84.92707	Curve			
16/03/23	8:48:0	45	0.1	290	30.3	2900	2992	G	25.41372	84.9262	Normal			
16/03/23	8:48:24	45	0.1	260	30.3	2600	2712	G	25.41367	84.92546	Normal			
16/03/23	8:48:24	45	0.1	250	30.3	2500	2618	G	25.41363	84.92484	Normal			
16/03/23	8:48:24	45	0.1	280	20.2	2800	2899	G	25.41487	84.92426	Normal			
16/03/23	8:48:24	45	0.1	280	20.2	2800	2899	G	25.41052	84.92382	Normal			
16/03/23	8:49:0	45	0.1	270	30.3	2700	2805	G	25.41519	84.92316	Normal			
16/03/23	8:49:0	45	0.1	210	30.3	2100	2244	G	25.41532	84.92206	Curve			
16/03/23	8:49:35	45	0.1	290	30.3	2900	2992	G	25.41545	84.92104	Normal			
16/03/23	8:49:35	45	0.1	220	30.3	2200	2337	G	25.41571	84.92019	Normal			
16/03/23	8:49:35	45	0.1	370	20.2	3700	3741	G	25.41583	84.91928	Normal			
16/03/23	8:50:0	45	0.1	350	20.2	3500	3554	G	25.41624	84.91856	Curve			
16/03/23	8:50:10	45	0.1	290	30.3	2900	2992	G	25.04172	84.91857	Normal			
16/03/23	8:50:10	45	0.1	290	30.3	2900	2992	G	25.41722	84.91775	Normal			
16/03/23	8:52:0	45	0.1	280	30.3	2800	2899	G	25.41752	84.91691	Normal			
16/03/23	8:52:0	45	0.1	350	20.2	3500	3554	G	25.41821	84.91662	Curve			
16/03/23	8:52:0	45	0.1	300	30.3	3000	3086	G	25.41866	84.91621	Normal			
16/03/23	8:55:20	45	0.1	270	30.3	2700	2805	G	25.4182	84.91556	Normal			
16/03/23	8:55:20	45	0.1	280	30.3	2800	2899	G	25.41796	84.91484	Normal			
16/03/23	8:55:35	45	0.1	270	30.3	2700	2805	G	25.41819	84.91393	Normal			
16/03/23	8:58:15	45	0.1	260	30.3	2600	2712	G	25.41848	84.9129	Curve			
16/03/23	8:58:15	45	0.1	230	30.3	2300	2431	G	25.41875	84.9118	Normal			



16/03/23	8:58:15	45	0.1	280	30.3	2800	2899	G	25.41891	84.91095	Normal			
16/03/23	8:58:45	45	0.1	280	30.3	2800	2899	G	25.41897	84.91011	Normal			
16/03/23	8:59:24	45	0.1	320	30.3	3200	3273	G	25.41883	84.90924	Normal			
16/03/23	8:59:24	45	0.1	300	30.3	3000	3086	G	25.41895	84.90822	Normal			
Total			3.7	10340	999.9	103400	107070		939.9784	3142.103				
Average						2794.594	2893.783							

82
16/03/2023
05

80
16/3/23
CC



Name of Customer : Patliputra Infra Construction Pvt

Name of Work/ Road : Daripur Main Road May

Lab Job number :

Date : 16-03-2023

Section No. 45

Test Date : 16-03-2023 Road Name : Daripur Main Road May

Machine No : 374 Road Type : (R) RURAL ROAD

Start S No : Side : Interval

Start E No : Weather : UIV Range : 1150 To 5000 1000 mm/km

Start Location : Dist Range : 0 To 3.8 0.1 * 1000 m

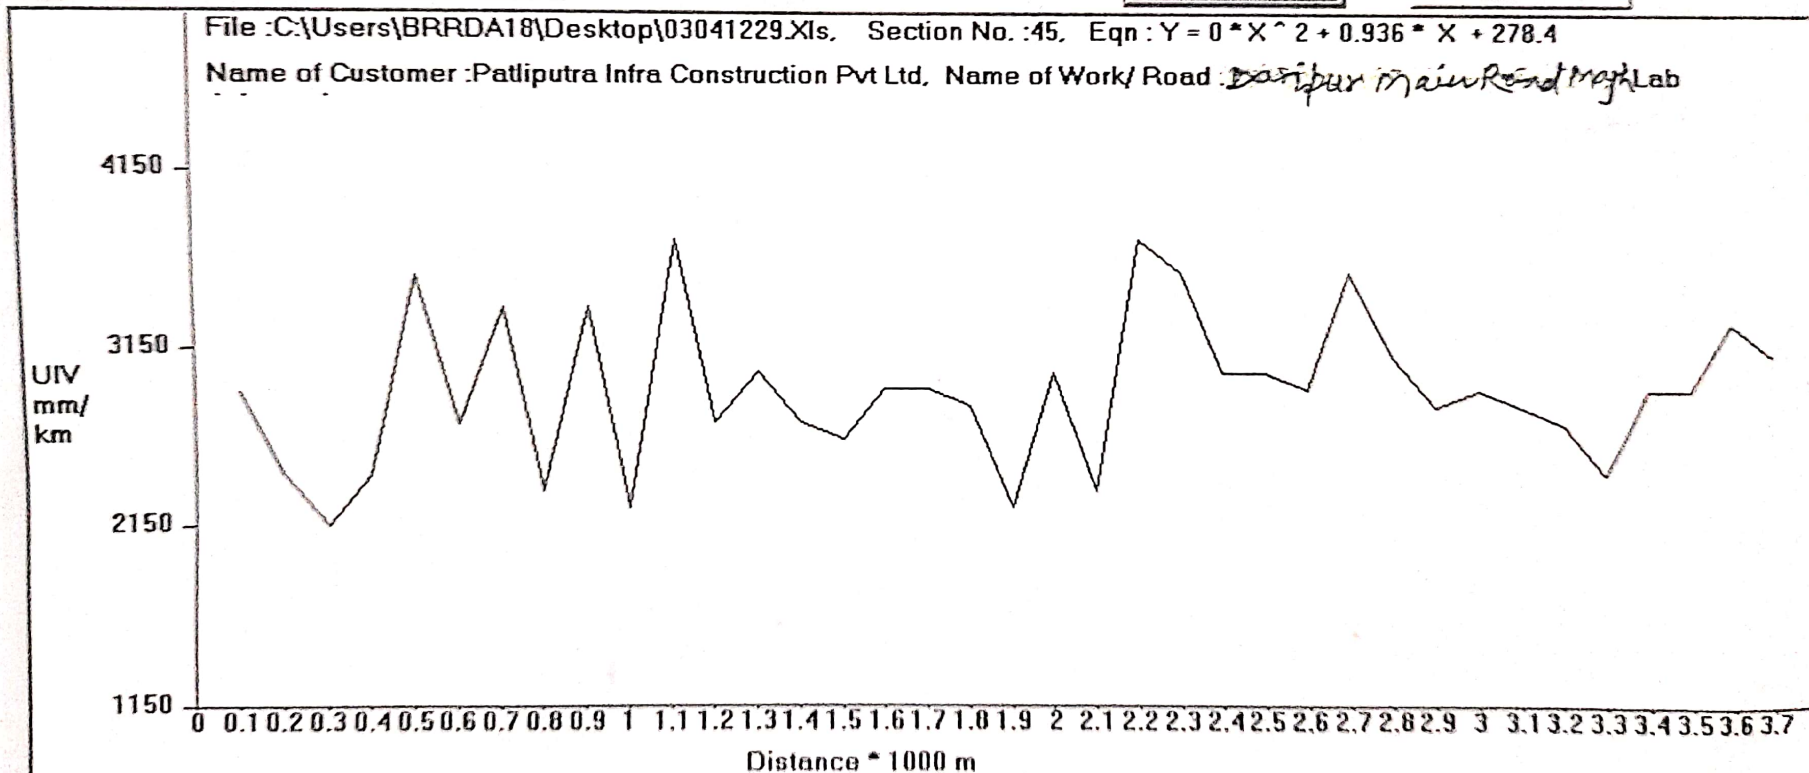
End Location : Equation : $Y = 0 * X^2 + 0.936 * X + 278.4$

Print

Generate Report and Graph

Redraw Graph

Map View



16/03/2023
DS

16/3/23
CC

