

पत्रांक 446(3130) /

शेखपुरा, दिनांक 17/03/2023 /

प्रेषक:-

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, शेखपुरा।

सेवा में,

नोडल पदाधिकारी,
3054 (M.R.) कोषांग,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:-

शीर्ष 3054 नई अनुरक्षण नीति-2018 अन्तर्गत Initial Rectification and Surface Renewal कराये गए कार्य हेतु अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक कहना है कि विहित प्रपत्र में संलग्न विवरणी के अनुसार शीर्ष 3054 नई अनुरक्षण नीति-2018 अन्तर्गत Initial Rectification and Surface Renewal कराये गए कार्य हेतु राशि रूपये 67,43,211/- (सड़सठ लाख तेतालीस हजार दो सौ ग्यारह रूपये) मात्र राशि की आवश्यकता है।

अतः कार्यहित में अनुरोध है कि उक्त अधियाचित राशि रूपये 67,43,211/- (सड़सठ लाख तेतालीस हजार दो सौ ग्यारह रूपये) मात्र उपलब्ध कराने की कृपा की जाय। ताकि कराये जा रहे कार्यों का विपत्र भुगतान किया जा सके।

अनु०:-1. अधियाचना प्रपत्र।

2. IRI Value Report

3. Map

4. प्रमाण पत्र।

विश्वासभाजन

कार्यपालक अभियन्ता
ग्रा०का०वि०, कार्य प्रमण्डल,
शेखपुरा
17/3/23
17/3/23


प्रमाण-पत्र


पथ का नाम :- T01 बेलछी मोड़ से बेलछी पथ।

लम्बाई :-2.000 कि०मी०

बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत कराये गये कार्य के विरुद्ध उक्त पथ के अधियाचना हेतु विभागीय पत्रांक--5047 दिनांक 23.12.2021 के अनुपालन में निम्नलिखित शर्त को प्रमाणित किया जाता है :-

1. यह कि अधियाचित पथ के मापी पुस्त पर कनीय अभियन्ता एवं सहायक अभियन्ता द्वारा दर्ज किया गया है कि कार्य गुणवत्ता पूर्ण कराया गया है एवं विशिष्टियों के अनुरूप है।
2. यह कि अधियाचित पथ में कराये गये कार्यों के सभी अवयवों के अवयववार 100प्रतिशत कार्य का दर्ज मापी को संबंधित कनीय अभियन्ता द्वारा एवं 50प्रतिशत कार्य का दर्ज मापी संबंधित सहायक अभियन्ता एवं 10प्रतिशत कार्य का दर्ज मापी का सत्यापन कार्यपालक अभियन्ता द्वारा किया जा चुका है।


कनीय अभियन्ता
ग्रा०का०वि०, कार्य प्रशाखा
अरियरी


सहायक अभियन्ता
ग्रा०का०वि०, का०अ०प्रमं०
अरियरी


कार्यपालक अभियन्ता
ग्रा०का०वि०, कार्य प्रमं०
शेखपुरा

RWD Works Division, Sheikhpura

Requisition Format for Scheme Head- MR (3054) Under Bihar Rural Road " New Maintenance Policy 2018" (Initial Rectification and Surface Renewal)

Name of Division:-Sheikhpura

S. N.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (A.A) Letter No. & Date	Administrative Approval (A.A)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IR1 in MM/KM	Thickness of Bitumen Layer (in MM)	Value of Bitumen Content (in %)	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (K.M)	Amount (in Lakh)	Initial Rectification Surface Renewal (in Lakh)	5 Year Routine Maintenance										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/22-23, Sheikhpura/04	T01-Belchhi_More-Belchhi	NE:A22000973	Letter no.-2011, dt:02.05.2022	2.000	103.700	67.43211	20.20499	18(MBD)/22-23 16.07.22	15.04.2023	---	2928.75	25	5.020	0	0	67.43211	
																	67.43211	

D.A.O.
RWD Works Division,
Sheikhpura

Executive Engineer
RWD Works Division,
Sheikhpura

Name of Road :- T01-Belchhi More Belchhi.

Section no.-23

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
17/3/23	10: 2: 11	23	0.1	300	0	3000	3031	G	25.104172	85.853439	Normal
17/3/23	10: 2: 43	23	0.1	290	10.1	2900	2929	G	25.104145	85.852688	Speed Breaker
17/3/23	10: 3: 19	23	0.1	270	10.1	2700	2724	G	25.104201	85.851787	Normal
17/3/23	10: 3: 43	23	0.1	280	10.1	2800	2827	G	25.104247	85.850854	Curve
17/3/23	10: 4: 1	23	0.1	290	10.1	2900	2929	G	25.104342	85.849948	Normal
17/3/23	10: 4: 29	23	0.1	310	10.1	3100	3133	G	25.104528	85.849031	Normal
17/3/23	10: 4: 47	23	0.1	300	10.1	3000	3031	G	25.104586	85.848043	Normal
17/3/23	10: 5: 4	23	0.1	280	10.1	2800	2827	G	25.104637	85.847157	Normal
17/3/23	10: 5: 33	23	0.1	320	10.1	3200	3235	G	25.104689	85.846154	Normal
17/3/23	10: 5: 56	23	0.1	300	10.1	3000	3031	G	25.104068	85.845519	Normal
17/3/23	10: 6: 3	23	0.1	310	10.1	3100	3133	G	25.104149	85.844642	Normal
17/3/23	10: 6: 27	23	0.1	260	10.1	2600	2622	G	25.104199	85.84375	Normal
17/3/23	10: 7: 2	23	0.1	280	10.1	2800	2827	G	25.104231	85.842896	Normal
17/3/23	10: 7: 8	23	0.1	270	10.1	2700	2724	G	25.1043	85.842037	Curve
17/3/23	10: 7: 42	23	0.1	260	10.1	2600	2622	G	25.103863	85.841311	Curve
17/3/23	10: 8: 3	23	0.1	320	10.1	3200	3235	G	25.10402	85.840242	Normal
17/3/23	10: 8: 34	23	0.1	310	10.1	3100	3133	G	25.103522	85.839891	Normal
17/3/23	10: 8: 58	23	0.1	280	10.1	2800	2827	G	25.10345	85.841327	Normal
17/3/23	10: 9: 35	23	0.1	300	10.1	3000	3031	G	25.102819	85.84119	Normal
17/3/23	10: 10: 2	23	0.1	270	10.1	2700	2724	G	25.102115	85.841033	Normal

Total = 2.00 Km

Avg. 2928.75


 Executive Engineer
 R.W.D. (W) Division,
 Sheikhpura
 17.3.23
 A/E



Steco Analyzer

Name of Customer : Sanjay Kumar Technocrate Pvt
Name of Work/ Road : T01 - Belchhi More Belchhi
Lab Job number : 23
Date : 17 03 2023
Section No. : 23

Print Generate Report and Graph

Test Date : 17 03 2023 Road Name : T01 - Belchhi More Belchhi
Machine No : 399 Road Type : (R) RURAL ROAD
Start S No : Side :
Start E No : Interval
Weather :
Start Location :
End Location :
Equation : $Y = 0 * X^2 + 1.021 * X - 31.77$

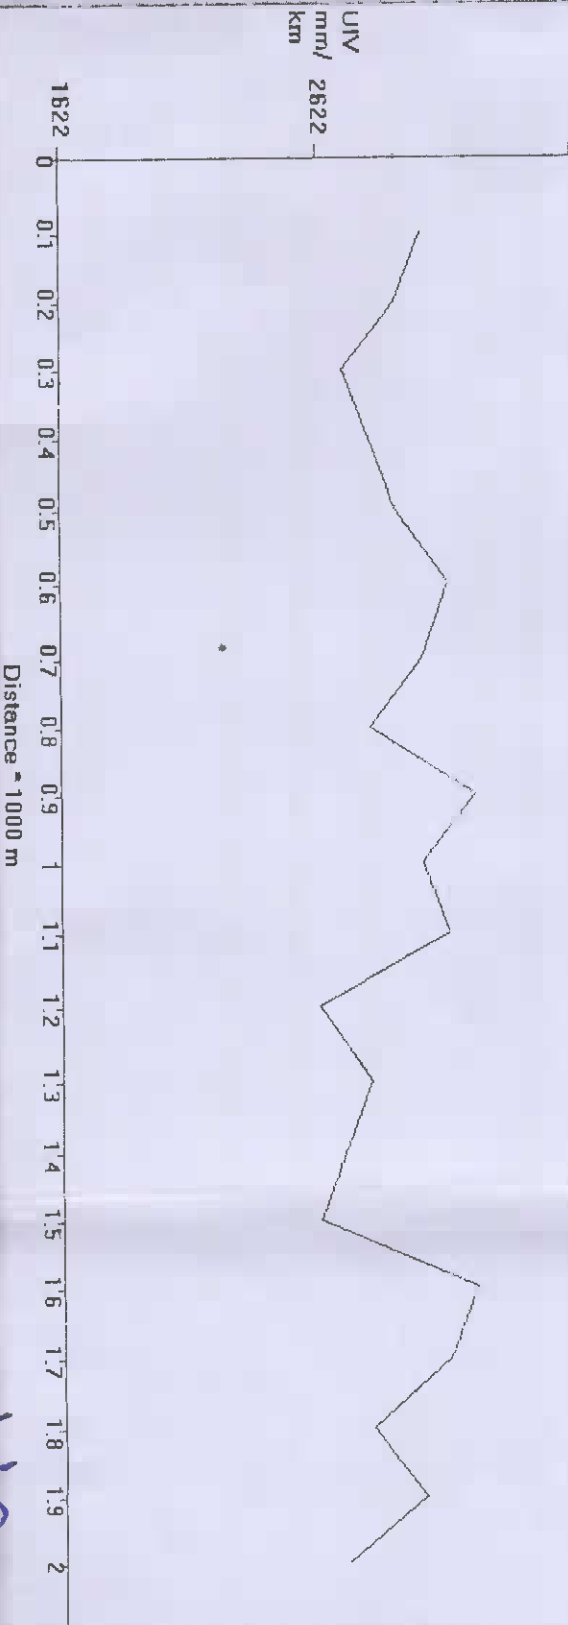
UIV Range : 1622 To 4000 mm/km
Dist Range : 0 To 2.1 0.1 * 1000 m

Redraw Graph

Map View

File : C:\Users\USER\Desktop\T01 Belchhi More Belchhi\17031010.Xls. Section No. 23. Eqn : $Y = 0 * X^2 + 1.021$

Name of Customer : Sanjay Kumar Technocrate Pvt. Ltd. Name of Work/ Road : T01 - Belchhi More Belchhi. Lab Job



Sanjay Kumar
17.03.23

Sanjay Kumar
17.03.23
AE

Executive Engineer
Rural Works Department
Works Division, Sheikhpura
