

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, चकिया, (पूर्वी चम्पारण)।

पत्रांक: ५३३/अनु०/ चकिया, दिनांक: १७/०३/२०२३

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, चकिया।

सेवामे,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- विभाग के नई निति रख-रखाव २०१८ M.R (३०५४) योजना के अन्तर्गत
निर्माणाधीन कार्य के लिए निधि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में विभाग के नई निति रख-रखाव २०१८ M.R (३०५४) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए पथवार मांगी जाने वाली आवंटन की सूची पत्र के साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:- १. आवंटन की सूची।

२. Bump Test Integrator Machine

ज्ञापांक-५३३ दिनांक-१७-०३-२०२३

प्रतिलिपि-नोडल पदाधिकारी (३०५४), ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

अनु०:- १. आवंटन की सूची

२. Bump Test Integrator Machine

विश्वासभाजन,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Chakia.**

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Chakia

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval ((AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)			Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In mm/km)	Thickness of Bitumen layer (In mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In lakh)	up-to- date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (In lakh)	5 Years Routine Maintenance (In Lakh)	Agreement No. & Date									
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/E/CHA/22/0005	Bradharpur Pach Road - Mithanpura	31708202067	Letter No.1585 Date-30.03.2022	2.850	124.26000	88.74911	25.18046	23 MBD/2022-23 Date-31.12.2022	30.09.2023	In Progress	2615	25	05.00	0.00000	0.00000	88.66500	Work in Progress
					2.850	124.26000	88.74911	25.18046									88.66500	

- 1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
काँस्ट्रक्शन, चकिया
11/09/22



Name of work : Bahadurpur Chowk to PMGSY Road Milhanpura 140 Package Tak Name of customer : DHIRENDRA CONSTRUCTION PVT LTD. (R)Rural Road Good Average Poor < 4000 4001 - 5000 > 5000															
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	Ut(mm/Km)	Corrected Ut (mm/Km)	(R)	Status	Latitude	Direction	Longitude	Direction1	Remarks
15/03/23	10 23 03	53	0	0	0.0 cm	10.9 Km/Hr	0.0 mm/Km	205	0.37	Good	26.3783917	N	84.7890940	E	Normal
15/03/23	10 25 06	53	100	100	28.0 cm	14.0 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.3285352	N	85.1059122	E	Normal
15/03/23	10 25 30	53	100	200	25.0 cm	14.7 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.3282360	N	85.1040049	E	Normal
15/03/23	10 25 51	53	100	300	27.0 cm	16.8 Km/Hr	2700.0 mm/Km	2708	3.68	Good	26.3290338	N	85.1031122	E	Normal
15/03/23	10 26 11	53	100	400	29.0 cm	18.1 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3287535	N	85.1023758	E	Normal
15/03/23	10 26 29	53	100	500	26.0 cm	20.4 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.3291101	N	85.1013346	E	Normal
15/03/23	10 26 44	53	100	600	28.0 cm	24.4 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.3297549	N	85.1010065	E	Normal
15/03/23	10 27 03	53	100	700	29.0 cm	18.7 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3307104	N	85.1013458	E	Normal
15/03/23	10 27 20	53	100	800	26.0 cm	21.3 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.3307219	N	85.1004877	E	Normal
15/03/23	10 27 42	53	100	900	28.0 cm	16.8 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.3308363	N	85.0994501	E	Normal
15/03/23	10 27 58	53	100	1000	27.0 cm	21.8 Km/Hr	2700.0 mm/Km	2708	3.68	Good	26.3315935	N	85.0998239	E	Normal
15/03/23	10 28 11	53	100	1100	29.0 cm	26.4 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3324232	N	85.1002970	E	Normal
15/03/23	10 28 28	53	100	1200	26.0 cm	21.8 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.3332243	N	85.1008768	E	Normal
15/03/23	10 28 43	53	100	1300	25.0 cm	23.8 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.3339281	N	85.1014348	E	Normal
15/03/23	10 28 59	53	100	1400	29.0 cm	22.2 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3346205	N	85.1021662	E	Normal
15/03/23	10 29 19	53	100	1500	30.0 cm	18.0 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.3353071	N	85.1027384	E	Normal
15/03/23	10 29 37	53	100	1600	25.0 cm	20.0 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.3360109	N	85.1033564	E	Normal
15/03/23	10 29 51	53	100	1700	28.0 cm	26.7 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.3368139	N	85.1039743	E	Normal
15/03/23	10 30 05	53	100	1800	28.0 cm	25.4 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.3376398	N	85.1035852	E	Normal
15/03/23	10 30 20	53	100	1900	27.0 cm	24.4 Km/Hr	2700.0 mm/Km	2708	3.68	Good	26.3382864	N	85.1039362	E	Normal
15/03/23	10 30 35	53	100	2000	29.0 cm	23.9 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3386164	N	85.1048822	E	Normal

15/3/23
 JE

15/03/2023
 DRE

Name of work : Bahadurpur Chowk to PMGSY Road Mithanpura 140 Package
Tak

Name of customer : DHIRENDRA CONSTRUCTION PVT LTD.

(R) Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000


15/03/23	10:30:53	53	100	2100	21.0 cm	19.8 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.3388281	N	85.1055155	E	Normal
15/03/23	10:31:14	53	100	2200	21.0 cm	17.4 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.3388281	N	85.1055155	E	Normal
15/03/23	10:31:29	53	100	2300	21.0 cm	22.8 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.3388281	N	85.1055155	E	Normal
15/03/23	10:31:44	53	100	2400	29.0 cm	23.6 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3388281	N	85.1055155	E	Normal
15/03/23	10:32:03	53	100	2500	28.0 cm	19.8 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.3388281	N	85.1055155	E	Normal
15/03/23	10:32:20	53	100	2600	21.0 cm	21.3 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.3388281	N	85.1055155	E	Normal
15/03/23	10:32:41	53	100	2700	26.0 cm	17.3 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.3388281	N	85.1055155	E	Normal
15/03/23	10:32:58	53	100	2800	30.0 cm	21.1 Km/Hr	3000.0 mm/Km	2998	4.01	Good	26.3388281	N	85.1055155	E	Normal
15/03/23	10:33:21	53	100	2900	24.0 cm	15.9 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.3388281	N	85.1055155	E	Normal

Avg IRI-2615

Lat/Long
15/3/23
JE

Signature
15/03/2023
DE

Name of Customer: DIHIRENDRA CONSTRUCTION PVT LTD., Machine no: 19191, Road: Bahadurpur Chowk to PMGSY Road Mithanpura 140 Package Tak, Date: 15-03-23, Section No: 53, Equation: $Y = 0.927 X + 204.8$

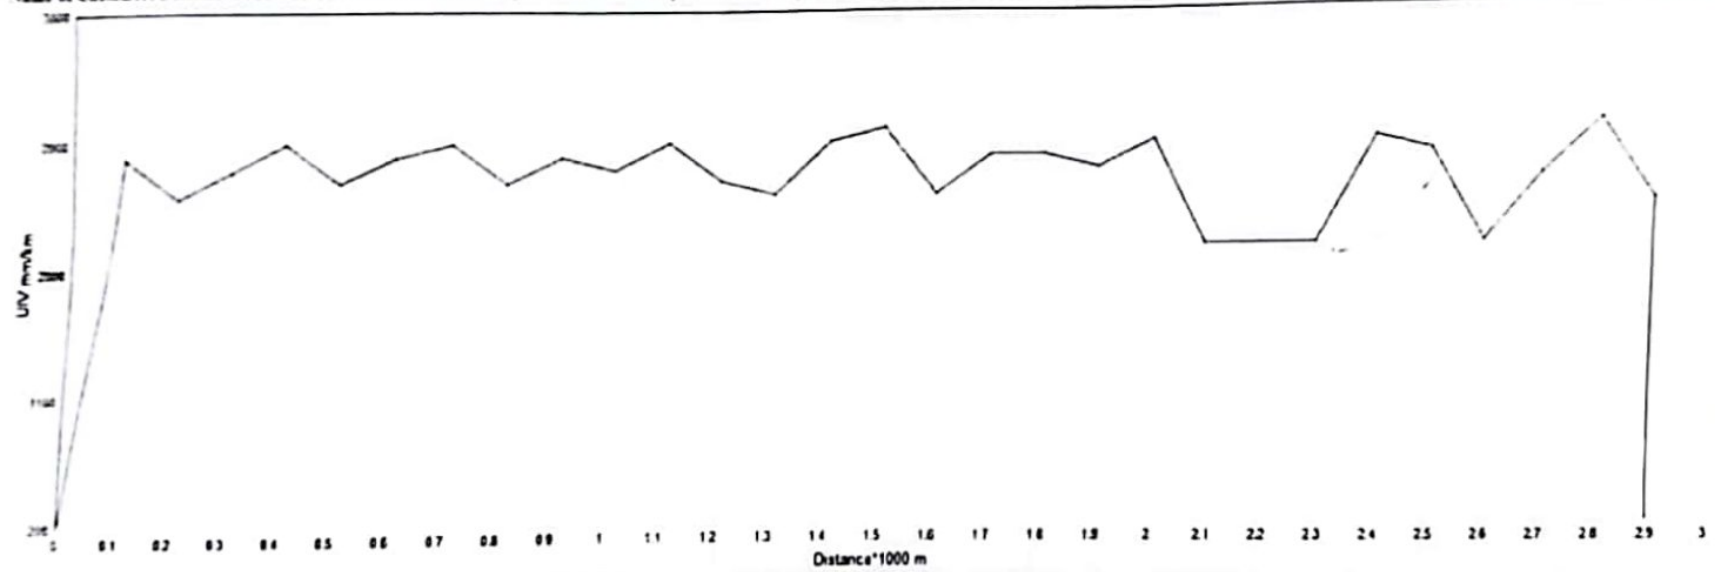

LCMRB
15/3/23
JE

DIHIRENDRA
15/03/2023
AE
