

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, चकिया, (पूर्वी चम्पारण)।

पत्रांक: ५५१/अनु० / चकिया, दिनांक: २० / ०३ / २०२३

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, चकिया।

सेवामे,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए निधि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए पथवार मांगी जाने वाली आवंटन की सूची पत्र के साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय।

- अनु०:- 1. आवंटन की सूची।
2. Bump Test Integrator Machine

विश्वासभाजन,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

ज्ञापांक-५५१ दिनांक-२०-०३-२०२३

प्रतिलिपि-नोडल पदाधिकारी (3054), ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

- अनु०:- 1. आवंटन की सूची
2. Bump Test Integrator Machine

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Chakia.**

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Chakia


Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA)	Agreement Amount (In Lakh)				Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks	
					Length (In Km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/EA/CHA/22/0005	L059-L028 Sahshi Jagiraha to Imaliya (VR19)	31708402027	Latter No.1686 Date-30.03.2022	3.010	136.60000	101.10736	22.89785	23 MBD/2022-23 Date-31.12.2022	30.09.2023	In Progress	2478	25	05.00	0.00000	0.00000	101.05500	Work in Progress
					3.010	136.60000	101.10736	22.89785							0.00000	0.00000	101.05500	

1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.

2 Up-to-date Physical Progress has been uploaded in MIS.

Executive Engineer,
Rural Works Department,
Works Division, Chakia.
27/03/23

Name of Customer: DHIRENDRA CONSTRUCTION PVT LTD. , Machine no: 19191 , Road: L059-L028 Sahshi Jagiraha to Imaliya (VR19) , Date: 19-03-23 , Section No: 54 , Equation: $Y = 0.927 X + 204.8$

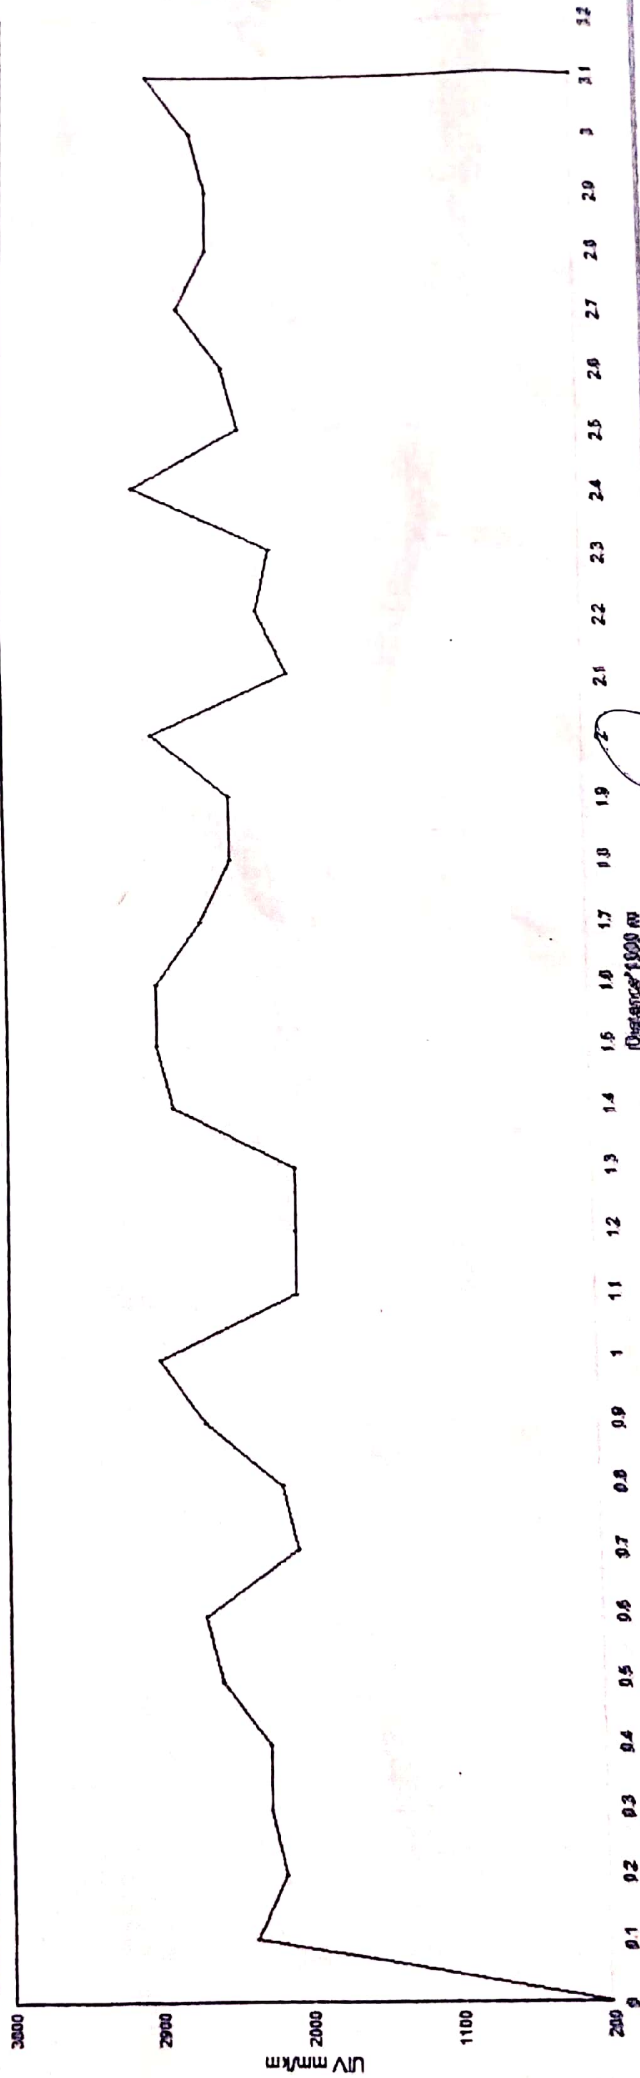

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, चकरीया

20/03/23
J.E

Name of work : L059-028 Sahshi Jagiraha to Imaliya (VR19)

Name of customer : DHIRENDRA CONSTRUCTION PVT LTD.

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	Wt(mm/Km)	Corrected Wt (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
19/03/23	10:37:21	54	0	0				205	0.37	Good					
19/03/23	10:38:06	54	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	205	0.37	Good	26.5535727	N	84.9210291	E	Normal
19/03/23	10:38:31	54	100	100	23.0 cm	16.7 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.4739675	N	84.9355784	E	Normal
19/03/23	10:38:52	54	100	200	21.0 cm	14.2 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.4733648	N	84.9363261	E	Normal
19/03/23	10:38:13	54	100	300	22.0 cm	17.1 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.4728231	N	84.9368983	E	Normal
19/03/23	10:38:44	54	100	400	22.0 cm	17.1 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.4723597	N	84.9378893	E	Normal
19/03/23	10:38:44	54	100	500	25.0 cm	12.1 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.4716768	N	84.9383784	E	Normal
19/03/23	10:40:03	54	100	600	26.0 cm	18.9 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.4707212	N	84.9382334	E	Normal
19/03/23	10:40:26	54	100	700	20.0 cm	13.7 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4698992	N	84.9380198	E	Normal
19/03/23	10:40:37	54	100	800	21.0 cm	32.0 Km/Hr	2100.0 mm/Km	2152	2.89	Good	26.4690561	N	84.9376994	E	Normal
19/03/23	10:40:46	54	100	900	26.0 cm	31.5 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.4681578	N	84.9374171	E	Normal
19/03/23	10:40:59	54	100	1000	29.0 cm	32.4 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.4674044	N	84.9371577	E	Normal
19/03/23	10:41:08	54	100	1100	20.0 cm	40.3 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4669447	N	84.9371577	E	Normal
19/03/23	10:41:16	54	100	1200	20.0 cm	43.2 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4653406	N	84.9368144	E	Normal
19/03/23	10:41:26	54	100	1300	20.0 cm	37.8 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4644461	N	84.9366084	E	Normal
19/03/23	10:41:43	54	100	1400	28.0 cm	21.3 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.4636412	N	84.9364939	E	Normal
19/03/23	10:41:54	54	100	1500	29.0 cm	30.9 Km/Hr	2000.0 mm/Km	2893	3.9	Good	26.4627695	N	84.9363642	E	Normal
19/03/23	10:42:07	54	100	1600	29.0 cm	27.3 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.4617643	N	84.9363642	E	Normal
19/03/23	10:42:19	54	100	1700	26.0 cm	30.0 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.4612150	N	84.9371577	E	Normal
19/03/23	10:42:30	54	100	1800	24.0 cm	31.8 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.4606026	N	84.9370814	E	Normal
19/03/23	10:42:41	54	100	1900	24.6 cm	34.9 Km/Hr	2400.0 mm/Km	2439	3.34	Good	26.4594957	N	84.9368847	E	Normal

20/03/23
S.E.
20/03/23
S.E.



Name of work : L059-L028 Sahshi Jagiraha to Imaliya (VR19)

Name of customer : DHIRENDRA CONSTRUCTION PVT LTD.

(R)Rural Road

Good		Average					Poor				
< 4000		4001 - 5000					> 5000				
19/03/23	10.42:51	54	100	2000	29.0 cm	35.6 Km/Hr	2800.0 mm/Km	2883	3.9	Good	26.4589281
19/03/23	10.43:00	54	100	2100	20.0 cm	38.1 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4579383
19/03/23	10.43:10	54	100	2200	22.0 cm	36.0 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.4571104
19/03/23	10.43:50	54	100	2300	21.0 cm	29.4 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.4560480
19/03/23	10.44:17	54	100	2400	30.0 cm	12.8 Km/Hr	3000.0 mm/Km	2988	4.01	Good	26.4556208
19/03/23	10.44:33	54	100	2500	23.0 cm	22.0 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.4559908
19/03/23	10.44:44	54	100	2600	24.0 cm	31.2 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.4567156
19/03/23	10.44:55	54	100	2700	27.0 cm	34.9 Km/Hr	2700.0 mm/Km	2708	3.68	Good	26.4575129
19/03/23	10.45:05	54	100	2800	25.0 cm	34.2 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.4581594
19/03/23	10.45:20	54	100	2900	25.0 cm	25.4 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.4592009
19/03/23	10.46:16	54	100	3000	26.0 cm	16.4 Km/Hr	2600.0 mm/Km	2815	3.58	Good	26.4599605
19/03/23	10.47:54	54	100	3100	29.0 cm	13.6 Km/Hr	2900.0 mm/Km	2853	3.9	Good	26.4586033
			0	3100				2205	0.37	Good	

Avg IRI-2478

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, चकीया

22/3/23
T.E
