

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, चकिया, (पूर्वी चम्पारण)।

पत्रांक: 524/अनु0/चकिया, दिनांक: 24/03/2023

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, चकिया।

सेवामे,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय— विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए निधि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए पथवार मांगी जाने वाली आवंटन की सूची पत्र के साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय।

अनु0:— 1. आवंटन की सूची।

2. Bump Test Integrator Machine

विश्वासभाजन,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

ज्ञापांक— 524 दिनांक— 24-03-2023

प्रतिलिपि—नोडल पदाधिकारी (3054), ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

अनु0:— 1. आवंटन की सूची

2. Bump Test Integrator Machine

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Chakia.**

Regulisation Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Chakia

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Latter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (In Km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/EA/CHA/22/0011	Harthapur Ram Babu Ke Ghar Se Aikhwan Hote Hue Ayodhya Bhagal Ke Khet Tak	31708412001	Latter No.105 Date-03.06.2022	3.588	193.26	144.03342	34.61171	02MBD/2022-23 Date-06.09.2022	05.06.2023	In Progress	2564	25	05.00	0.00000	0.00000	144.02000	Work in Progress
					3.588	193.26	144.03342	34.61171									144.02000	


- 1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.



Executive Engineer,
Rural Works Department,
Works Division, Chakia.

24/05/23

ie of Customer: Harshvardhan Construction , Machine no: 19191 , Road: Haribaiapur Ram Babu Ke Ghar Se Alkhwani Hote Hue Ayodhya Bhagat Ke Khet Tak , Date: 23-03-23 , Section No: 57 , Equation: $Y = 0.927 X + 200$

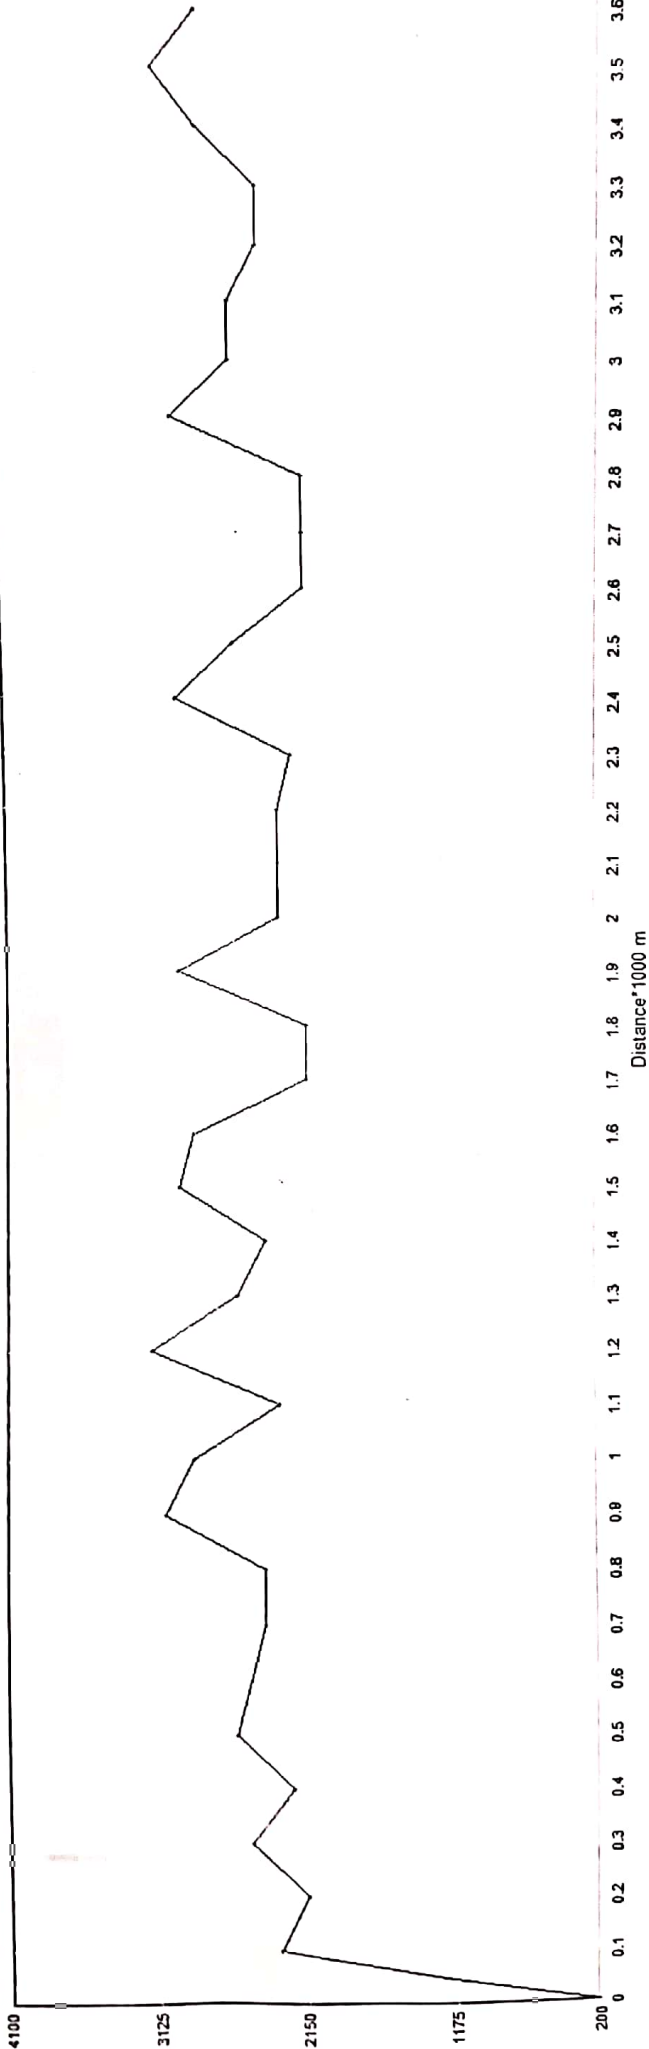

कार्यप्रसक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, चेकीया

24/03/23
H

24/03/23
H

Name of work : Harihaipur Ram Babu Ke Ghar Se Alkhwani Hote Hue Ayodhya
Bhagat Ke Khet Tak

Name of customer : Harshvardhan Construction

(R)Rural Road

Good				Average				Poor							
< 4000				4001 - 5000				> 5000							
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
23/03/23	10:40:10	57	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	205	0.37	Good	26.5535727	N	84.9210291	E	Normal
23/03/23	10:41:30	57	100	100	23.0 cm	13.8 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.4739675	N	84.9355784	E	Normal
23/03/23	10:41:51	57	100	200	21.0 cm	17.0 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.4733648	N	84.9363261	E	Normal
23/03/23	10:42:05	57	100	300	25.0 cm	25.4 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.4728231	N	84.9368983	E	Normal
23/03/23	10:42:19	57	100	400	22.0 cm	26.7 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.4723597	N	84.9379893	E	Normal
23/03/23	10:42:35	57	100	500	26.0 cm	22.5 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.4716768	N	84.9383784	E	Normal
23/03/23	10:42:55	57	100	600	25.0 cm	18.2 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.4707212	N	84.9382334	E	Normal
23/03/23	10:43:16	57	100	700	24.0 cm	16.6 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.4698992	N	84.9380198	E	Normal
23/03/23	10:43:55	57	100	800	24.0 cm	19.6 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.4690561	N	84.9376994	E	Normal
23/03/23	10:44:15	57	100	900	31.0 cm	17.4 Km/Hr	3100.0 mm/Km	3079	4.12	Good	26.4681578	N	84.9374171	E	Normal
23/03/23	10:44:40	57	100	1000	28.0 cm	15.0 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.4674044	N	84.9371577	E	Normal
23/03/23	10:45:02	57	100	1100	23.0 cm	15.8 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.4669447	N	84.9371577	E	Normal
23/03/23	10:45:33	57	100	1200	32.0 cm	11.5 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.4653406	N	84.9368144	E	Normal
23/03/23	10:45:56	57	100	1300	26.0 cm	16.0 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.4644461	N	84.9366084	E	Normal
23/03/23	10:46:17	57	100	1400	24.0 cm	17.2 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.4636412	N	84.9364939	E	Normal
23/03/23	10:46:40	57	100	1500	30.0 cm	15.6 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.4627695	N	84.9363642	E	Normal
23/03/23	10:47:09	57	100	1600	29.0 cm	12.6 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.4617643	N	84.9363642	E	Normal
23/03/23	10:47:33	57	100	1700	21.0 cm	14.8 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.4612150	N	84.9371577	E	Normal
23/03/23	10:47:56	57	100	1800	21.0 cm	15.5 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.4605036	N	84.9370814	E	Normal
23/03/23	10:48:18	57	100	1900	30.0 cm	16.3 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.4595957	N	84.9366847	E	Normal
23/03/23	10:48:33	57	100	2000	23.0 cm	22.9 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.4589281	N	84.9361964	E	Normal

24/03/23

24/3/23



