

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग,

कार्य प्रमंडल- मंडौल-बखरी।

Email id-xen.rwd.manjhaul@gmail.com

पत्रांक.....535 (अनु०)

मंडौल-बखरी, दिनांक...27.03.23

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल मंडौल-बखरी।

सेवा में,

नोडल पदाधिकारी,
3054 कोषांग,
ग्रामीण कार्य विभाग,
बिहार, पटना।


विषय:- शीर्ष नई अनुरक्षण नीति 2018 के अंतर्गत स्वीकृत योजनाओं में किये जा रहे कार्यों के विरुद्ध अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि ग्रामीण कार्य विभाग, कार्य प्रमंडल मंडौल-बखरी अंतर्गत कार्यान्वित कराये जा रहे नई अनुरक्षण नीति 2018 के अंतर्गत GARHPURA SHURI - SAMASTIPUR MAALPUR पथ की अधियाचना (विहित प्रपत्र) में अंकित राशि रुपये 91,11,578.00 (इक्यानवे लाख न्यारह हजार पाँच सौ अठ्ठतर) मात्र विमुक्ति हेतु भेजी जा रही है।

अनु०:-विहित प्रपत्र।

विश्वासभाजन



27/3/23
कार्यपालक अभियंता,

ग्रामीण कार्य विभाग,

कार्य प्रमंडल मंडौल-बखरी

FORM 19-A

Form of Utilisation Certificate upto 27th March 2023
MR-3054 (New Maintenance Policy 2018)

PIU : E.E. RWD, (W) Division, Manjhaur-Bakhari

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (In Rs. Lacs)	Amount Received (In Rs. Lacs)	Particulars
1	Construction of Rural roads under MR-3054 (New Maintenance Policy 2018)	Vide Letter No. 17 dt 26.02.2021	29.30900	Certified that out of Rs 2904.26666 Lac received in favour of Executive Engineer, RWD, Works Division, Manjhaur-Bakhari; a sum of Rs 2904.26646 Lac has been utilized for the purpose of MR-3054 (New Maintenance Policy 2018) Schemes as given in the margin for which it was sanctioned and that the balance Fund Rs 0.00020 Lac
		Vide Letter No. 20 dt 19.03.2021	29.30900	
		Vide Letter No. 52(Encl) dt 24.08.2021	44.80488	
		Vide Letter No. 58(Encl) dt 27.10.2021	423.61826	
		Vide Letter No. 60(Encl) dt 09.11.2021	66.75987	
		Vide Letter No. 02(Encl) dt 03.01.2022	227.65333	
		Vide Letter No. 05(Encl) dt 25.01.2022	381.46495	
		Vide Letter No. 13 (Encl) dt 28.02.2022	110.77364	
		Vide Letter No. 31 (Encl) dt 24.03.2022	102.40516	
		Vide Letter No. 43 (Encl) dt 08.04.2022	-0.01973	
		Vide Letter No.48 (Encl) dt 13.04.2022	32.35712	
		Vide Letter No.49 (Encl) dt 27.04.2022	286.71988	
		Vide Letter No.01 (Encl) dt 20.05.2022	108.53999	
		Vide Letter No.03 (Encl) dt 08.06.2022	34.66451	
		Vide Letter No.22 (Encl) dt 08.08.2022	292.71986	
		Vide Letter No.47 (Encl) dt 24.11.2022	23.49791	
		Vide Letter No.09 (Encl) dt 23.01.2023	41.98250	
		Vide Letter No.24 (Encl) dt 23.02.2023	168.16413	
		Vide Letter No.35 (Encl) dt 14.03.2023	441.06615	
		Vide Letter No.49 (Encl) dt 23.03.2023	58.57625	
	Total		2904.26666	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other / codal formalities have been observed.

3 Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD Works.

[Signature]
27/03/23
D.O. II

RWD, Works Division,
Manjhaur-Bakhari

[Signature]
27/3/23
Executive Engineer
RWD, Works Division,
Manjhaur-Bakhari

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : **Manjhaul-Bakhri**

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (in lac)	Remarks
					Length (in Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (in lac)										
1	MR-N/22-23 Manjhaul Bakhri/05	GAREHPURA SHURI - SAMASTIPUR MAALPUR	32010502022	3991/dt 15.12.22	3.300	143.25000	91.42746	30.30155	02/ABD/MR- 3054(NMP 2018)/22-23 Dt-13-12-2022	9/12/2023	Ongoing	Attached	25	5	0.00000	0.00000	91.11578	Physically Completed

(Rs. Ninety One Lac Eleven Thousand Five Hundred Seventy Eight Only)

91.11578

[Signature]
28/3/23
Executive Engineer

412 PWD Works Division Manjhaul-Bakhri.

28/3/23

1st estimate bill.

1.

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
N/W:-	Construction of Road from				
	Gastpura Sabhauri to Sarnadiya				
	Madhpura				
Agency:-	Smit construction engineering				
	Pvt. Ltd.				
Agd No:-	22/10/2022-23 (New - print-9)				
	2018/2022-23				
Agd Rate:-	11.20% as per B.O.D.				
D.O.S:-	13-12-2022 as per Agd				
D.O.C:-	12-09-2023 as per Agd				
Date of entry:-	25-03-22				
	Abstract of cost				
	(7) clearing & grubbing				

	the Road land - at,				
0.660 Hect	at videy (1) m/s				
	@ Rs 62032.43/Hect - Rs 409412				
(212)	Construction of Sub				
	grade & earthwork				
	shoulders - - - at,				
1908.0 m/s	at videy (14) m/s				
	@ Rs 254.40/m - Rs 485395				
(213)	juni-Construction of				
	Gravel with road grade				
	Material - - - at,				
(23.715 m/s)	at videy (2) m/s				
Unit					
23.63 m/s	@ Rs 3377.65/m - Rs 798142				

0.11 m/s

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
			B.f	R	88446892
45.0m ³ clay (16) Tm					
			R 3897.08/m ²	R	1253692
				R	90200582
Add 12% GST (+)				R	10829072
Add 1% LC (+)				R	902012
Add S. fee (+)				R	681202
				R	102607862
16.5 11.20.1.2 per 1000				R	11492082
				R	91,11,5782
C&P					
27/3/23					

C/S
 27/3/23
 Executive Engineer
 RWD Works Division
 Manjhaul Bakhari


Name of Customer: Soft Construction Engineering Private Limited
 Name of Work/Road: GARHPURA SHURI - SAMASTIPUR MAALPUR
 Lab Job Number: 02
 Date: 25 March 2023
 Section No: 02

Test Date: 27 March 2023
 Machine no: 19204
 Start S. No.: 0.000
 Start E. No.: 3.300
 Weather: _____
 Start Location: _____
 End Location: _____

Road Name: GARHPURA SHURI - SAMASTIPUR MAALPUR
 Road Type: (B) BITUMINOUS CONCRETE
 Side: _____
 UIV Range: _____
 Dist Range: 0.000 To 3.300 Internal: _____
 Equations: $Y = 0.929X + 237.9$ mm/km
 To 1000 m

Graph: Graph Connected UIV v/s Distance Connected IRI v/s distance Data

e of Customer: Soft Construction Engineering Private Limited, Machine no: 19204, Road: GARHPURA SHURI - SAMASTIPUR MAALPUR, Date: 25-03-23, Section No: 02, Equation: $Y = 0.929X +$

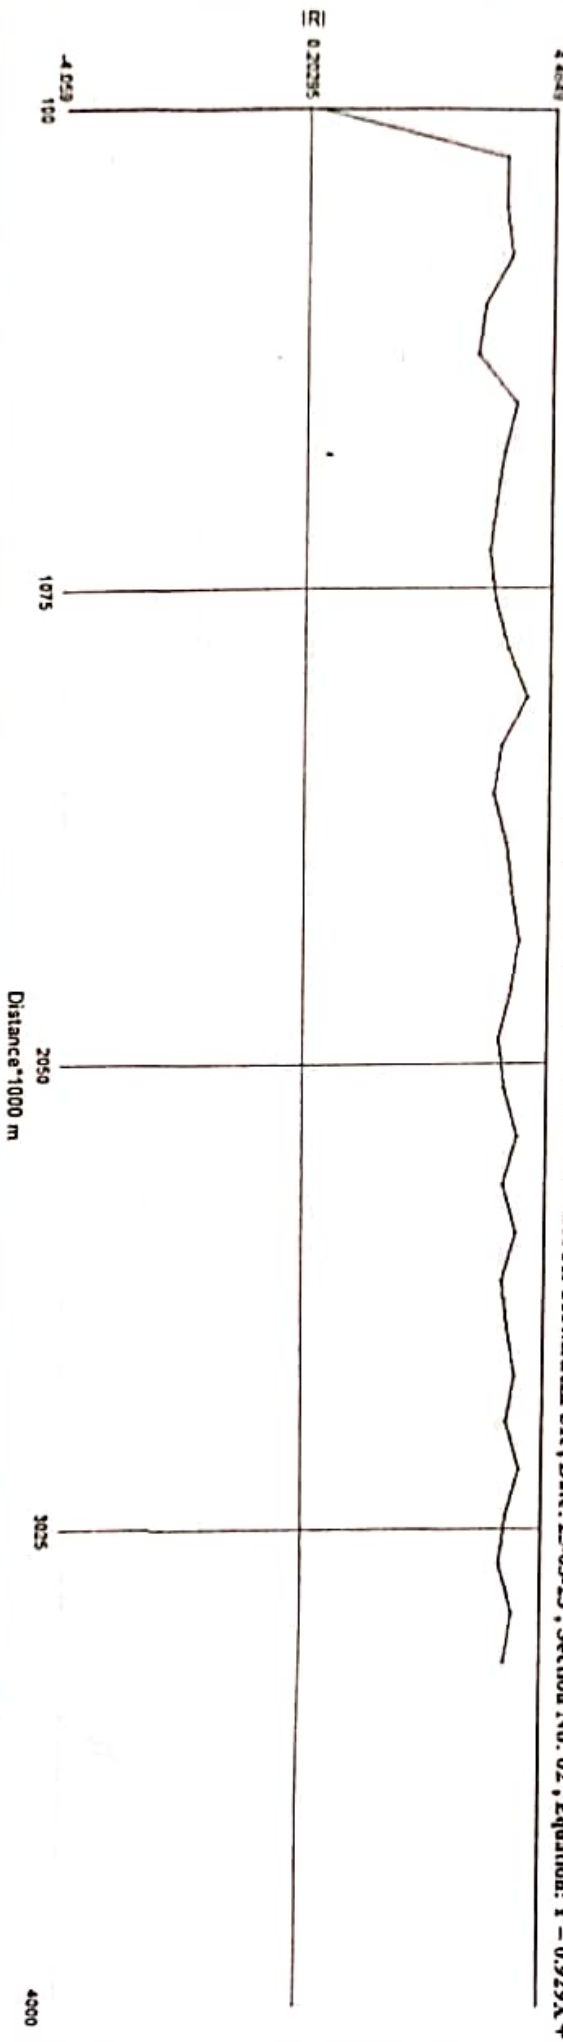

127-3-23
8

20/3/23

Executive Engineer
 Division

Name of the work: GARHPURA SHURI - SAMASTIPUR MAALPUR

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUANP (cm)	Speed (km/hr)	UI (mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
25-03-2023	15:09:06	2	100	100	0.0 cm	8.9	0.0	237.9	0.419	Good	25.72952 N		86.13686 E		Normal
25-03-2023	15:09:46	2	100	200	26.0 cm	13.6	2600.0	2653.3	3.61	Good	25.72935 N		86.1373 E		Curve
25-03-2023	15:10:39	2	100	300	26.0 cm	17.6	2600.0	2653.3	3.61	Good	25.72852 N		86.13699 E		Normal
25-03-2023	15:11:04	2	100	400	27.0 cm	17.8	2700.0	2746.2	3.723	Good	25.72852 N		86.13699 E		Curve
25-03-2023	15:11:33	2	100	500	23.0 cm	17.6	2300.0	2374.6	3.27	Good	25.7277 N		86.1367 E		Normal
25-03-2023	15:11:59	2	100	600	22.0 cm	17.8	2200.0	2281.7	3.155	Good	25.7267 N		86.13653 E		Normal
25-03-2023	15:12:29	2	100	700	28.0 cm	18.0	2800.0	2839.1	3.835	Good	25.72586 N		86.1364 E		Normal
25-03-2023	15:12:58	2	100	800	26.0 cm	17.5	2600.0	2653.3	3.61	Good	25.72506 N		86.13633 E		Normal
25-03-2023	15:13:21	2	100	900	25.0 cm	17.0	2500.0	2560.4	3.497	Good	25.72424 N		86.13606 E		Normal
25-03-2023	15:13:46	2	100	1000	24.0 cm	18.2	2500.0	2467.5	3.384	Good	25.72342 N		86.13567 E		Normal
25-03-2023	15:14:08	2	100	1100	25.0 cm	18.4	2700.0	2560.4	3.497	Good	25.72261 N		86.13583 E		Curve
25-03-2023	15:14:31	2	100	1200	27.0 cm	19.7	3000.0	2746.2	3.723	Good	25.72191 N		86.13633 E		Normal
25-03-2023	15:14:55	2	100	1300	30.0 cm	19.2	2600.0	3024.9	4.059	Good	25.72106 N		86.13645 E		Curve
25-03-2023	15:15:22	2	100	1400	26.0 cm	19.7	2500.0	2653.3	3.61	Good	25.72025 N		86.1368 E		Normal
25-03-2023	15:15:47	2	100	1500	25.0 cm	21.4	2700.0	2560.4	3.497	Good	25.71954 N		86.13726 E		Normal
25-03-2023	15:16:11	2	100	1600	27.0 cm	17.5	2800.0	2746.2	3.723	Good	25.71866 N		86.13738 E		Normal
25-03-2023	15:16:44	2	100	1700	28.0 cm	18.4	2900.0	2839.1	3.835	Good	25.71777 N		86.13752 E		Normal
25-03-2023	15:17:10	2	100	1800	29.0 cm	18.8	2800.0	2932	3.947	Good	25.71697 N		86.13762 E		Normal
25-03-2023	15:17:32	2	100	1900	28.0 cm	18.1	2600.0	2839.1	3.835	Good	25.71625 N		86.13795 E		Normal
25-03-2023	15:17:57	2	100	2000	26.0 cm	18.8	2700.0	2653.3	3.61	Good	25.71544 N		86.13832 E		Normal
25-03-2023	15:18:20	2	100	2100	27.0 cm	18.8	2700.0	2746.2	3.723	Good	25.71468 N		86.13873 E		Normal

Y=0.929X+237.9

RURAL ROAD

Good Average Poor
<4000 4001-5000 >5000

127-3-23
88

25-03-2023	15:18:42	2	100	2200	29.0 cm	18.8 km/hr	2900.0 mm/Km	2932	3.947	Good	25.71391 N	86.13925 E	Curve
25-03-2023	15:19:03	2	100	2300	29.0 cm	19.6 km/hr	2700.0 mm/Km	2746.2	3.723	Good	25.71375 N	86.14008 E	Normal
25-03-2023	15:20:37	2	100	2400	29.0 cm	18.8 km/hr	2900.0 mm/Km	2932	3.947	Good	25.72815 N	86.13787 E	Curve
25-03-2023	15:20:59	2	100	2500	27.0 cm	18.9 km/hr	2700.0 mm/Km	2746.2	3.723	Good	25.72815 N	86.13787 E	Normal
25-03-2023	15:21:19	2	100	2600	28.0 cm	19.9 km/hr	2800.0 mm/Km	2839.1	3.835	Good	25.72789 N	86.13882 E	Normal
25-03-2023	15:21:39	2	100	2700	29.0 cm	19.8 km/hr	2900.0 mm/Km	2932	3.947	Good	25.72765 N	86.1398 E	Curve
25-03-2023	15:22:01	2	100	2800	28.0 cm	19.2 km/hr	2800.0 mm/Km	2839.1	3.835	Good	25.72753 N	86.14067 E	Normal
25-03-2023	15:22:51	2	100	2900	30.0 cm	19.7 km/hr	3000.0 mm/Km	3024.9	4.059	Good	25.72746 N	86.1416 E	Curve
25-03-2023	15:23:12	2	100	3000	28.0 cm	19.2 km/hr	2800.0 mm/Km	2839.1	3.835	Good	25.72776 N	86.14222 E	Normal
25-03-2023	15:23:35	2	100	3100	27.0 cm	19.7 km/hr	2700.0 mm/Km	2746.2	3.723	Good	25.72852 N	86.14256 E	Curve
25-03-2023	15:23:57	2	100	3200	29.0 cm	21.3 km/hr	2900.0 mm/Km	2932	3.947	Good	25.72936 N	86.14287 E	Normal
25-03-2023	15:24:21	2	100	3300	28.0 cm	17.4 km/hr	2800.0 mm/Km	2839.1	3.835	Good	25.73099 N	86.14384 E	Normal

27-3-23
18

EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION- MANJHAUL-BAKHRI.

27/3/23
