

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

पत्रांक- 981(अनु०)

दिनांक- 26/05/2023

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति 2018” (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति 2018” योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण
नीति 2018” योजनान्तर्गत पथ:-

1. T03 to Kehuniya (VR62)

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना
विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल नरकटियागंज

26/05/2023

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR/22/0027	T03 to Kehuniya (VR62)	31808902204	105 03.06.2022	2.521	126.86000	86.86309	29.70020	58/22-23 20.02.2023	19.11.2023		2772	SDBC-25mm	5%	0.00000	0.00000	85.62644	Surface Complete


 Executive Engineer
 Rural Works Department
 Work(s) Division Narkatiaganj
 24/5/2023

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- T03 to Kehuniya (VR62)

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- Anil Kumar Mishra

Length of Road :- 2.521 KM

Project ID :- 31808902204

Package No. :- RM/WE/NAR/22/0027

Name of Block :- Narkatiaganj

Certified that all item wise 100% measurement has been taken by me

Hin
24/5/2023
JE

Certified that all item wise 50% measurement has been verified by me

Exnated
25.5.23

AE

Certified that all item wise 10% measurement has been verified by me

Handwritten signature
26/5/23

EE

Name of Road - T03 to Kehuniya (VR62) (Sec-95)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
24/ 5/ 23	12: 11: 52	95	0.1	280	22.5	2800	2768	G	27.47528	84.44712	Normal
24/ 5/ 23	12: 12: 0	95	0.1	270	22.6	2700	2710	G	27.4695	84.44648	Normal
24/ 5/ 23	12: 12: 26	95	0.1	280	22.6	2800	2784	G	27.46257	84.445925	Normal
24/ 5/ 23	12: 13: 1	95	0.1	320	32.7	3200	3184	G	27.4546	84.445453	Normal
24/ 5/ 23	12: 13: 1	95	0.1	280	22.6	2800	2849	G	27.44585	84.44512	Normal
24/ 5/ 23	12: 13: 36	95	0.1	280	22.6	2800	2837	G	27.43725	84.44515	Normal
24/ 5/ 23	12: 14: 0	95	0.1	270	22.6	2700	2745	G	27.42802	84.444882	Normal
24/ 5/ 23	12: 14: 12	95	0.1	280	12.5	2800	2824	G	27.41957	84.444747	Normal
24/ 5/ 23	12: 14: 12	95	0.1	300	22.6	3000	2954	G	27.41035	84.44468	Normal
24/ 5/ 23	12: 14: 12	95	0.1	280	22.6	2800	2849	G	27.401	84.444512	Curve
24/ 5/ 23	12: 14: 47	95	0.1	250	22.6	2500	2478	G	27.39822	84.44537	Normal
24/ 5/ 23	12: 15: 0	95	0.1	240	12.5	2400	2373	G	27.39228	84.446027	Normal
24/ 5/ 23	12: 15: 0	95	0.1	300	22.6	3000	2954	G	27.38645	84.446632	Normal
24/ 5/ 23	12: 15: 22	95	0.1	280	22.6	2800	2849	G	27.38095	84.447255	Normal
24/ 5/ 23	12: 15: 22	95	0.1	260	25.6	2600	2582	G	27.3762	84.448198	Normal
24/ 5/ 23	12: 15: 22	95	0.1	290	27.5	2900	2868	G	27.37273	84.449107	Normal
24/ 5/ 23	12: 16: 0	95	0.1	260	25.8	2600	2575	G	27.37052	84.45005	Normal
24/ 5/ 23	12: 16: 0	95	0.1	290	26.0	2900	2947	G	27.36925	84.45106	Normal
24/ 5/ 23	12: 16: 33	95	0.1	270	25.5	2700	2680	G	27.36818	84.452255	Normal
24/ 5/ 23	12: 17: 0	95	0.1	250	25.5	2500	2546	G	27.36887	84.453265	Normal
24/ 5/ 23	12: 17: 8	95	0.1	250	32.7	2500	2533	G	27.3722	84.454225	Normal
24/ 5/ 23	12: 17: 43	95	0.1	260	32.7	2600	2642	G	27.37525	84.45508	Normal
24/ 5/ 23	12: 18: 19	95	0.1	290	23.8	2900	2891	G	27.37365	84.456093	Normal
24/ 5/ 23	12: 18: 19	95	0.1	260	32.7	2600	2613	G	27.371	84.457087	Normal
24/ 5/ 23	12: 20: 40	95	0.1	300	32.7	3000	3008	G	27.37618	84.457357	Normal
24/ 5/ 23	12: 21: 15	95	0.021	300	25.9	3000	3018	G	27.37478	84.457288	Normal
Average IRI Value=							2772				

Hin
24/5/2023

S. S. 23
AE

[Signature]
Executive Engineer
Rural Works Department
Narkatiyaganj

Name of Customer : Anil Kumar Mishra

Name of Work/ Road : T03 to Kehuniya (VR62)

Lab Job number :

Date : 24-05-2023

Section No. : 95

Test Date : 24-05-2023

Road Name : T03 to Kehuniya (VR62)

Machine No : 402

Road Type : (R) RURAL ROAD

Start S No :

Side :

Start E No :

Interval

Weather :

UIV Range : 1373 To 4000 1000 mm/km

Start Location :

Dist Range : 0 To 2.7 0.1 * 1000 m

End Location :


Equation : $Y = 0 * X^2 + 1.021 * X - 31.77$

Print

Generate Report and Graph

Redraw Graph

Map View

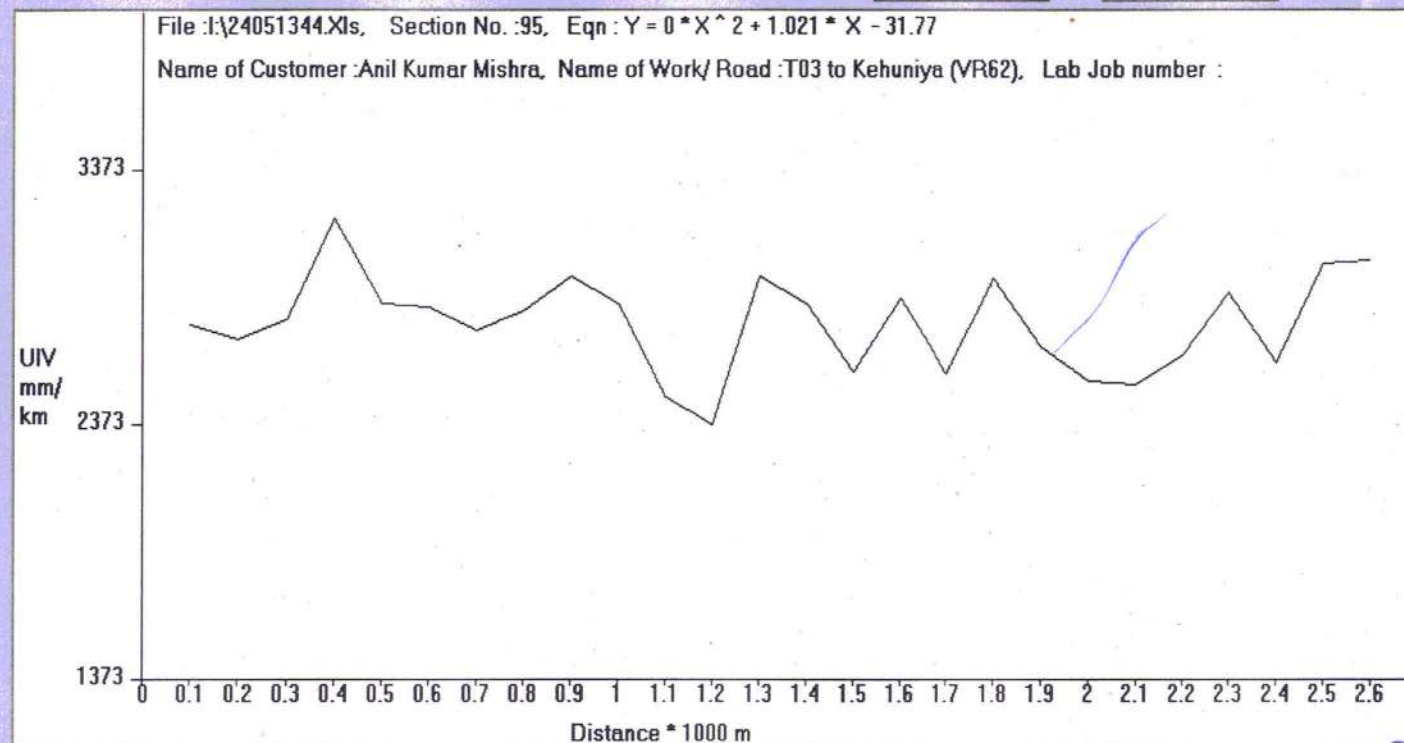

Aty
24/5/2023

Sanjeev
25-5-23
A/E

Executive Engineer
Rural Works Department
Works Division, Narkatiyaganj
24/5/2023
