

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 1979(अनु०)

/नरकटियागंज, दिनांक 31/10/2023

प्रेषक,

ई० मुकेश कुमार सिंह,
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति-2018” (3054-MR),
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति-2018” योजनान्तर्गत पथ के निर्माण में संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण नीति-2018” योजनान्तर्गत पथ:-


1. Done Canal – Serpur
2. BELSANDI PANCHYAT KE BELSANDI SE BAHARWA, SERWA MASJIDWA HOTE HUE MATEARIYA SONBERSA TAK SADAK NIRMAN
3. PWD ROAD - DHAMOURA

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



ई० मुकेश कुमार सिंह

कार्यपालक अभियन्ता,

ग्रा०का०वि०, का०प्र०, नरकटियागंज

31/10/2023

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR/21/0002	Done Canal - Serpur	31808802079	1099 31.03.2021	5.670	253.26500	218.32536	55.56075	27/22-23 23.09.2022	22.06.2023		2824	SDBC-25mm	5%	0.00000	0.00000	130.00000	Surface Complete
2	RM/WE/NAR/21/0002	BELSANDI PANCHYAT KE BELSANDI SE BAHARWA, SERWA MASJIDWA HOTE HUE MATEARIYA SONBERSA TAK SADAK NIRMAL.	31808901008	1099 31.03.2021	8.820	396.22700	292.75988	68.88645	27/22-23 23.09.2022	22.06.2023		2983	SDBC-25mm	5%	0.00000	0.00000	273.64825	Surface Complete
3	RM/WE/NAR/22/0013	PWD ROAD - DHAMOURA	31808802110	105 03.06.2022	1.800	168.62000	132.47557	20.24890	55/22-23 02.02.2023	01.11.2023		2993	SDBC-25mm	5%	0.00000	0.00000	120.00000	Surface Complete

Pranav
31-10-23
JC

Pranav
31.10.23
AE

[Signature]
Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj
[Signature]
21/10/2023

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- Done Canal - Serpur

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- M/S Jai Bhawani Construction

Length of Road :- 5.670 KM

Project ID :- 31808802079

Package No. :- RM/WE/NAR/21/0002

Name of Block :- Gaunaha

Certified that all item wise 100% measurement has been taken by me

Prunwar
31-10-23
JE

Certified that all item wise 50% measurement has been verified by me

Prunwar
31/10/23
AE

Certified that all item wise 10% measurement has been verified by me

Prunwar
31/10/23
EE

Name of Road - Done Canal - Serpur (Sec-28)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
28/ 10/ 23	8: 58: 29	28	0.1	280	22.8	2800	2801	G	27.24508	84.42626	Normal
28/ 10/ 23	8: 59: 6	28	0.1	270	22.9	2700	2743	G	27.24598	84.42626	Normal
28/ 10/ 23	8: 59: 6	28	0.1	280	22.9	2800	2817	G	27.24672	84.42677	Normal
28/ 10/ 23	8: 59: 41	28	0.1	320	33	3200	3217	G	27.24735	84.42743	Normal
28/ 10/ 23	9: 0: 17	28	0.1	290	22.9	2900	2882	G	27.24818	84.42782	Normal
28/ 10/ 23	9: 0: 17	28	0.1	290	22.9	2900	2870	G	27.24902	84.42821	Normal
28/ 10/ 23	9: 0: 17	28	0.1	280	22.9	2800	2778	G	27.24984	84.42860	Normal
28/ 10/ 23	9: 1: 0	28	0.1	290	12.8	2900	2857	G	27.25071	84.42869	Normal
28/ 10/ 23	9: 1: 0	28	0.1	300	22.9	3000	2987	G	27.25102	84.42775	Normal
28/ 10/ 23	9: 1: 27	28	0.1	290	22.9	2900	2882	G	27.25135	84.42679	Normal
28/ 10/ 23	9: 1: 27	28	0.1	250	22.9	2500	2511	G	27.25165	84.42581	Normal
28/ 10/ 23	9: 1: 27	28	0.1	240	12.8	2400	2406	G	27.25194	84.42488	Normal
28/ 10/ 23	9: 2: 1	28	0.1	300	22.9	3000	2987	G	27.25192	84.42386	Normal
28/ 10/ 23	9: 2: 1	28	0.1	290	22.9	2900	2882	G	27.25192	84.42285	Normal
28/ 10/ 23	9: 2: 37	28	0.1	260	25.9	2600	2615	G	27.25226	84.42192	Normal
28/ 10/ 23	9: 2: 37	28	0.1	290	27.8	2900	2901	G	27.25281	84.42114	Curve
28/ 10/ 23	9: 3: 0	28	0.1	260	26.1	2600	2608	G	27.25340	84.42039	Normal
28/ 10/ 23	9: 3: 12	28	0.1	300	26.3	3000	2980	G	27.25424	84.42038	Normal
28/ 10/ 23	9: 3: 12	28	0.1	270	25.8	2700	2713	G	27.25509	84.42070	Normal
28/ 10/ 23	9: 3: 12	28	0.1	260	25.8	2600	2579	G	27.25605	84.42085	Normal
28/ 10/ 23	9: 3: 47	28	0.1	260	33	2600	2566	G	27.25693	84.42104	Normal
28/ 10/ 23	9: 4: 0	28	0.1	270	33	2700	2675	G	27.25795	84.42073	Normal
28/ 10/ 23	9: 4: 23	28	0.1	290	24.1	2900	2924	G	27.25858	84.42041	Normal
28/ 10/ 23	9: 4: 23	28	0.1	260	33	2600	2646	G	27.25943	84.42015	Normal
28/ 10/ 23	9: 4: 23	28	0.1	300	33	3000	3041	G	27.26036	84.41993	Normal
28/ 10/ 23	9: 5: 0	28	0.1	310	26.2	3100	3051	G	27.26125	84.41971	Normal
28/ 10/ 23	9: 5: 0	28	0.1	240	26.2	2400	2427	G	27.26211	84.41943	Normal
28/ 10/ 23	9: 5: 33	28	0.1	310	26.2	3100	3069	G	27.26296	84.41938	Normal
28/ 10/ 23	9: 5: 33	28	0.1	280	26.2	2800	2795	G	27.26384	84.41948	Normal

Name of Road - Done Canal - Serpur (Sec-28)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
28/10/23	9:6:0	28	0.1	290	26.2	2900	2898	G	27.26473	84.41948	Normal
28/10/23	9:6:8	28	0.1	290	33	2900	2855	G	27.26563	84.41951	Normal
28/10/23	9:6:8	28	0.1	310	26.2	3100	3070	G	27.26659	84.41947	Normal
28/10/23	9:6:8	28	0.1	270	33	2700	2746	G	27.26749	84.41941	Normal
28/10/23	9:6:44	28	0.1	280	23	2800	2757	G	27.26840	84.41929	Normal
28/10/23	9:6:44	28	0.1	270	24	2700	2653	G	27.26925	84.41914	Normal
28/10/23	9:7:0	28	0.1	250	24	2500	2457	G	27.27009	84.41883	Normal
28/10/23	9:7:19	28	0.1	280	24	2800	2757	G	27.27097	84.41852	Normal
28/10/23	9:7:19	28	0.1	280	24	2800	2787	G	27.27184	84.41839	Normal
28/10/23	9:7:19	28	0.1	280	24	2800	2766	G	27.27265	84.41877	Normal
28/10/23	9:7:19	28	0.1	290	24	2900	2948	G	27.27353	84.41890	Normal
28/10/23	9:8:0	28	0.1	320	24	3200	3153	G	27.27439	84.41873	Normal
28/10/23	9:8:0	28	0.1	310	24	3100	3139	G	27.27532	84.41856	Normal
28/10/23	9:8:0	28	0.1	290	24	2900	2888	G	27.27618	84.41837	Normal
28/10/23	9:8:0	28	0.1	320	24	3200	3195	G	27.27704	84.41810	Normal
28/10/23	9:8:30	28	0.1	290	25.2	2900	2867	G	27.27790	84.41787	Normal
28/10/23	9:8:30	28	0.1	300	25.2	3000	2969	G	27.27882	84.41794	Normal
28/10/23	9:8:30	28	0.1	310	25.2	3100	3093	G	27.27972	84.41783	Normal
28/10/23	9:9:5	28	0.1	280	25.2	2800	2766	G	27.28034	84.41718	Normal
28/10/23	9:9:5	28	0.1	290	25.2	2900	2873	G	27.28116	84.41682	Normal
28/10/23	9:9:5	28	0.1	320	25.2	3200	3174	G	27.28199	84.41641	Normal
28/10/23	9:9:40	28	0.1	280	25.2	2800	2757	G	27.28261	84.41573	Normal
28/10/23	9:9:40	28	0.1	280	25.2	2800	2786	G	27.28326	84.41506	Normal
28/10/23	9:10:0	28	0.1	290	25.2	2900	2859	G	27.28380	84.41427	Normal
28/10/23	9:10:15	28	0.1	250	25.2	2500	2480	G	27.28427	84.41337	Normal
28/10/23	9:10:15	28	0.1	310	25.2	3100	3072	G	27.28451	84.41237	Normal
28/10/23	9:10:15	28	0.1	260	25.2	2600	2561	G	27.28454	84.41180	Normal
28/10/23	9:11:0	28	0.07	250	25.2	2500	2459	G	27.28451	84.41174	Normal
Average IRI Value=							2824				

Ramon
31-10-23
(JCB)

[Signature]
31/10/23

Executive Engineer

Name of Customer : M/S Jai Bhawani Construction
Name of Work/ Road : Done Canal - Serpur
Lab Job number :
Date : 28-10-2023
Section No. : 28


Test Date : 28-10-2023 Road Name : Done Canal - Serpur
Machine No : 402 Road Type : (R) RURAL ROAD
Start S No : Side :
Start E No : Interval
Weather : UIV Range : 1406 To 4000 1000 mm/km
Start Location : Dist Range : 0 To 5.8 0.1 * 1000 m
End Location : Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

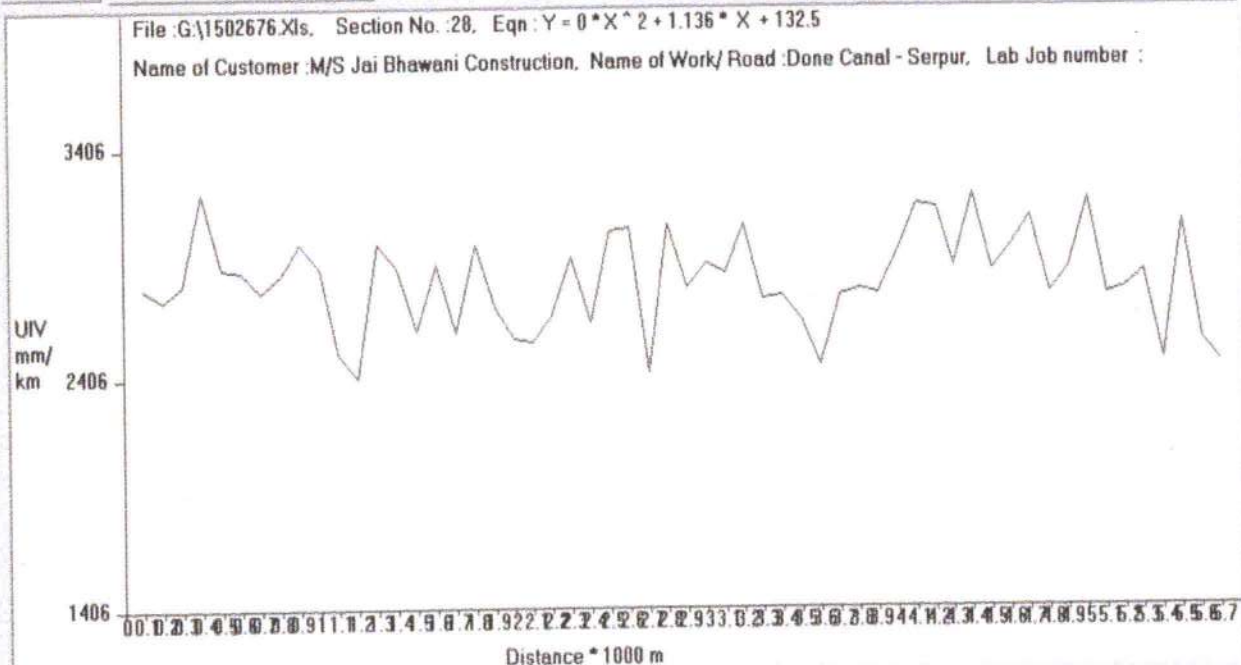

Pruman
31-10-23
(JE)

Pruman
31/10/23
AE

Executive Engineer
Rural Works Department
Work Division, Narkatiyaganj
31/10/23
