

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 1853(अनु०)

/नरकटियागंज, दिनांक 10/10/2023

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति 2018" (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) "नई अनुरक्षण नीति 2018" योजनान्तर्गत पथ के निर्माण में संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) "नई अनुरक्षण नीति 2018" योजनान्तर्गत पथ:-

1. T03 to Dharmapur (VR26)

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



कार्यपालक अभियन्ता,

ग्रा०का०वि०, का०प्र०, नरकटियागंज
10/10/2023

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR/22/0033	T03 to Dharmapur (VR26)	31808902138	105 03.06.2022	5.450	432.97000	301.38378	53.83085	59/22-23 10.03.2023	09.12.2023		2926	SDBC-25mm BM-50mm	5%	200.13878	200.13878	95.70132	Surface Complete

Pan
10/10/23
AE

[Signature]
Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj
[Signature]
10/10/2023

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- T03 to Dharmapur (VR26)

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- Khurshid Alam

Length of Road :- 5.450 KM

Project ID :- 31808902138

Package No. :- RM/WE/NAR/22/0033

Name of Block :- **Sikta**

Certified that all item wise 100% measurement has been taken by me

Hiv
10/10/2023
JE

Certified that all item wise 50% measurement has been verified by me

Poc...
10/10/23
AE

Certified that all item wise 10% measurement has been verified by me

...
10/10/23
EE

Name of Road - T03 to Dharmapur (VR26) (Sec-82)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
18/-8/23	8:34:6	82	0.1	280	21.3	2800	2753	G	27.28657	84.64476	Normal
18/8/23	8:35:0	82	0.1	270	21.4	2700	2695	G	27.28327	84.64566	Normal
18/8/23	8:35:52	82	0.1	280	21.4	2800.	2769	G	27.27938	84.64665..	Normal
18/8/23	8:36:0	82	0.1	320	31.5	3200	3169	G	27.27553	84.64751	Normal
18/8/23	8:37:2	82	0.1	280	21.4	2800	2834	G	27.27192	84.64843	Normal
18/8/23	8:37:37	82	0.1	280	21.4	2800	2822	G	27.26823	84.64931	Normal
18/8/23	8:38:13	82	0.1	270	21.4	2700	2730	G	27.26445	84.65020	Normal
18/8/23	8:38:48	82	0.1	340	11.3	3400	3358	G	27.26100	84.65111	Normal
18/8/23	8:39:22	82	0.1	290	21.4	2900	2939	G	27.25727	84.65202	Normal
18/8/23	8:40:0	82	0.1	280	21.4	2800	2834	G	27.25300	84.65291	Normal
18/8/23	8:40:33	82	0.1	350	21.4	3500	3463	G	27.24955	84.65380	Normal
18/8/23	8:41:8	82	0.1	340	11.3	3400	3358	G	27.24602	84.65470	Normal
18/8/23	8:41:43	82	0.1	290	21.4	2900	2939	G	27.24228	84.65559	Normal
18/8/23	8:42:19	82	0.1	280	21.4	2800	2834	G	27.23787	84.65663	Normal
18/8/23	8:43:0	82	0.1	260	24.4	2600	2567	G	27.23362	84.65769	Normal
18/8/23	8:43:29	82	0.1	330	26.3	3300	3253	G	27.22960	84.65857	Normal
18/8/23	8:44:5	82	0.1	260	24.6	2600	2560	G	27.22573	84.65953	Normal
18/8/23	8:44:40	82	0.1	290	24.8	2900	2932	G	27.22210	84.66042	Normal
18/8/23	8:45:15	82	0.1	270	24.3	2700	2665	G	27.21828	84.66133	Normal
18/8/23	8:45:50	82	0.1	330	24.3	3300	3253	G	27.21463	84.66222	Normal
18/8/23	8:46:26	82	0.1	320	31.5	3200	3209	G	27.21095	84.66313	Normal
18/8/23	8:47:1	82	0.1	320	31.5	3200	3207	G	27.20738	84.66397	Normal
18/8/23	8:47:36	82	0.1	290	22.6	2900	2876	G	27.20380	84.66488	Normal
18/8/23	8:48:12	82	0.1	310	31.5	3100	3121	G	27.20020	84.66581	Normal
18/8/23	8:49:0	82	0.1	300	31.5	3000	2993	G	27.19753	84.66672	Normal
18/8/23	8:49:22	82	0.1	300	24.7	3000	3003	G	27.19668	84.66771	Normal
18/8/23	8:50:0	82	0.1	330	24.7	3300	3309	G	27.19588	84.66869	Normal
18/8/23	8:50:33	82	0.1	300	24.7	3000	3021	G	27.19520	84.66970	Normal
18/8/23	8:51:8	82	0.1	310	24.7	3100	3147	G	27.19438	84.67067	Normal
18/8/23	8:52:0	82	0.1	320	24.7	3200	3207	G	27.19335	84.67163	Normal

Handwritten signature and date: 10/10/23

Handwritten signature and date: 10/10/23

Name of Road - T03 to Dharmapur (VR26) (Sec-82)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
18/8/23	8:52:19	82	0.1	280	31.5	2800	2807	G	27.19275	84.67261	Normal
18/8/23	8:53:0	82	0.1	300	24.7	3000	3022	G	27.19195	84.67359	Normal
18/8/23	8:53:29	82	0.1	270	31.5	2700	2698	G	27.19130	84.67456	Normal
18/8/23	8:54:4	82	0.1	270	21.5	2700	2709	G	27.19060	84.67556	Normal
18/8/23	8:55:0	82	0.1	260	22.5	2600	2605	G	27.18960	84.67655	Normal
18/8/23	8:55:15	82	0.1	240	22.5	2400	2409	G	27.18988	84.67749	Bridge
18/8/23	8:56:0	82	0.1	270	22.5	2700	2709	G	27.18792	84.67843	Normal
18/8/23	8:56:26	82	0.1	320	22.5	3200	3207	G	27.18752	84.67943	Normal
18/8/23	8:57:1	82	0.1	270	22.5	2700	2718	G	27.18670	84.68042	Normal
18/8/23	8:57:36	82	0.1	290	22.5	2900	2900	G	27.18580	84.68141	Normal
18/8/23	8:58:8	82	0.1	310	22.5	3100	3105	G	27.18492	84.68242	Normal
18/8/23	8:58:47	82	0.1	310	22.5	3100	3091	G	27.18425	84.68337	Normal
18/8/23	8:59:22	82	0.1	280	22.5	2800	2840	G	27.18372	84.68438	Normal
18/8/23	8:59:57	82	0.1	310	22.5	3100	3147	G	27.18292	84.68534	Normal
18/8/23	9:0:33	82	0.1	280	23.7	2800	2819	G	27.18235	84.68635	Normal
18/8/23	9:1:8	82	0.1	290	23.7	2900	2921	G	27.18172	84.68732	Normal
18/8/23	9:1:43	82	0.1	300	23.7	3000	3045	G	27.18120	84.68832	Normal
18/8/23	9:2:18	82	0.1	270	23.7	2700	2718	G	27.18023	84.68929	Normal
18/8/23	9:3:0	82	0.1	280	23.7	2800	2825	G	27.17980	84.69027	Normal
18/8/23	9:3:29	82	0.1	310	23.7	3100	3126	G	27.17908	84.69126	Normal
18/8/23	9:4:4	82	0.1	270	23.7	2700	2709	G	27.17823	84.69224	Normal
18/8/23	9:5:0	82	0.1	270	23.7	2700	2738	G	27.17745	84.69322	Normal
18/8/23	9:5:15	82	0.1	280	23.7	2800	2811	G	27.17695	84.69419	Normal
18/8/23	9:6:0	82	0.1	240	23.7	2400	2432	G	27.17625	84.69517	Normal
18/8/23	9:7:1	82	0.05	300	23.7	3000	3024	G	27.17550	84.69614	Normal
Average IRI Value=							2926				

Aty
10/10/2023
T.C


Pan
10/10/23
AE


Executive Engineer
Rural Works Department
Work Division, Narkatiyagani

Name of Customer : Khurshid Alam
Name of Work/ Road : T03 to Dharampur
Lab Job number :
Date : 18-08-2023
Section No. : 82

Test Date : 18-08-2023 Road Name : T03 to Dharampur
Machine No : 402 Road Type : (R) RURAL ROAD
Start S No : Side :
Start E No : Interval
Weather : UIV Range : 1409 To 4000 1000 mm/km
Start Location : Dist Range : 0 To 5.6 0.1 * 1000 m
End Location : Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print Generate Report and Graph Redraw Graph Map View

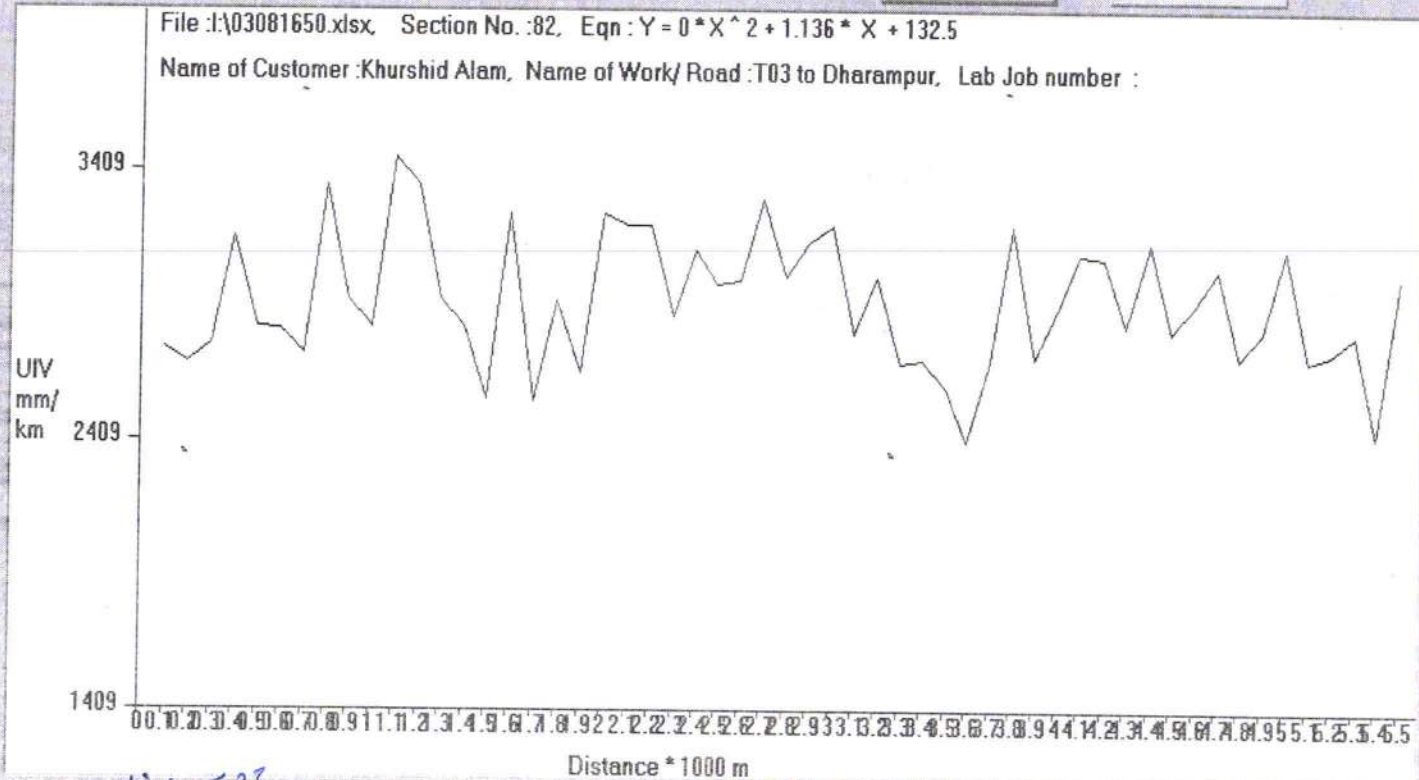

HiV
10/10/2023
J.C.

10/10/23
AE

Executive Engineer
Rural Works Department
Work Division, Narkatiyaganj
10/10/23
