

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सोनपुर

Mob No :- 8986915436

E.Mail :- eerwdsonpur@gmail.com

पत्रांक ४२४ अगु०

सोनपुर, दिनांक २२.०४.२०२४

प्रेषक,

ई० अशोक कुमार
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर।

सेवा में,

नोडल पदाधिकारी (3054),
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय:- बिहार ग्रामीण पथ अनुरक्षण निति-2018 के तहत स्वीकृत योजना में
आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक ग्रामीण कार्य विभाग कार्य प्रमंडल सोनपुर के अंतर्गत बिहार
ग्रामीण पथ अनुरक्षण निति-2018 के तहत स्वीकृत योजना के क्रियान्वयन हेतु आवंटन की
मांग विहित प्रपत्र में तैयार कर भेजी जा रही है।

अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की
जाये।

अनु०:-उपयोगित प्रमाण-पत्र।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सोनपुर
22/04/24

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the month of **April-2024**

PIU:- E.E.,R.W.D. Works Division Sonapur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18		8007.41999	Certified that out of Rs 8007.41999 lakh received during the years 2020-21 to 2023-24 in favour of E.E.R.W.D. works division Sonapur a sum of Rs 8005.58741 Lakh has been utilized for the purpose of New Maintenance Policy-18 Scheme as given in the margin for which it was sanctioned and that the balance of Rs 1.83258 Lakh remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.

[Signature]
22/04/24
D.A.O-I

R.W.D. Works Division Sonapur.

[Signature]
22/04/24

EXECUTIVE ENGINEER

R.W.D. Works Division Sonapur.

[Signature]
22/4/24

Requisition Formate for Scheme Head - MR-3054 Under Bihar Rural Road Maintenance Policy 2018 (In Rectification and surface Renewal)

Division Name:- Rural Works Department, Works Division- Sonpur

Sl.No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lac)			Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In Km)	Thickness of Bitumen Layer (In mm)	Value of Bitumen Content In %	Previous Total Allotted Amount (In Lac)	Upto date expenditure as per MIS (In Lac)	Requisition against Work Done (In Lac)	Remarks
1	RM/SA/SON/23/0007	Sonepur Rewaghat road - Sareya(Saraiya)	NEA220001798	1797 20.03.23	0.911	54.014	35.35426	11.42275	14/MBD/2023-24 02.03.2024	01.12.2024	-	3245	25	5.03	0.00000	0.00000	35.27185		
TOTAL																			35.27185

[Signature]
D.A.O-I

R.W.D Works Div- Sonpur

[Signature]
Executive Engineer
R.W.D Works Div- Sonpur
01/12/2024

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर


का0आ0सं0.....828.....सोनपुर, दिनांक 22.04.2024

कार्यालय आदेश

प्रमाणित किया जाता है कि बिहार ग्रामीण पथ अनुरक्षण निती-2018 योजनान्तर्गत Sonepur Rewaghat road - Sareya(Saraiya) (Project ID-NEA220001798) का कार्य गुणवत्ता एवं विशिष्टियों के अनुरूप पूर्ण कराया गया है। पथ के मापीपुस्त की जाँच मेरे द्वारा 25 प्रतिशत एवं सहायक अभियंता के द्वारा 50 प्रतिशत एवं कनीय अभियंता के द्वारा शत प्रतिशत किया गया है।


22/4/24

कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा दरियापुर


24/4/24

सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल दरियापुर


22/4/24

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

Name of work : Sonepur Rewaghat road - Sareya(Saraiya)

Name of customer : Indu Kumari

(R)Rural Road			
Good	Average	Poor	
< 4000	4001 - 5000	> 5000	

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
14/04/24	11:50:18	34	0	0	0.0 cm	6.0 Km/Hr	0.0 mm/Km	127	0.24	Good	25.826199	N	85.141328	E	Normal
14/04/24	11:51:56	34	100	100	17.0 cm	16.2 Km/Hr	1700.0 mm/Km	1705	2.43	Good	25.826038	N	85.141384	E	Normal
14/04/24	11:52:22	34	100	200	31.0 cm	19.1 Km/Hr	3100.0 mm/Km	3004	4.03	Good	25.825873	N	85.141376	E	Normal
14/04/24	11:52:47	34	100	300	39.0 cm	24.6 Km/Hr	3900.0 mm/Km	3747	4.91	Good	25.824901	N	85.141229	E	Normal
14/04/24	11:53:08	34	100	400	37.0 cm	28.9 Km/Hr	3700.0 mm/Km	3561	4.69	Good	25.824013	N	85.141064	E	Normal
14/04/24	11:53:25	34	100	500	34.0 cm	21.2 Km/Hr	3400.0 mm/Km	3283	4.37	Good	25.823123	N	85.141006	E	Normal
14/04/24	11:53:47	34	100	600	38.0 cm	26.0 Km/Hr	3800.0 mm/Km	3654	4.8	Good	25.822402	N	85.140737	E	Normal
14/04/24	11:54:21	34	100	700	36.0 cm	22.8 Km/Hr	3600.0 mm/Km	3468	4.59	Good	25.821655	N	85.139804	E	Normal
14/04/24	11:54:40	34	100	800	31.0 cm	28.6 Km/Hr	3100.0 mm/Km	3004	4.03	Good	25.822231	N	85.139798	E	Normal
14/04/24	11:55:35	34	100	900	38.0 cm	26.9 Km/Hr	3800.0 mm/Km	3654	4.8	Good	25.822891	N	85.139983	E	Normal


Handwritten signature

Handwritten signature

Handwritten signature

Handwritten signature

Name of Customer: Indu Kumari, Machine no: 19205, Road: Sonapur Rewaghat road - Sareya(Saraiya), Date: 14-04-24, Section No: 34, Equation: $Y=0.923X+127.3$

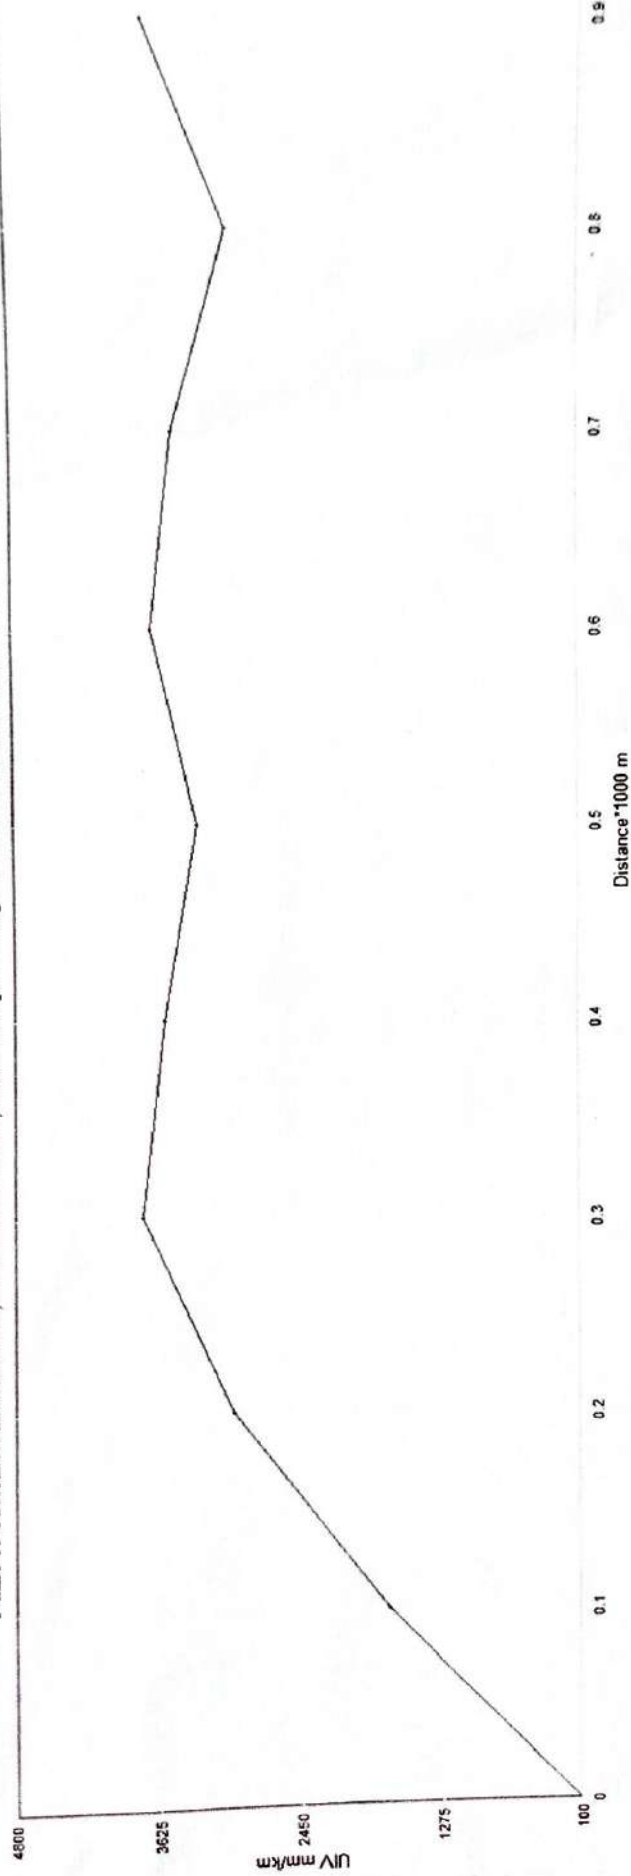

Kumari

14/4/24

16/4/24

18/4/24

Est on A.C. Bill

Name of Work - To 2 Smpur. Kewasahal road to
 Situation of Work - Saxau
 Agency by which work is executed - Gandu Kumar
 Date of Measurement -
 No. and date of agreement - 14/10/2023-24
 (These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Agreement Value					308.96 + 133.29
Date of start					02.03.2024
Date of Completion					
Date of measurement					02/11/24
1. Clearing and grubbing					
The road land					
					20 x 30 x 2 x 0.75 = 9.00
					10 x 30 x 2 x 0.75 = 4.50
					12 x 30 x 2 x 0.75 = 5.40
					1 x 11.00 x 2 x 0.75 = 1.65
					1 x 2 x 2 x 0.75 = 0.30
					1366.50
					Or 0.1366 Ha
2. Construction of granular					
Sub-base by providing					
Well graded material					
Ch. 0.00m to 4.50m					
					2 x 6.11 x 0.39 = 4.77
					2 x 6.42 x 0.65 = 8.35
					2 x 7.28 x 0.73 = 10.60
					3 x 4.96 x 0.26 = 3.85
					2 x 5.98 x 0.39 = 4.66

Continuation

Continuation
