

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हथुआ।

पत्रांक- 1429 अनु०

दिनांक- 04-12-2024

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार, ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय :- बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत क्रियान्वित पथ मरम्मत कार्य हेतु राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषयक बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत क्रियान्वित पथ मरम्मत कार्य हेतु राशि की अधियाचना विहित प्रपत्र में की जा रही है।

अतः भवदीय से अनुरोध है कि कॉलम 18 में अंकित राशि उपलब्ध कराने की कृपा की जाय।

अनु०- यथोक्त ।

विश्वासभाजन,

04.12.24
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

Requisition Format for Scheme Head- MR (3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and Surface Renewal)																		
Name of Works Division :- Rural Works Department, Works Division Hathua.																		
SI No.	Package No.	Name of Road	Project ID as Per MIS	Administrative Approval (AA) Letter No & Date.	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No & Date	Date & Completion as per Agreement.	Actual Date of Completion	Value of IRI (in MM/KM)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	UP-to date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (In Lakh)	Amount (In Lakh)	Initial Rectification with surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/23-24/Hathua/-04	Hussepur Kalyanpur Panchayat Bhawan to Kharkasa	31407117002	Letter-6115, Dt-05.12.2023	2.350	128.770	98.10184	16.43322	03/MBD/2024-25 Date-22.08.2024	21.05.2025	-	Good	25	5.00	93.08550	93.08550	5.01562	Surface Complete
					2.350	128.770	98.10184	16.43322							93.08550	93.08550	5.01562	

प्रमाणित किया जाता है कि पथ में कराये गये कार्य मानक एवं विशिष्टियों के अनुरूप है।

J.E
Bhore

A.E
Bhore

04/11/24

D.A.O
R.W.D Works Division, Hathua.

04/11/24
Executive Engineer,
R.W.D Works Division, Hathua.

FORM GFR 19 - A

(See Government of India's Decision (1) below Rule - 150)
Form utilisation Certificate up to the month of Up to 31.10.2024

MR-3054 (New Maintenance Policy-2018)**RWD Works Division - HATHUA**

1	Head	Amount Received		Expenditure		Balance	
	MR-3054 (New Maintenance Policy-2018)	IN A/C-	0.00	IN A/C-	0.00	IN A/C-	0.00
		By CFMS-	1213172768.00	By CFMS-	1213158273.00	By CFMS-	14495.00
		Total-	1213172768.00	Total-	1213158273.00	Total-	14495.00
						Certified that sum of Rs 12131.58 Lac has been utilized for the purpose of MR-3054 (New Maintenance Policy-2018) Schemes as given in the margin for which it was sanctioned and that the balance of Rs 0.14495 Lac Lacs remaining utilized at the end of the period under.	

2. Certified that I have satisfied myself that the conditions on which the grants-in aid was sanctioned have been duly
Kind of Checks exercised :-

- (i) Works have been supervised by Executive Engineer/Superintending Engineer.
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- (iii) Construction material have been tested.
- (iv) Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
- (v) All other codal formalities have been observed.

3. Physical Progress achieved :-

- (i) Construction of Road Works.
- (ii) Construction of CD Works

ASJ
04.12.24
D.A.O

Rural Works Department
Works Division Hathua

[Signature]
04.12.24

Executive Engineer
Rural Works Department
Works Division Hathua

Name of work : Husepur Kalyanpur(Panchyat Bhawan) TO Kharkasa
Name of customer : M/S Vindyavashni Construction

(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMPI(cm)	Speed(Km/Hr)	U/(mm/Km)	Corrected U/(mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
18/10/24	15:23:42	107	0	0	0.0 cm	6.0 Km/Hr	0.0 mm/Km	245	0.43	Good	26.4737196	N	84.1560068	E	Normal
18/10/24	15:24:27	107	100	100	17.0 cm	20.3 Km/Hr	1700.0 mm/Km	1836	2.6	Good	26.4735689	N	84.1569376	E	Normal
18/10/24	15:24:52	107	100	200	12.0 cm	15.3 Km/Hr	1200.0 mm/Km	1368	2	Good	26.4732885	N	84.1578913	E	Normal
18/10/24	15:25:20	107	100	300	12.0 cm	11.9 Km/Hr	1200.0 mm/Km	1368	2	Good	26.4733171	N	84.1587763	E	Normal
18/10/24	15:25:34	107	100	400	14.0 cm	24.5 Km/Hr	1400.0 mm/Km	1556	2.24	Good	26.4731989	N	84.1595850	E	Normal
18/10/24	15:25:48	107	100	500	20.0 cm	27.0 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.4732103	N	84.1606607	E	Normal
18/10/24	15:26:04	107	100	600	13.0 cm	22.0 Km/Hr	1300.0 mm/Km	1462	2.12	Good	26.4734716	N	84.1613626	E	Normal
18/10/24	15:26:17	107	100	700	24.0 cm	28.2 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.4730558	N	84.1624689	E	Normal
18/10/24	15:26:37	107	100	800	13.0 cm	17.8 Km/Hr	1300.0 mm/Km	1462	2.12	Good	26.4724207	N	84.1631708	E	Normal
18/10/24	15:27:15	107	100	900	18.0 cm	19.8 Km/Hr	1800.0 mm/Km	1930	2.72	Good	26.4721937	N	84.1640329	E	Normal
18/10/24	15:27:34	107	100	1000	13.0 cm	18.0 Km/Hr	1300.0 mm/Km	1462	2.12	Good	26.4720793	N	84.1649713	E	Normal
18/10/24	15:27:59	107	100	1100	11.0 cm	15.0 Km/Hr	1100.0 mm/Km	1275	1.88	Good	26.4715223	N	84.1654825	E	Normal
18/10/24	15:28:14	107	100	1200	19.0 cm	22.9 Km/Hr	1900.0 mm/Km	2024	2.83	Good	26.4707823	N	84.1651087	E	Normal
18/10/24	15:28:30	107	100	1300	11.0 cm	22.5 Km/Hr	1100.0 mm/Km	1275	1.88	Good	26.4699144	N	84.1646509	E	Normal
18/10/24	15:28:42	107	100	1400	12.0 cm	30.9 Km/Hr	1200.0 mm/Km	1368	2	Good	26.4692354	N	84.1640635	E	Normal
18/10/24	15:28:53	107	100	1500	15.0 cm	31.2 Km/Hr	1500.0 mm/Km	1649	2.36	Good	26.4684992	N	84.1633615	E	Normal
18/10/24	15:29:07	107	100	1600	22.0 cm	26.2 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4677019	N	84.1630564	E	Normal
18/10/24	15:29:21	107	100	1700	20.0 cm	26.7 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.4674292	N	84.1641092	E	Normal
18/10/24	15:29:34	107	100	1800	21.0 cm	26.1 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.4667406	N	84.1640940	E	Normal
18/10/24	15:29:46	107	100	1900	22.0 cm	32.0 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4657774	N	84.1638498	E	Normal
18/10/24	15:30:02	107	100	2000	22.0 cm	22.9 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4654760	N	84.1642237	E	Normal

18/10/24

18.10.24
Executive Engineer
R.W.D. Works Division
Hathua

Name of work : Husepur Kalyanpur(Panchyal Bhawan) TO Kharkasa

Name of customer : M/S Vindavashni Construction

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000


18/10/24	15.30.15	107	100	2100	20.0 cm	25.7 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.4645929	N	84.1645212	E	Normal
18/10/24	15.30.27	107	100	2200	26.0 cm	29.7 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4637175	N	84.1643076	E	Normal
18/10/24	15.30.43	107	100	2300	23.0 cm	22.9 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4631357	N	84.1647654	E	Normal
18/10/24	15.31.36	107	100	2400	21.0 cm	7.1 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.4621191	N	84.1647119	E	Normal


18-10-24


Inspector
R.W.D. Works Division
Husepur


18/10/24

Name of Customer: M/S Vindyaashini Construction, Machine no: 19193, Road: Husepur Kalyanpur(Panchayat Bhawan) TO Kharkasa, Date: 18-10-24, Section No: 107, Equation: $Y=0.936X+245.3$

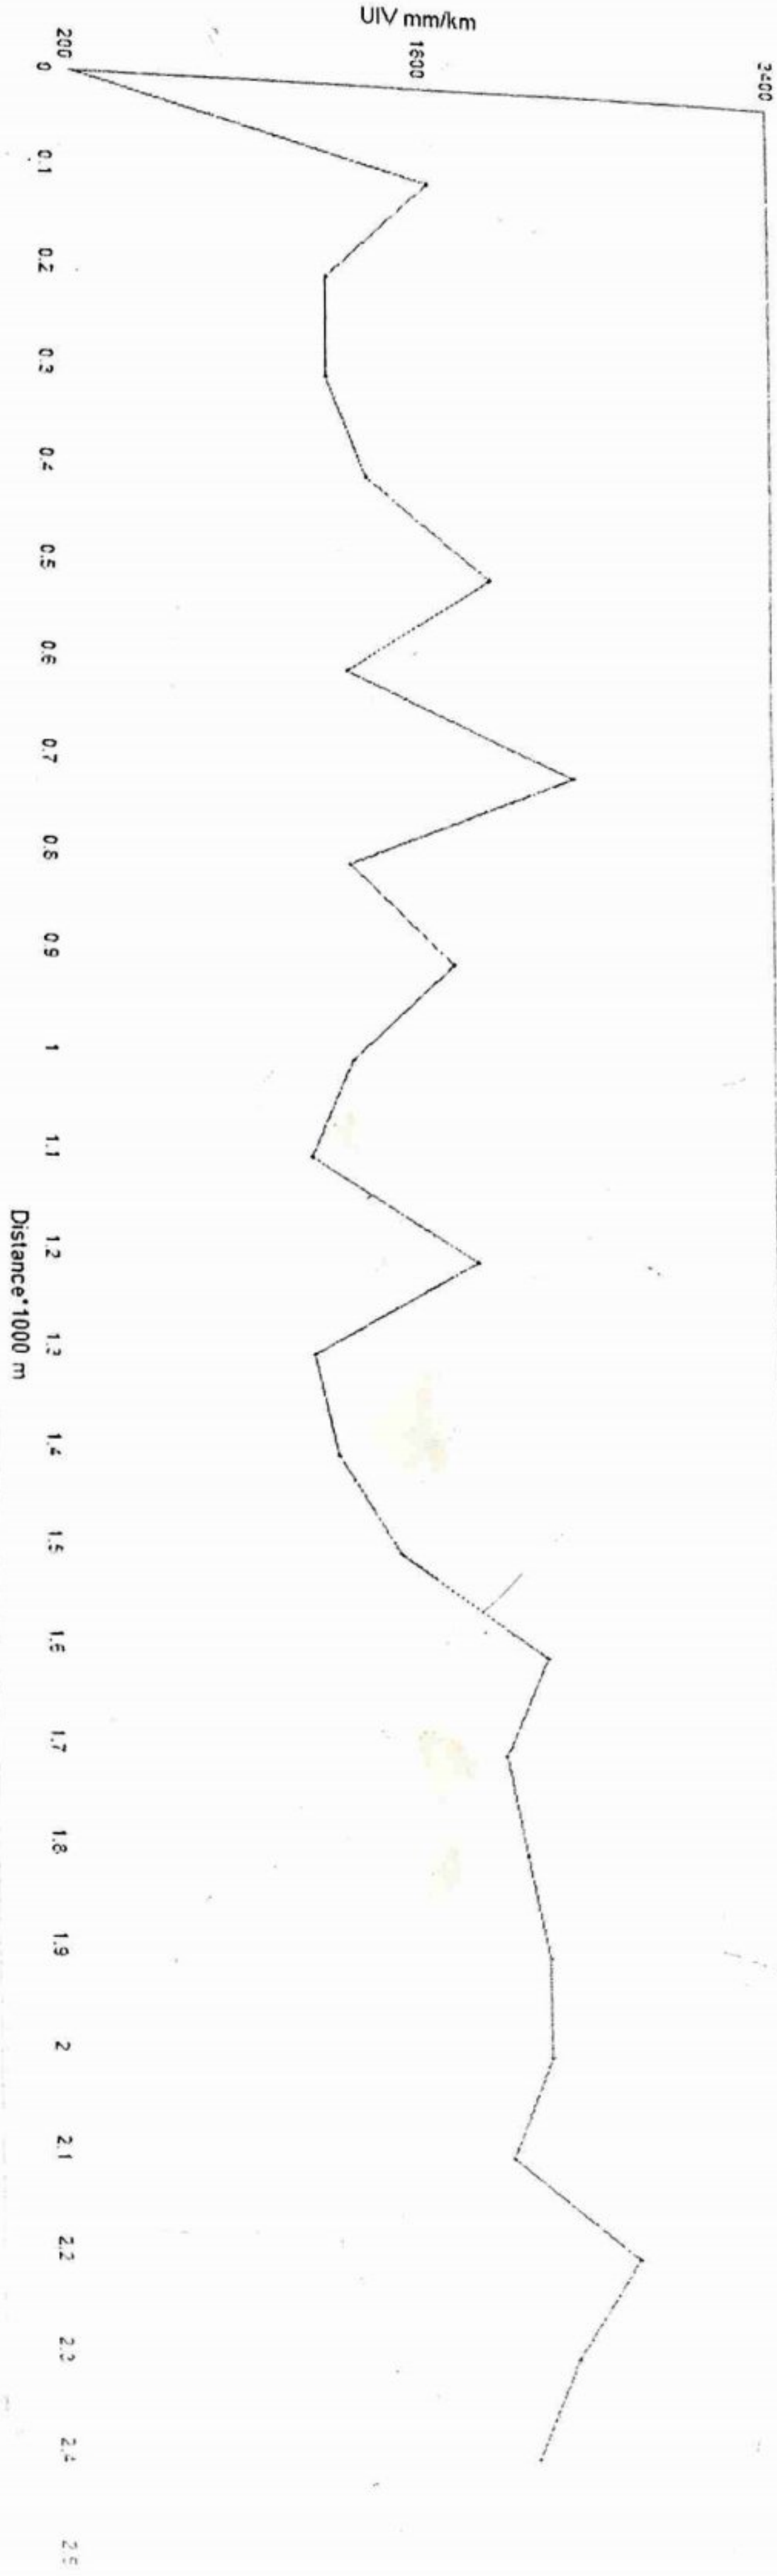

R-2 R-1
18/10/24


18.10.24
Executive Engineer
R.W.D. Works Division
Hatrada
