

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल पुपरी।

पत्रांक:- 3032 / पुपरी दिनांक:- 19/12/2024

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, पुपरी

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी -सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण, पटना।
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:-

MR-3054-BIHAR RURAL ROAD NEW MAINTENANCE POLICY-2018 योजना
अंतर्गत निर्माण कार्य की राशि के अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054-BIHAR RURAL ROAD
NEW MAINTENANCE POLICY-2018 योजना अंतर्गत संलग्न सुची के आधार पर पथ में निर्माण
कार्य की राशि का आवंटन उपलब्ध कराने की कृपा की जाए।

अनु०- यथोक्त।

विश्वासभाजन

19/12/24
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पुपरी
19/12/24

Requisition for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018.

Name of Division- RWD (W) Division Pupri

Name of Division- RWD (W) Division Pupri																		
Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lakh)	5 years Routine Maintenance (in Lakh)	Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer / PCC Layer (in mm)	Value of Bitumen Content in Percentage / Grade of Concrete	Previous Total Allocated Amount (in Lakh)	Up-to date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)												
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/SI/PUP/24/0008	LD39-Harpurwa to Bhagwanpur - Harpurwa (NR26)	31607802043	6515 dt-26.12.2023	4.200	189.48	139.08637	40.74984	13 MBD/2024-25 26.09.2024	25.06.2025	-	2659	25 / 125	5% / M30	0.00000	0.00000	95.00000	

Executive Engineer,
R.W.D. (W) Division,
Pupri
19/11/2024

Name of work : L039-Harpurwa to Bhagwanpur - Harpurwa (VR26)															
Name of customer : Tathagat Construction Private Limited															
(R) Rural Road															
Good					Average					Poor					
< 4000					4001 - 5000					> 5000					
Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(cm)	Speed(Km/Hr)	Ultima(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
10-12-2024	11:45:29	26	100	100	28.0 cm	3.9 Km/Hr	2800.0 mm/Km	2921	3.83	Good	26.553408	N	85.614143	E	Normal
10-12-2024	11:45:48	26	100	200	30.0 cm	10.1 Km/Hr	3000.0 mm/Km	3106	4.16	Good	26.553285	N	85.614082	E	Normal
10-12-2024	11:46:06	26	100	300	22.0 cm	12.2 Km/Hr	2200.0 mm/Km	2365	3.26	Good	26.553263	N	85.614093	E	Normal
10-12-2024	11:46:27	26	100	400	21.0 cm	16.2 Km/Hr	2100.0 mm/Km	2273	3.14	Good	26.553337	N	85.614081	E	Normal
10-12-2024	11:46:46	26	100	500	23.0 cm	20.3 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.551037	N	85.613608	E	Normal
10-12-2024	11:47:03	26	100	600	29.0 cm	16.4 Km/Hr	2600.0 mm/Km	3014	4.04	Good	26.546353	N	85.611148	E	Normal
10-12-2024	11:47:20	26	100	700	25.0 cm	18.3 Km/Hr	2500.0 mm/Km	2643	3.6	Good	26.543957	N	85.611228	E	Normal
10-12-2024	11:47:37	26	100	800	32.0 cm	18.8 Km/Hr	3200.0 mm/Km	3291	4.38	Good	26.5434	N	85.610533	E	Normal
10-12-2024	11:47:54	26	100	900	26.0 cm	24.3 Km/Hr	2600.0 mm/Km	2736	3.71	Good	26.545762	N	85.610685	E	Normal
10-12-2024	11:48:11	26	100	1000	28.0 cm	25.7 Km/Hr	2800.0 mm/Km	2921	3.93	Good	26.543838	N	85.609691	E	Normal
10-12-2024	11:48:25	26	100	1100	20.0 cm	20.2 Km/Hr	2000.0 mm/Km	2160	3.03	Good	26.543905	N	85.601693	E	Normal
10-12-2024	11:48:36	26	100	1200	23.0 cm	23.1 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.543888	N	85.601788	E	Normal
10-12-2024	11:48:53	26	100	1300	27.0 cm	27.5 Km/Hr	2700.0 mm/Km	2628	3.82	Good	26.556439	N	85.592459	E	Normal
10-12-2024	11:49:07	26	100	1400	29.0 cm	27.6 Km/Hr	2900.0 mm/Km	3014	4.04	Good	26.556581	N	85.592481	E	Normal
10-12-2024	11:49:21	26	100	1500	21.0 cm	27.5 Km/Hr	2100.0 mm/Km	2273	3.14	Good	26.556592	N	85.592481	E	Normal
10-12-2024	11:49:35	26	100	1600	30.0 cm	23.9 Km/Hr	3000.0 mm/Km	3106	4.16	Good	26.557246	N	85.59283	E	Normal
10-12-2024	11:49:46	26	100	1700	19.0 cm	21.7 Km/Hr	1900.0 mm/Km	2088	2.91	Good	26.558014	N	85.5928	E	Normal
10-12-2024	11:50:01	26	100	1800	27.0 cm	24.4 Km/Hr	2700.0 mm/Km	2628	3.82	Good	26.558196	N	85.592555	E	Normal
10-12-2024	11:50:14	26	100	1900	28.0 cm	25.8 Km/Hr	2800.0 mm/Km	2921	3.93	Good	26.558713	N	85.592701	E	Normal

8mm/11H
10/12/24
AE

18/11/24

Name of work : LC39-Harpurwa to Bhagwanpur - Harpurwa (VR26)															
Name of customer : Tathagat Construction Private Limited															
(R)Rural Road															
Good					Average					Poor					
< 4000					4001 - 5000					> 5000					
10-12-2024	1150.27	26	100	2000	26.0 cm	28.8 Km/Hr	2600.0 mm/Km	2736	3.71	Good	26.559286	N	85.593013	E	Normal
10-12-2024	1150.40	26	100	2100	23.0 cm	28.8 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.560087	N	85.59565	E	Normal
10-12-2024	1150.53	26	100	2200	27.0 cm	20.8 Km/Hr	2700.0 mm/Km	2828	3.82	Good	26.560671	N	85.593665	E	Normal
10-12-2024	1151.08	26	100	2300	24.0 cm	24.4 Km/Hr	2400.0 mm/Km	2550	3.49	Good	26.545457	N	85.590535	E	Normal
10-12-2024	1151.25	26	100	2400	30.0 cm	26.5 Km/Hr	3000.0 mm/Km	3108	4.16	Good	26.545853	N	85.589505	E	Normal
10-12-2024	1151.41	26	100	2500	24.0 cm	23.9 Km/Hr	2400.0 mm/Km	2550	3.49	Good	26.54591	N	85.588803	E	Normal
10-12-2024	1151.57	26	100	2600	18.0 cm	25.9 Km/Hr	1800.0 mm/Km	1995	2.8	Good	26.545832	N	85.588455	E	Normal
10-12-2024	1152.13	26	100	2700	19.0 cm	22.6 Km/Hr	1900.0 mm/Km	2088	2.91	Good	26.545832	N	85.588455	E	Normal
10-12-2024	1152.28	26	100	2800	21.0 cm	24.1 Km/Hr	2100.0 mm/Km	2273	3.14	Good	26.544287	N	85.586335	E	Normal
10-12-2024	1152.45	26	100	2900	23.0 cm	24.9 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.545105	N	85.582183	E	Normal
10-12-2024	1152.62	26	100	3000	27.0 cm	25.7 Km/Hr	2700.0 mm/Km	2828	3.82	Good	26.545105	N	85.582183	E	Normal
10-12-2024	1153.19	26	100	3100	31.0 cm	24.0 Km/Hr	3100.0 mm/Km	3199	4.27	Good	26.545832	N	85.588455	E	Normal
10-12-2024	1153.36	26	100	3200	26.0 cm	22.9 Km/Hr	2600.0 mm/Km	2736	3.71	Good	26.54537	N	85.583888	E	Normal
10-12-2024	1153.53	26	100	3300	23.0 cm	23.8 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.54537	N	85.580888	E	Normal
10-12-2024	1154.11	26	100	3400	25.0 cm	20.2 Km/Hr	2500.0 mm/Km	2843	3.6	Good	26.545832	N	85.588455	E	Normal
10-12-2024	1154.26	26	100	3500	19.0 cm	22.9 Km/Hr	1900.0 mm/Km	2088	2.91	Good	26.54528	N	85.585647	E	Normal
10-12-2024	1154.47	26	100	3600	28.0 cm	22.3 Km/Hr	2800.0 mm/Km	2821	3.89	Good	26.54528	N	85.585647	E	Normal
10-12-2024	1155.01	26	100	3700	29.0 cm	22.9 Km/Hr	2900.0 mm/Km	3014	4.04	Good	26.54508	N	85.585298	E	Normal
10-12-2024	1155.15	26	100	3800	29.0 cm	22.0 Km/Hr	2900.0 mm/Km	3014	4.04	Good	26.54508	N	85.585298	E	Normal
10-12-2024	1155.28	26	100	3900	24.0 cm	18.9 Km/Hr	2400.0 mm/Km	2550	3.49	Good	26.544812	N	85.585508	E	Normal

19/11/24
863


19/11/24

Name of work		: L039-Harpurwa to Bhagwanpur - Harpurwa (VR26)													
Name of customer		Tathagat Construction Private Limited													
		(R)Rural Road													
		* Good		Average		Poor									
		< 4000		4001 - 5000		> 5000									
10-12-2024	11 55 55	20	100	4000	23.0 cm	14.7 Km/hr	2300.0 mm/Km	24.55	3.37	Good	20.544312	N	85.585508	E	Normal

Signature
19/12/24

19/12/24

Name of Customer: Talhagar Construction Private Limited, Machine no: 19199, Road: L039 Harpura to Bhagwanpur - Harpura (VR26), Date: 10-12-24, Section No: 26, Equation: $Y=0.926X+128.1$

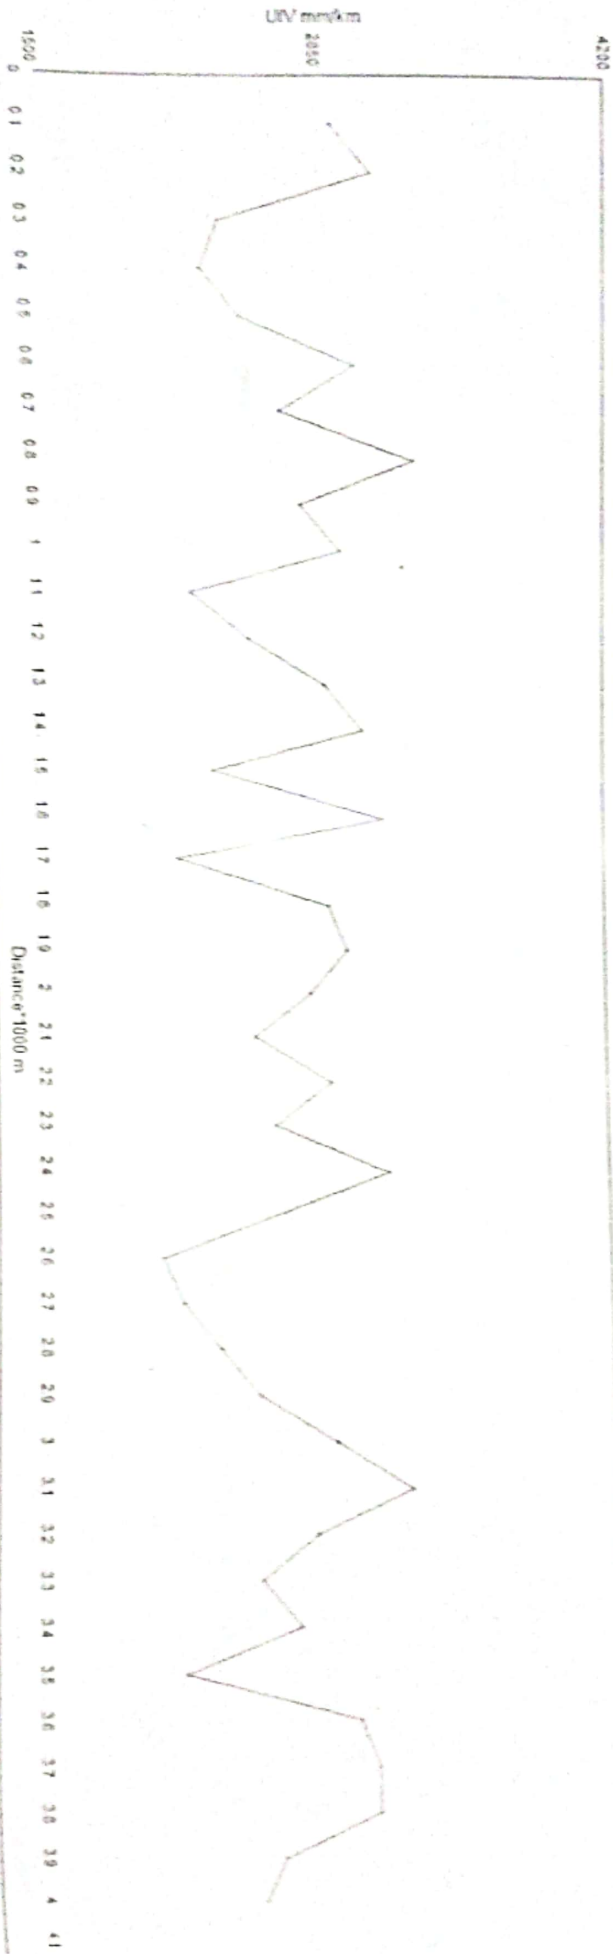

Passively
19/12/24
ATE

15/12/24
