

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सोनपुर

Mob No :- 8986915436

E.Mail :- eerwdsonpur@gmail.com

पत्रांक1294.....

सोनपुर, दिनांक 02-07-2024

प्रेषक,

ई0 अशोक कुमार
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर।

सेवा में,

नोडल पदाधिकारी (3054),
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय:- बिहार ग्रामीण पथ अनुरक्षण निति-2018 के तहत स्वीकृत योजना में
आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपर्युक्त विषयक ग्रामीण कार्य विभाग कार्य प्रमंडल सोनपुर के अंतर्गत बिहार
ग्रामीण पथ अनुरक्षण निति-2018 के तहत स्वीकृत योजना के क्रियान्वयन हेतु आवंटन की
मांग विहित प्रपत्र में तैयार कर भेजी जा रही है।

अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की
जाये।

अनु0:-उपयोगिता प्रमाण-पत्र।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर


07/07/24

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the month of **July-2024**
PIU:- E.E.,R.W.D. Works Division Sonapur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18		8793.49618	Certified that out of Rs 8793.49618 lakh received during the years 2020-21 to 2023-24 in favour of E.E.R.W.D. works division Sonapur a sum of Rs 8788.39194 Lakh has been utilized for the purpose of New Maintenance Policy-18 Scheme as given in the margin for which it was sanctioned and that the balance of Rs 5.10424 Lakh remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.




D.A.O-I

R.W.D. Works Division Sonpur.



EXECUTIVE ENGINEER

R.W.D. Works Division Sonpur.



Requisition Formate for Scheme Head - MR-3054 Under Bihar Rural Road Maintenance Policy 2018 (In Rectification and surface Renewal)																			
Division Name:- Rural Works Department, Works Division- Sonpur																			
Sl.No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lac)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content In %	Previous Total Allotted Amount (In Lac)	Upto date expenditure as per MIS (In Lac)	Requisition against Work Done (In Lac)	Remarks	
					Length (in Km.)	Amount (In Lac)	Initial Rectification on with Surface Renewal (In Lac)	5 Years Routine Maintenance (In Lac)											
1	RM/SA/SON/23/0008	L060 - Nunfar To Sisaumi (VR38)	31306402107	1797 20.03.23	1.750	113.117	67.53559	24.16235	08/MBD/2023-24 14.09.2023	13.06.2024	-	3028	25	5.03	0.00000	0.00000	67.44016		
TOTAL																		67.44016	

Signature

D.A.O-I

R.W.D Works Div- Sonpur

Signature

Executive Engineer

R.W.D Works Div- Sonpur


01/11/24


कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

का0आ0सं0.....1294.....सोनपुर, दिनांक 02-07-2024.....

कार्यालय आदेश

प्रमाणित किया जाता है कि बिहार ग्रामीण पथ अनुरक्षण निती-2018 योजनान्तर्गत L060 - Nunfar To Sisauni (VR38) (Project ID-31306402107) का कार्य गुणवत्ता एवं विशिष्टियों के अनुरूप पूर्ण कराया गया है। पथ के मापीपुस्त की जाँच मेरे द्वारा 25 प्रतिशत एवं सहायक अभियंता के द्वारा 50 प्रतिशत एवं कनीय अभियंता के द्वारा शत प्रतिशत किया गया है।


13.6.24
कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा दरियापुर


13/6/24
सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल दरियापुर


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

Name of work		: L060 - Nunfar To Sisauni (VR38)													
Name of customer		: Raj Kumar Rai													
(R)Rural Road															
Good		Average		Poor											
< 4000		4001 - 5000		> 5000											
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
07/06/24	13:19:28	42	0	0	0.0 cm	3.6 Km/Hr	0.0 mm/Km	127	0.24	Good	25.848134	N	84.944505	E	Normal
07/06/24	13:19:47	42	100	100	28.0 cm	19.0 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.847949	N	84.944563	E	Normal
07/06/24	13:20:09	42	100	200	34.0 cm	16.2 Km/Hr	3400.0 mm/Km	3283	4.37	Good	25.847131	N	84.944101	E	Normal
07/06/24	13:20:30	42	100	300	36.0 cm	17.8 Km/Hr	3600.0 mm/Km	3468	4.59	Good	25.846169	N	84.943488	E	Normal
07/06/24	13:21:47	42	100	400	37.0 cm	24.8 Km/Hr	3700.0 mm/Km	3561	4.69	Good	25.8445536	N	84.843181	E	Normal
07/06/24	13:22:06	42	100	500	32.0 cm	18.2 Km/Hr	3200.0 mm/Km	3097	4.14	Good	25.844774	N	84.943173	E	Normal
07/06/24	13:22:36	42	100	600	38.0 cm	12.7 Km/Hr	3800.0 mm/Km	3654	4.8	Good	25.844138	N	84.943587	E	Normal
07/06/24	13:23:03	42	100	700	33.0 cm	13.1 Km/Hr	3300.0 mm/Km	3190	4.26	Good	25.843358	N	84.942933	E	Normal
07/06/24	13:23:30	42	100	800	26.0 cm	13.7 Km/Hr	2600.0 mm/Km	2540	3.47	Good	25.846921	N	84.944980	E	Normal
07/06/24	13:23:55	42	100	900	29.0 cm	14.2 Km/Hr	2900.0 mm/Km	2819	3.81	Good	25.846943	N	84.945368	E	Normal
07/06/24	13:24:14	42	100	1000	35.0 cm	18.4 Km/Hr	3500.0 mm/Km	3375	4.48	Good	25.846526	N	84.948288	E	Normal
07/06/24	13:25:52	42	100	1100	34.0 cm	23.7 Km/Hr	3400.0 mm/Km	3283	4.37	Good	25.845878	N	84.947766	E	Normal
07/06/24	13:26:22	42	100	1200	36.0 cm	12.1 Km/Hr	3600.0 mm/Km	3468	4.59	Good	25.844958	N	84.946841	E	Normal
07/06/24	13:26:41	42	100	1300	28.0 cm	19.0 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.844188	N	84.946295	E	Normal
07/06/24	13:27:21	42	100	1400	32.0 cm	28.7 Km/Hr	3200.0 mm/Km	3097	4.14	Good	25.843444	N	84.945767	E	Normal
07/06/24	13:27:41	42	100	1500	35.0 cm	18.0 Km/Hr	3500.0 mm/Km	3375	4.48	Good	25.842657	N	84.945317	E	Normal
07/06/24	13:29:30	42	100	1600	29.0 cm	23.2 Km/Hr	2900.0 mm/Km	2819	3.81	Good	25.842317	N	84.944558	E	Normal
07/06/24	13:29:46	42	100	1700	32.0 cm	21.1 Km/Hr	3200.0 mm/Km	3097	4.14	Good	25.842563	N	84.944292	E	Normal
07/06/24	13:29:58	42	50	1750	25.0 cm	30.6 Km/Hr	2500.0 mm/Km	2447	3.36	Good	25.842705	N	84.944329	E	Normal


Signature
8/11/24

8-6-24
02

8/7/24/24

Executive Engineer
R.W.D. Works Division Sonapur

Name of Customer: Raj Kumar Rai, Machine no: 19205, Road: L060 - Nunfar To Sisauni (VR39), Date: 07-06-24, Section No: 42, Equation: $Y=0.923X+127.3$

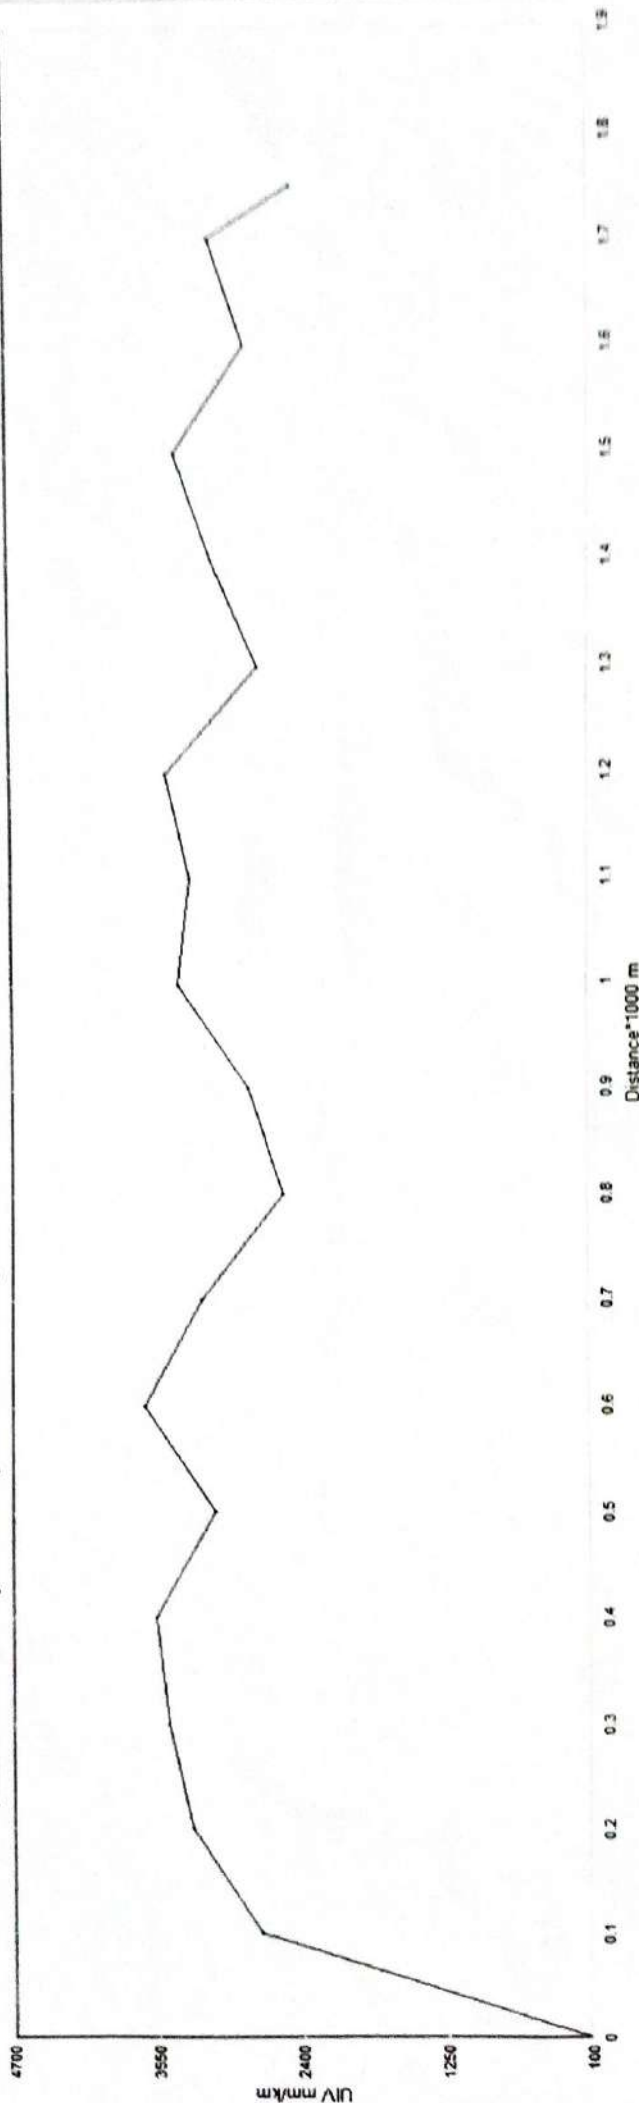

[Signature]


Executive Engineer
R.W.D. Works Division Sonapur

[Signature]
8/11/24

[Signature]
8-6-24

[Signature]
07/06/24

Name of Customer: Raj Kumar Rai, Machine no: 19205, Road: L060 - Nunfar To Sisauni (VR38), Date: 07-06-24, Section No: 42, Equation: $Y=0.928X+127.3$

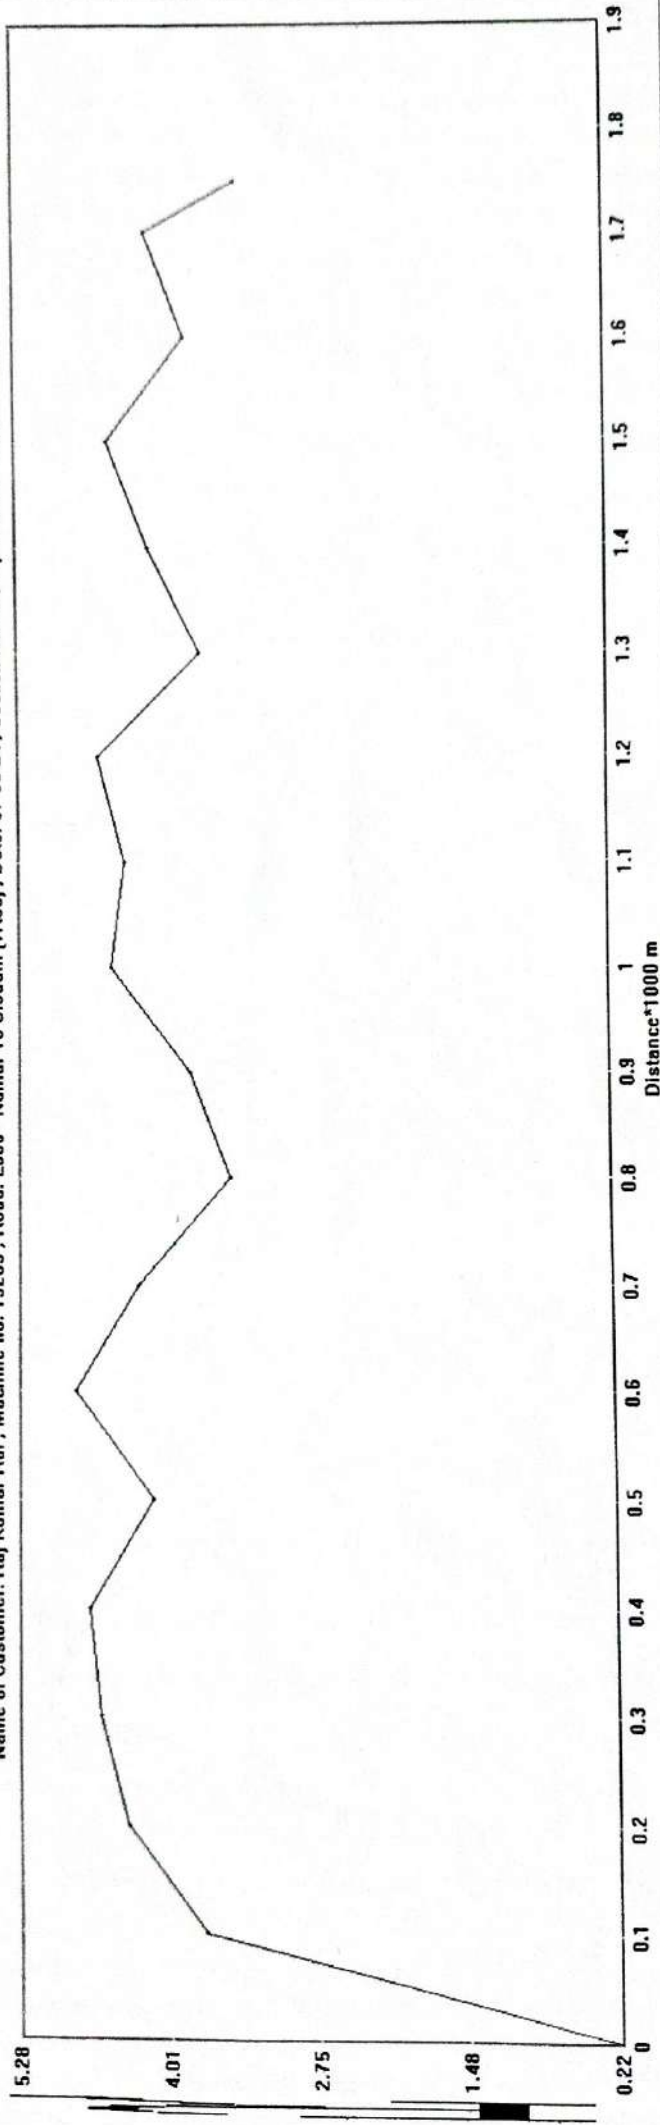

Raj
21/08/24

Executive Engineer
R.W.D. Works Division Sonapur

Raj
21/08/24

Raj
21/08/24

Raj
07/06/24

1.

Name of work -

Situation of work -

Agency by which work is executed -

Date of measurement -

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement			Contents of area
	No.	L	B or D.	
Name of work: - M.R. of Road				
from Number to Sisauri				
Agency: - Raj Kumar Rai				
Ag No: - 08/MBD/2023-24				
Date of start: 11.09.2023				
Date of Comp: - 18.06.2024				

① clearing and grubbing
of R/L Canal - old - all compounds

$$2 \times 5 \times 30.0 \times 0.750 = 225.00 \text{ m}^2$$

$$2 \times 10 \times 30.0 \times 0.750 = 450.00$$

$$2 \times 10 \times 30.0 \times 0.750 = 450.00$$

$$2 \times 10 \times 30.0 \times 0.750 = 450.00$$

$$2 \times 10 \times 30.0 \times 0.750 = 450.00$$

$$2 \times 10 \times 30.0 \times 0.750 = 450.00$$

$$2 (3 \times 30.0 + 10) \times 0.750 = 150.00$$

$$2625.00 \text{ m}^2$$

$$\text{or } 0.2625 \text{ Hae}$$

2.4.24
or

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
(11) 600 mm x 400 mm					
23 Rect					
04 No @ R 4308.38/ea					17234.0
(14) 900 mm Side octa					
24 gonal					
02 No @ R 8777.74/ea					17555.4
(35) P.M and Placing					
30 typical cast +					
mount beam					
2 ea (38) P-17					
02 No @ R 11015.90/ea					22032.0

Total R					6252214.0
					6251216.0
					1125219.0
Add 18% GST @ R					1125399.0
					62512.0
Add 1% L. cost @ R					62522.0
					54404.0
S. fee @					55902.0
					7496037.0
					7493351.0
Less 10% Retention @ R					749604.0
					749335.0
					6746433.0
					6744016.0
Total					13.624
					07
Signature					13/6/24

Continuation
