

ctif

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, उदाकिशुनगंज
पत्रांक.....1111.....उदाकिशुनगंज, दिनांक.....21/08.....2024

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल-उदाकिशुनगंज ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी --सह- सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :-MR New maintenance Policy 2018 योजना से संबंधित कार्यों के भुगतान हेतु आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त बिषयक संबंध में कहना है, कि ग्रामीण कार्य विभाग, कार्य प्रमण्डल उदाकिशुनगंज में **MR New maintenance Policy 2018** योजना के अंतर्गत चल रहे कार्यों के भुगतान हेतु विहित प्रपत्र में अधियाचना पत्र तैयार कर समर्पित किया जाता है। अतः अनुरोध है, कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय, ताकि संवेदक को भुगतान किया जा सके।

अनु०:- यथोक्त विहित प्रपत्र में।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल उदाकिशुनगंज।

29.08.24

FORM GFR 19-A

Letter No-

Date-

(See Government of India's Decision (1) below Rule-150)

Form of Utilisation Certificate up to 30 June 2024

New MR 2018

Executive Engineer Rural Works Department Works Division Udakishunganj

SI No	Name of Scheme	Sanction No.& Date with Amount (in Rs. Lacs)	Amount Received (in Rs. lac)	particulars
1	New MR 2018	Secretary-Cum-Empowered Officer BRRDA, Patna Letter No-68 WE Date- 06.05.2024	8946.75348	Certified that Rs:- 8946.75348 Lac received Till the date in favour of Executive Engineer, RWD Work Division Udakishunganj. A sum of Rs. 8946.75348 Lac has been utilized for the purpose of New MR 2018 Scheme as given in the margin for which it was sanctioned and that the balance of Rs. 0.0 Lacs remaining .
TOTAL			8946.75348	

2. Certified that I have satisfied myself that conditions on which the grants in -aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.
kind of checks exercised:-

- (i) Works have been supervised by Executive Engineer
- (ii) periodical inspection has been conducted by Executive Engineer
- (iii) construction material have been tested.
- (iv) Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer,
- (v) All other codal formalities have been observed.

3. Physical progress achieved: as per progress report.

D.A.O
Rural Works Department
Works Division Udakishunganj

Executive Engineer
Rural Works Department
Works Division Udakishunganj

29/06/24

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Udakishunganj

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allocated Amount (Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (in lac)	Remarks
					Length (in Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (in lac)										
1	RM/MA/UD A/24/0002	T05 - SARAUINI KALA	21004802025	6120 Dt. 04.12.23	1.75	97.446	86.85945	13.21025	37MBD/23-24	12/13/2024	25.06.24	3474.47	25mm	5%	0	0	86.80000	Comp.
2	RM/MA/UDA/24/0002	Gwalpara Bazar To Nohar Kali Mandir Triloki Asthan Sahpur Bhagwati Asthan	21004812037	6120 Dt. 04.12.23	1.78	106.065	88.84635	15.98375	37MBD/23-24	12/13/2024	25.06.24	3432.50	25mm	5%	0	0	88.80000	Comp.
3	RM/MA/UD A/24/0002	Reo Path Sindhawari To Balwa Mushari	21004813017	6120 Dt. 04.12.23	1.56	94.235	81.36219	13.04910	37MBD/23-24	12/13/2024	25.06.24	3397.86	25mm	5%	0	0	81.00000	Comp.
4	RM/MA/UDA/19/0001	Road from khandar basa kabai basa via chandra sara to Alamnagar Kara PWD Road.	21004801011	2170DDt. 06.07.2019	2.505	120.4856	85.459	25.06864	01MBD/2020-21 Dt.23.01.2021	22.10.2021	26.06.24	3459.68	25mm	5%	20.60079	20.60079	64.80000	Comp.
																	321.40000	

**D.A.O
RWD Works Division
Udakishunganj**

**Executive Engineer
RWD Works Division
Udakishunganj**

[Handwritten Signature]
25.06.24

Name of Raod:-Const of Road from khantar basa kabai basa via chandra sara to Alamnagar Kara PWD Road .

Name of Contractor:-Rahul Kumar

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
26/6/24	11:56:27	24	0.1	300	30.3	3000	3540	G	4.66 25.61239	86.85614	Normal
26/6/24	11:56:38	24	0.1	310	30.3	3000	3269	G	4.8 25.61233	86.85551	Normal
26/6/24	11:56:47	24	0.1	300	40.4	3000	3540	G	4.66 25.61179	86.85545	Curve
26/6/24	11:57:0	24	0.1	340	40.4	2900	3594	G	5.19 25.61110	86.85556	Normal
26/6/24	11:57:11	24	0.1	320	40.4	3200	3767	G	4.93 25.61028	86.85572	Normal
26/6/24	11:58:23	24	0.1	320	30.2	3200	3767	G	4.93 25.60970	86.85594	Curve
26/6/24	11:59:0	24	0.1	300	30.2	3000	3540	G	4.66 25.60979	86.85527	Normal
26/6/24	11:59:12	24	0.1	310	30.3	2600	3054	G	4.8 25.60988	86.85457	Normal
26/6/24	11:59:34	24	0.1	320	30.3	3200	3767	G	4.93 25.60989	86.85374	Normal
26/6/24	11:59:44	24	0.1	290	30.3	2900	3426	G	4.53 25.61036	86.85296	Normal
26/6/24	12:0:0	24	0.1	280	20.2	2800	3313	G	4.4 25.61160	86.85268	Normal
26/6/24	12:0:9	24	0.1	220	10.1	2200	2631	G	3.58 25.61166	86.85237	Culvert
26/6/24	12:0:44	24	0.1	270	20.2	2700	3199	G	4.26 25.61146	86.85154	Normal
26/6/24	12:0:53	24	0.1	280	30.3	2800	3313	G	4.4 25.61169	86.85036	Normal
26/6/24	12:1:0	24	0.1	310	30.3	3100	3654	G	4.8 25.61181	86.84919	Normal
26/6/24	12:1:0	24	0.1	310	30.3	3100	3654	G	4.8 25.61181	86.84849	Normal
26/6/24	12:1:20	24	0.1	320	30.3	3200	3767	G	4.93 25.61160	86.84758	Normal
26/6/24	12:1:27	24	0.1	320	30.3	3200	3767	G	4.93 25.61034	86.84725	Normal
26/6/24	12:1:36	24	0.1	330	30.3	2800	3381	G	5.06 25.60991	86.84564	Normal
26/6/24	12:2:0	24	0.1	330	30.3	2800	3381	G	5.06 25.60897	86.84421	Normal
26/6/24	12:2:12	24	0.1	300	30.3	3000	3540	G	4.66 25.60888	86.84338	Normal
26/6/24	12:2:18	24	0.1	330	30.3	2800	3381	G	5.06 25.60966	86.84299	Normal
26/6/24	12:2:30	24	0.1	310	30.3	2600	3054	G	4.8 25.61026	86.84244	Normal
26/6/24	12:2:41	24	0.1	290	30.3	2900	3426	G	4.53 25.61078	86.84188	Normal
26/6/24	12:2:52	24	0.1	320	30.3	3200	3767	G	4.93 25.61130	86.83943	Normal
Average IRI=							3459.68				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 2800$$

$$Y = 3313$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

26/6/24
S.E

26/6/24
A.E

→ . G . →

Name of Customer : Rahul Kumar
 Name of Work/ Road : to Alamnagar Kara PWD Road
 Lab Job number : 26-Jun-24
 Date : 24
 Section No. : 24



Test Date : 26-Apr-24 Road Name : to Alamnagar Kara PWD Road
 Machine No : 924 Road Type : (R) RURAL ROAD
 Start S No : 1 Side : Interval
 Start E No : 1000 UIV Range : 1631 To 5000 Interval 1000 mm/km
 Weather : 0 To 26 01 * 1000 m
 Start Location : PWD Road Dist Range : 0 To 26 * 1000 m
 End Location : Kabaiya basa Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

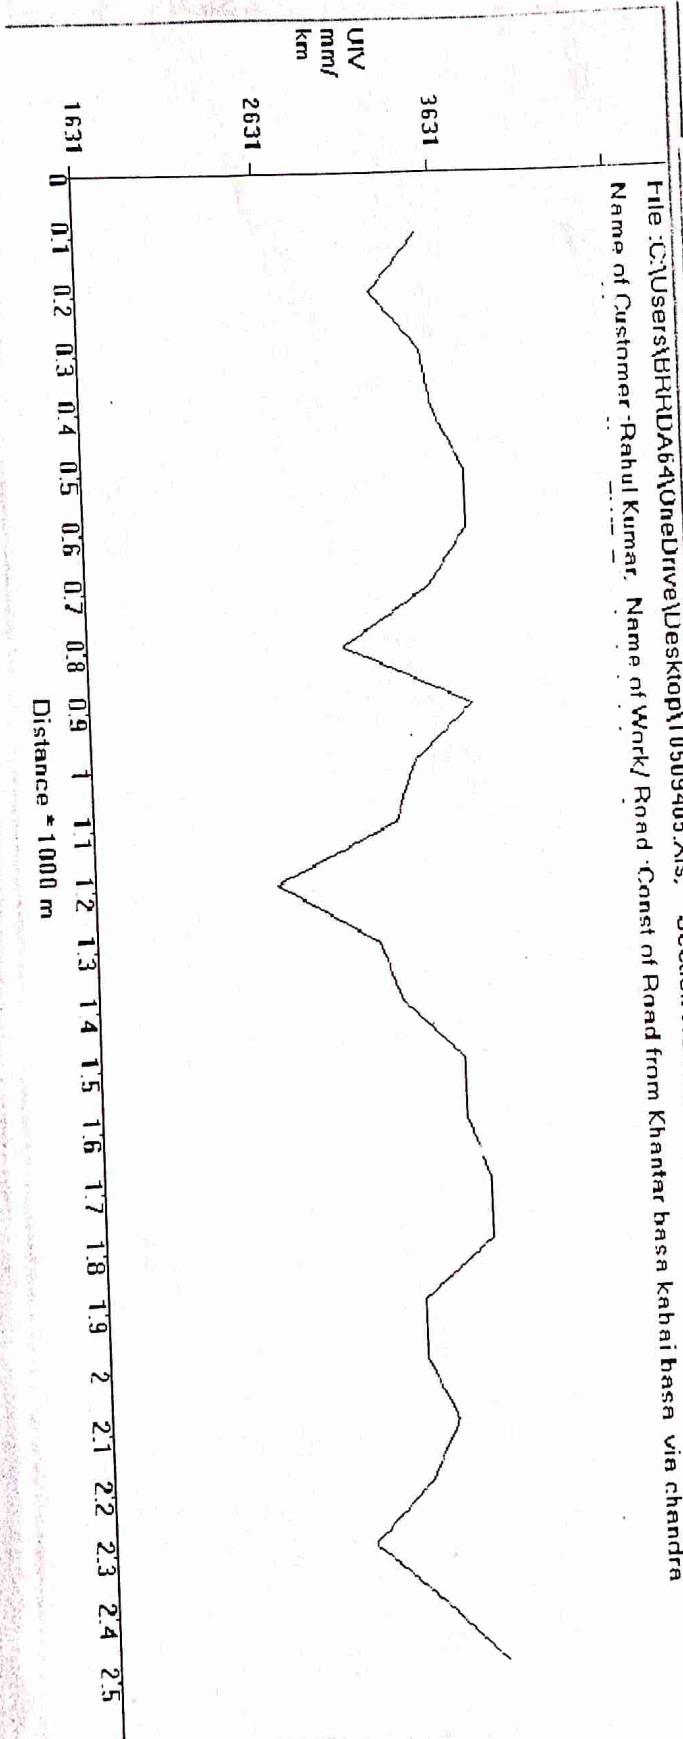

26/6/24
0.1E

26/6/24
AE
