

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, समस्तीपुर
e-mail- eerwdsamastipur@gmail.com

पत्रांक 1464/24 दिनांक 6/7/24

प्रेषक:— कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, समस्तीपुर।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी—सह—सचिव
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:— शीर्ष New Maintenance Policy 2018 मद में आवंटन उपलब्ध कराने के संबंध में।
महाशय,
उपर्युक्त विषयक शीर्ष New Maintenance Policy 2018 योजनान्तर्गत निर्मित/
निर्माणाधीन पथों का विहित प्रपत्र में अधियाचना पत्र संलग्न कर भेजा जा रहा है।

अतः अनुरोध है कि संलग्न अधियाचना पत्र के अनुसार आवंटन उपलब्ध कराने की कृपा
की जाय।
अनु०—यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, समस्तीपुर
6.7.24

FROM GFR 19-A**(See Government of India's Division (I) below Rule- 150)****Form of Utilization Certificate upto 05.07.2024****PIU- E.E., R.W.D. Works Division, Samastipur**

S.N.	Name of Scheme	Sanction No.& Date	Amount Received	Particulars
1	Construction of Rural Road under New Maintenance Policy-2018	Secretary cum Empowered Officer BRRDA Bihar Patna vide upto Lt. n.-82, dt.28.06.2024	1167856945.00	Certified that out of Rs.1167856945.00 received upto 05.07.2024 in favour of Executive Engineer R.W.D. Works Division Samastipur a sum of Rs.1154086624.00 has been utilized for the purpose of New Maintenance Policy-2018 Schemes as given in the margine for which it was sanctioned and that the balance of Rs.13770321.00 remaining unutilized at the end of period under report.
			1,167,856,945.00	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for the which it was sanctioned.

Kind of Checks exercised:-

- i Works have been supervised by Executive/Superintending engineer.
- ii Periodical inspection has been conducted by Executive/Superintending engineer.
- iii Construction materials have been tested.
- iv Measurements have been recorded in the MB's and test check conducted by Assistant Engineer/Executive
- v All other codal formalities have been observed.

3 Physical Progress achieved:-

- i Construction of Road work.
- ii Construction of CD works.

Executive Engineer
Works Division Samastipur
Rural Works Dipartment

Rev.
6.7.24

Requisition Format for scheme Head : MR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division : Samastipur																		
Sl No	Package No	Project ID as Per MIS	Name of Road	Administrative Approval (AA) Letter No & Date	Administrative		Agreement /Amount		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In mm/km)	Thickness of Bitumen Layer (In MM)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (In Lakh)	Upto date Expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (Km)	Amount (In Lakh)	Initial Rectification with Surface Renewal	5 Year Routine Maintenance										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/SA/SAM/24/0005	32010102135	L023-MDR T04 to Shrivastav Supt Cabin	1971 & 31.03.2023	1.350	77.720	55.838	15.939	25(MBD)/2023-24	20.09.2024	Complete	3042	25	5.0	45.00	45.00	10.750	Complete
2		32010102138	L024-MDR T04 to Anant (VR24)		1.550	97.918	68.565	11.208			Complete	2995	25	5.0	55.00	55.00	13.550	Complete
3		NEA22060584	MDR T01 - GOITIY/HH		2.150	119.379	82.438	27.100			Complete	3015	25	5.0	66.00	66.00	16.400	Complete
4		32010112034	T01 Shripad To Primary School Saha Tak		1.410	85.155	68.565	11.208			Complete	3503	25	5.0	55.00	55.00	13.550	Complete
5	RM/SA/SAM/24/0001	NEA220601253	T03 - BELAH	1959 & 31.03.2023	2.400	147.130	103.740	29.260	21(MBD)/2023-24	26.07.2024	Complete	3100	25	5.0	0.00	0	103.500	Complete
6		3201011039553	Chak naka to Hapurwa Wairinagan		3.800	244.050	173.670	46.779			Complete	3008	25	5.0	139.00	139.00	34.600	Complete
7		NEA220601258	MUKTAPUR HATHAURI MOHIDDIN NAGAR		2.770	174.710	119.322	38.683			Complete	3436	25	5.0	96.00	96.00	23.300	Complete
8	RM/SA/SAM/23/0010	32010102114	L035 - 102 to Korwadha Road (VR35)	2328 dt. 04.05.2023	1.550	103.980	82.843	12.068	27(MBD)/2023-24	20.09.2024	Complete	3086	25	5.0	0.00	0	82.500	Complete
9		3201011033109	MORSAND PANCHAYAT BHAWAN TO SARKHAN CHOWK VIA BISWANATH SINGH HOUSE GOKUL TOL SHIV MANDIR		1.400	97.880	86.682	14.508			Complete	3150	25	5.0	0	0	86.500	Complete
10		32010102136	L022-T04 to Gobarsita		2.900	218.879	179.566	23.150			Complete	2929	25	5.0	160.00	160.00	19.400	Complete

1 Signed Hard Copy and Soft Copy (In Excel) of recorded IRI is enclosed.

2 Up-to-date Physical Progress has been uploaded in MIS


Executive Engineer
RWD (W) Div. Samastipur
6.9.24



Steco Analyzer


Name of Customer :	Wakil Ray
Name of Work/Road :	T03-Belahi
Lab Job number :	24
Date :	19.06.2024
Section No. :	24

Test Date :	19.06.2024	Road Name :	T03-Belahi
Machine No :	396	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval	
Weather :		UV Range :	To 4000
Start Location :		Dist Range :	To 2.5
End Location :		Equation :	$Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Redraw Graph

Map View

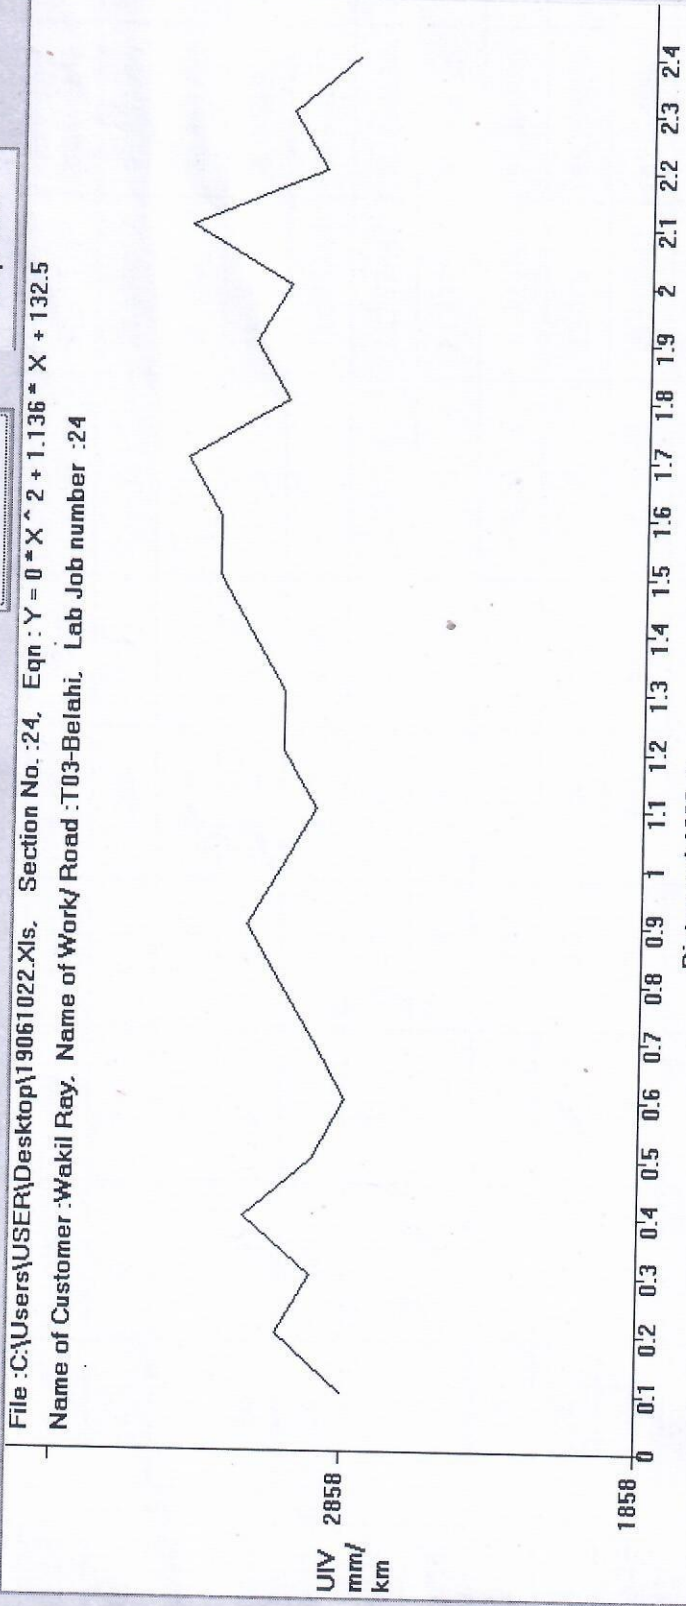

Handwritten signature
19/06/2024

Handwritten signature
19/06/2024

Name of Road :- T03 -Belahi

Section no.-24

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
19/6/24	10:11:7	24	0.1	240	0	2400	2858	G	25.87359	85.895182	Normal
19/6/24	10:11:41	24	0.1	260	10.1	2600	3086	G	25.87448	85.895078	Normal
19/6/24	10:12:19	24	0.1	250	10.1	2500	2972	G	25.877891	85.867131	Normal
19/6/24	10:12:53	24	0.1	270	10.1	2700	3199	G	25.877457	85.867103	Normal
19/6/24	10:13:10	24	0.1	250	10.1	2500	2972	G	25.875238	85.866122	Normal
19/6/24	10:13:44	24	0.1	240	10.1	2400	2858	G	25.875108	85.866145	Normal
19/6/24	10:14:12	24	0.1	250	10.1	2500	2972	G	25.878077	85.867236	Normal
19/6/24	10:14:54	24	0.1	260	10.1	2600	3086	G	25.878124	85.867147	Normal
19/6/24	10:15:11	24	0.1	270	10.1	2700	3199	G	25.878305	85.866335	Normal
19/6/24	10:15:40	24	0.1	260	10.1	2600	3086	G	25.878314	85.866542	Normal
19/6/24	10:16:9	24	0.1	250	10.1	2500	2972	G	25.877377	85.866827	Normal
19/6/24	10:16:46	24	0.1	260	10.1	2600	3086	G	25.877513	85.866765	Normal
19/6/24	10:17:4	24	0.1	260	10.1	2600	3086	G	25.875762	85.865888	Curve
19/6/24	10:17:43	24	0.1	270	10.1	2700	3199	G	25.875578	85.865776	Normal
19/6/24	10:18:5	24	0.1	280	10.1	2800	3313	G	25.877661	85.866982	Normal
19/6/24	10:18:51	24	0.1	280	10.1	2800	3313	G	25.877543	85.866861	Normal
19/6/24	10:19:11	24	0.1	290	10.1	2900	3426	G	25.878057	85.866825	Normal

Handwritten signature and date: 19/6/24

Handwritten signature and date: 19/6/24

Handwritten signature and date: 19/6/24

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
19/6/24	10:19:56	24	0.1	260	10.1	2600	3086	ROAD	25.878145	85.866613	Normal
19/6/24	10:20:15	24	0.1	270	10.1	2700	3199	G	25.87359	85.895182	Normal
19/6/24	10:20:43	24	0.1	260	10.1	2600	3086	G	25.873442	85.895247	Curve
19/6/24	10:21:9	24	0.1	290	10.1	2900	3426	G	25.873544	85.895142	Normal
19/6/24	10:21:44	24	0.1	250	10.1	2500	2972	G	25.878107	85.867288	Curve
19/6/24	10:22:8	24	0.1	260	10.1	2600	3086	G	25.878235	85.867157	Normal
19/6/24	10:22:51	24	0.1	240	10.1	2400	2858	G	25.878443	85.867473	Normal
Total=							2.400 Km	Avg. 3099.83			


 Executive Engineer
 R.W.D.(W) Division,
 Samastipur


 Executive Engineer
 R.W.D.(W) Division,
 Samastipur


 Executive Engineer
 R.W.D.(W) Division,
 Samastipur

19/6/24

19/6/24

19/6/24
