

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, समस्तीपुर
e-mail- eerwdsamastipur@gmail.com

पत्रांक 1464/24 दिनांक 6/7/24

प्रेषक:- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, समस्तीपुर।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:- शीर्ष New Maintenance Policy 2018 मद में आवंटन उपलब्ध कराने के संबंध में।
महाशय,
उपर्युक्त विषयक शीर्ष New Maintenance Policy 2018 योजनान्तर्गत निर्मित/
निर्माणाधीन पथों का विहित प्रपत्र में अधियाचना पत्र संलग्न कर भेजा जा रहा है।

अतः अनुरोध है कि संलग्न अधियाचना पत्र के अनुसार आवंटन उपलब्ध कराने की कृपा
की जाय।
अनु0-यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, समस्तीपुर
6.7.24

FROM GFR 19-A**(See Government of India's Division (I) below Rule- 150)****Form of Utilization Certificate upto 05.07.2024****PIU- E.E., R.W.D. Works Division, Samastipur**

S.N.	Name of Scheme	Sanction No.& Date	Amount Received	Particulars
1	Construction of Rural Road under New Maintenance Policy-2018	Secretary cum Empowered Officer BRRDA Bihar Patna vide upto Lt. n.-82, dt.28.06.2024	1167856945.00	Certified that out of Rs.1167856945.00 received upto 05.07.2024 in favour of Executive Engineer R.W.D. Works Division Samastipur a sum of Rs.1154086624.00 has been utilized for the purpose of New Maintenance Policy-2018 Schemes as given in the margine for which it was sanctioned and that the balance of Rs.13770321.00 remaining unutilized at the end of period under report.
			1,167,856,945.00	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for the which it was sanctioned.

Kind of Checks exercised:-

- i Works have been supervised by Executive/Superintending engineer.
- ii Periodical inspection has been conducted by Executive/Superintending engineer.
- iii Construction materials have been tested.
- iv Measurements have been recorded in the MB's and test check conducted by Assistant Engineer/Executive
- v All other codal formalities have been observed.

3 Physical Progress achieved:-

- i Construction of Road work.
- ii Construction of CD works.


Executive Engineer
Works Division Samastipur
Rural Works Dipartment


6.7.24

Requisition Format for scheme Head : MR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)


RWD, Works Division : Samastipur																			
Sl No	Package No	Project ID as Per MIS	Name of Road	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In mm/km)	Thickness of Bitumen Layer (In MM)	Value of Bitumen Content in Percentage	Previous Total Alotted Amount (In Lakh)	Upto date Expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks	
					Length (Km)	Amount (In Lakh)	Initial Rectification with Surface Renewal	5 Year Routine Maintenance											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	RM/SA/SAM/24/0005	32010102135	L022-MDR T04 to Shrivastav Supt Cabin	1971 & 31.03.2023	1.350	77.720	55.838	15.939	25(MBD)/2023-24	20.09.2024	Complete	3042	25	5.0	45.00	45.00	10.750	Complete	
2		32010102138	L024-MDR T04 to Anraanti (VR24)		1.550	97.918	68.565	11.208			Complete	2995	25	5.0	55.00	55.00	13.550	Complete	
3		NEA22060584	MDR T01 - GOITIY/HH		2.150	119.379	82.438	27.100			Complete	3015	25	5.0	66.00	66.00	16.400	Complete	
4		32010112034	T01 Shrivastav To Primary School Sthla Tak		1.410	85.155	68.565	11.208			Complete	3503	25	5.0	55.00	55.00	13.550	Complete	
5	RM/SA/SAM/24/0001	NEA220601253	T03 - BELAHI	1959 & 31.03.2023	2.400	147.130	103.740	29.260	21(MBD)/2023-24	26.07.2024	Complete	3100	25	5.0	0.00	0	103.500	Complete	
6		3201011039553	Chak nalka to Hapurwa Warishnagar		3.800	244.050	173.670	46.779			Complete	3008	25	5.0	139.00	139.00	34.600	Complete	
7		NEA220601258	MUKTAPUR HATHAURI MOHIDDIN NAGAR		2.770	174.710	119.322	38.683			Complete	3436	25	5.0	96.00	96.00	23.300	Complete	
8	RM/SA/SAM/23/0010	32010102114	L035 - 102 to Korwadha Road (VR35)	2328 dt. 04.05.2023	1.550	103.980	82.843	12.068	27(MBD)/2023-24	20.09.2024	Complete	3086	25	5.0	0.00	0	82.500	Complete	
9		3201011033109	MORSAND PANCHAYAT BHAWAN TO SARIKHAN CHOWK VIA BISWANATH SINGH HOUSE GOKUL TOL SHIV MANDIR		1.400	97.880	86.682	14.508			Complete	3150	25	5.0	0.00	0	86.500	Complete	
10		32010102136	L022-T04 to Gobarsita		2.900	218.879	179.566	23.150			Complete	2929	25	5.0	160.00	160.00	19.400	Complete	

1 Signed Hard Copy and Soft Copy (In Excel) of recorded IRI is enclosed.

2 Up-to-date Physical Progress has been uploaded in MIS


Executive Engineer
RWD (W) Div. Samastipur
6.9.24

Name of Customer: Wakil Ray, Machine no: 19192, Road: Muktapur Hathauri Mohidinagar, Date: 02-05-24, Section No: 15, Equation: $Y=0.889X+355$

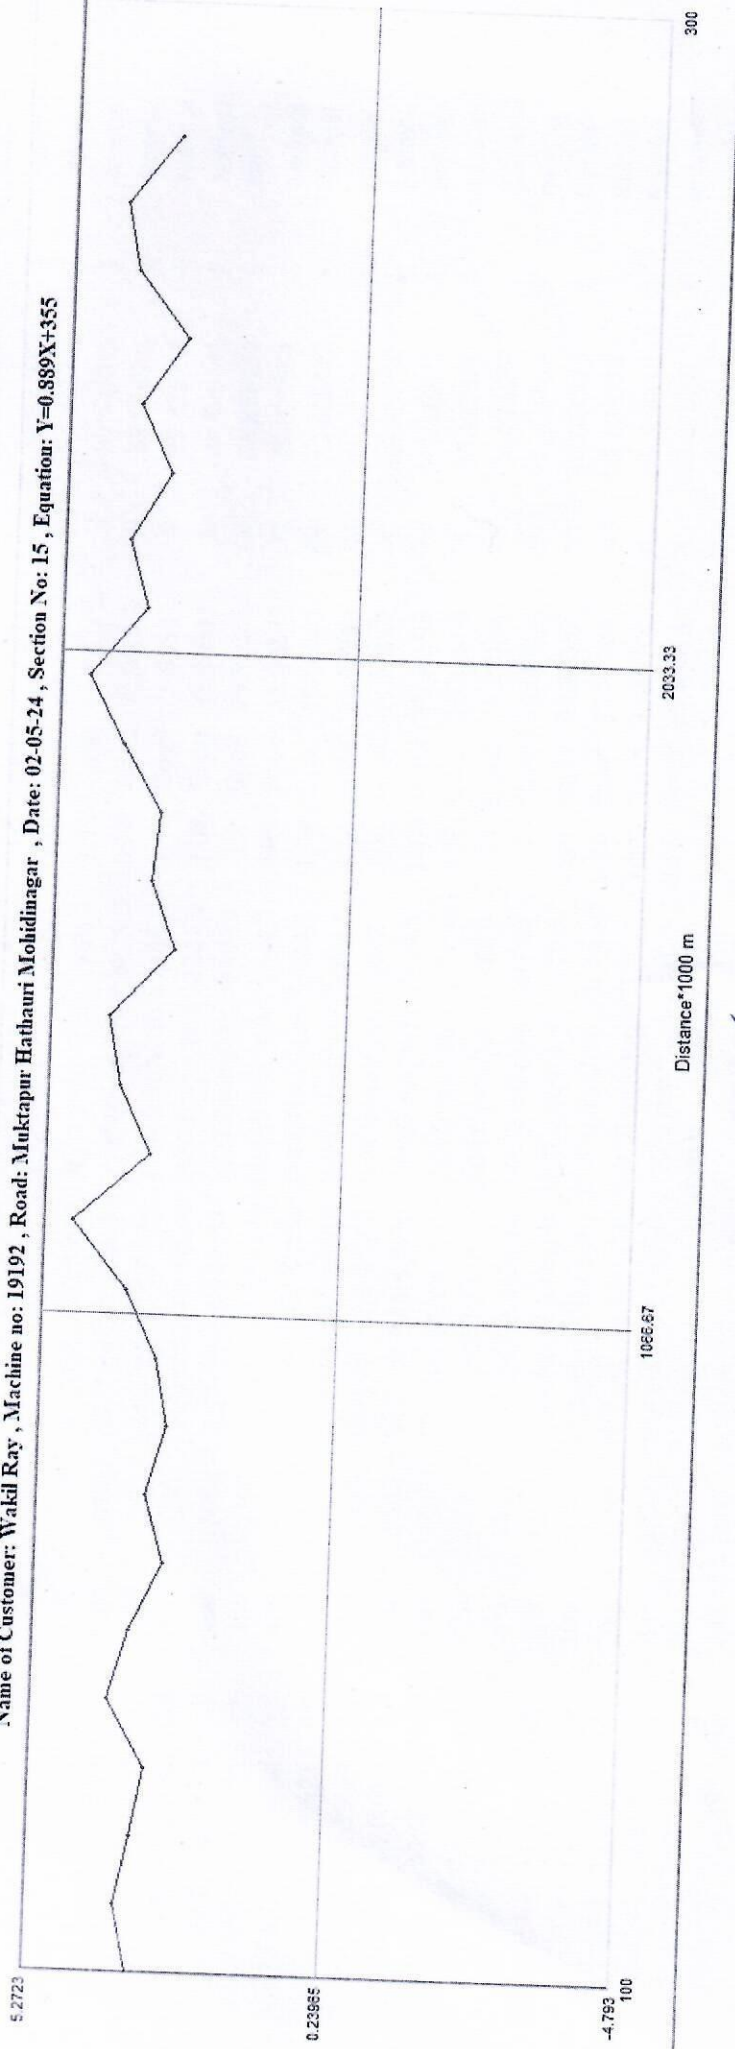

(Signature)
02/05/2024
At

(Signature)
02/05/2024

Name of the work: Muktapur Hathauri Mohidinagar

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed (Km/Hr)	UI (mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
02-05-2024	10:54:16	15	100	100	25.0 cm	11.7 Km/Hr	2500.0 mm/Km	2577.5	3.52	Good	25.90832	N	85.824648	1	Normal
02-05-2024	10:54:41	15	100	200	27.0 cm	14.2 Km/Hr	2700.0 mm/Km	2755.3	3.73	Good	25.90859	N	85.824926	E	Normal
02-05-2024	10:55:03	15	100	300	25.0 cm	16.0 Km/Hr	2500.0 mm/Km	2577.5	3.52	Good	25.90833	N	85.827234	E	Normal
02-05-2024	10:55:21	15	100	400	23.0 cm	20.4 Km/Hr	2300.0 mm/Km	2399.7	3.3	Good	25.90755	N	85.827662	E	Normal
02-05-2024	10:55:39	15	100	500	29.0 cm	19.6 Km/Hr	2900.0 mm/Km	2933.1	3.95	Good	25.90615	N	85.827735	E	Normal
02-05-2024	10:55:54	15	100	600	26.0 cm	24.3 Km/Hr	2600.0 mm/Km	2666.4	3.63	Good	25.90446	N	85.827269	E	Normal
02-05-2024	10:56:12	15	100	700	21.0 cm	19.8 Km/Hr	2100.0 mm/Km	2221.9	3.08	Good	25.90356	N	85.826981	E	Normal
02-05-2024	10:56:32	15	100	800	24.0 cm	17.4 Km/Hr	2400.0 mm/Km	2488.6	3.41	Good	25.90345	N	85.826751	E	Normal
02-05-2024	10:56:49	15	100	900	21.0 cm	21.1 Km/Hr	2100.0 mm/Km	2221.9	3.08	Good	25.90321	N	85.826541	E	Normal
02-05-2024	10:57:56	15	100	1000	23.0 cm	17.9 Km/Hr	2300.0 mm/Km	2399.7	3.3	Good	25.90303	N	85.826152	E	Normal
02-05-2024	10:58:21	15	100	1100	28.0 cm	14.2 Km/Hr	2800.0 mm/Km	2844.2	3.84	Good	25.90279	N	85.825954	E	Normal
02-05-2024	10:58:54	15	100	1200	37.0 cm	11.3 Km/Hr	3700.0 mm/Km	3644.3	3.79	Good	25.90249	N	85.825412	E	Normal
02-05-2024	10:59:21	15	100	1300	25.0 cm	13.0 Km/Hr	2500.0 mm/Km	2577.5	3.52	Good	25.90204	N	85.825078	E	Normal
02-05-2024	10:59:49	15	100	1400	30.0 cm	12.8 Km/Hr	3000.0 mm/Km	3022	3.06	Good	25.90182	N	85.824732	E	Normal
02-05-2024	11:00:19	15	100	1500	32.0 cm	12.0 Km/Hr	3200.0 mm/Km	3199.8	3.27	Good	25.88596	N	85.825477	E	Normal
02-05-2024	11:00:50	15	100	1600	22.0 cm	11.9 Km/Hr	2200.0 mm/Km	2310.8	3.19	Good	25.88646	N	85.825878	E	Normal
02-05-2024	11:02:20	15	100	1700	26.0 cm	13.7 Km/Hr	2600.0 mm/Km	2666.4	3.63	Good	25.88756	N	85.825877	E	Normal
02-05-2024	11:02:49	15	100	1800	25.0 cm	12.4 Km/Hr	2500.0 mm/Km	2577.5	3.52	Good	25.88944	N	85.826118	E	Normal
02-05-2024	11:03:36	15	100	1900	31.0 cm	17.6 Km/Hr	3100.0 mm/Km	3110.9	3.16	Good	25.89052	N	85.826219	E	Normal
02-05-2024	11:04:16	15	100	2000	37.0 cm	18.9 Km/Hr	3700.0 mm/Km	3644.3	3.79	Good	25.89174	N	85.826321	E	Normal
02-05-2024	11:04:50	15	100	2100	28.0 cm	10.8 Km/Hr	2800.0 mm/Km	2844.2	3.84	Good	25.89381	N	85.826615	E	Normal
02-05-2024	11:11:27	15	100	2200	31.0 cm	10.8 Km/Hr	3100.0 mm/Km	3110.9	3.16	Good	25.89514	N	85.826771	E	Normal
02-05-2024	11:11:59	15	100	2300	25.0 cm	11.3 Km/Hr	2500.0 mm/Km	2577.5	3.52	Good	25.89539	N	85.826854	E	Normal
02-05-2024	11:12:41	15	100	2400	30.0 cm	18.4 Km/Hr	3000.0 mm/Km	3022	3.06	Good	25.89555	N	85.826945	E	Normal
02-05-2024	11:13:36	15	100	2500	23.0 cm	16.7 Km/Hr	2300.0 mm/Km	2399.7	3.3	Good	25.89712	N	85.827112	E	Normal
02-05-2024	11:14:20	15	100	2600	31.0 cm	18.0 Km/Hr	3100.0 mm/Km	3110.9	3.16	Good	25.89769	N	85.827423	E	Normal
02-05-2024	11:14:51	15	100	2700	33.0 cm	12.0 Km/Hr	3300.0 mm/Km	3288.7	3.37	Good	25.89793	N	85.827784	E	Normal
02-05-2024	11:15:27	15	100	2800	25.0 cm	19.9 Km/Hr	2500.0 mm/Km	2577.5	3.52	Good	25.89808	N	85.828012	E	Normal

IRI Value 3436

Machine ID 19192

Projeer for 02/05/2024 A-E

Handwritten signature and date 02/05/2024
