

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना

पटना / दिनांक :- 03/06/24

पत्रांक :- 855 (3/24)

प्रेषक,

ई0 राजेश कुमार चौधरी,
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बी.आर.आर.डी.ए.,
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय :- शीर्ष-MR (3054) Under Bihar Rural Road Maintenance Policy-2018 योजना
अन्तर्गत पथ का आवंटन का अधियाचना के संबंध में ।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष-MR (3054) Under Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथ का आवंटन का अधियाचना का मांग विहित-प्रपत्र में तैयार कर अधियाचना हेतु भेजी जा रही है । पथ का कार्य विशिष्टियों के अनुरूप किया गया है ।

अतः अनुरोध है कि उक्त योजना का आवंटन उपलब्ध कराने की कृपा की जाय, ताकि संवेदक का भुगतान किया जा सके ।

अनु०:- यथोक्त ।

विश्वासभाजन

(ई0 राजेश कुमार चौधरी)
कार्यपालक अभियंता

ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना

3/6/24



Requisition Format for Scheme Head-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Division :- Patna

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of Road IRI (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/PA/PAT/23/0014	L.039-Fatuha Niyazipur PMGSY Road to Buddhu Chak via Mominpur (VR30)	10100102293	1941/29.03.2023 1942/29.03.2023	1.870	107.63	84.71124	16.03096	34/MBD/23-24/26.08.2023	25.05.2024	-	2772.631	25mm SDBC	5%	82.50587	82.50587	2.20537	
2	RM/PA/PAT/23/0014	Mohiuddinpur PWD Road to Narma	10100101014	1941/29.03.2023 1942/29.03.2023	1.650	114.751	91.86243	14.24658	34/MBD/23-24/26.08.2023	25.05.2024	-	2882.352	25mm SDBC	5%	90.49260	90.49260	1.36983	कराये गये कार्य पूर्णतया पूर्ण विवरित है कि अनुमान है कि सड़क का अंतिम रूप प्राप्त होगा।
3	RM/PA/PAT/23/0014	Fatuha Chandasi Path Se Uttar Chamardeeh Parsi Tola Prathmik Vidyalaya Tak	1111899848	1941/29.03.2023 1942/29.03.2023	0.550	39.74132	30.07219	5.64329	34/MBD/23-24/26.08.2023	25.05.2024	-	2768.833	25mm SDBC	5%	29.18624	29.18624	0.88595	कराये गये कार्य पूर्णतया पूर्ण विवरित है कि अनुमान है कि सड़क का अंतिम रूप प्राप्त होगा।
4	RM/PA/PAT/23/0014	Fatuha Railway Station (Yard) to Four Lane (NH-3) Via Nisbuchak	1111036239	1942/29.03.2023	2.0	157.741	132.25353	17.38440	34/MBD/23-24/26.08.2023	25.05.2024	-	2824.5	25mm SDBC + 20mm MSS	5%	116.3958	116.3958	15.85773	

G. K. 3/1/24
Divisional Accounts Officer
RWD Works Division, Patna

3/1/24
Executive Engineer
RWD Works Division, Patna

Form GFR 19-A

(See Government of India's Decision (I) below Rule - 150)

Form of Utilization Certificate 06.02.2024

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs)	Amount Received (in lacs)	Particulars
		By Bank		
1	3054 (MR) New Maintenance Policy, 2018	Letter No. 14 Dated 06.02.2024	10509.37930	Certified that out of Rs. 10509.37930 lacs of grants in aid sanctioned during upto 06.02.2024 in favour of Executive Engineer, RWD Works Division, Patna under this Department, a sum of Rs. 10320.11145 lacs has been utilized for the purpose of 3054 (MR) as given in the margin for which it was sanctioned and that the balance of Rs. 189.26785 remaining unutilized at the end of the period under report.
		Total	10509.37930	

Certified and verified myself that the conditions on which the grants in aid was sanctioned have been duly fulfilled / and being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which.

Kinds of Checks exercised :-

- Works have been supervised by Executive Engineer / Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer / Superintending Engineer.
- Construction material have been tested,
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.
- All other codal formalities have been observed.

Physical Progress achieved :-

- Construction of Road works.
- Construction of CD works.

G. K.
 3/4/24
 Divisional Accounts Officer Gr. I
 RWD Works Division, Patna

03/02/24
 Executive Engineer
 RWD Works Division, Patna



Scanned with OKEN Scanner

Scanned with CamScanner

Name of The Road :Mohiudinpur PWD path to Narma

Length : 1.65 KM

Division : Patna

Block : Fatuha

Contractor Name :Sunny Contractors And Engineers Pvt Ltd

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD						
25-10-2023	8: 56: 28	91	0.1	270	0	2700	2705	G	25.450312	85.268927	Normal	$Y = 0 * X^2 + 0.936 * X + 278.4$		
25-10-2023	8: 56: 41	91	0.1	230	30.3	2300	2367	G	25.450866	85.268665	Curve	$X = 2900$		
25-10-2023	8: 57: 0	91	0.1	310	30.3	3100	3180	G	25.451676	85.268655	Normal	$Y = 2992$		
25-10-2023	8: 57: 13	91	0.1	300	20.2	3000	3086	G	25.452127	85.268064	Normal	(R) RURAL ROAD		
25-10-2023	8: 57: 28	91	0.1	330	30.3	3300	3367	G	25.452333	85.267073	Normal	Good	Average	Poor
25-10-2023	8: 57: 39	91	0.1	300	20.2	3000	3033	G	25.452447	85.265141	Normal	<4000	4001-5000	>5001
25-10-2023	8: 57: 52	91	0.1	270	30.3	2700	2741	G	25.452828	85.264388	Normal			
25-10-2023	8: 57: 52	91	0.1	270	30.3	2700	2741	G	25.4537	85.264542	Normal			
25-10-2023	8: 58: 0	91	0.1	300	20.2	3000	3086	G	25.454893	85.264767	Curve			
25-10-2023	8: 58: 14	91	0.1	270	10.1	2700	2705	G	25.455108	85.263714	Normal			
25-10-2023	8: 58: 49	91	0.1	310	30.3	3100	3180	G	25.454981	85.26253	Normal			
25-10-2023	8: 59: 0	91	0.1	240	20.2	2400	2460	G	25.454939	85.261888	Normal			
25-10-2023	8: 59: 12	91	0.1	300	30.3	3000	3086	G	25.455061	85.261882	Normal			
25-10-2023	8: 59: 24	91	0.1	260	30.3	2600	2612	G	25.455157	85.261187	Normal			
25-10-2023	8: 59: 35	91	0.1	290	30.3	2900	2992	G	25.455925	85.260898	Curve			
25-10-2023	8: 59: 46	91	0.1	270	30.3	2700	2780	G	25.456484	85.259102	Normal			
25-10-2023	9: 0: 0	91	0.1	260	30.3	2600	2638	G	25.456724	85.259139	Normal			
25-10-2023	9: 0: 25	91	0.05	290	30.3	2900	2982	G	432.715561	1449.490562				
Total			1.65	4800	424.2	2823.529	2882.352							
Average														

[Signature]
25/10/23
J.E.

[Signature]
25-10-23
AE

[Signature]
25/10/23

Analyzer

Name of Customer : Contractors And Engineers Pvt

Name of Work/ Road : Mohiudinpur PWD path to narma

Lab Job number :

Date : 25-10-2023

Section No. : 91

Test Date : 25-10-2023 Road Name : Mohiudinpur PWD path to narma

Machine No : 374 Road Type : (R) RURAL ROAD

Start S No : Side : Interval

Start E No :

Weather : UIV Range : 1367 To 4000 1000 mm/km

Start Location : Dist Range : 0 To 1.8 0.1 * 1000 m


End Location : Equation : $Y = 0 * X^2 + 0.936 * X + 278.4$

Print

Generate Report and Graph

Redraw Graph

Map View

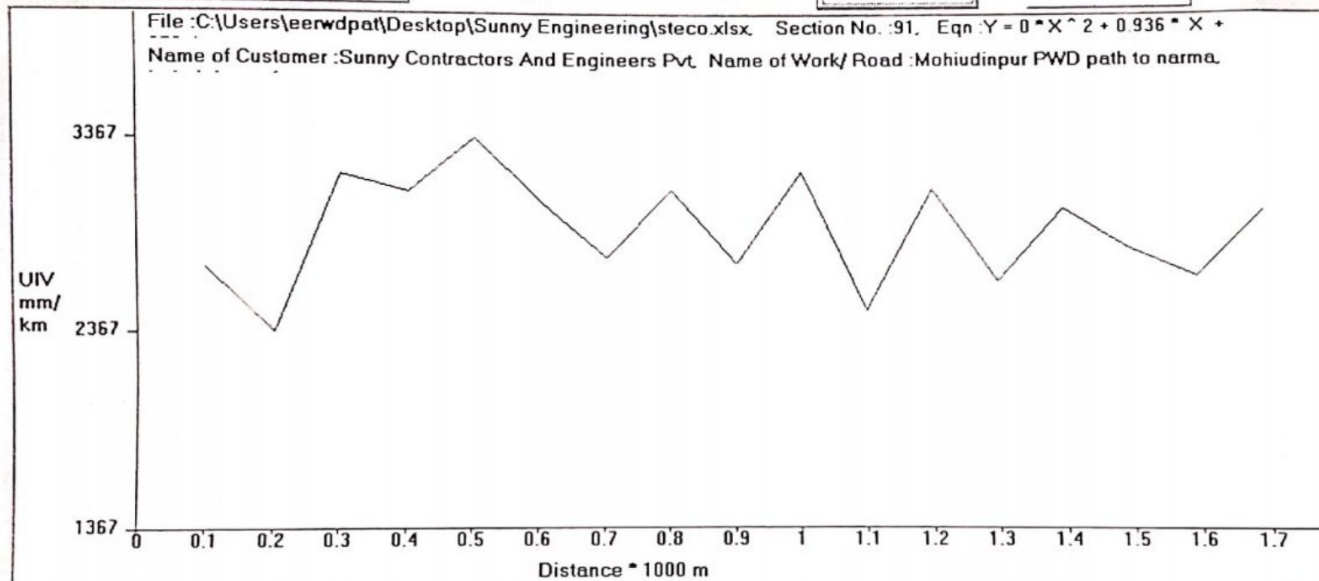

Signature
25/10/23
J.E.

Signature
25-10-23
JE

Signature
25/10/23
