

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हथुआ।

पत्रांक- 264

दिनांक- 01-03-2024

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार, ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय :- बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत क्रियान्वित पथ मरम्मत कार्य हेतु राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषयक बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत क्रियान्वित पथ मरम्मत कार्य हेतु राशि की अधियाचना विहित प्रपत्र में की जा रही है।

अतः भवदीय से अनुरोध है कि कॉलम 18 में अंकित राशि उपलब्ध कराने की कृपा की जाय।

अनु0- यथोक्त।

विश्वासभाजन,


01-03-24
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।
01/03/24

Requisition Format for Scheme Head- MR (3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and Surface Renewal)

SI No.	Package No.	Name of Road	Project ID as Per MIS	Administrative Approval (AA) Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No & Date	Date & Completion as per Agreement.	Actual Date of Completion	Value of IRI (in MM/KM)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content (in Percentage)	Previous Total Allocated Amount (in Lakh)	Up-to date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length (in Lakh)	Amount (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N-20-23/Hathua-03	Piprahli to Chhatyavw.	314711034344	Letter-4860, Dt-08.12.2021	2.400	225.410	174.11572	30.80788	11/580(3054-NMP-2018)2022-23 Date-06.12.2022	05.09.2023	-	Good	25	5.00	121.45000	121.45000	50.36877	Surface Completed.
1	MR-N-22-23/Hathua-03	1039-T01 Bijajpur to Bijajpur Yadavola (VR17)	31407102015	Letter-2882, Dt-16.10.2022	0.730	42.752	36.45597	7.73905	04/MBD/2023-24 Date-27.06.2023	26.03.2024	-	Good	25	5.00	25.51500	25.15500	10.89678	Surface Completed.
					3.130	268.162	210.57169	38.54693							146.96500	146.60500	61.26555	

प्रमाणित किया जाता है कि पथ में कराये गये कार्य मानक एवं विशिष्टियों के अनुरूप है।

J.E
Vijaypur

A.E
Vijaypur

D.A.O
R.W.D Works Division, Hathua.

Executive Engineer,
R.W.D Works Division, Hathua.
01/03/24

FORM GFR 19 - A

(See Government of India's Decision (1) below Rule - 150)

Form utilisation Certificate up to the month of Up to 28.02.2024

MR-3054 (New Maintenance Policy-2018)

RWD Works Division - HATHUA

1	Head	Amount Received		Expenditure		Balance	
	MR-3054 (New Maintenance Policy-2018)	IN A/C-	0.00	IN A/C-	0.00	IN A/C-	0.00
		By CFMS-	1022956659.00	By CFMS-	1011877308.00	By CFMS-	11079351.00
		Total-	1022956659.00	Total-	1011877308.00	Total-	11079351.00
						Certified that sum of Rs 10118.77 Lac has been utilized for the purpose of MR-3054 (New Maintenance Policy-2018) Schemes as given in the margin for which it was sanctioned and that the balance of Rs 110.79 Lac Lacs remaining utilized at the end of the period under.	

2. Certified that I have satisfied myself that the conditions on which the grants-in aid was sanctioned have been duly

Kind of Checks exercised :-

- (i) Works have been supervised by Executive Engineer/Superintending Engineer.
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- (iii) Construction material have been tested.
- (iv) Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
- (v) All other codal formalities have been observed.

3. Physical Progress achieved :-

- (i) Construction of Road Works.
- (ii) Construction of CD Works

Ar. J.
01.3.24

D.A.O

Rural Works Department
Works Division Hathua

[Signature]
01-03-24
Executive Engineer

Rural Works Department
Works Division Hathua

[Signature]
01/03/24

Name of work : PIPRAHI TO CHHATTYAW

Name of customer : Anand Mishra

(R)Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	Ull(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
04/11/23	18:46:03	70	0	0	0.0 cm	11.5 Km/Hr	0.0 mm/Km	245	0.43	Good	26.3833265	N	84.3302240	E	Normal
04/12/23	18:37:42	70	100	100	17.0 cm	4.3 Km/Hr	1700.0 mm/Km	1836	2.6	Good	26.5003843	N	84.0430689	E	Normal
04/12/23	18:38:05	70	100	200	19.0 cm	16.0 Km/Hr	1900.0 mm/Km	2024	2.93	Good	26.5003462	N	84.0442209	E	Normal
04/12/23	18:38:25	70	100	300	17.0 cm	17.2 Km/Hr	1700.0 mm/Km	1836	2.6	Good	26.5002813	N	84.0451517	E	Normal
04/12/23	18:38:45	70	100	400	19.0 cm	18.0 Km/Hr	1900.0 mm/Km	2024	2.83	Good	26.5005579	N	84.0458002	E	Normal
04/12/23	18:39:00	70	100	500	11.0 cm	23.1 Km/Hr	1100.0 mm/Km	1275	1.88	Good	26.5003672	N	84.0467768	E	Normal
04/12/23	18:39:15	70	100	600	14.0 cm	24.9 Km/Hr	1400.0 mm/Km	1550	2.24	Good	26.5003462	N	84.0477686	E	Normal
04/12/23	18:39:37	70	100	700	13.0 cm	18.8 Km/Hr	1300.0 mm/Km	1462	2.12	Good	26.5005293	N	84.0485989	E	Normal
04/12/23	18:39:53	70	100	800	11.0 cm	11.6 Km/Hr	1100.0 mm/Km	1275	1.88	Good	26.5006361	N	84.0486073	E	Normal
04/12/23	18:40:10	70	100	900	15.0 cm	21.2 Km/Hr	1500.0 mm/Km	1649	2.36	Good	26.5011110	N	84.0504399	E	Normal
04/12/23	18:40:26	70	100	1000	17.0 cm	22.9 Km/Hr	1700.0 mm/Km	1836	2.6	Good	26.5014906	N	84.0513697	E	Normal
04/12/23	18:40:42	70	100	1100	17.0 cm	22.2 Km/Hr	1700.0 mm/Km	1836	2.6	Good	26.5018930	N	84.0522470	E	Normal
04/12/23	18:40:57	70	100	1200	13.0 cm	24.1 Km/Hr	1300.0 mm/Km	1402	2.12	Good	26.5022230	N	84.0531549	E	Normal
04/12/23	18:46:46	70	100	1300	12.0 cm	10.1 Km/Hr	1200.0 mm/Km	1368	2	Good	26.5022879	N	84.0538111	E	Normal
04/12/23	18:47:07	70	100	1400	14.0 cm	17.6 Km/Hr	1400.0 mm/Km	1556	2.24	Good	26.5022154	N	84.0549784	E	Normal
04/12/23	18:47:24	70	100	1500	14.0 cm	20.9 Km/Hr	1500.0 mm/Km	1556	2.24	Good	26.5020933	N	84.0556498	E	Normal
04/12/23	18:47:41	70	100	1600	15.0 cm	20.8 Km/Hr	1600.0 mm/Km	1649	2.36	Good	26.5020286	N	84.0562963	E	Normal
04/12/23	18:48:04	70	100	1700	16.0 cm	15.7 Km/Hr	1600.0 mm/Km	1930	2.72	Good	26.5023241	N	84.0577784	E	Normal
04/12/23	18:48:26	70	100	1800	12.0 cm	16.9 Km/Hr	1200.0 mm/Km	1368	2	Good	26.5022345	N	84.0587702	E	Normal
04/12/23	18:48:47	70	100	1900	16.0 cm	16.8 Km/Hr	1600.0 mm/Km	1743	2.48	Good	26.5017347	N	84.0594416	E	Normal
04/12/23	18:49:32	70	100	2000	17.0 cm	18.1 Km/Hr	1700.0 mm/Km	1836	2.6	Good	26.5013037	N	84.0602579	E	Normal

Anand Mishra
01/03/24
J.EAnand Mishra
01/03/2021
J.E

S. E


Name of work : PIPRAHI TO CHHATYAW															
Name of customer : Anand Mishra															
(R)Rural Road															
Good					Average					Poor					
< 4000					4001 - 6000					> 6000					
04/12/23	18:49:59	70	100	2100	19.0 cm	13.4 Km/Hr	1800.0 mm/Km	2024	2.83	Good	28.5905969	N	84.0607080	E	Normal
04/12/23	18:50:23	70	100	2200	20.0 cm	14.8 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.5000088	N	84.0611663	E	Normal
04/12/23	18:52:22	70	100	2300	17.0 cm	13.1 Km/Hr	1700.0 mm/Km	1830	2.0	Good	26.4691140	N	84.0612345	E	Normal
04/12/23	18:52:54	70	100	2400	13.0 cm	11.3 Km/Hr	1300.0 mm/Km	1492	2.12	Good	28.4692571	N	84.0621119	E	Normal

Anand Mishra
 01/03/24
 S.E

Anand Mishra
 01/03/2024
 AE


 01-03-24

Name of Customer: Anand Mishra, Machine no: 19193, Road: PIPRAHI TO CHHATTISGARH, Date: 06/12/23, Section No: 70, Equation: $Y=0.936X+245.3$

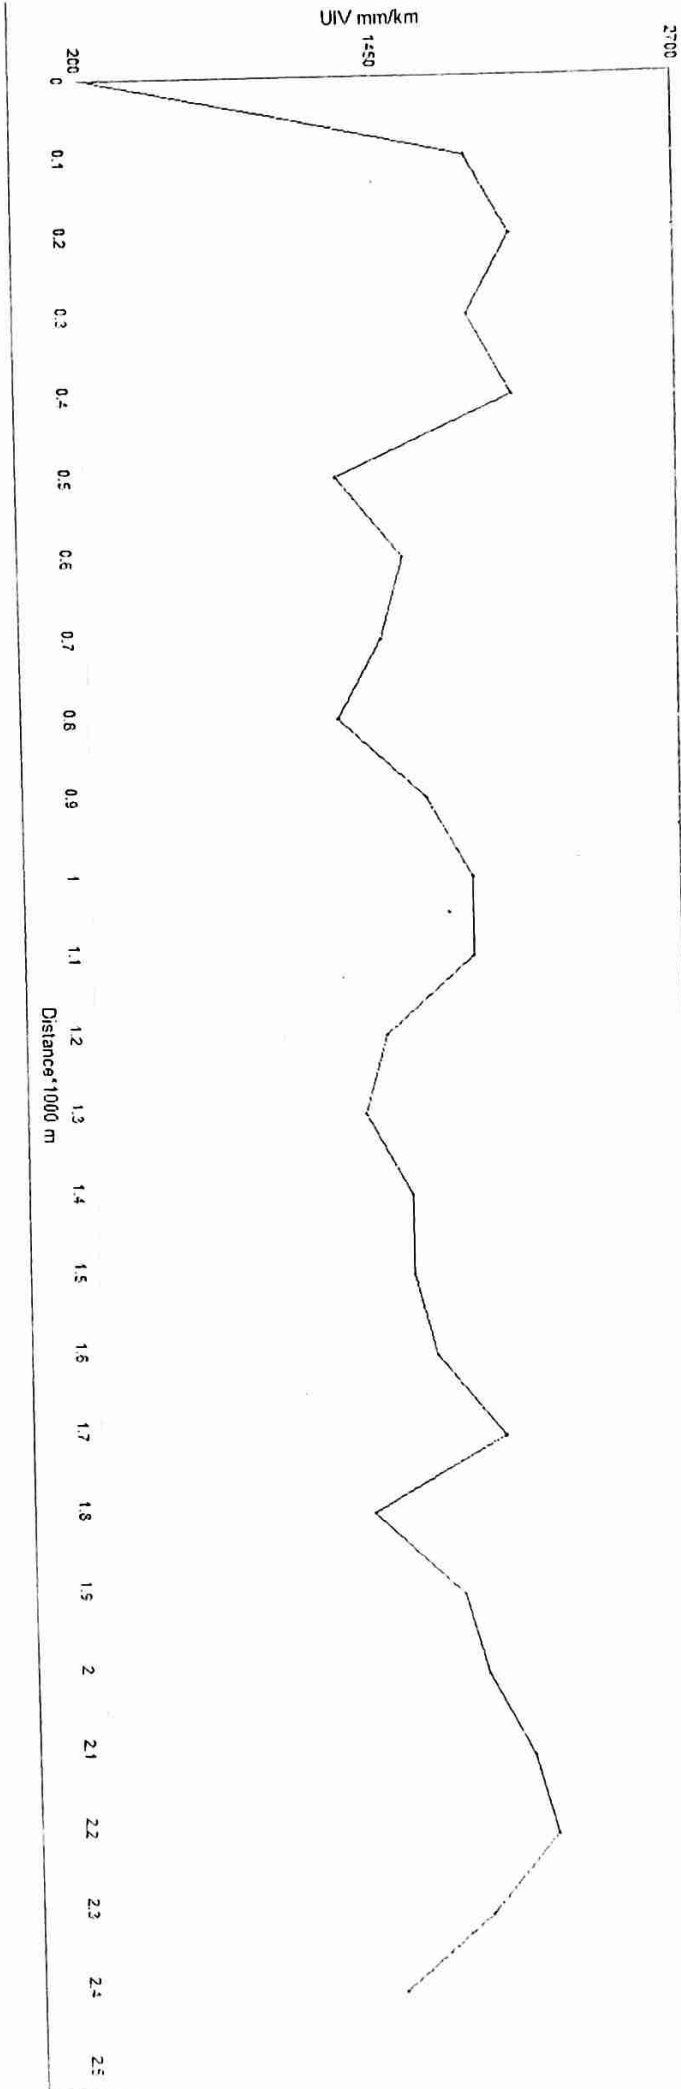

Indira
01/03/24
I.E

Mr. Anand Mishra
01/03/24
AE


01/03/24

Name of work : L039-T01 Bijapur to Bijapur Yadavola (VR17)

Name of customer : Gopalganj Construction Private Limited

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUWP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
21/12/23	14:38:22	74	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	245	0.43	Good	26.4017305	N	84.1184549	E	Normal
21/12/23	14:40:03	74	100	100	11.0 cm	13.4 Km/Hr	1100.0 mm/Km	1275	1.80	Good	26.4017305	N	84.1184549	E	Normal
21/12/23	14:40:45	74	100	200	14.0 cm	18.2 Km/Hr	1400.0 mm/Km	1556	2.24	Good	26.4610891	N	83.9843913	E	Normal
21/12/23	14:41:15	74	100	300	17.0 cm	12.1 Km/Hr	1700.0 mm/Km	1036	2.6	Good	26.4597101	N	83.9853526	E	Normal
21/12/23	14:41:51	74	100	400	15.0 cm	19.9 Km/Hr	1500.0 mm/Km	1649	2.36	Good	26.4595785	N	83.9856959	E	Normal
21/12/23	14:42:59	74	100	500	13.0 cm	15.4 Km/Hr	1300.0 mm/Km	1482	2.12	Good	26.4595785	N	83.9856959	E	Normal
21/12/23	14:43:26	74	100	600	20.0 cm	12.9 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.4595785	N	83.9850950	E	Normal
21/12/23	14:43:46	74	100	700	20.0 cm	17.8 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.4595785	N	83.9856959	E	Normal
21/12/23	14:46:14	74	100	800	14.0 cm	20.4 Km/Hr	1400.0 mm/Km	1556	2.24	Good	26.4595785	N	83.9856959	E	Normal


Indhi
01/03/24

Adhir Gadhvi
01/03/24
AE

01-03-24

2700

Name of Customer: Gopalenji Construction Private Limited . Machine no: 19193 , Road: L039-T01 Bijnipur to Bijnipur Yadavrola (VR17) . Date: 21/12/23 . Section No: 74 . Equation: $Y=0.936X+245.3$

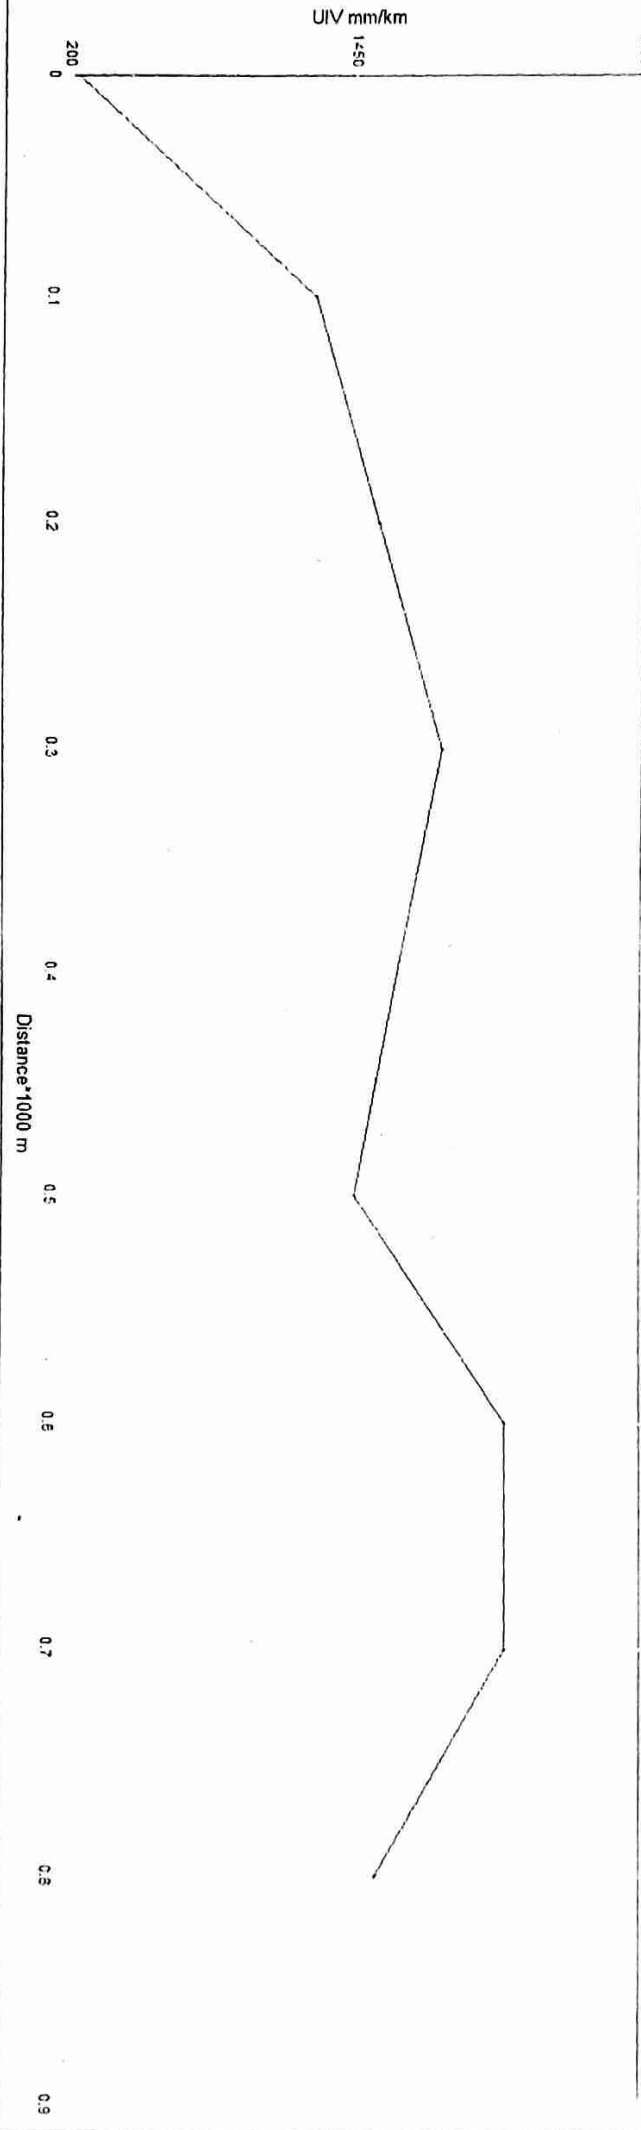

Indu
01/03/24
I.E

Alister Gumbert
01/03/2024
AE

01-03-24
