




ग्रामीण कार्य विभाग

Rural Works Department, Govt of Bihar

DETAILED PROJECT REPORT FOR FDR

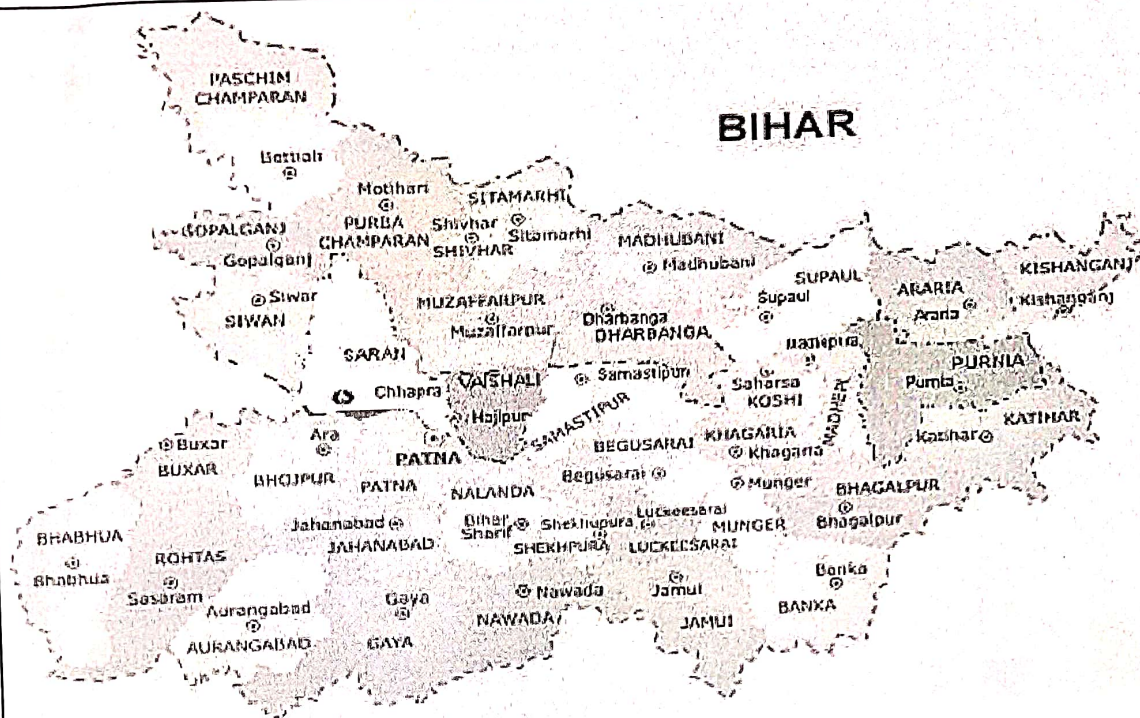

Name of the Road :- RAMPUR PWD ROAD to SAMBHUTA

DISTRICT		Muzaffarpur	
DIVISION		Muzaffarpur East-2	
BLOCK		Aurai	
Damage LENGTH OF ROAD	:	0.040	KM
CONSTRUCTION COST	:	4.797	Lac

Submitted By :- Executive Engineer
RWD Work Division Muzaffarpur East-2

GENERAL ABSTRACT

Name of Road RAMPUR PWD ROAD to SAMBHUATA

District Muzaffarpur

Block Aurni

Division Muzaffarpur East-2

Damage length

Sl no	DESCRIPTION	AMOUNT (LAKHS)
1	Brick-Bats	474181.40
2	Local Sand	5574.33
3	HP	0.00
4	Cement Bag	0.00
	GARAND SUB TOTAL	479755.73
TOTAL COST OF PROJECT IN LACS=		479755.73

Sy Rs. 4.80 Lacs

Sham
A.E 12/11/24

D. E.
12.11.24

Post facto technical sanctioned for Rs 480 lacs (Rs. four lacs eighty thousand) only


Sham 11/11/24
Superintending Engineer
Rural Works Department
Work Circle: Muzaffarpur

Sham
15/11/24

Name of Road- RAMPUR PWD ROAD to SAMBHUTA
Block- Aurai

Measurement for Supplying of Brick Bats								
S. No	Chainage	Nos	Length (M)	Width (M)	Av. Width (M)	Thickness (M)	Av. Thickness (M)	Quantity (Cum)
1		1	35.00		4.10		2.50	358.75
Total (Cum) :-								358.75


Assistant Engineer,
Rural Works Department,
Work Sub Division, Aurai
Muzaffarpur East-2


Executive Engineer,
Rural Works Department,
Work Division,
Muzaffarpur East-2

Name of Road-

RAMPUR PWD ROAD to SAMBHUTA

Block-


Aurai

Measurement for Supplying of Local Sand

S. No	Chainage	Nos	Length (M)	Width (M)	Av. Width (M)	Thicknes s (M)	Av. Thickness (M)	Quantity (Cum)
1		1	35.00		4.10		0.15	21.53
Total (Cum) :-								21.53



Assistant Engineer,
Rural Works Department,
Work Sub Division, Aurai
Muzaffarpur East-2



Executive Engineer,
Rural Works Department,
Work Division,
Muzaffarpur East-2

RAMPUR PWD ROAD to SAMBHUTA

Name of Work

Sl no	SDB Sl No	MORD Ref No	Description	Unit	QUANTITY	RATE	AMOUNT (In Rs.)
1			Providing brick bats including spreading laying hand packing and compacting with C.I. Hammer in layers not exceeding 75 mm thick including cost of light barriers, danger signals, chowkidar, taxes, royalty etc.all complete job as per specification and direction of E/I including carriage cost of bricks	M3	358.75	1321.76	474181.40
2			Supplying, Laying and spreading Local Sand at work site including all cost of Tax and Royalties etc.	M3	21.53	258.97	5574.33
3			Providing and laying sand bangs with filling of local sand in empty cement bags, stitching including all cost of Tax and Royalties etc..	No	0.00	29.19	0.00
4			Providing and Laying Reinforced Cement Concrete Pipe NP3 1000 mm dia as per desing in Single Row	M	0.00	2240.61	0.00
Total							479755.73

Sham
12/11/24
A.E

Sham
12/11/24
