

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल पुपरी

पत्रांक411.....

पुपरी, दिनांक 22/02/2025

प्रेषक:-

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पुपरी

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण, पटना
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:-MR-3054 -BIHAR RURAL ROAD NEW MAINTENANCE POLICY-20018 योजना अन्तर्गत
निर्माण कार्य की राशि को अधियाचना के संबंध में।

महाशय

उपर्युक्त विषय के संबंध में कहना है कि MR-3054-BIHAR RURAL ROAD NEW
MAINTENANCE POLICY-20018 योजना अन्तर्गत संलग्न सूची के आधार पर पथ में निर्माण कार्य की
राशि का आवंटन उपलब्ध कराने की कृपा की जाए।

अनु०:-यथोक्त।

विश्वासभाजन


22-02-25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पुपरी


22-02-25

Office of the Executive Engineer, Rural Works Department, Works Division, Pupri

Requisition formate Scheme Head MR (3054) under Bihar road Maintenance Policy-2018 (Rectification and Surface Renewal)

Sl No.	Package No.	Road Name	Project Id as per MIS	Administrative Approval (AA) Letter No. and Date	Administrative Approval (AA)		Agreement (in Lakh)		Agreement No. and Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/KM)	Thickness of Bituminous Layer (in mm)	Value of Bituminous Content in Percentage	Previous total amount (in Lakh)	Up to Date expenditure as per MIS (in Lakh)	Requisition against Work Done (in Lakh)	Remarks
					Length (in Km)	Amount (in lakh)	Initial Rectification with Surface Renewal (in Lakh)	Five Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/SI/PUP/24/0005	LO39 Harpura to Bhagwanpur - Harpura (VR25)	31607802043	6515/26.12.2023	4.200	189.480	139.086	40.750	13 MBO/2024-25	25.06.2025	-	2659	25	5%	95.000	95.000	36.90233	Completed

नोट:-

दिनांक पत्रांक-मुआ(रु) 3054-4-04/2020 पार्त 4 5047 दिनांक 23.12.2021 के अलेक ने प्रमाणित किया जाता है कि-

1. गुणवत्ता पूर्ण एवं विशिष्टियों के अनुसार कार्य कराने के बाद MIB में दर्ज किया गया है।

2. सम्बन्धित कार्य कर्माय अभियंता द्वारा कटवा गया (100% जांचा गया) तत्पश्चात अभियंता द्वारा 50% तथा कार्यपालक अभियंता द्वारा 10% जांचा गया तथा MIS पर Upload किया गया।

22.02.25
EXECUTIVE ENGINEER
RWD, WORKS DIVISION,
PUPRI

Name of work : L039-Harpurwa to Bhagwanpur - Harpurwa (VR26)																			
Name of customer : Tathagat Construction Private Limited																			
(R)Rural Road																			
Good										Average					Poor				
< 4000										4001 - 5000					> 5000				
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	Ultimate(Km)	Corrected U (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks				
15-12-2024	11:45:25	26	100	103	28.0 cm	3.8 Km/Hr	2600.0 mm/Km	2921	3.83	Good	26.553408	N	85.614143	E	Normal				
15-12-2024	11:45:48	26	100	200	30.0 cm	10.1 Km/Hr	3000.0 mm/Km	3106	4.16	Good	26.553285	N	85.614082	E	Normal				
15-12-2024	11:46:06	26	100	300	22.0 cm	12.2 Km/Hr	2200.0 mm/Km	2385	3.26	Good	26.553263	N	85.614093	E	Normal				
15-12-2024	11:46:27	26	100	400	21.0 cm	16.2 Km/Hr	2100.0 mm/Km	2273	3.14	Good	26.553337	N	85.614081	E	Normal				
15-12-2024	11:46:46	26	100	500	23.0 cm	20.3 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.551037	N	85.613006	E	Normal				
15-12-2024	11:47:03	26	100	600	29.0 cm	16.4 Km/Hr	2600.0 mm/Km	3014	4.04	Good	26.546353	N	85.611148	E	Normal				
15-12-2024	11:47:20	26	100	700	25.0 cm	18.3 Km/Hr	2500.0 mm/Km	2643	3.6	Good	26.543957	N	85.611226	E	Normal				
15-12-2024	11:47:37	26	100	800	32.0 cm	18.8 Km/Hr	3200.0 mm/Km	3231	4.38	Good	26.5434	N	85.610533	E	Normal				
15-12-2024	11:47:54	26	100	900	26.0 cm	24.3 Km/Hr	2600.0 mm/Km	2736	3.71	Good	26.545702	N	85.610685	E	Normal				
15-12-2024	11:48:11	26	100	1000	26.0 cm	25.7 Km/Hr	2600.0 mm/Km	2923	3.93	Good	26.543828	N	85.60981	E	Normal				
15-12-2024	11:48:25	26	100	1100	20.0 cm	20.2 Km/Hr	2000.0 mm/Km	2160	3.03	Good	26.543905	N	85.601693	E	Normal				
15-12-2024	11:48:35	26	100	1200	23.0 cm	23.1 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.543898	N	85.601798	E	Normal				
15-12-2024	11:48:53	26	100	1300	27.0 cm	27.5 Km/Hr	2700.0 mm/Km	2628	3.82	Good	26.556439	N	85.592459	E	Normal				
15-12-2024	11:49:07	26	100	1400	26.0 cm	27.6 Km/Hr	2600.0 mm/Km	3014	4.04	Good	26.556581	N	85.592431	E	Normal				
15-12-2024	11:49:21	26	100	1500	21.0 cm	27.5 Km/Hr	2100.0 mm/Km	2273	3.14	Good	26.556592	N	85.592481	E	Normal				
15-12-2024	11:49:35	26	100	1600	30.0 cm	22.9 Km/Hr	3000.0 mm/Km	3106	4.16	Good	26.557246	N	85.59283	E	Normal				
15-12-2024	11:49:48	26	100	1700	18.0 cm	21.7 Km/Hr	1800.0 mm/Km	2088	2.91	Good	26.558014	N	85.5928	E	Normal				
15-12-2024	11:50:01	26	100	1800	27.0 cm	24.4 Km/Hr	2700.0 mm/Km	2628	3.82	Good	26.558196	N	85.592555	E	Normal				
15-12-2024	11:50:14	26	100	1900	28.0 cm	25.8 Km/Hr	2800.0 mm/Km	2923	3.93	Good	26.558713	N	85.592701	E	Normal				

1
Sammith
10/11/24
AT

18/11/24

Name of work		: L039-Harpurwa to Bhagwanpur - Harpurwa (VR26)													
Name of customer		: Tathagat Construction Private Limited													
(R)Rural Road															
Good				Average				Poor							
< 4000				4001 - 5000				> 5000							
10-12-2024	11 50 27	26	100	2000	26.0 cm	28.8 Km/Hr	2600.0 mm/Km	2735	3.71	Good	26.559286	N	85.595013	E	Normal
10-12-2024	11 50 40	26	100	2100	23.0 cm	28.6 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.560087	N	85.59565	E	Normal
10-12-2024	11 50 53	26	100	2200	27.0 cm	20.8 Km/Hr	2700.0 mm/Km	2828	3.82	Good	26.560671	N	85.593865	E	Normal
10-12-2024	11 51 09	26	100	2300	24.0 cm	24.4 Km/Hr	2400.0 mm/Km	2550	3.46	Good	26.545457	N	85.590535	E	Normal
10-12-2024	11 51 25	26	100	2400	30.0 cm	26.5 Km/Hr	3000.0 mm/Km	3106	4.16	Good	26.545853	N	85.589605	E	Normal
10-12-2024	11 51 41	26	100	2500	24.0 cm	23.9 Km/Hr	2400.0 mm/Km	2550	3.49	Good	26.54591	N	85.588803	E	Normal
10-12-2024	11 51 57	26	100	2600	18.0 cm	25.9 Km/Hr	1800.0 mm/Km	1995	2.8	Good	26.545832	N	85.588435	E	Normal
10-12-2024	11 52 13	26	100	2700	19.0 cm	22.6 Km/Hr	1900.0 mm/Km	2088	2.91	Good	26.545632	N	85.589455	E	Normal
10-12-2024	11 52 29	26	100	2800	21.0 cm	24.1 Km/Hr	2100.0 mm/Km	2273	3.14	Good	26.544287	N	85.585335	E	Normal
10-12-2024	11 52 45	26	100	2900	23.0 cm	24.9 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.545105	N	85.582183	E	Normal
10-12-2024	11 53 02	26	100	3000	27.0 cm	25.7 Km/Hr	2700.0 mm/Km	2828	3.82	Good	26.545105	N	85.582183	E	Normal
10-12-2024	11 53 18	26	100	3100	31.0 cm	24.0 Km/Hr	3100.0 mm/Km	3199	4.27	Good	26.545832	N	85.588455	E	Normal
10-12-2024	11 53 36	26	100	3200	26.0 cm	22.9 Km/Hr	2600.0 mm/Km	2736	3.71	Good	26.54537	N	85.583868	E	Normal
10-12-2024	11 53 53	26	100	3300	23.0 cm	22.8 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.54537	N	85.580849	E	Normal
10-12-2024	11 54 11	26	100	3400	25.0 cm	20.2 Km/Hr	2500.0 mm/Km	2643	3.6	Good	26.545632	N	85.585435	E	Normal
10-12-2024	11 54 26	26	100	3500	19.0 cm	22.9 Km/Hr	1900.0 mm/Km	2088	2.91	Good	26.54528	N	85.585647	E	Normal
10-12-2024	11 54 47	26	100	3600	28.0 cm	22.3 Km/Hr	2800.0 mm/Km	2921	3.93	Good	26.54528	N	85.585399	E	Normal
10-12-2024	11 55 01	26	100	3700	29.0 cm	22.9 Km/Hr	2900.0 mm/Km	3014	4.04	Good	26.54508	N	85.585258	E	Normal
10-12-2024	11 55 15	26	100	3800	29.0 cm	22.0 Km/Hr	2900.0 mm/Km	3014	4.04	Good	26.54508	N	85.585258	E	Normal
10-12-2024	11 55 29	26	100	3900	24.0 cm	18.9 Km/Hr	2400.0 mm/Km	2550	3.49	Good	26.544812	N	85.585508	E	Normal

19/11/24
83

19/11/24

Signature
19/12/24


19/12/24

Name of work :		L039-Harpurwa to Bhagwanpur - Harpurwa (VR26)													
Name of customer :		Tattajpat Construction Private Limited													
		(R)Rural Road													
		Good		Average		Poor									
		< 4000		4001 - 6000		> 6000									
10.12-2024	11.55.55	20	100	4000	23.0 cm	14.7 m/min	2200.0 mm/min	2458	3.37	Good	20.544812	N	85.585508	E	Normal



4230

Name of Customer: Tathagat Construction Private Limited, Machine no: 19199, Road: 10/9 Harpuwa to Bhagwanpur - Harpuwa (Vr26), Date: 10/12/24, Section No: 26, Equation: $Y=0.026X+328.1$

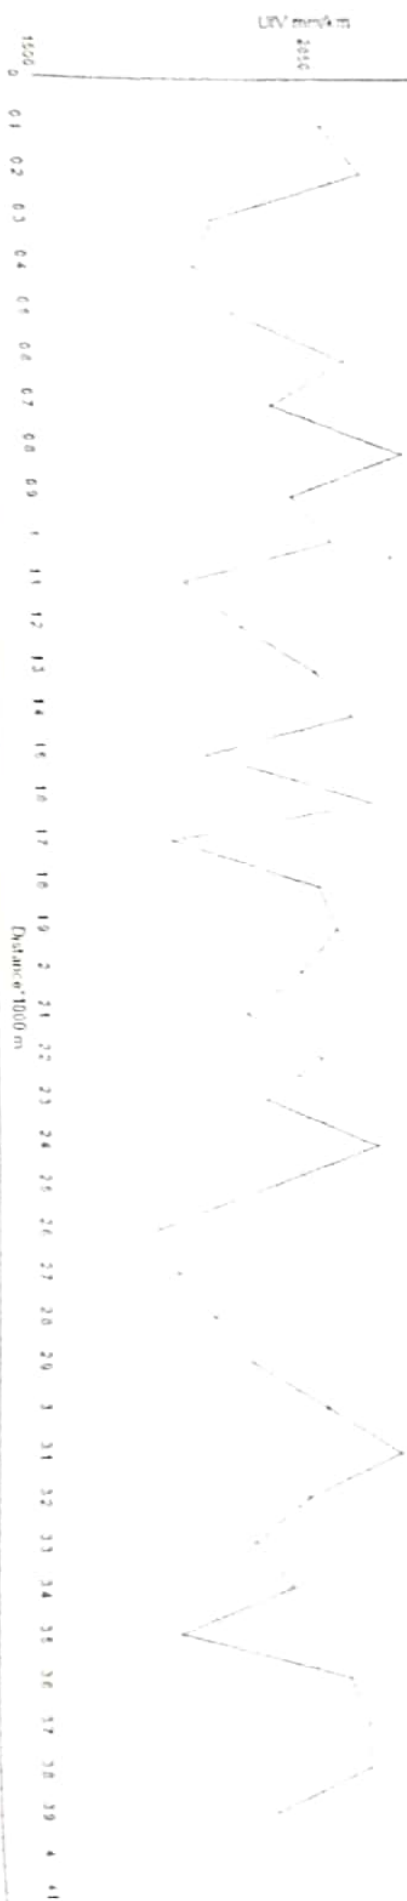

10/12/24
ATE

15/11/24



Scanned with OKEN Scanner

Scanned with CamScanner
