

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, झंझारपुर

पत्रांक- 20 353

दिनांक-07/01/2025

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, झंझारपुर

सेवा में,

नोडल पदाधिकारी,
3054 एम.आर. कोषांग,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- MMGSUY(SC) के क्रियान्वित पथों के भुगतान हेतु अधियाचना के संबंध में।

महाशय,


उपर्युक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि कार्यप्रमण्डल झंझारपुर अन्तर्गत MMGSUY (SC) के पथ में पूर्ण कराये गये कार्यों का भुगतान हेतु अधियाचना विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

अनु0- 1. अधियाचना विहित प्रपत्र में।

2. Recorder IRI की प्रतिहस्ताक्षरित प्रति।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, झंझारपुर



GFR 12-B


[SEE Rule 256(2)]

FORM OF UTILIZATION CERTIFICATE

- (1) Certified that out of the Loan of RS 67239466, Sanctioned under MMGSUY(SC), dated 27.12.2024, in favour of Executive Engineer, RWD Works Division Jhanjharpur, during the year 2024-25, an amount of Rs 63806867, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs 3432599, remaining unutilized at the end of the year 0.00000 has been surrendered to the Government (vide No....., dated.....)/will be adjusted towards the loan payable during the next financial year.
- (2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

1. Works have been supervised by Executive Engineer/ Superintending Engineer.
2. Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
3. Construction material have been tested.
4. Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
5. All other codal formalities have been observed.



Executive Engineer

R.W.D Works Division Jhanjharpur



Rural Works Department

MMGSUY(SC) Allotment Requisition Format

Name Of Division:- Jhanjharpur

Sl No	Requisition Number	Project ID as per MIS	Name of Road	AA Length (in km)	Administrative Approval (Construction work) Amount (in lakh)	Agreement Construction work) Amount (in lakh)	Agreement No & Date	Date Of Completion as per agreement	Actual date of completion on	Wk Status (WBW/MMW/BM/SDBC etc.)	Value of RI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	up to date expenditure as per MIS (in Lakh)	Value Of Work Done (in lakh)	Current Demand	Remarks
1	MMGSUY/23-24 Jhanjharpur/05	62209803000005	Repair of road from Tamuriya Kachchhawi Chanauraganj	8.300	1201.43000	1231.99802	11 MBD /2024-25 05.10.2024	04.07.2025	1	BM SDBC Complete	3343	75mm	BM-3.3% and SDBC-5%	419.32809	419.32809	1069.45357	650.12548	Surface Work in progress

It is certified that physical and financial progress has been updated in MIS

NOTE:-

- 1 Above signed copy along with forwarding letter and Utilization Certificate must be uploaded in MIS
- 2 Signed hard copy and soft copy (in excel sheet) of recorded RI is enclosed (As Applicable)

Executive Engineer
RWD Works Division

Jhanjharpur

[Signature]
07/10/25

BUMP INTEGRATOR TEST

**NAME OF WORK :- REPAIR OF ROAD FROM
TAMURIYA KACHEHHAWI CHANAURAGANJ UNDER
RWD WORKS DIVISION- JHANJHARPUR FROM
CHAINAGE :- 0.700 KM TO 4.000 KM. & 7.50 KM TO
8.050 KM**

NAME OF CONTRACTOR :- ARBIND KUMAR SHARMA

RWD WORKS DIVISION - JHANJHARPUR

Name Of Contractor :- Arbind Kumar Sharma

Name Of Work :- Repair of Road from Tamuriya Kachehawi Chanauraganj under RWD Works Division- Jhanjharpur from Chainage :- 0.700 Km To 4.000 Km. & 7.50 Km To 8.050 Km


From (km)	To (km)	L.H.S Average Bumps (cm / km)	R.H.S Average Bumps (cm / km)	Average Observed Bumps In (cm)	Observed Roughness In (x) (mm / km)	Corrected Roughness In (mm/Per km [v=(1.193X-481.6)])	Average Corrected Roughness In (mm/km)	Remarks
-----------	---------	-------------------------------	-------------------------------	--------------------------------	-------------------------------------	---	--	---------

Date Of Testing :- 21-11-2024 To 23-11-2024

Chainage :- 0.700 Km To 4.00 Km. & 7.50 Km To 8.050 Km

0.700	0.800	33	33	33.000	3300	3455	3300	4000 mm
0.800	0.900	32	35	33.500	3350	3515		
0.900	1.000	31	31	31.000	3100	3217		
1.000	1.100	32	35	33.500	3350	3515		
1.100	1.200	29	35	32.000	3200	3336		
1.200	1.300	30	32	31.000	3100	3217		
1.300	1.400	30	34	32.000	3200	3336		
1.400	1.500	30	30	30.000	3000	3097		
1.500	1.600	27	30	28.500	2850	2918		
1.600	1.700	32	33	32.500	3250	3396		
1.700	1.800	30	33	31.500	3150	3276	3414	4000 mm
1.800	1.900	35	34	34.500	3450	3634		
1.900	2.000	31	33	32.000	3200	3336		
2.000	2.100	33	31	32.000	3200	3336		
2.100	2.200	31	32	31.500	3150	3276		
2.200	2.300	30	33	31.500	3150	3276		
2.300	2.400	33	32	32.500	3250	3396		
2.400	2.500	33	34	33.500	3350	3515		
2.500	2.600	34	34	34.000	3400	3575		
2.600	2.700	33	34	33.500	3350	3515		
2.700	2.800	35	36	35.500	3550	3754	3322	4000 mm
2.800	2.900	36	35	35.500	3550	3754		
2.900	3.000	32	31	31.500	3150	3276		
3.000	3.100	33	33	33.000	3300	3455		
3.100	3.200	30	28	29.000	2900	2978		
3.200	3.300	31	30	30.500	3050	3157		

From (km)	To (km)	L.H.S Average Bumps (cm / km)	R.H.S Average Bumps (cm / km)	Average Observed Bumps in (cm)	Observed Roughness in (X) (mm / km)	Corrected Roughness in (mm/Per km [Y=(1.193X-481.6)])	Average Corrected Roughness in (mm/km)	Remarks
Date Of Testing :- 21-11-2024 To 23-11-2024								
Chainage :- 0.700 Km To 4.00 Km. & 7.50 Km To 8.050 Km								
3.300	3.400	30	32	31.000	3100	3217	3322	4000 mm
3.400	3.500	30	29	29.500	2950	3038		
3.500	3.600	33	32	32.500	3250	3396		
3.600	3.700	32	32	32.000	3200	3336		
3.700	3.800	32	31	31.500	3150	3276		
3.800	3.900	33	30	31.500	3150	3276		
3.900	4.000	32	31	31.500	3150	3276		

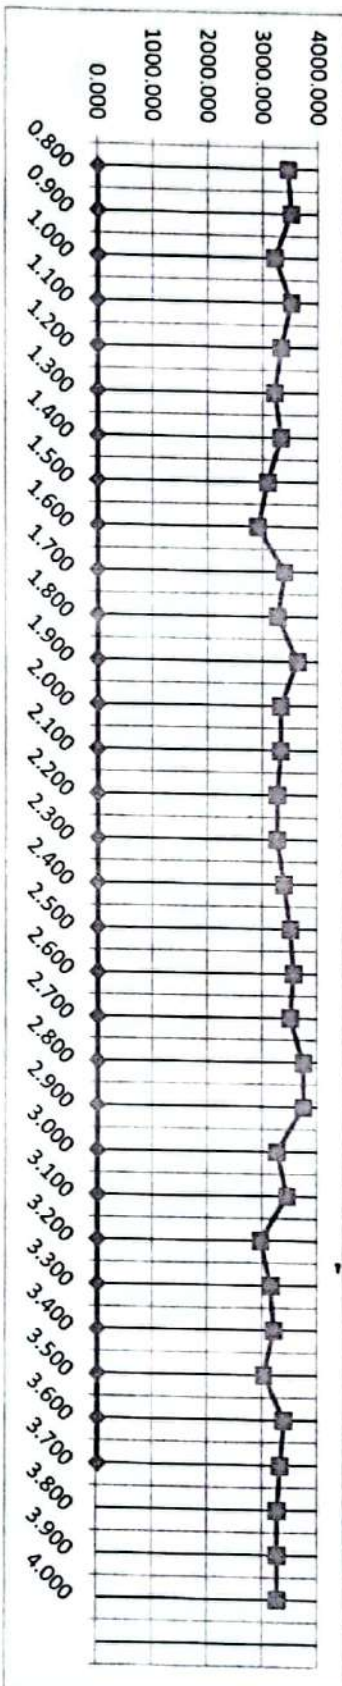


Head Office :- House of Silta Niwash, Gali No-16, Front of Rajendra Nagar Terminal, Kankebarbagh, Patna, Bihar
 Mob:- 08538985610, 09279295759, email id :- civilsolutionpatna@gmail.com

Name Of Contractor :- Arbind Kumar Sharma

Name Of Work :- Repair of Road From Tamuriya Kachehawi Chanauraganj under RWD Works Division- Jhanjharpur from Chainage :- 0.700 Km To 4.000 Km. & 7.50 Km To 8.050 Km

From (km)	To (km)	L.H.S Average Bumps (cm / km)	R.H.S Average Bumps (cm / km)	Average Observed Bumps In (cm)	Observed Roughness In (X) (mm / km)	Corrected Roughness In MM.Per km [v=(1.193X-481.6)]	Average Corrected Roughness In (mm/km)	Remarks
Date Of Testing :- 21-11-2024 To 23-11-2024								
Chainage :- 0.700 Km To 4.00 Km. & 7.50 Km To 8.050 Km								
7.500	7.600	32	32	32.000	3200	3336	3237	> 4000 mm
7.600	7.700	31	34	32.500	3250	3396		
7.700	7.800	30	30	30.000	3000	3097		
7.800	7.900	29	32	30.500	3050	3157		
7.900	8.000	29	35	32.000	3200	3336		
8.000	8.050	29	31	30.000	3000	3097		

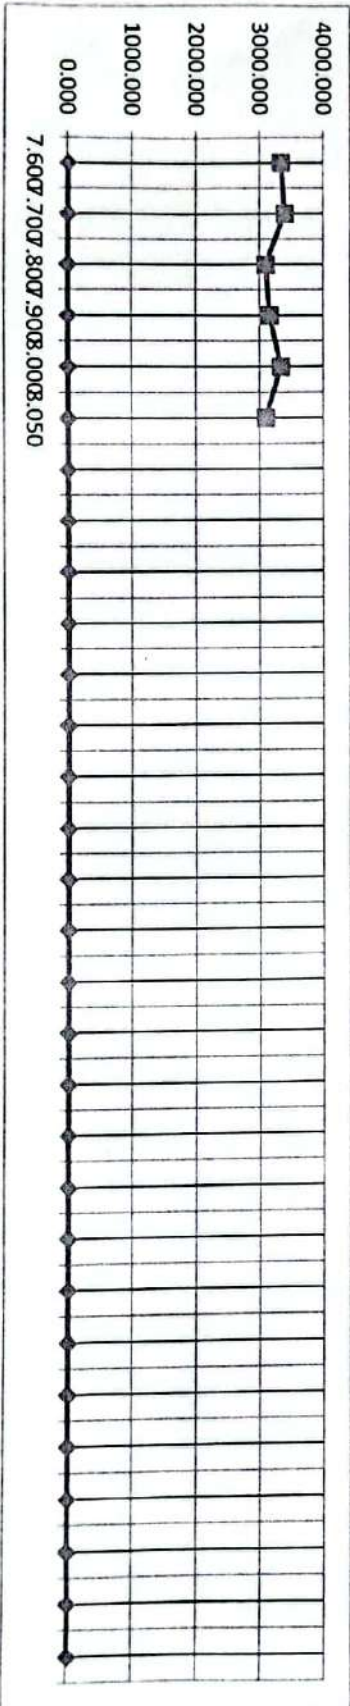

Head Office :- House of Sita Niwash, Gali No-16, Front of Rajendra Nagar Terminal, Kankarbagh, Patna, Bihar

Mob:- 08538985610, 09279295759, email id :- civilsolutionpatna@gmail.com
