

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हथुआ।

पत्रांक- **18**

दिनांक- **09-01-2025**

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार, ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय :- बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत क्रियान्वित पथ मरम्मति कार्य हेतु राशि उपलब्ध कराने के संबंध में।

महाशय

उपरोक्त विषयक बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत क्रियान्वित पथ मरम्मति कार्य हेतु राशि की अधियाचना विहित प्रपत्र में की जा रही है।

अतः भवदीय से अनुरोध है कि कॉलम 18 में अंकित राशि उपलब्ध कराने की कृपा की जाय।

अनु0- यथोक्त।

विश्वासभाजन,



09.01.25
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

Name of Works Division :- Rural Works Department, Works Division Hathua.																		
Sl No.	Package No.	Name of Road	Project ID as Per MIS	Administrative Approval (AA) Letter No & Date.	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No & Date	Date & Completion as per Agreement.	Actual Date of Completion	Value of IRI (In MM/KM)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (In Lakh)	UP-to date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (In Lakh)	Amount (In Lakh)	Initial Rectification with surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/23-24/Hathua/-04	L023-Chhathiyaon Mahradion to Dighwa (VR6)	31407102010	Letter-6116, Dt-04.12.2023	3.000	178.200	119.64152	21.79975	03/MBD/2024-25 Date-22.08.2024	21.05.2025	-	Good	25	5.00	0.00000	0.00000	117.50000	Surface Complete
2	MR-N/23-24/Hathua/-04	Kukur Bhuka Main road TO Chkarwa Khas	31407117005	Letter-6116, Dt-04.12.2023	1.951	133.490	110.22864	12.36943	03/MBD/2024-25 Date-22.08.2024	21.05.2025	-	Good	25	5.00	0.00000	0.00000	90.00000	Surface Complete
					4.951	311.690	229.87016	34.16918							0.00000	0.00000	207.50000	

प्रमाणित किया जाता है कि पथ में कराये गये कार्य मानक एवं विशिष्टियों के अनुरूप है।


J.E.
Bhore


A.E.
Bhore


D.A.O.
Bhore


09-DI-25
Executive Engineer,
R.W.D Works Division, Hathua.

FORM GFR 19 - A

(See Government of India's Decision (1) below Rule - 150)

Form utilisation Certificate up to the month of Up to 31.10.2024

MR-3054 (New Maintenance Policy-2018)

RWD Works Division - HATHUA

	Head	Amount Received		Expenditure		Balance	
		IN A/C-	0.00	IN A/C-	0.00	IN A/C-	0.00
1	MR-3054 (New Maintenance Policy-2018)	By CFMS-	1213172768.00	By CFMS-	1213158273.00	By CFMS-	14495.00
		Total-	1213172768.00	Total-	1213158273.00	Total-	14495.00
						Certified that sum of Rs 12131.58 Lac has been utilized for the purpose of MR-3054 (New Maintenance Policy-2018) Schemes as given in the margin for which it was sanctioned and that the balance of Rs 0.14495 Lac Lacs remaining utilized at the end of the period under.	

2. Certified that I have satisfied myself that the conditions on which the grants-in aid was sanctioned have been duly
Kind of Checks exercised :-

- (i) Works have been supervised by Executive Engineer/Superintending Engineer.
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- (iii) Construction material have been tested.
- (iv) Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
- (v) All other codal formalities have been observed.

3. Physical Progress achieved :-

- (i) Construction of Road Works.
- (ii) Construction of CD Works

Ag. J.
09.11.25
D.A.O

Rural Works Department
Works Division Hathua

[Signature]
09-01-25

Executive Engineer
Rural Works Department
Works Division Hathua

Name of work : Kukur Bhuka Main road TO Chikarwa Khas

Name of customer : M/S Vindhyavasthi Construction

(R)Rural Road

Good Average Poor

< 4000 4001 - 5000 > 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	U1(mm/Km)	Corrected U1 (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
09/01/25	20:01:40	133	0	0	0.0 cm	25.2 Km/Hr	0.0 mm/Km	245	0.43	Good	26.4736376	N	84.0632029	E	Normal
09/01/25	20:43:41	133	100	100	23.0 cm	15.2 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:44:00	133	100	200	29.0 cm	18.9 Km/Hr	2900.0 mm/Km	2980	3.98	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:44:16	133	100	300	25.0 cm	22.9 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:44:30	133	100	400	22.0 cm	24.4 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:44:49	133	100	500	21.0 cm	20.0 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:45:07	133	100	600	25.0 cm	19.0 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:45:22	133	100	700	29.0 cm	24.9 Km/Hr	2900.0 mm/Km	2980	3.98	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:45:46	133	100	800	25.0 cm	14.8 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:46:03	133	100	900	27.0 cm	21.1 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:46:17	133	100	1000	22.0 cm	23.9 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:46:30	133	100	1100	21.0 cm	27.7 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:46:43	133	100	1200	21.0 cm	28.2 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:46:58	133	100	1300	29.0 cm	25.2 Km/Hr	2900.0 mm/Km	2980	3.98	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:47:22	133	100	1400	28.0 cm	14.7 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:50:12	133	100	1500	20.0 cm	12.0 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:51:36	133	100	1600	22.0 cm	14.3 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:52:01	133	100	1700	24.0 cm	14.2 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:52:23	133	100	1800	25.0 cm	18.2 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:53:05	133	100	1900	24.0 cm	18.9 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.4437265	N	84.0791712	E	Normal
09/01/25	20:53:36	133	100	2000	23.0 cm	11.3 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4437265	N	84.0791712	E	Normal

SA/GE


SA/GE

सहायक अभियन्ता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, भोरे

09.01.25

Executive Engineer
R.W.D. Works Division
Hathua

Name of Customer: M S Vindhyavashni Construction , Machine no: 19193 , Road: Kukur Bhuka Main road IO Chkarwa Khas . Date: 09-01-25 , Section No: 133 . Equation: $Y=0.936X+245.3$

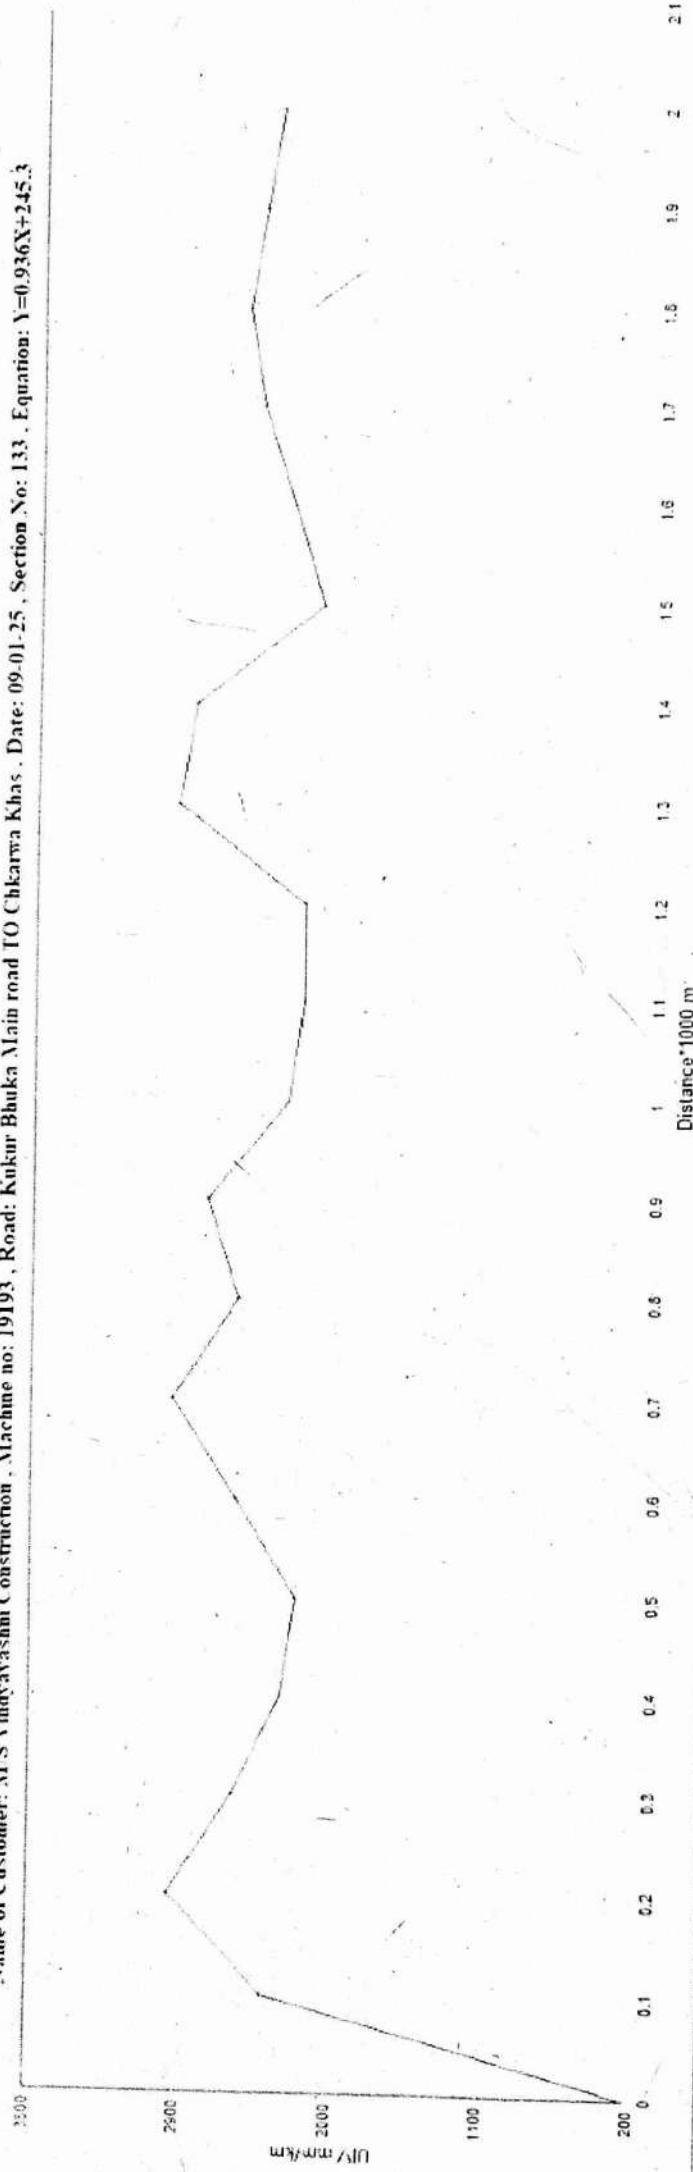

R. K. Jaiswal
SE

R. K. Jaiswal
वा नाई
सहायक अभियन्ता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, भोरे

R. K. Jaiswal
09.01.25
Executive Engineer
R.W.D. Works Division
Hathua

Name of work : L023-Chhathiyaon Manradion to Dighwa (VR6)

Name of customer : M/S Vindyaavashni Construction

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	Ul(mm/Km)	Corrected Ul (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
09/01/25	18:32:46	132	0	0	0.0 cm	1.4 Km/Hr	0.0 mm/Km	245	0.43	Good	26.4495649	N	83.9186030	E	Normal
09/01/25	19:46:26	132	100	100	23.0 cm	17.7 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4956140	N	84.0627451	E	Normal
09/01/25	19:47:11	132	100	200	28.0 cm	17.7 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.4953661	N	84.0635767	E	Normal
09/01/25	19:47:25	132	100	300	21.0 cm	23.6 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.4945960	N	84.0640345	E	Normal
09/01/25	19:47:39	132	100	400	24.0 cm	27.2 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.4939756	N	84.0641413	E	Normal
09/01/25	19:47:55	132	100	500	21.0 cm	22.2 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.4931574	N	84.0644846	E	Normal
09/01/25	19:48:11	132	100	600	20.0 cm	22.2 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.492934	N	84.0645533	E	Normal
09/01/25	19:48:25	132	100	700	27.0 cm	25.2 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.4916429	N	84.0644083	E	Normal
09/01/25	19:48:39	132	100	800	29.0 cm	26.2 Km/Hr	2900.0 mm/Km	2860	3.98	Good	26.4907408	N	84.0641413	E	Normal
09/01/25	19:49:58	132	100	900	21.0 cm	14.8 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.4900312	N	84.0637217	E	Normal
09/01/25	19:50:24	132	100	1000	20.0 cm	13.9 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.4899130	N	84.0627298	E	Normal
09/01/25	19:51:06	132	100	1100	22.0 cm	18.4 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4891481	N	84.0625467	E	Normal
09/01/25	19:51:30	132	100	1200	23.0 cm	15.2 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4882746	N	84.0623713	E	Normal
09/01/25	19:53:17	132	100	1300	28.0 cm	13.5 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.4872484	N	84.0624704	E	Normal
09/01/25	19:55:45	132	100	1400	29.0 cm	12.3 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4864798	N	84.0623865	E	Normal
09/01/25	19:56:03	132	100	1500	26.0 cm	20.0 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4855795	N	84.0623560	E	Normal
09/01/25	19:56:19	132	100	1600	29.0 cm	22.0 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4847250	N	84.0623407	E	Normal
09/01/25	19:56:35	132	100	1700	29.0 cm	22.0 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4837618	N	84.0624170	E	Normal
09/01/25	19:56:50	132	100	1800	25.0 cm	24.7 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4830046	N	84.0623560	E	Normal
09/01/25	19:57:06	132	100	1900	26.0 cm	22.1 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4822474	N	84.0625696	E	Normal
09/01/25	19:57:19	132	100	2000	29.0 cm	26.7 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4812918	N	84.0624323	E	Normal

RAJAT
09/01/25
सहायक अभियन्ता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, भोरे

09.01.25
Executive Engineer
R.W.D. Works Division
Hathua

Name of work : L023-Chhathiyaon Mahradion to Dighwa (VR6)

Name of customer : M/S Vindayavashni Construction

(R)Rural Road

Good		Average				Poor									
< 4000		4001 - 5000				> 5000									
09/01/25	19:57:37	132	100	2100	20.0 cm	21.2 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.4805269	N	84.0618372	E	Normal
09/01/25	19:57:59	132	100	2200	20.0 cm	15.8 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.4796972	N	84.0618143	E	Normal
09/01/25	19:58:05	132	100	2300	23.0 cm	15.6 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4787855	N	84.0617533	E	Normal
09/01/25	19:59:30	132	100	2400	27.0 cm	14.4 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.4785700	N	84.0625849	E	Normal
09/01/25	20:00:01	132	100	2500	26.0 cm	11.7 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4778566	N	84.0629435	E	Normal
09/01/25	20:00:26	132	100	2600	26.0 cm	13.7 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4770479	N	84.0632334	E	Normal
09/01/25	20:00:46	132	100	2700	29.0 cm	18.5 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4763441	N	84.0632791	E	Normal
09/01/25	20:01:03	132	100	2800	23.0 cm	20.4 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4755754	N	84.0635767	E	Normal
09/01/25	20:01:19	132	100	2900	23.0 cm	23.4 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4750586	N	84.0634470	E	Normal
09/01/25	20:01:33	132	100	3000	19.0 cm	25.2 Km/Hr	1900.0 mm/Km	2024	2.83	Good	26.4740820	N	84.0632181	E	Normal


Signature
62

Signature
11/11/25

सहायक अभियन्ता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, भोरे

Signature
09.01.25
Executive Engineer
R.W.D. Works Division
Hathua

Name of Customer: M/S Vindyaavashni Construction , Machine no: 19193 , Road: L023-Chhatiyon Mahradion to Dighwa (VR6) , Date: 09-01-25 , Section No: 132 , Equation: $Y=0.936X+245.3$

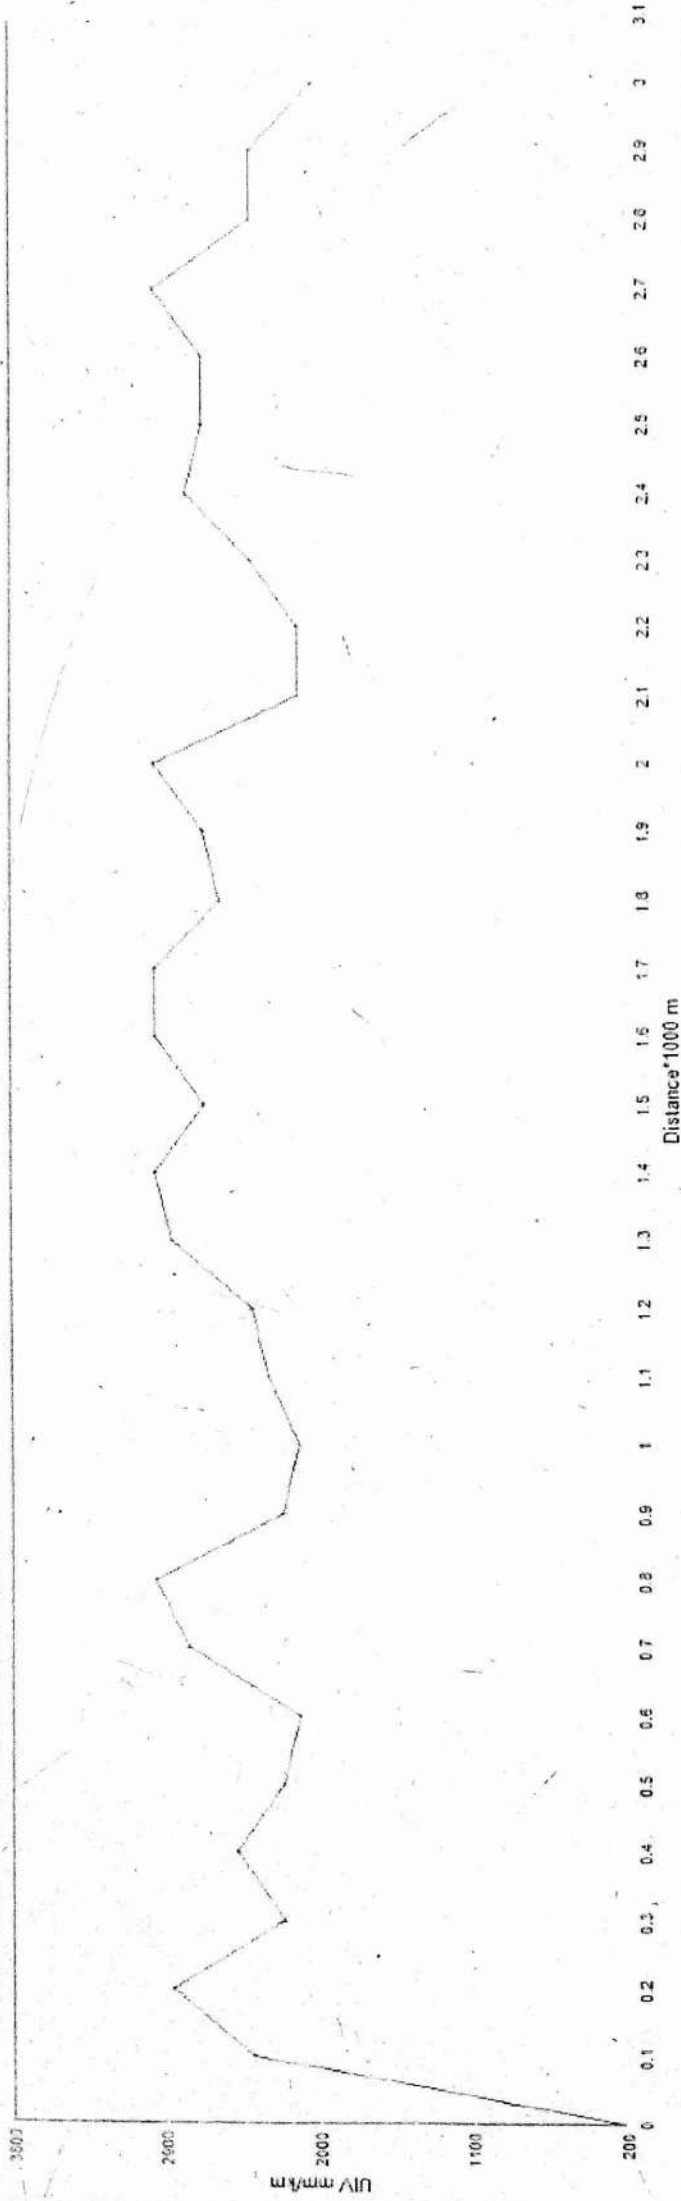

सहायक अभियन्ता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, भोरे

नागार्जुन

09-01-25

Executive Engineer
R.W.D. Works Division
Hathua
