

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिकहरना, ढाका।
पत्रांक - 33(अनु)/सिकहरना, ढाका, दिनांक-11.01.2024

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिकहरना, ढाका।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
ग्रामीण कार्य विभाग,
विश्वसरैया भवन, पाच्चा तल्ला, बिहार, पटना।

विषय :- M/R (3054) New Maintenance Police 2018 योजना हेतु आवंटन अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि इस प्रमंडलान्तर्गत M/R (3054) New Maintenance Police 2018 योजना के अधीन कराये गये कार्य के विरुद्ध भुगतान हेतु आवंटन अधियाचना विहित-प्रपत्र में संलग्न कर समर्पित किया जाता है।

अनुलग्नक :- यथोक्त।

विश्वासभाजन


23/12/24
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
सिकहरना, ढाका।
23/12/24

Rural Works Department
Requisition Formate for Scheme Head-MR(3054) under Bihar Rural New Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
 Name of the Division :- Rural Works Department, Works Div. Dhaka

Sl.	Package No.	Name of Road	Project id as per MIS	A/A Letter No. & Date	Administrative Approval		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to date expenditure as per MIS	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/EA/SIK/24/0004	Pachpakri Gurhenwa to yadavpur Nankar tola	31708617006	1086/01.03.2024	3.900	206.72000	176.14795	31.61569	03 MBD-23.08.2024	22.08.2025		3403	25	5	174.98659	174.98659	1.15342	
2		Ghorasahan Bakuliya path nahar to parariya, ward no.-1	31786103671		1.480	154.70000	107.86763	11.15669		22.08.2025		2730	25	5	106.46789	106.46789	0.95171	
3		Purnahiya Vijayce road to Vijayce khas, ward no.-4,5 Pachhiyari tola	31708612040		1.700	120.83000	116.84217	4.30397		22.08.2025		3116	25	5	115.24945	115.24945	1.12403	
4		Nanaura Gurniya diu path to nanaura Dakshinwari tola, ward no.-13,14,16,19 (Musalman tola, SAV)	31708617007		2.018	135.74000	129.69413	6.43943		22.08.2025		2953	25	5	127.99430	127.99430	1.19701	
Total :-															524.70	524.70	4.42617	

प्रमाणित किया जाता है कि पथ में किये गये कार्य के सभी अवयववार 100 प्रतिशत कार्य का दर्ज मापी का सत्यापन संबंधित कनीय अभियंता 50 प्रतिशत मापी का सत्यापन संबंधित सहायक अभियंता एवं 10 प्रतिशत मापी का सत्यापन अशोहस्ताक्षरी यथा कार्यपालक अभियंता द्वारा किया जा चुका है।
 कराया गया कार्य मानक एवं विशिष्टियों के अनुरूप है।

Divisional Secretary Officer
 Rural Works Div, Dhaka

Executive Engineer
 RWD (W) Div. Dhaka

FORM GFR 19-A

(See Government of Indian's Decision (1) below Rule-150)
Form of Utilization Certificate Upto the Month of upto.....
MR-3054 (New Maintenance Policy)

PIU :- EE RWD (W) DIVISION DHAKA

Sl.	Name of the Scheme	Sanction No. & Date with Amount (Rs. In Lakh)	Amount Received (Rs. In Lakh)	Particulars
1	Construction of Rural Roads Under MR-3054 (New maintenance Policy)			Certified that out of Rs. <u>1041.98630</u> Lacs received the year 2024-25 in favor of Executive Engineer, R.W.D. (W), Division Dhaka a sum of Rs. <u>1041.98630</u> ... lacks has been utilized for the purpose of MR-3054 (New Maintenance Policy) Schemes as given in the margin for which it was sanctioned of Rs..... <u>Nil</u> Remaining unutilized at the end of the period under.
Total :-				

Certified that I have satisfied my self that the condition on which the grants-in-aid was sanctioned have been duly fulfilled are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.



Divisional Account Officer
R.W.D. (W) Div., Dhaka

Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conduct by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurement have been recorded in the MBs and test check conducted by the Assistant.
- All other codal Formalities have been observed.

Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD Works.


Executive Engineer

R.W.D.(W) Div., Dhaka


29/12/24

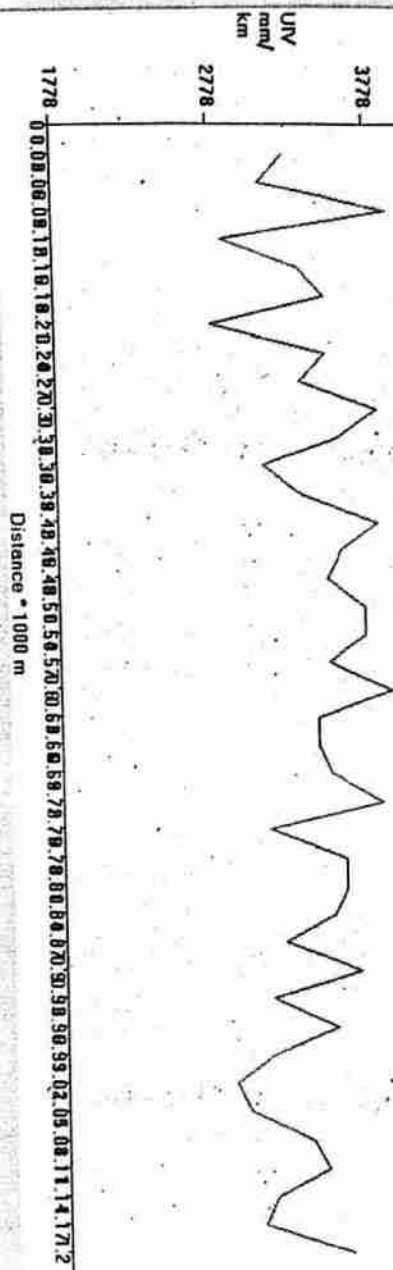
Name of Customer: Vijayee Champaran Construction
 Name of Work: Pachpokri Gunherwa to Tada
 Road:
 Lab Job number:
 Date: 07-Oct-24
 Section No.: 15

Test Date: 07-Oct-24 Road Name: pinwa to Tadapuri Nankar Tola
 Machine No.: 483 Road Type: (R) RURAL ROAD
 Start S No.: Side: Interval:
 Start E No.: UIV Range: 1778 To 5000 mm/Km
 Weather: Dist Range: 0 To 123 0.03 * 1000 m
 Start Location: Equation: $Y = 0 * X^2 + 0.872 * X + 127$
 End Location:

Print Generate Report and Graph

File: C:\Users\DELL\Desktop\07102038.Xls. Section No.: 15. Eqn: $Y = 0 * X^2 + 0.872 * X + 127$

Name of Customer: Vijayee Champaran Construction Private Limited. Name of Work/ Road: Pachpokri Gunherwa to



Redraw Graph

Map View

Subendraraj
09.10.24
J.E

09/11/24
K.E

16.10.24
ET

Name of Contractor:-Vijayee Champaran Construction Private Limited

Name of Road:-Pachpakri Gurhenwa to Yadavpur Nankar Tola

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
7/10/24	10:44:19	15	0.1	370	10.1	3700	3268	G	26.721608	85.184948	Normal
7/10/24	10:45:0	15	0.1	350	10.1	3500	3104	G	26.72106	85.185773	Normal
7/10/24	10:45:29	15	0.1	450	10.1	4500	3920	G	26.720625	85.186665	Normal
7/10/24	10:46:5	15	0.1	320	10.1	3200	2860	G	26.720037	85.187373	Normal
7/10/24	10:46:5	15	0.1	380	10.1	3800	3349	G	26.719758	85.188332	Normal
7/10/24	10:46:40	15	0.1	400	10.1	4000	3512	G	26.719307	85.189123	Normal
7/10/24	10:47:0	15	0.1	310	10.1	3100	2778	G	26.718393	85.189208	Speed
7/10/24	10:47:15	15	0.1	400	10.1	4000	3512	G	26.717477	85.189175	Breaker
7/10/24	10:48:0	15	0.1	380	20.2	3800	3349	G	26.716557	85.189057	Normal
7/10/24	10:48:0	15	0.1	440	20.2	4400	3839	G	26.715593	85.188955	Speed
7/10/24	10:48:26	15	0.1	410	10.1	4100	3594	G	26.714703	85.18882	Breaker
7/10/24	10:49:1	15	0.1	350	20.2	3500	3104	G	26.713778	85.188838	Normal
7/10/24	10:49:1	15	0.1	380	10.1	3800	3349	G	26.712843	85.188955	Normal
7/10/24	10:49:36	15	0.1	440	10.1	4400	3839	G	26.712163	85.189562	Curve
7/10/24	10:50:12	15	0.1	410	10.1	4100	3594	G	26.711272	85.18983	Curve
7/10/24	10:50:47	15	0.1	400	10.1	4000	3512	G	26.710393	85.1901	Normal
7/10/24	10:51:0	15	0.1	430	20.2	4300	3757	G	26.709595	85.19002	Normal
7/10/24	10:51:0	15	0.1	430	20.2	4300	3757	G	26.708762	85.190235	Normal
7/10/24	10:51:22	15	0.1	400	20.2	4000	3512	G	26.707837	85.190168	Speed
7/10/24	10:51:22	15	0.1	450	20.2	4500	3920	G	26.706937	85.19013	Breaker
7/10/24	10:53:43	15	0.1	390	10.1	3900	3431	G	26.706013	85.19007	Normal
7/10/24	10:54:0	15	0.1	390	10.1	3900	3431	G	26.705293	85.190437	Curve
7/10/24	10:54:19	15	0.1	400	20.2	4000	3512	G	26.704428	85.190638	Normal
7/10/24	10:54:19	15	0.1	440	20.2	4400	3839	G	26.704503	85.191598	Speed
7/10/24	10:55:0	15	0.1	350	20.2	3500	3104	G	26.70451	85.192608	Breaker
7/10/24	10:55:29	15	0.1	410	10.1	4100	3594	G	26.704252	85.193585	Normal
7/10/24	10:55:29	15	0.1	410	20.2	4100	3594	G	26.70378	85.194443	Speed
7/10/24	10:56:0	15	0.1	400	20.2	4000	3512	G	26.70349	85.19537	Breaker

$$Y = 0 * X^2 + 0.872 * X + 127$$

X = 8400

Y = 7451

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

Subendrayakr
03.10.24
J. E

9/10/24

9/10/24

9/10/24

Name of Contractor:-Vijayee Champaran Construction Private Limited

Name of Road:-Pachpakri Gurhenwa to Yadavpur Nankar Tola

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
7/10/24	10:56:4	15	0.1	360	20.2	3600	3186	G	26.702992	85.196245	Normal
7/10/24	10:56:4	15	0.1	420	20.2	4200	3676	G	26.7023	85.196968	Normal
7/10/24	10:56:40	15	0.1	350	20.2	3500	3104	G	26.701482	85.197423	Normal
7/10/24	10:57:0	15	0.1	400	20.2	4000	3512	G	26.701048	85.198298	Curve
7/10/24	10:57:15	15	0.1	350	20.2	3500	3104	G	26.701378	85.199175	Normal
7/10/24	10:57:15	15	0.1	320	20.2	3200	2860	G	26.701597	85.20008	Normal
7/10/24	10:57:50	15	0.1	330	10.1	3300	2941	G	26.70194	85.200892	Normal
7/10/24	10:58:0	15	0.1	380	20.2	3800	3349	G	26.702178	85.201902	Speed Breaker
7/10/24	10:58:26	15	0.1	390	20.2	3900	3431	G	26.702523	85.202878	Normal
7/10/24	10:58:26	15	0.1	350	20.2	3500	3104	G	26.703057	85.20367	Normal
7/10/24	10:59:1	15	0.1	340	20.2	3400	3023	G	26.703113	85.203838	Normal
		Length	3.900		Avg	IRI	132736				
						IRI Value	3403				

Handwritten signature
9/10/24

Handwritten signature
9/10/24

Handwritten signature
16.10.24
