

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हथुआ।

पत्रांक- 51

दिनांक- 16-01-2025

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार, ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय :- बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत क्रियान्वित पथ मरम्मत कार्य हेतु राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषयक बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत क्रियान्वित पथ मरम्मत कार्य हेतु राशि की अधियाचना विहित प्रपत्र में की जा रही है।

अतः भवदीय से अनुरोध है कि कॉलम 18 में अंकित राशि उपलब्ध कराने की कृपा की जाय।

अनु0- यथोक्त।

विश्वासभाजन,


16-01-25

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

SI No.	Package No.	Name of Road	Project ID as Per MIS	Administrative Approval (AA) Letter No & Date.	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No & Date	Date & Completion as per Agreement.	Actual Date of Completion	Value of IRI (In MM/KM)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (In Lakh)	UP-to date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (In Lakh)	Amount (In Lakh)	Initial Rectification with surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/23-24/Hathua/06	1052-Hathua Kusaundhi Road To Bigahli Jagadish (VR52)	31407102037	Letter-6115, Dt-04.12.2023	2.900	138.730	101.53517	25.19500	04/MBD/2024-25 Date-22.08.2024	21.05.2025	-	Good	25	5.00	0.000000	0.000000	101.47500	Surface Complete
					2.900	138.730	101.53517	25.19500							0.000000	0.000000	101.47500	

प्रमाणित किया जाता है कि पथ में कराये गये कार्य मानक एवं विशिष्टियों के अनुरूप है।

13/05/2025
13/05/2025

J.E
Hathua

16/01/25
16-01-25

D.A.O
R.W.D Works Division, Hathua.

16-01-25
16-01-25

Executive Engineer,
R.W.D Works Division, Hathua.

FORM GFR 19 - A

(See Government of India's Decision (1) below Rule - 150)
Form utilisation Certificate up to the month of Up to 31.12.2024
MR-3054 (New Maintenance Policy-2018)

RWD Works Division - HATHUA

	Head	Amount Received		Expenditure		Balance	
		IN A/C-	0.00	IN A/C-	0.00	IN A/C-	0.00
1	MR-3054 (New Maintenance Policy-2018)	By CFMS-	1251920318.00	By CFMS-	1249094949.00	By CFMS-	2825369.00
		Total-	1251920318.00	Total-	1249094949.00	Total-	2825369.00
						Certified that sum of Rs 12490.95 Lac has been utilized for the purpose of MR-3054 (New Maintenance Policy-2018) Schemes as given in the margin for which it was sanctioned and that the balance of Rs 28.25 Lac Lacs remaining utilized at the end of the period under.	

2. Certified that I have satisfied myself that the conditions on which the grants-in aid was sanctioned have been duly
Kind of Checks exercised :-

- (i) Works have been supervised by Executive Engineer/Superintending Engineer.
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- (iii) Construction material have been tested.
- (iv) Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
- (v) All other codal formalities have been observed.

3. Physical Progress achieved :-

- (i) Construction of Road Works.
- (ii) Construction of CD Works

15.1.25

D.A.O

Rural Works Department
Works Division Hathua

16.01.25

Executive Engineer

Rural Works Department
Works Division Hathua

Name of work : L052-Hatua Kusaundi Road To Bigah Jagadish (VR52)

Name of customer : Halhwa Construction Private Limited

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	U(m/Km)	Corrected U (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
16/01/25	00:19:21	136	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	245	0.43	Good	26.3639784	N	84.3334970	E	Normal
16/01/25	00:19:56	136	100	100	20.0 cm	18.1 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.3770838	N	84.2580576	E	Normal
16/01/25	00:20:14	136	100	200	23.0 cm	19.6 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.3770761	N	84.2579737	E	Normal
16/01/25	00:20:57	136	100	300	24.0 cm	18.3 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.3772840	N	84.2563791	E	Normal
16/01/25	00:21:12	136	100	400	24.0 cm	22.7 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.3772840	N	84.2563791	E	Normal
16/01/25	00:21:26	136	100	500	24.0 cm	25.2 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.3772840	N	84.2563791	E	Normal
16/01/25	00:21:39	136	100	600	26.0 cm	27.9 Km/Hr	2600.0 mm/Km	2879	3.64	Good	26.3772840	N	84.2563791	E	Normal
16/01/25	00:21:51	136	100	700	25.0 cm	30.3 Km/Hr	2500.0 mm/Km	2565	3.53	Good	26.3772840	N	84.2563791	E	Normal
16/01/25	00:22:04	136	100	800	16.0 cm	26.2 Km/Hr	1600.0 mm/Km	1743	2.48	Good	26.3772840	N	84.2563791	E	Normal
16/01/25	00:22:20	136	100	900	20.0 cm	24.6 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.3772840	N	84.2563791	E	Normal
16/01/25	00:22:44	136	100	1000	23.0 cm	14.4 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.3772840	N	84.2563791	E	Normal
16/01/25	00:23:07	136	100	1100	21.0 cm	15.7 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.3772840	N	84.2563791	E	Normal
16/01/25	00:23:17	136	100	1200	23.0 cm	12.9 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.3786917	N	84.2486658	E	Normal
16/01/25	00:26:37	136	100	1300	25.0 cm	14.3 Km/Hr	2500.0 mm/Km	2565	3.53	Good	26.3783063	N	84.2490396	E	Normal
16/01/25	00:27:06	136	100	1400	26.0 cm	11.8 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.3774081	N	84.2494440	E	Normal
16/01/25	00:27:40	136	100	1500	22.0 cm	11.2 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.3776369	N	84.2502756	E	Normal
16/01/25	00:28:01	136	100	1600	27.0 cm	16.2 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.3772345	N	84.2511377	E	Normal
16/01/25	00:28:15	136	100	1700	18.0 cm	25.7 Km/Hr	1800.0 mm/Km	1930	2.72	Good	26.3772154	N	84.2521296	E	Normal
16/01/25	00:28:28	136	100	1800	20.0 cm	28.0 Km/Hr	2000.0 mm/Km	2117	2.95	Good	26.3770933	N	84.2531595	E	Normal
16/01/25	00:28:41	136	100	1900	21.0 cm	28.2 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.3769102	N	84.2541361	E	Normal
16/01/25	00:28:10	136	100	2000	18.0 cm	12.0 Km/Hr	1800.0 mm/Km	1930	2.72	Good	26.3763809	N	84.2543955	E	Normal

15/01/2025

16-01-25

Name of work : L052-Hathua Kusaunchi Road To Bigahi Jagadish (VR52)

Name of customer : Hathua Construction Private Limited


(R)Rural Road				
Good		Average		Poor
< 4000		4001 - 5000		> 5000

16/01/25	00:29:25	136	100	2100	16.0 cm	24.0 Km/Hr	1600.0 mm/Km	1743	2.48	Good	26.3755751	N	84.2537470	E	Normal
16/01/25	00:29:38	136	100	2200	13.0 cm	27.2 Km/Hr	1300.0 mm/Km	1462	2.12	Good	26.3748465	N	84.2532206	E	Normal
16/01/25	00:29:52	136	100	2300	19.0 cm	24.9 Km/Hr	1900.0 mm/Km	2024	2.83	Good	26.3740683	N	84.2529459	E	Normal
16/01/25	00:30:07	136	100	2400	16.0 cm	23.4 Km/Hr	1800.0 mm/Km	1743	2.48	Good	26.3742895	N	84.2520227	E	Normal
16/01/25	00:30:20	136	100	2500	15.0 cm	29.7 Km/Hr	1500.0 mm/Km	1649	2.36	Good	26.3742189	N	84.2512217	E	Normal
16/01/25	00:30:43	136	100	2600	14.0 cm	16.2 Km/Hr	1400.0 mm/Km	1556	2.24	Good	26.3732138	N	84.2507029	E	Normal
16/01/25	00:31:04	136	100	2700	12.0 cm	17.1 Km/Hr	1200.0 mm/Km	1368	2	Good	26.3726931	N	84.2503595	E	Normal
16/01/25	00:31:25	136	100	2800	15.0 cm	17.4 Km/Hr	1500.0 mm/Km	1649	2.36	Good	26.3715944	N	84.2498713	E	Normal
16/01/25	00:32:00	136	100	2900	13.0 cm	10.2 Km/Hr	1300.0 mm/Km	1462	2.12	Good	26.3713217	N	84.2489786	E	Normal

15/01/25
15/01/25

16-01-25

Name of Customer: Hathwa Construction Private Limited , Machine no: 19193 , Road: L052-Hathwa Kusaundhi Road To Bigahi Jagadish (VR52) , Date: 15-01-25 , Section No: 137 , Equation: $Y=0.936X+245.3$

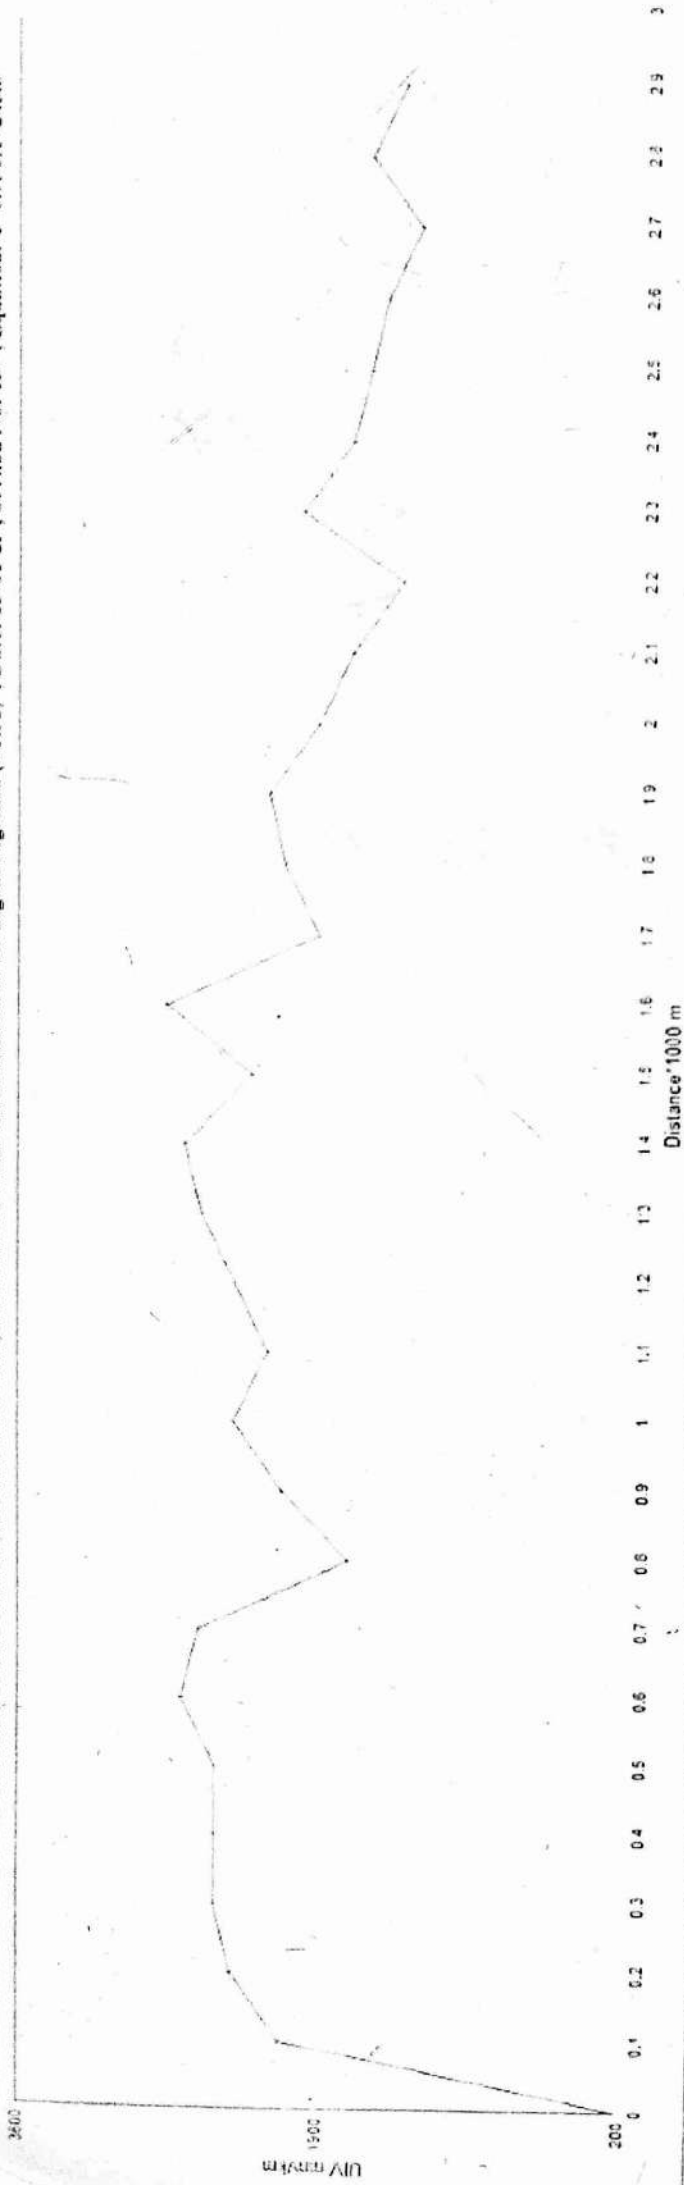

[Signature]
(15.01.25)

[Signature]
15/01/2025
