

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य सिमरी बख्तियारपुर।

पत्रांक:- 56/2025

सिमरी बख्तियारपुर दिनांक:- 09.01.2025

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिमरी बख्तियारपुर।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
ब्राडा, पटना।

विषय:- 3054 बिहार ग्रामीण पथ नई अनुरक्षण नीति 2018 के योजना अन्तर्गत में
अधियाचित राशि का आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के अनुपालन में 3054 बिहार ग्रामीण पथ नई
अनुरक्षण नीति 2018 के योजना अन्तर्गत राशि की मांग संलग्न विहित प्रपत्र में पथवार की
गई है।


अतः भवदीय से अनुरोध है कि विहित प्रपत्र के कॉलम 18 में अंकित कुल राशि
का आवंटन उपलब्ध कराने की कृपा की जाय। अधियाचित राशि के संदर्भ में Bump
Intrigater Report की छाया प्रति संलग्न कर समर्पित किया जा रहा है।

अनु० यथोक्त।

विश्वासभाजन


09/01/25

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिमरी बख्तियारपुर।


09.01.2025

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Simri Bakhtiyarpur

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allotted Amount (1 Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (In lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (In lac)										
1	RM/SA/SIM/24/0004	Sonpura Panchyat Near sonpura Pokhar TO Pillu Tola	20904412021	Letter no-6120 Dated-04.12.2023	1.23	55.666	30.3925	12.1889	05MBD/MR-3054/2024-25 dated -19.08.2024	18/05/2025	28/10.2024	2.810	25mm	5%	0.00	0.00	30.39250	Complete
2	RM/SA/SIM/24/0004	Bhatauni Panchayat NH-107 Sonvarsa Raj Road Bhatauni Hospital TO Bhagwanpur Tola	20904412025	Letter no-6120 Dated-04.12.2023	1.365	84.23	60.24482	9.99941	05MBD/MR-3054/2024-25 dated -19.08.2024	18/05/2025	6/1/2025	2.920	25mm	5%	0.00	0.00	50.00000	Complete
3	RM/SA/SIM/24/0004	NH-107 Bhatauni Panchayat TO Tengrahi Harijan Tola via Tulsiyahi	20904413013	Letter no-6120 Dated-04.12.2023	4.0	199.869	132.5185	31.50000	05MBD/MR-3054/2024-25 dated -19.08.2024	18/05/2025	6/1/2025	3.190	25mm	5%	0.00	0.00	70.00000	Complete
4	RM/SA/SIM/24/0004	Mahamadpur Panchyat Bela Tola Mushari TO Morkahi	20904412022	Letter no-6120 Dated-04.12.2023	1.08	55.06	36.58792	8.85645	05MBD/MR-3054/2024-25 dated -19.08.2024	18/05/2025	6/1/2025	2.600	25mm	5%	0.00	0.00	36.58792	Complete
5	RM/SA/SIM/24/0005	Saroja Panchayat bakhtiyarpur chapram road brahmasthan to harijan tola	20904413009	Letter no-6120 Dated-04.12.2023	0.550	26.658	15.27659	5.59290	04/MBD/MR-3054/2024-25 dated-19.08.2024	18/05/2025	9/1/2025	3.010	25mm	5%	0.00	0.00	15.27659	Complete

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allotted Amount (I Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (In lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (In lac)										
6	RM/SA/SIM/24/0005	Saroja Panchayat Bhaktiyarpur Chapram Main Road Rampur Haat TO Rampur Village	20904412020	Letter no-6120 Dated-04.12.2023	1.050	61.808	43.37436	8.75885	04/MBD/MR-3054/2024-25 dated-19.08.2024	18/05/2025	9/1/2025	2.820	25mm	5%	0.00	0.00	43.37436	Complete
7	RM/SA/SIM/24/0005	Saroja panchayat balwa bakhtiyarpur chapram road rampur brahmasthan to paswan tola	20904413008	Letter no-6120 Dated-04.12.2023	0.730	38.558	26.40792	6.14560	04/MBD/MR-3054/2024-25 dated-19.08.2024	18/05/2025	9/1/2025	2.750	25mm	5%	0.00	0.00	26.40792	Complete


 09/10/25
 Executive Engineer
 RWD Works Division
 Simri Bakhtiyarpur
 09.10.2025

Form GFR 19- A
(See Government of India's Decision (I) below Rule - 150)
Form of Utilazation Certificate upto the month of Jan -2025
New Maintenance Policy 2018

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs)	Amount Received (in lacs)	Particulars
1	1	Letter No 103 Dated 01.10.2024	Rs 7057.11436 Vide Letter No 140 Dated 27/12/2024	Certified that out of RS 7057.11436 lacs of grants in aid sanctioned during the Years up to 2024-25 in favour of Executive Engineer, RWD Works Division Simri Bakhtiyarpur under this Department, a sum of Rs 6787.33436 lacs has been utilized for the purpose of New_MR Scheme remaining 269.78000 unutilized at the end of the period under report.
		Total :	7057.11436	

Certified and verified myself that the conditions on which the grants in aid was sanctioned have been duly fulfilled / are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kinds of Checks exercised :-

- i Works have been supervised by Executive Engineer/ Superintending Engineer.
- ii Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- iii Construction material have been tested.
Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
- iv
- v All other codal formalities have been observed.

Physical Progress achieved :-

- i Construction of Road works.
- ii Construction of CD works

Sr D.A.O
RWD works Division
Simri Bakhtiyarpur

Executive Engineer
RWD works Division
Simri Bakhtiyarpur

Sr D.A.O
09/01/25
Mo
09/01/25


Name of work :	Sonpura Panchyat Near sonpura Pokhar TO Pillu Tola	
Name of customer :	MD Belal	
(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
06/01/2025	15:00:43	238	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	88	0.17	Good	25.749968	N	86.540818	E	Normal
06/01/2025	15:01:26	238	100	100	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.749968	N	86.540818	E	Normal
06/01/2025	15:01:44	238	100	200	14.0 cm	31.8 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.749968	N	86.540818	E	Normal
06/01/2025	15:01:56	238	100	300	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.749968	N	86.540818	E	Normal
06/01/2025	15:02:06	238	100	400	21.0 cm	29.7 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.749968	N	86.540818	E	Normal
06/01/2025	15:02:15	238	100	500	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.749968	N	86.540818	E	Normal
06/01/2025	15:02:31	238	100	600	21.0 cm	25.7 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.74883	N	86.539867	E	Normal
06/01/2025	15:02:44	238	100	700	17.0 cm	20.2 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.74883	N	86.539867	E	Normal
06/01/2025	15:03:02	238	100	800	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.743491	N	86.532735	E	Normal
06/01/2025	15:03:23	238	100	900	21.0 cm	25.7 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.743491	N	86.532735	E	Normal
06/01/2025	15:03:49	238	100	1000	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.743491	N	86.532735	E	Normal
06/01/2025	15:04:06	238	100	1100	18.0 cm	21.6 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.743491	N	86.532735	E	Normal
06/01/2025	15:04:31	238	100	1200	21.0 cm	25.7 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.743491	N	86.532735	E	Normal
06/01/2025	15:04:47	238	100	1300	17.0 cm	20.2 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.743491	N	86.532735	E	Normal

Mans
09/01/2025
ASTM

SM
09/01/25
EE

Name of Customer: MD Belal, Machine no: 19215, Road: Sonpura Panchyat Near sonpura Pakhar TO Pillu Tola, Date: 16/01/25, Section No: 238, Equation: $Y=0.934X+88.4$

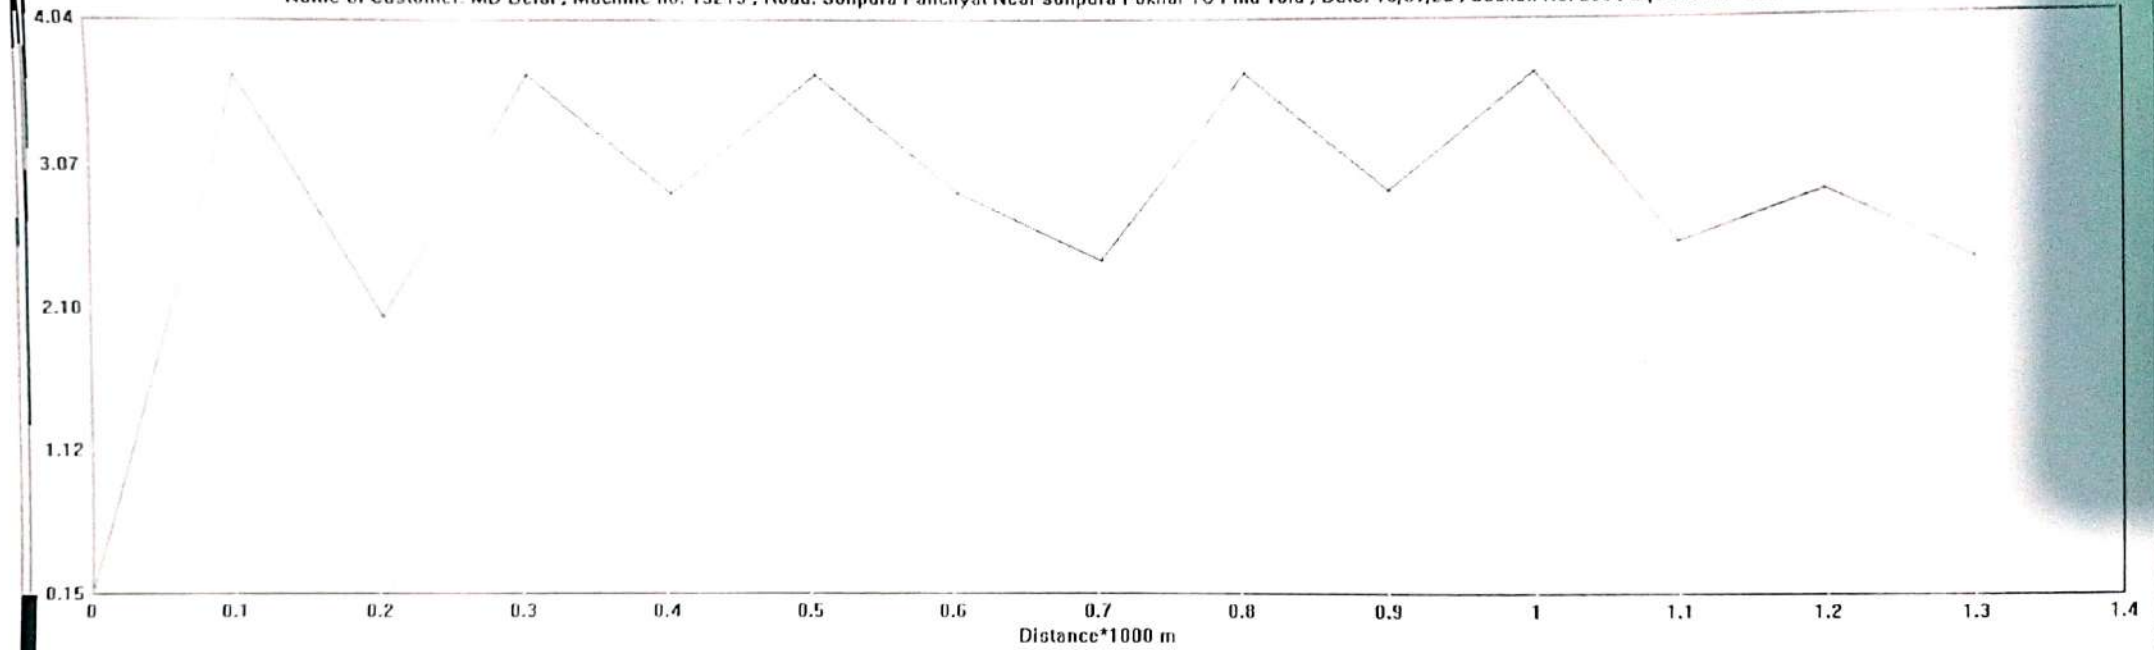

Manu
09/01/2025
ASTM

Su
09/01/25
EE

Name of work : Bhatauni Panchayat NH-107 Sonvarsa Raj Road Bhatauni
Hospital TO Bhagwanpur Tola

Name of customer : MD Belal

(R)Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000


Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
06/01/2025	15:47:43	241	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	86	0.17	Good	25.720337	N	86.668193	E	Normal
06/01/2025	15:47:43	241	100	100	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.720337	N	86.668193	E	Normal
06/01/2025	15:47:43	241	100	200	14.0 cm	31.8 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.720337	N	86.668193	E	Normal
06/01/2025	15:47:43	241	100	300	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.720337	N	86.668193	E	Normal
06/01/2025	15:47:43	241	100	400	21.0 cm	29.7 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.717998	N	86.666784	E	Normal
06/01/2025	15:47:43	241	100	500	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.717998	N	86.666784	E	Normal
06/01/2025	15:49:13	241	100	600	21.0 cm	25.7 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.717998	N	86.666784	E	Normal
06/01/2025	15:49:13	241	100	700	17.0 cm	20.2 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.717998	N	86.666784	E	Normal
06/01/2025	15:49:13	241	100	800	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.717348	N	86.668372	E	Normal
06/01/2025	15:49:13	241	100	900	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.717348	N	86.668372	E	Normal
06/01/2025	15:52:03	241	100	1000	14.0 cm	31.8 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.717348	N	86.668372	E	Normal
06/01/2025	15:52:03	241	100	1100	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.717792	N	86.668065	E	Normal
06/01/2025	15:52:03	241	100	1200	21.0 cm	29.7 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.717792	N	86.668065	E	Normal
06/01/2025	15:52:03	241	100	1300	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.717792	N	86.668065	E	Normal
06/01/2025	15:52:03	241	100	1400	21.0 cm	25.7 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.717792	N	86.668065	E	Normal

Mans
09/01/2025
ASTM

SW
09/01/25
EE



Name of Customer: MD Belal , Machine no: 19215 , Road: Bhatauni Panchayat NH 107 Sonversa Raj Road Bhatauni Hospital TO Bhagwanpur Tola , Date: 16/01/25 , Section No: 241 , Equation: $Y=0.934X+88.4$

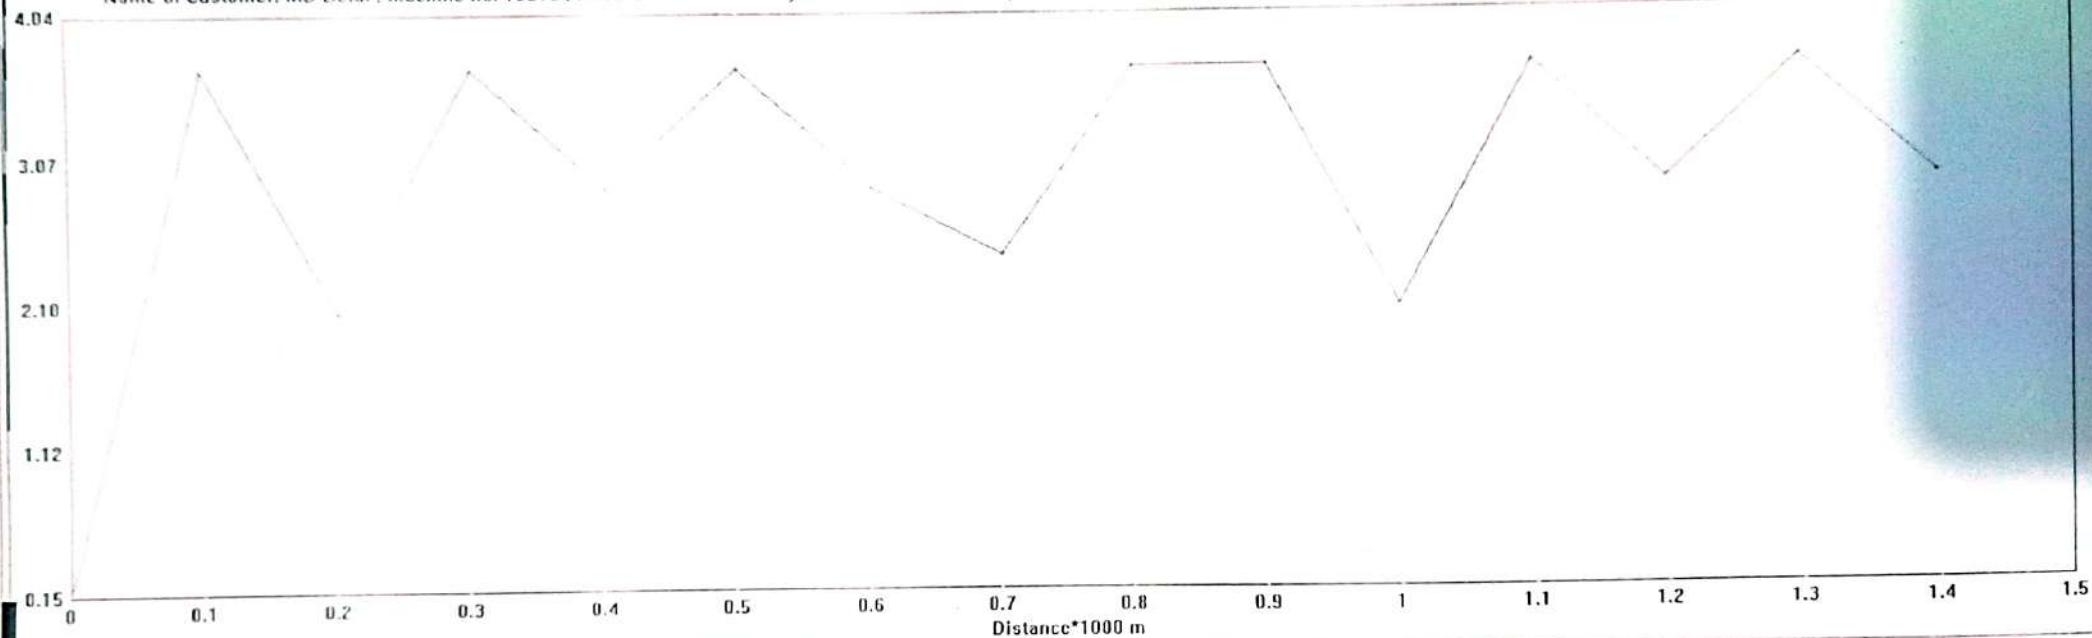

Manu
09/01/2025
ASTM

SW
09/01/25
EE

Name of work : NH-107 Bhatauni Panchayat TO Tengrohi Harljan Tola via
Tulsiyahi

Name of customer : MD Belal

(R) Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
6/1/2025	18:04:43	242	0	0	0.0 cm	27.3 Km/Hr	0.0 mm/Km	88	0.17	Good	25.722198	N	86.67669	E	Normal
6/1/2025	18:04:43	242	100	100	14.0 cm	18.0 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.722198	N	86.67669	E	Normal
6/1/2025	18:04:43	242	100	200	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.722198	N	86.67669	E	Normal
6/1/2025	18:04:43	242	100	300	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.722198	N	86.67669	E	Normal
6/1/2025	18:04:43	242	100	400	20.0 cm	12.4 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.722198	N	86.67669	E	Normal
6/1/2025	18:05:17	242	100	500	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.714701	N	86.676509	E	Normal
6/1/2025	18:05:38	242	100	600	21.0 cm	25.2 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.714701	N	86.676509	E	Normal
6/1/2025	18:06:29	242	100	700	19.0 cm	43.2 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.714701	N	86.676509	E	Normal
6/1/2025	18:06:59	242	100	800	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.714701	N	86.676509	E	Normal
6/1/2025	18:07:27	242	100	900	25.0 cm	41.8 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.714701	N	86.676509	E	Normal
6/1/2025	18:07:41	242	100	1000	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.714701	N	86.676509	E	Normal
6/1/2025	18:07:56	242	100	1100	21.0 cm	25.2 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.713999	N	86.679282	E	Normal
6/1/2025	18:08:18	242	100	1200	25.0 cm	41.8 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.713999	N	86.679282	E	Normal
6/1/2025	18:09:02	242	100	1300	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.713999	N	86.679282	E	Normal
6/1/2025	18:09:24	242	100	1400	21.0 cm	25.2 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.713999	N	86.679282	E	Normal
6/1/2025	18:09:46	242	100	1500	25.0 cm	41.8 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.713999	N	86.679282	E	Normal
6/1/2025	18:10:29	242	100	1600	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.713445	N	86.684496	E	Normal
6/1/2025	18:10:53	242	100	1700	21.0 cm	25.2 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.713445	N	86.684496	E	Normal
6/1/2025	18:11:08	242	100	1800	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.713445	N	86.684496	E	Normal
6/1/2025	18:11:24	242	100	1900	25.0 cm	41.8 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.713445	N	86.684496	E	Normal
6/1/2025	18:11:48	242	100	2000	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.713445	N	86.684496	E	Normal

Mans
09/01/2025
ASTM

SM
09/01/25
EE



Name of work : NH-107 Bhatauni Panchayat TO Tengrahi Harijan Tola via
Tulsiyahi

Name of customer : MD Belal

(R)Rural Road

Good

Average

Poor

< 4000

4001 - 5000


> 5000

6/1/2025	18:12:02	242	100	2100	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.713445	N	86.684496	E	Normal
6/1/2025	18:12:23	242	100	2200	21.0 cm	25.2 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.714681	N	86.687248	E	Normal
6/1/2025	18:12:38	242	100	2300	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.714681	N	86.687248	E	Normal
6/1/2025	18:13:04	242	100	2400	20.0 cm	32.7 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.714681	N	86.687248	E	Normal
6/1/2025	18:13:19	242	100	2500	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.714681	N	86.687248	E	Normal
6/1/2025	18:13:34	242	100	2600	21.0 cm	25.2 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.714681	N	86.687248	E	Normal
6/1/2025	18:13:53	242	100	2700	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.715426	N	86.687387	E	Normal
6/1/2025	18:14:09	242	100	2800	25.0 cm	41.8 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.715426	N	86.687387	E	Normal
6/1/2025	18:14:22	242	100	2900	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.715426	N	86.687387	E	Normal
6/1/2025	18:14:38	242	100	3000	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.715426	N	86.687387	E	Normal
6/1/2025	18:14:59	242	100	3100	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.715426	N	86.687387	E	Normal
6/1/2025	18:15:13	242	100	3200	21.0 cm	25.2 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.715426	N	86.687387	E	Normal
6/1/2025	18:15:30	242	100	3300	19.0 cm	43.2 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.720937	N	86.684392	E	Normal
6/1/2025	18:15:48	242	100	3400	25.0 cm	41.8 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.720937	N	86.684392	E	Normal
6/1/2025	18:16:03	242	100	3500	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.720937	N	86.684392	E	Normal
6/1/2025	18:16:29	242	100	3600	25.0 cm	41.8 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.720937	N	86.684392	E	Normal
6/1/2025	18:16:50	242	100	3700	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.722058	N	86.683093	E	Normal
6/1/2025	18:17:13	242	100	3800	17.0 cm	13.8 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.722058	N	86.683093	E	Normal
6/1/2025	18:17:46	242	100	3900	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.722058	N	86.683093	E	Normal
6/1/2025	18:18:14	242	100	4000	25.0 cm	41.8 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.722058	N	86.683093	E	Normal

Mans
09/01/2025
ASTM

SM
09/01/25
EE



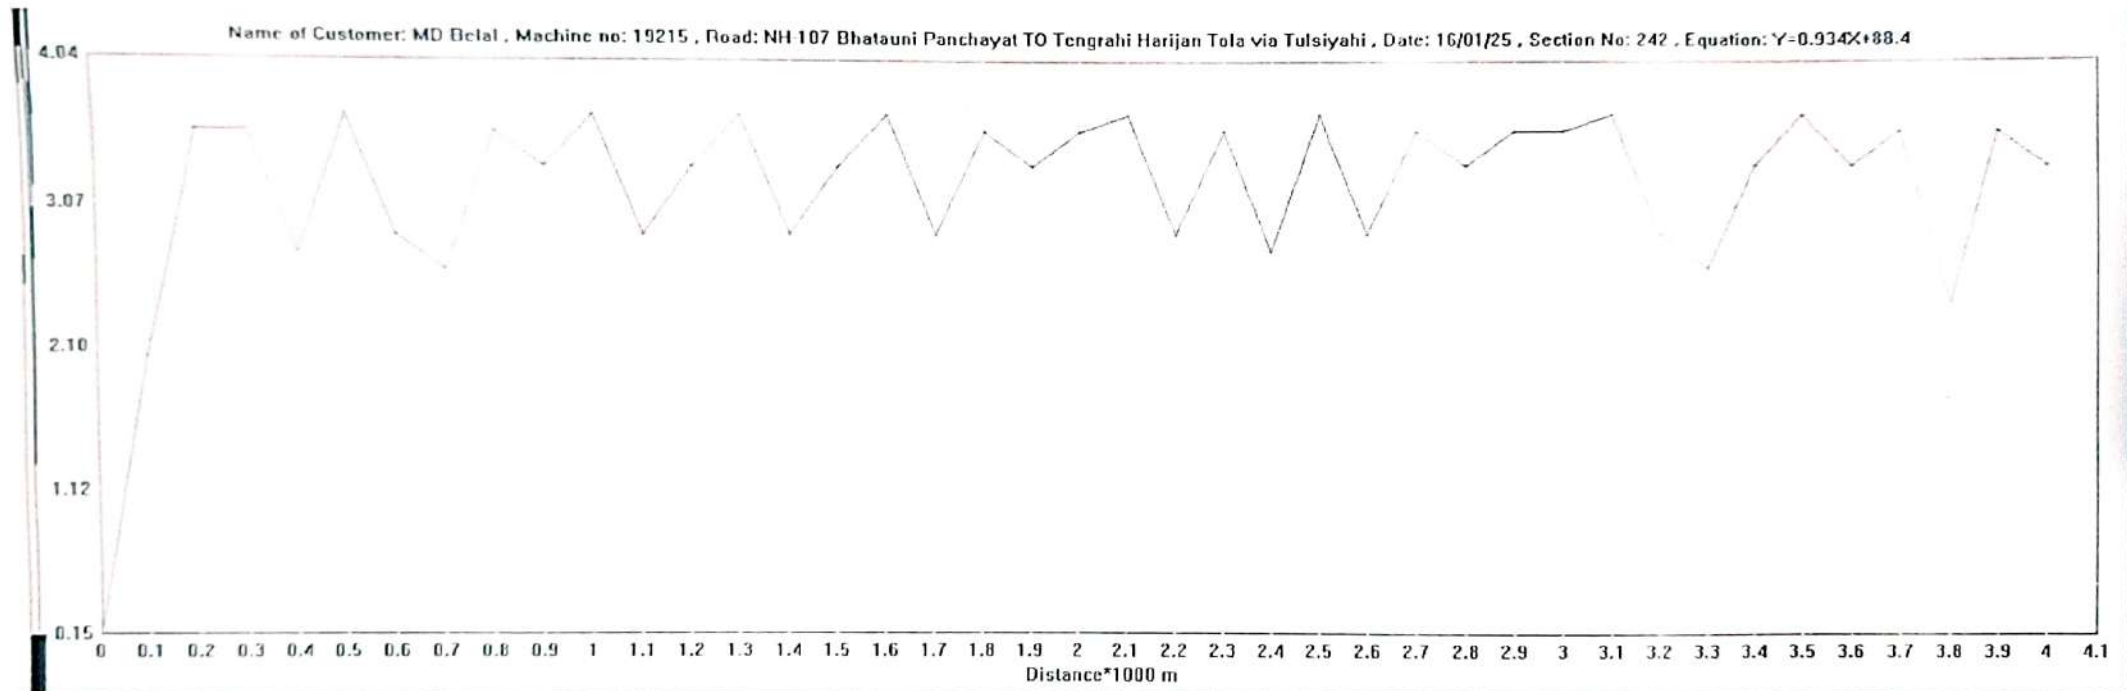

Mans
09/01/2025
ATM

S/S
09/01/25
EE

Name of work :	Mahamadpur Panchyat Bela Tola Mushari TO Morkahl		
Name of customer :	MD Belal		
(R)Rural Road			
Good	Average	Poor	
< 4000	4001 - 5000	> 5000	

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
6/1/2025	15:19:35	239	0	0	0.0 cm	15.7 Km/Hr	0.0 mm/Km	88	0.17	Good	25.783565	N	86.513635	E	Normal
6/1/2025	15:19:35	239	100	100	19.0 cm	36.5 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.783565	N	86.513635	E	Normal
6/1/2025	15:19:35	239	100	200	25.0 cm	44.5 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.783565	N	86.513635	E	Normal
6/1/2025	15:19:35	239	100	300	20.0 cm	32.4 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.783565	N	86.513635	E	Normal
6/1/2025	15:19:35	239	100	400	18.0 cm	19.2 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.762993	N	86.515065	E	Normal
6/1/2025	15:22:05	239	100	500	20.0 cm	32.4 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.762993	N	86.515065	E	Normal
6/1/2025	15:22:05	239	100	600	18.0 cm	19.2 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.762993	N	86.515065	E	Normal
6/1/2025	15:22:05	239	100	700	20.0 cm	32.4 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.762993	N	86.515065	E	Normal
6/1/2025	15:22:05	239	100	800	19.0 cm	36.5 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.762392	N	86.516575	E	Normal
6/1/2025	15:22:05	239	100	900	25.0 cm	44.5 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.762392	N	86.516575	E	Normal
6/1/2025	15:22:05	239	100	1000	18.0 cm	19.2 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.762392	N	86.516575	E	Normal
6/1/2025	15:22:05	239	100	1100	25.0 cm	44.5 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.762392	N	86.516575	E	Normal


Mamz
09/01/2025
ASTM

SW
09/01/25
EE





Name of Customer: MD Belal , Machine no: 19215 , Road: Mahamadpur Panchyat Bela Tola Mushari TO Morkahi , Date: 16/01/25 , Section No: 239 , Equation: $Y=0.934X+88.4$

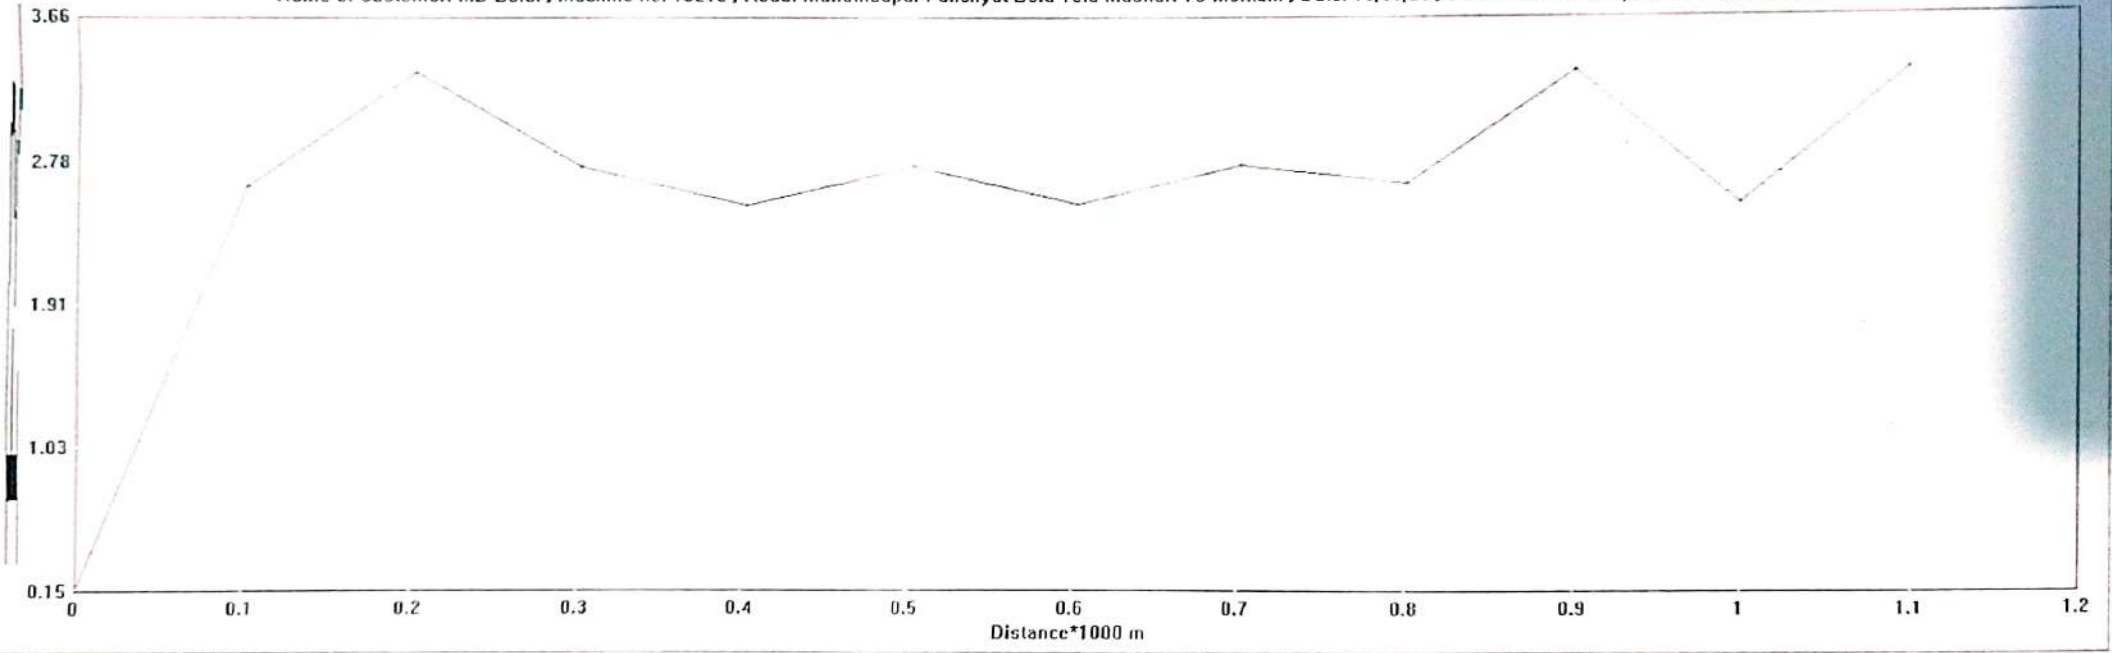

Manus
09/01/2025
ASTM

SW
09/01/25
EE

Name of work : Saroja Panchayat bakhliarpur chapram road brahmasthan to harijan tola

Name of customer : M/S Bijay Kumar Singh

(R)Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000


Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
7/1/2025	13:04:43 PM	245	0	0	0.0 cm	27.3 Km/Hr	0.0 mm/Km	88	0.17	Good	25.764483	N	86.528477	E	Normal
7/1/2025	13:04:43 PM	245	100	100	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.764483	N	86.528477	E	Normal
7/1/2025	13:04:43 PM	245	100	200	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.764483	N	86.528477	E	Normal
7/1/2025	13:06:03 PM	245	100	300	21.0 cm	25.2 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.767407	N	86.526862	E	Normal
7/1/2025	13:06:03 PM	245	100	400	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.767407	N	86.526862	E	Normal
7/1/2025	13:06:03 PM	245	100	500	26.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.767407	N	86.526862	E	Normal
7/1/2025	13:06:03 PM	245	100	600	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.767407	N	86.526862	E	Normal

Mans
09/01/2025
ASTM

SW
09/01/25
EE



Name of Customer: M/S Bijay Kumar Singh , Machine no: 19215 , Road: Saroja Panchayat bakhtiyarpur chaprami road brahminasthan to harijan tola , Date: 16/01/25 , Section No: 245 , Equation: $Y=0.934X+00.4$

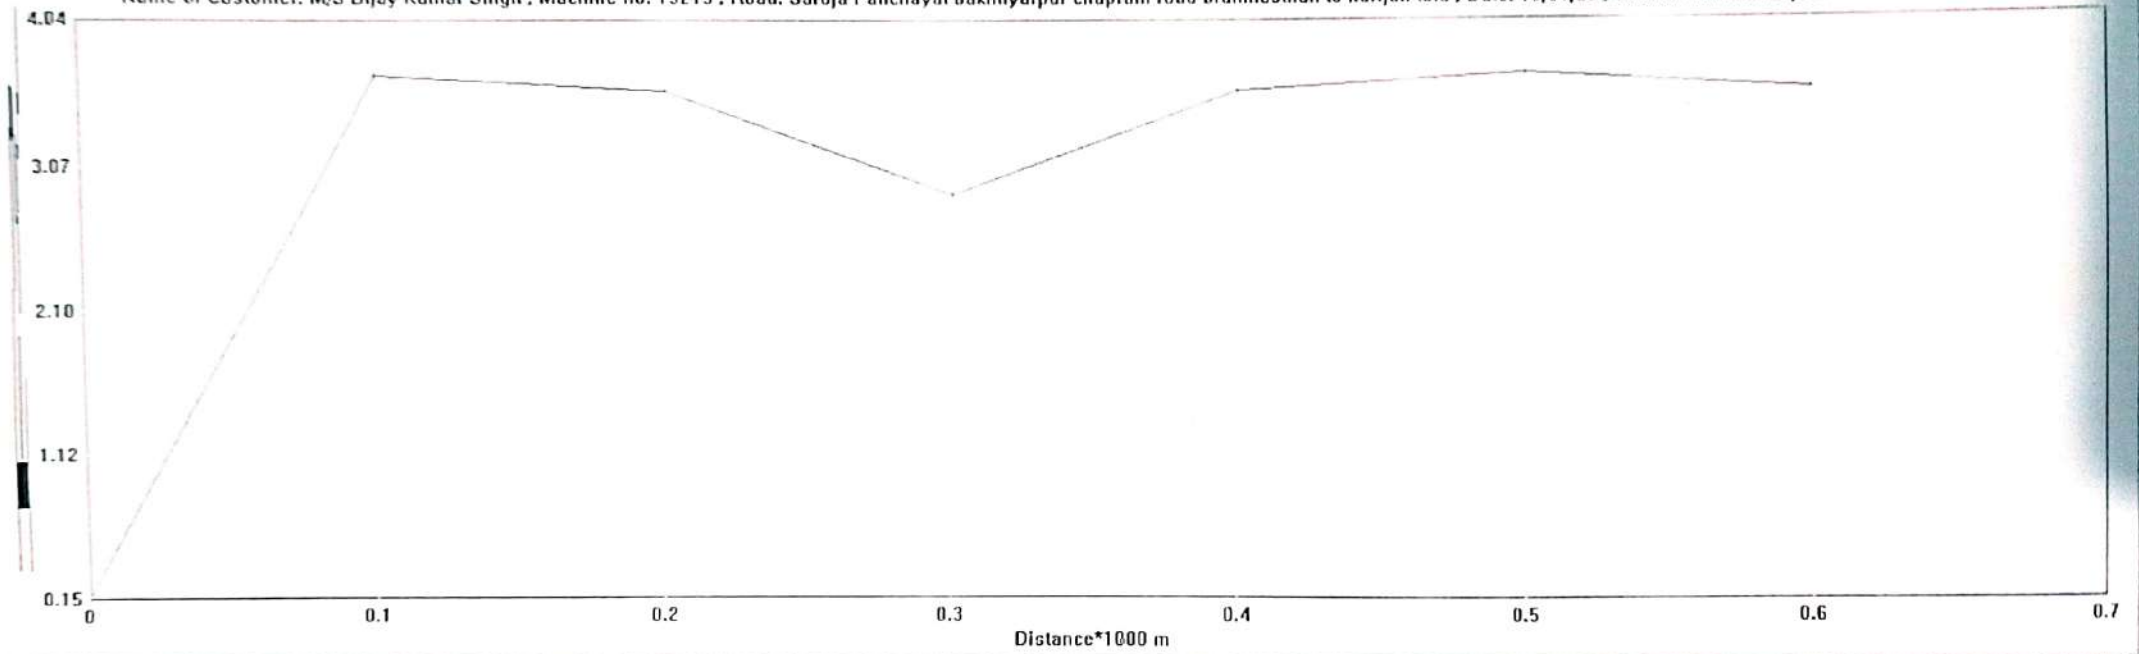

Mans
09/01/2025
ASTM

Sus
09/01/25
EE

Name of work : Saroja Panchayat Bhaktiyarpur Chapram Main Road Rampur
Haat TO Rampur Village

Name of customer : M/S Bijay Kumar Singh

(R) Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000


Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
7/1/2025	15:00:43	244	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	88	0.17	Good	25.764319	N	86.527876	E	Normal
7/1/2025	15:01:26	244	100	100	26.0 cm	9.3 Km/Hr	2600.0 mm/Km	2517	3.44	Good	25.764319	N	86.527876	E	Normal
7/1/2025	15:01:44	244	100	200	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.764319	N	86.527876	E	Normal
7/1/2025	15:01:56	244	100	300	17.0 cm	13.2 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.764319	N	86.527876	E	Normal
7/1/2025	15:02:06	244	100	400	26.0 cm	9.3 Km/Hr	2600.0 mm/Km	2517	3.44	Good	25.765777	N	86.527186	E	Normal
7/1/2025	15:02:15	244	100	500	20.0 cm	19.6 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.765777	N	86.527186	E	Normal
7/1/2025	15:02:31	244	100	600	15.0 cm	23.6 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.765777	N	86.527186	E	Normal
7/1/2025	15:02:44	244	100	700	26.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.765777	N	86.527186	E	Normal
7/1/2025	15:03:02	244	100	800	17.0 cm	20.2 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.763627	N	86.525048	E	Normal
7/1/2025	15:03:23	244	100	900	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.763627	N	86.525048	E	Normal
7/1/2025	15:03:49	244	100	1000	17.0 cm	13.2 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.763627	N	86.525048	E	Normal
7/1/2025	15:03:49	244	100	1100	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.763627	N	86.525048	E	Normal

Mans
09/01/2025
ASTM

SW
09/01/25
EE



Name of Customer: M/S Bijay Kumar Singh, Machine no: 19215, Road: Seroja Panchayat Bhaktiyarpur Chapram Main Road Rampur Haat TO Rampur Village, Date: 16/01/25, Section No: 244, Equation: $Y=0.934X+88.4$

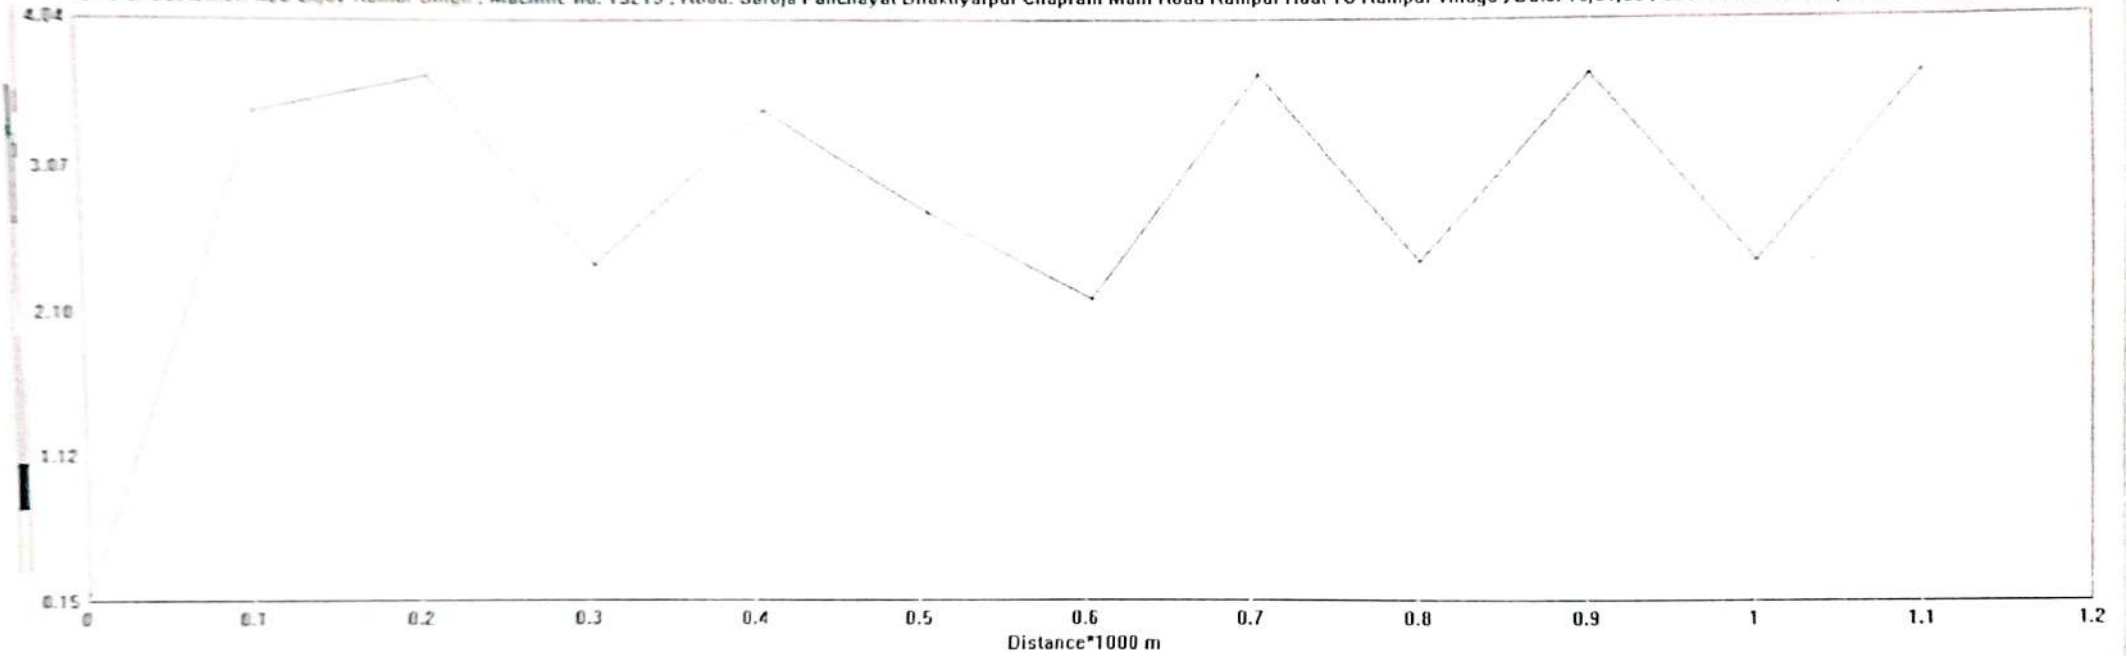

Mans
09/01/2025
ASTM

SW
09/01/25
EE



Name of work : Saroja panchayat balwa bakhtiyarpur chapram road rampur
brahmasthan to paswan tola

Name of customer : M/S Bijay Kumar Singh

(R) Rural Road

Good

Average

Poor

< 4000

4001 - 5000


> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
7/1/2025	18:04:43	246	0	0	0.0 cm	27.3 Km/Hr	0.0 mm/Km	88	0.17	Good	25.764362	N	86.52854	E	Normal
7/1/2025	18:04:43	246	100	100	26.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.764362	N	86.52854	E	Normal
7/1/2025	18:04:43	246	100	200	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.764362	N	86.52854	E	Normal
7/1/2025	18:04:43	246	100	300	15.0 cm	15.6 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.764362	N	86.52854	E	Normal
7/1/2025	18:04:43	246	100	400	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.764362	N	86.52854	E	Normal
7/1/2025	18:05:17	246	100	500	17.0 cm	28.8 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.765488	N	86.525875	E	Normal
7/1/2025	18:05:38	246	100	600	26.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.765488	N	86.525875	E	Normal
7/1/2025	18:06:29	246	100	700	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.765488	N	86.525875	E	Normal
7/1/2025	18:06:59	246	100	800	14.0 cm	18.0 Km/Hr	1400.0 mm/Km	1395	2.03	Good	25.765488	N	86.525875	E	Normal

Mamz
09/01/2025
ASTM

SM
09/01/25
EE



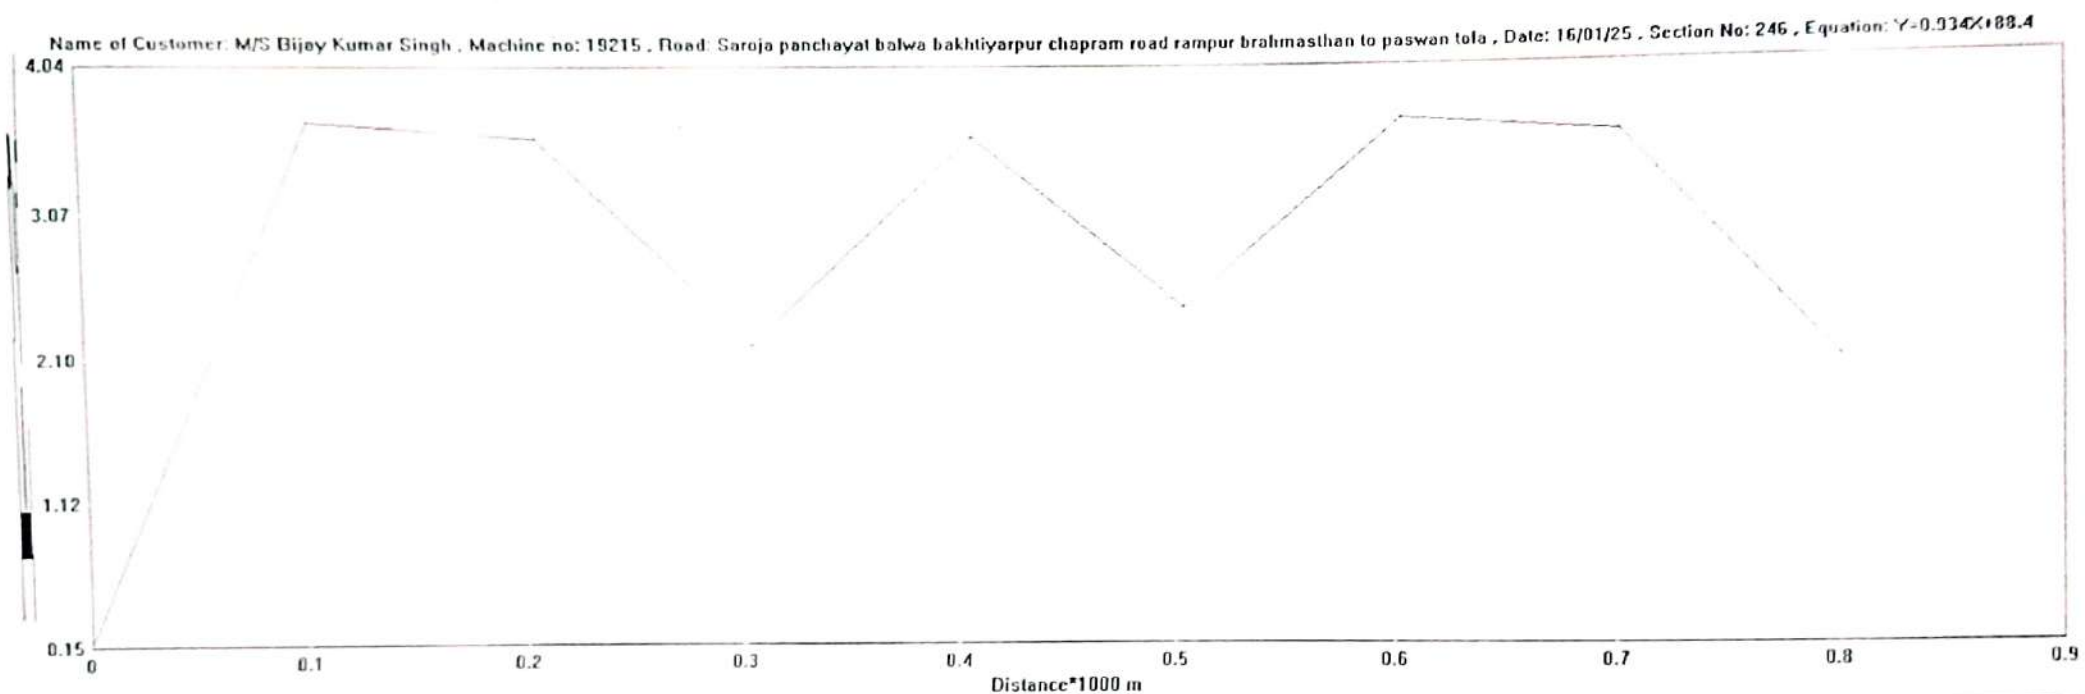

Mans
09/01/2025
ASTM

SV
09/01/25
EE
