

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, नवादा।

पत्रांक :- 428 अनु

/नवादा, दिनांक :- 11/03/2025

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, नवादा।

सेवा में,

नोडल पदाधिकारी (MMGSUY),
ग्रामीण कार्य विभाग,
बिहार पटना।

विषय: MMGSUY (Gen) योजना अंतर्गत आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय से संबंधित विहित प्रपत्र में वांछित सूचना उपलब्ध कराते हुए
अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।
अनु०- यथोक्त।

विश्वासभाजन

ASH
11/03/2025

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नवादा।

K. J.
11/3/25

GENERAL FINANCIAL RULES 2017
Ministry of Finance
Department of Expenditure

GFR 12-B
[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of **Rs. 4,76,13,237/-** , Sanctioned under **2024-25** Vide Letter No. 06 (WE) dated 17.01.2025 in favour of Rural Works Department, Works Division, Nawada, during the year **2024-25** an amount of **Rs. 3,51,00,629/-**, has been utilized for the purpose for which it was sanctioned, and that the balance of **Rs. 1,25,12,608/-** remaining unutilized at the end of the year. has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

1. Works have been supervised by Executive Engineer/ Superintending Engineer
2. Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- 3.
3. Construction materials have been tested
4. Measurements have been recorded in MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
5. All other codal formalities have been observed


DAO 11/3/25
Rural Works Department
Nawada


11/03/2025
Executive Engineer
Rural Works Department
Nawada

Requisition Format for Scheme MMGSUY (General/SC/ST)

Name of the Works Division :- Rural Works Department, Works Division, Nawada

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/BM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
		MMGSUY/23-24/Nawada/03																
		1050260280002																
			NH-31 to Stil Nagar	5.06	530.709	362.49606	05/MMGSUY/MBD/2024-25 17.12.2024	16.12.2025		Completed	3096	25	5.01	72.00000	72.00000	362.49606	290.49606	Completed
			Total	5.060	530.709	362.49606								72.000	72.000	362.496	290.496	

It is certified that Physical & Financial Progress has been updated in MIS.

RWD, Works Division Nawada


 Executive Engineer
 RWD, Works Division
 Nawada

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy (in excell) of recorded IRI is enclosed (As Applicable).

Name of Customer : Eklavya Stone And Mines Priv
 Name of Work/ Road : NH-31 To Sil Nagar
 Lab Job number : 69
 Date : 3/11/2025
 Section No. : 69

Test Date : 3/11/2025 Road Name : NH-31 To Sil Nagar
 Machine No : 408 Road Type : (A) ASPHALTIC
 Start S No : Side : Interval :
 Start E No : Weather :
 Start Location : NH-31 UV Range : 1050 To 5000 mm/km
 Dist Range : 0 To 5.2 0.1 * 1000 m
 End Location : STILL NAGAR Equation : test


Print

Generate Report and Graph

Redraw Graph

Map View


File : C:\Users\Win 10\Desktop\STILL NAGAR HARSH CONSTRUCTION.xlsx Section No. : 69. Egn : test
 Name of Customer : Eklavya Stone And Mines Private Limited. Name of Work/ Road : NH-31 To Sil Nagar. Lab

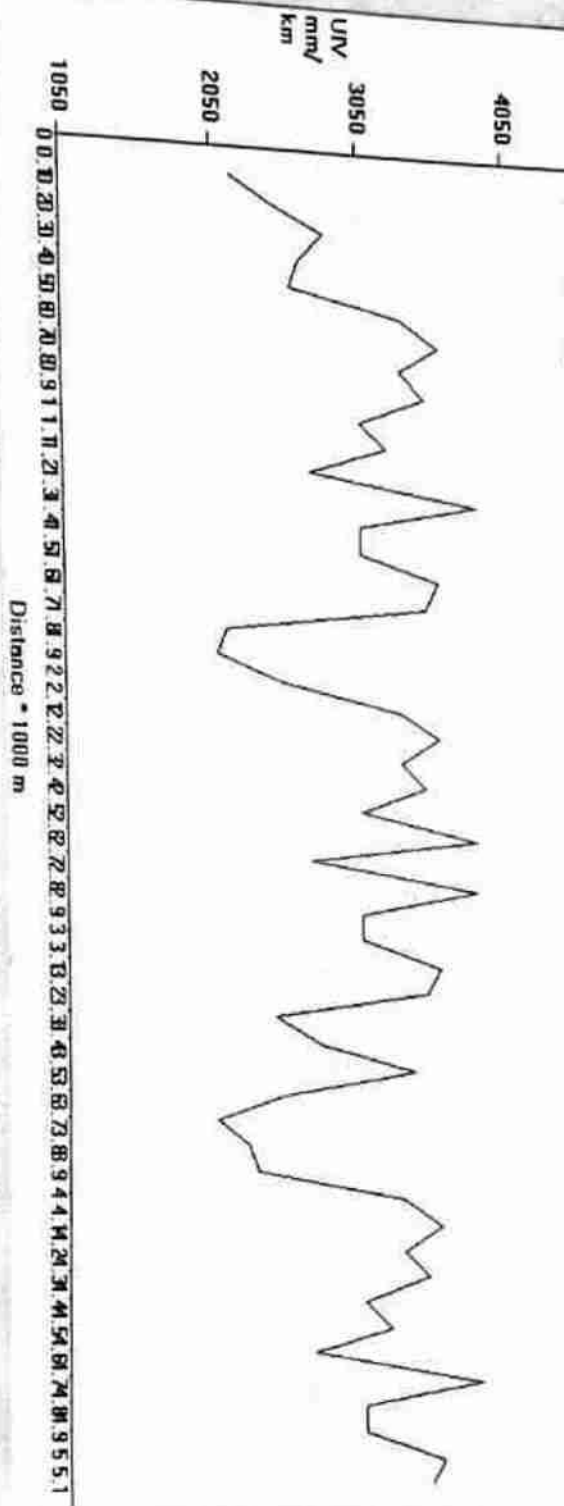

Handwritten:
 11/03/2025
 Laitm

Handwritten:
 11/03/2025
 Executive Engineer
 Rural Works Department
 Kolar Division NAWADA.

File : C:\Users\Win 10\Desktop\STIL NAGAR HARSH CONSTRUCTION.xlsx Section No. : 69, Eqn : test
 Name of Customer : Eklavya Stone And Mines Private Limited, Name of Work/ Road : NH-31 To Stil Nagar, Lab

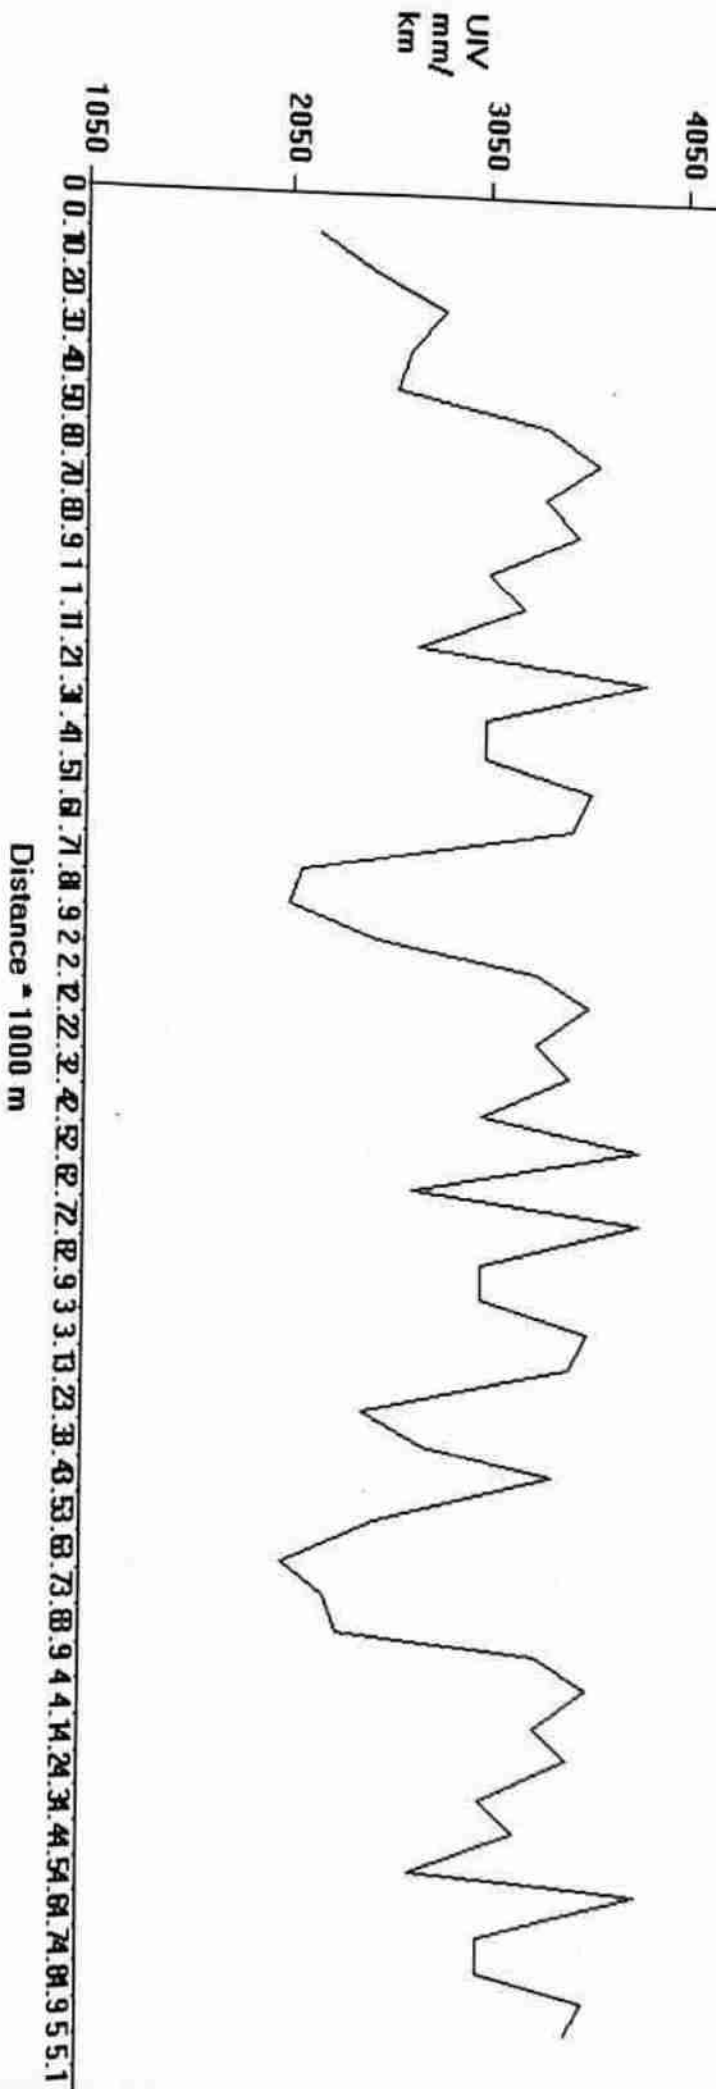

Sk. Singh
 11/03/2025

Sk.
 11/03/2025
 Executive Engineer
 Rural Works Department
 Works Division Nawada

NAME OF ROAD : NH-31 To Sti Nagar
NAME OF CONTRACTOR :- Eklavya Stone And Mines Private Limited
LENGTH OF ROAD (KM) : 5.060
PROJECT ID : 1050260280002

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGOR Y ROAD	Latitude	Longitude	Event			
11/3/2024	10:37:0	69	0.1	210	10.1	2100	2192	G	24.936197	85.53256	Normal			
11/3/2024	10:37:11	69	0.1	240	30.3	2400	2480	G	24.934917	85.533506	Normal			
11/3/2024	10:37:11	69	0.1	280	30.3	2800	2822	G	24.935872	85.51623	Curve			
11/3/2024	10:37:46	69	0.1	260	30.3	2600	2655	G	24.934603	85.515821	Curve			
11/3/2024	10:37:46	69	0.1	250	30.3	2500	2592	G	24.936839	85.521834	Normal			
11/3/2024	10:310:17	69	0.1	330	30.3	3300	3341	G	24.938547	85.531078	Normal			
11/3/2024	10:310:53	69	0.1	360	20.2	3600	3610	G	24.938351	85.530014	speed Breaker			
11/3/2024	10:39:16	69	0.1	330	20.2	3300	3341	G	24.938257	85.52885	Normal			
11/3/2024	10:39:51	69	0.1	350	30.3	3500	3520	G	24.937903	85.526897	Normal			
11/3/2024	10:40:0	69	0.1	300	30.3	3000	3071	G	24.937434	85.525157	Normal			
11/3/2024	10:40:0	69	0.1	320	30.3	3200	3251	G	24.937171	85.523823	Normal			
11/3/2024	10:40:27	69	0.1	260	30.3	2600	2712	G	24.937261	85.524287	Normal			
11/3/2024	10:40:27	69	0.1	390	30.3	3900	3880	G	24.937084	85.522602	Curve			
11/3/2024	10:40:27	69	0.1	300	30.3	3000	3071	G	24.937734	85.526358	Curve			
11/3/2024	10:40:27	69	0.1	300	30.3	3000	3071	G	24.937261	85.524287	Normal			
11/3/2024	10:41:2	69	0.1	360	30.3	3600	3610	G	24.937254	85.524284	Normal			
11/3/2024	10:41:2	69	0.1	350	30.3	3500	3520	G	24.936505	85.52095	Normal			
11/3/2024	10:41:2	69	0.1	210	10.1	2100	2140	G	24.936488	85.520957	Normal			
11/3/2024	10:41:2	69	0.1	200	30.3	2000	2073	G	24.936524	85.519391	Curve			

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Sl. No. 11/03/2025

Executive Engineer
Rural Works Department
Mortals Division Nivada.

NAME OF ROAD : NH-31 To Sili Nagar
NAME OF CONTRACTOR :- Eklavya Stone And Mines Private Limited
LENGTH OF ROAD (KM) : 5.060
PROJECT ID : 1050260280002

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event			
11/3/2024	10:41:37	69	0.1	250	30.3	2500	2524	G	24.936605	85.518344	Curve			
11/3/2024	10:41:37	69	0.1	330	30.3	3300	3341	G	24.93662	85.517426	Curve			
11/3/2024	10:42:0	69	0.1	360	20.2	3600	3610	G	24.936185	85.516849	Curve			
11/3/2024	10:42:12	69	0.1	330	20.2	3300	3341	G	24.935867	85.516178	Curve			
11/3/2024	10:42:12	69	0.1	350	30.3	3500	3520	G	24.935872	85.51623	Normal			
11/3/2024	10:42:12	69	0.1	300	30.3	3000	3071	G	24.934603	85.515821	Curve			
11/3/2024	10:42:410	69	0.1	390	30.3	3900	3880	G	24.934233	85.515061	speedBreaker			
11/3/2024	10:43:0	69	0.1	260	30.3	2600	2712	G	24.934017	85.514266	Curve			
11/3/2024	10:43:0	69	0.1	390	30.3	3900	3880	G	24.933775	85.513332	Normal			
11/3/2024	10:43:210	69	0.1	300	30.3	3000	3071	G	24.93342	85.512214	Curve			
11/3/2024	10:44:3	69	0.1	300	30.3	3000	3071	G	24.933145	85.511111	Curve			
11/3/2024	10:44:17	69	0.1	360	30.3	3600	3610	G	24.932725	85.510052	speedBreaker			
11/3/2024	10:44:17	69	0.1	350	30.3	3500	3520	G	24.932513	85.509021	Normal			
11/3/2024	10:44:52	69	0.1	240	30.3	2400	2454	G	24.932328	85.508104	Normal			
11/3/2024	10:45:46	69	0.1	270	10.1	2700	2768	G	24.932075	85.506181	Normal			
11/3/2024	10:46:17	69	0.1	340	20.2	3400	3427	G	24.931513	85.503912	Normal			
11/3/2024	10:46:53	69	0.1	250	20.2	2500	2518	G	24.931851	85.505181	Curve			
11/3/2024	10:47:16	69	0.1	200	20.2	2000	2050	G	24.931412	85.5033356	Normal			
11/3/2024	10:47:51	69	0.1	220	20.2	2200	2267	G	24.931186	85.501679	Normal			

ok
11/03/2025

Executive Engineer
Rural Works Department
Maddur Division Nawada.

ok
11/03/2025

NAME OF ROAD : NH-31 To Stil Nagar
NAME OF CONTRACTOR :- Eklavya Stone And Mines Private Limited
LENGTH OF ROAD (KM) : 5.060
PROJECT ID : 1050260280002

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event			
11/3/2024	10: 47: 59	69	0.1	230	20.2	2300	2331	G	24.931169	85.5004	Normal			
11/3/2024	10: 410: 05	69	0.1	330	30.3	3300	3341	G	24.929608	85.530806	Normal			
11/3/2024	10: 410: 27	69	0.1	360	20.2	3600	3610	G	24.931112	85.498524	Normal			
11/3/2024	10: 410: 47	69	0.1	330	20.2	3300	3341	G	24.931216	85.497765	Normal			
11/3/2024	10: 410: 55	69	0.1	350	30.3	3500	3520	G	24.93134	85.46691	Normal			
11/3/2024	10: 410: 510	69	0.1	300	30.3	3000	3071	G	24.931419	85.496256	Normal			
11/3/2024	10: 49: 2	69	0.1	320	30.3	3200	3251	G	24.931484	85.495784	Curve			
11/3/2024	10: 49: 15	69	0.1	260	30.3	2600	2712	G	24.932076	85.495579	Normal			
11/3/2024	10: 49: 26	69	0.1	390	30.3	3900	3880	G	24.932052	85.495355	Normal			
11/3/2024	10: 49: 41	69	0.1	300	30.3	3000	3071	G	24.932023	85.494214	Curve			
11/3/2024	10: 49: 57	69	0.1	300	30.3	3000	3071	G	24.932022	85.493955	Curve			
11/3/2024	10: 50: 37	69	0.1	360	30.3	3600	3610	G	24.932034	85.494055	Normal			
11/3/2024	10: 50: 47	69	0.06	350	30.3	3500	3520	G	24.931904	85.495684	Normal			
	Length (KM)		5.06		Average=		3096							

8/4/2025
11/03/2025

Executive engineer
Rural work Department,
works Division Nawada

Lab Job number :69

Date :3/11/2025

Name of Customer :Eklavaya Stone And Mines Private Limited

Name of Work/ Road :NH-31 To Stil Nagar

Sr.no Location of Corrected U.I test(in km) value(mm/km) Road catagory

2	0.1	
3	0.2	2192 G
4	0.3	2480 G
5	0.4	2822 G
6	0.5	2655 G
7	0.6	2592 G
8	0.7	3341 G
9	0.8	3610 G
10	0.9	3341 G
11	1	3520 G
12	1.1	3071 G
13	1.2	3251 G
14	1.3	2712 G
15	1.4	3880 G
16	1.5	3071 G
17	1.6	3071 G
18	1.7	3610 G
19	1.8	3520 G
20	1.9	2140 G
21	2	2073 G
22	2.1	2524 G
23	2.2	3341 G
24	2.3	3610 G
25	2.4	3341 G
26	2.5	3520 G
27	2.6	3071 G
28	2.7	3880 G
29	2.8	2712 G
30	2.9	3880 G
31	3	3071 G
32	3.1	3071 G
33	3.2	3610 G
34	3.3	3520 G
35	3.4	2454 G
36	3.5	2768 G
37	3.6	3427 G
38	3.7	2518 G
39	3.8	2050 G
40	3.9	2267 G
41	4	2331 G
		3341 G

8/11/2025
11/03/2025

ABH
11/03/2025
Executive Engineer
Rural Works Department
Waste Division Nawada.

42	4.1	3610 G
43	4.2	3341 G
44	4.3	3520 G
45	4.4	3071 G
46	4.5	3251 G
47	4.6	2712 G
48	4.7	3880 G
49	4.8	3071 G
50	4.9	3071 G
51	5	3610 G
52	5.1	3520 G

8/8/2025
11/03/2025

ABH
11/03/2025
Executive Engineer
Rural Works Department
Works Division Nawada
