

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, कटिहार।

पत्रांक :- 572 (उद्गुण)

/कटिहार, दिनांक- 12/03/2025

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

सेवा में,

अपर-मुख्य-कार्यपालक-पदाधिकारी,
BRRDA, बिहार, पटना।

विषय :- शीर्ष New Maintenance Policy-2018 योजनान्तर्गत निर्माण हेतु आवंटन की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष New Maintenance Policy-2018 योजनान्तर्गत ग्रा0का0वि0, कार्य प्रमंडल, कटिहार द्वारा विहित प्रपत्र में अधियाचना तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित की जाती है।

अनु0:- यथोक्त।

विश्वासभाजन,


12/3/25

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

ज्ञापांक:- 572

/कटिहार, दिनांक:- 14/03/2025

प्रतिलिपि:- नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।


12/3/25

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month of March, 2024

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

- i. Works have been supervised by Executive Engineer/Superintending Engineer.
 - ii. Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
 - iii. Construction materials have been tested.
 - iv. Measurements have been recorded in the MBs and test check conducted by the Assistant.
 - v. All other codal formalities have been observed.
3. Physical Progress achieved :-
 - i. Construction of Road Works.
 - ii. Construction of CD Works.
4. Certified that:-
 - i. Work has been done as per specification and with quality.

Executive Engineer,
WD (W) Division, Katihar.

BWD (W) Division, Katihar.
8/12/25


RWD, Works Division, Katihar

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Katihar


Sl No	Package no	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allotted Amount (In Lac)	up to date expenditure as per MIS (In Lac)	Requisition Against work done (In lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (In lac)										
1	MR-N/23-24 KATIHAR/08	Kalimandir Chowk To Bakhari Mandal Tola	21105512026	1086/01.03.24	0.731	55.446	37.9577	4.36905	06MBD/2024-25 19.08.2024	18.05.2025	-	3037.00	25mm	5.1%	0.00000	0.00000	36.00000	Surface Complete
2		Mahant Sthan To Nababganj Milik	21105512029	1086/01.03.24	2.700	206.330	140.16762	18.97795	06MBD/2024-25 19.08.2024	18.05.2025	-	3148.66	25mm	5.1%	0.00000	0.00000	135.00000	Surface Complete
3		Awdhesh Nagar To Badhiya Tola	21105513018	1086/01.03.24	3.400	222.350	148.69697	23.64180	06MBD/2024-25 19.08.2024	18.05.2025	-	2888.55	25mm	5.1%	0.00000	0.00000	140.00000	Surface Complete
Total															0.00000	0.00000	311.00000	


Divisional Accounts Officer
RWD, Works Division, Katihar



12/3/25
Executive Engineer
RWD, Works Division, Katihar

प्रमाण पत्र

प्रमाणित किया जाता है कि पथ— Mahant Sthan To Nababganj Milik का सभी अवयवों की जाँच शत प्रतिशत कनीय अभियंता द्वारा किया गया है। सहायक अभियंता द्वारा सभी अवयवों की 50 प्रतिशत से अधिक जाँच किया गया है। अधोहस्ताक्षरी द्वारा 10 प्रतिशत अवयवों की जाँच की गई है।


11/3/25
कनीय अभियंता


11/03/25
सहायक अभियंता


11/3/25
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

Lab Job number :10

Date :10-03-2025

Name of Customer :ARTI KUMARI

Name of Work/ Road :Mahant Sthan To Nababganj Milik

Sr.no	Location of test(in km)	Corrected U.I value(mm/km)	Road catagory
1	0.1	3086	G
2	0.2	2745	G
3	0.3	2404	G
4	0.4	2631	G
5	0.5	2518	G
6	0.6	3199	G
7	0.7	2631	G
8	0.8	2745	G
9	0.9	3540	G
10	1	3086	G
11	1.1	3426	G
12	1.2	3199	G
13	1.3	3426	G
14	1.4	2631	G
15	1.5	2631	G
16	1.6	3199	G
17	1.7	3654	G
18	1.8	3540	G
19	1.9	3767	G
20	2	3767	G
21	2.1	2858	G
22	2.2	3426	G
23	2.3	2858	G
24	2.4	3540	G
25	2.5	3540	G
26	2.6	3654	G
27	2.7	3313	G
		3148.66	

Permit
11/3/25
JE

Sumit
11/03/25
AE

Accepted
11/3/25
Executive Engineer
W.D. (W) Division Kathar

Lab Job number :10

Date :10-03-2025

Name of Customer :ARTI KUMARI

Name of Work/ Road :Mahant Sthan To Nababganj Milik

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
10/3/25	11:23:8	10	0.1	260	0	2600	3086	G	25.476195	87.240029	Normal
10/3/25	11:23:44	10	0.1	230	20.2	2300	2745	G	25.476076	87.239007	Normal
10/3/25	11:24:0	10	0.1	200	20.2	2000	2404	G	25.476069	87.239119	Normal
10/3/25	11:24:19	10	0.1	220	20.2	2200	2631	G	25.47617	87.239131	Normal
10/3/25	11:24:19	10	0.1	210	20.2	2100	2518	G	25.476632	87.238202	Curve
10/3/25	11:25:0	10	0.1	270	20.2	2700	3199	G	25.476393	87.238475	Normal
10/3/25	11:25:0	10	0.1	220	30.3	2200	2631	G	25.477041	87.237328	Normal
10/3/25	11:25:0	10	0.1	230	20.2	2300	2745	G	25.477215	87.236411	Normal
10/3/25	11:25:30	10	0.1	300	20.2	3000	3540	G	25.477386	87.235401	Normal
10/3/25	11:25:30	10	0.1	260	20.2	2600	3086	G	25.477197	87.23617	Normal
10/3/25	11:26:5	10	0.1	290	10.1	2900	3426	G	25.477514	87.234505	Normal
10/3/25	11:26:40	10	0.1	270	10.1	2700	3199	G	25.477441	87.235031	Normal
10/3/25	11:26:40	10	0.1	290	20.2	2900	3426	G	25.478086	87.234172	Normal
10/3/25	11:27:0	10	0.1	220	20.2	2200	2631	G	25.478391	87.233357	Normal
10/3/25	11:27:15	10	0.1	220	20.2	2200	2631	G	25.479337	87.233084	Normal
10/3/25	11:27:51	10	0.1	270	10.1	2700	3199	G	25.478391	87.233357	Speed Breaker
10/3/25	11:28:0	10	0.1	310	10.1	3100	3654	G	25.479437	87.231514	Normal
10/3/25	11:28:26	10	0.1	300	20.2	3000	3540	G	25.479787	84.232319	Normal
10/3/25	11:28:26	10	0.1	320	10.1	3200	3767	G	25.478822	87.231026	Normal
10/3/25	11:29:1	10	0.1	320	20.2	3200	3767	G	25.478201	87.230595	Normal
10/3/25	11:29:1	10	0.1	240	20.2	2400	2858	G	25.476404	87.229292	Normal
10/3/25	11:29:1	10	0.1	290	20.2	2900	3426	G	25.477233	87.229901	Normal
10/3/25	11:29:36	10	0.1	240	20.2	2400	2858	G	25.472654	87.226775	Culvert
10/3/25	11:30:12	10	0.1	300	10.1	3000	3540	G	25.471104	87.225706	Normal
10/3/25	11:30:12	10	0.1	300	10.1	3000	3540	G	25.469623	87.224669	Normal
10/3/25	11:31:22	10	0.1	310	10.1	3100	3654	G	25.470435	87.225172	Normal
10/3/25	11:32:0	10	0.1	280	10.1	2800	3313	G	25.468721	87.223701	Normal

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 2800$$

$$Y = 3313$$

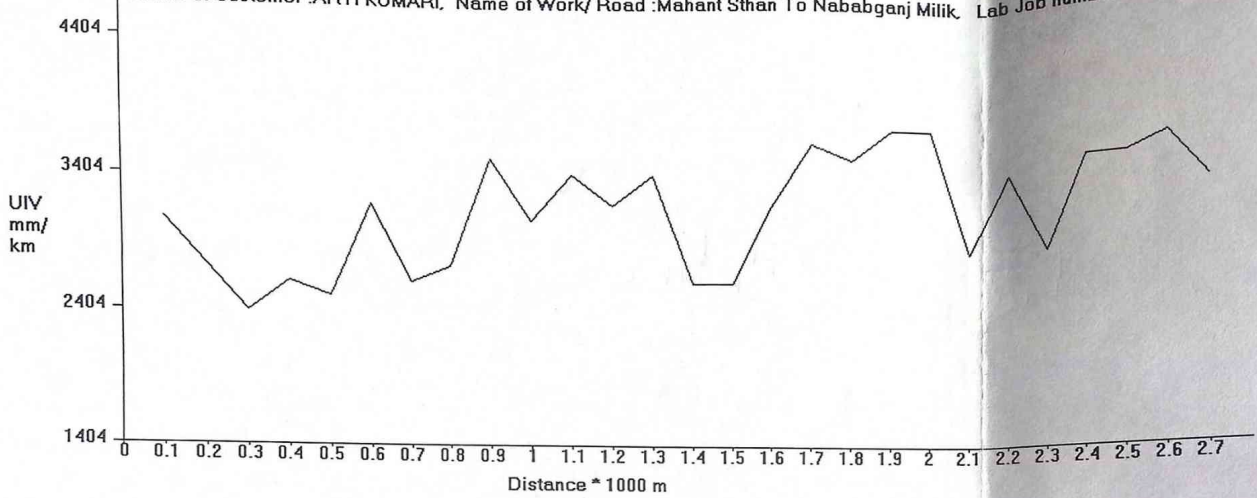
(R) RURAL ROAD
 Good Average Poor
 <4000 4001-5000 >5001

Ameth
 11/03/25
 JC

Sumit
 11/03/25

Sumit
 11/03/25
Executive Engineer
 R.W.D. (W) Division Kathar

File :E:\RAM KUMAR\MISC Files\Bump integrator\Contractor wise\Aarti kumari\Mahant Sthan To Nababganj
 Name of Customer :ARTI KUMARI, Name of Work/ Road :Mahant Sthan To Nababganj Milik, Lab Job number :10



Ramessh
 11/3/25
 JE

Sumit
 11/03/25
 AE

Sumit
 11/3/25
Executive Engineer
 R.W.D. (W) Division Kathar
