

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बांका -1

मोबाइल न०- 8986915292 ईमेल- ee.banka1@gmail.com

पत्रांक- 19603/20 बांका-1

दिनांक- 15.05.2025

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बांका -1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी – सह- सचिव
बिहार ग्रामीण पथ विकास अभिकरण
पटना।

विषय :- शीर्ष नई अनुरक्षण नीति 2018 अंतर्गत राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपरोक्त विषय से सम्बंधित शीर्ष नई अनुरक्षण नीति 2018 अंतर्गत कार्य की अद्यतन स्थिति के अनुसार अधियाचना वांछित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अतः अनुरोध है की आवंटन विमुक्त करने की कृपा की जाय ताकि संवेदक को ससमय भुगतान किया जा सके।

अनु०-यथोक्त।

विश्वासभाजन

Priyam
15.05.25

Priyam
15.5.25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बांका -1

Amem
10/05/2025

FORM GFR 19-A
(See Government of India's Decision (I) below Rule-150)
Form of Utilization Certificate of MR-New Maintenance Policy 2018
As on Dated - **10/05/2025**

PIU-	Banka-I	F.Yr.-- 2025-26		Rs. In Lakhs
Name of Scheme	Sl. No.	Sanction No. & Date	Amount Received (in Rs. Lakhs)	Particulars
Construction of Rural Roads under New Maintenance Policy 2018		Total Allotment-	01-04-2023	Rs. 11,745.10399
	1	Ltr. No.- 63	13-04-2023	Rs. 52.06483
	2	Ltr. No.- 67	27-04-2023	Rs. 262.01578
	3	Ltr. No.- 68	29-04-2023	Rs. -20.77630
	4	Ltr. No.- 72	10-05-2023	Rs. 179.25000
	5	Ltr. No.- 74	16-05-2023	Rs. 207.18858
	6	Ltr. No.- 78	24-05-2023	Rs. 143.00000
	7	Ltr. No.- 81	31-05-2023	Rs. 29.70412
	8	Ltr. No.- 85	14-06-2023	Rs. 32.10619
	9	Ltr. No.- 89	21-06-2023	Rs. 147.66008
	10	Ltr. No.- 92	28-06-2023	Rs. 62.00000
	11	Ltr. No.- 102	21-07-2023	Rs. 54.99612
	12	Ltr. No.- 106	02-08-2023	Rs. 61.51523
	13	Ltr. No.- 113	14-08-2023	Rs. 28.00000
	14	Ltr. No.- 117	28-08-2023	Rs. 40.00000
	15	Ltr. No.- 136	10-10-2023	Rs. 9.98181
	16	Ltr. No.- 159	29-11-2023	Rs. 129.90000
	17	Ltr. No.- 14	06-02-2024	Rs. 386.39997
	17	Ltr. No.- 31	09-03-2024	Rs. 123.04123
	18	Ltr. No.- 31	26-03-2024	Rs. 392.31591
	19	Ltr. No.- 68	06-05-2024	Rs. -15.44963
	20	Ltr. No.- 69	06-05-2024	Rs. 35.20736
	21	Ltr. No.- 74	03-06-2024	Rs. 190.58705
	22	Ltr. No.- 79	19-06-2024	Rs. 10.34984
	23		28-06-2024	Rs. 29.61548
	24		25-07-2024	Rs. 164.49833
	25		17-08-2024	Rs. 13.08163
	26			Rs. 72.80917
	27			Rs. 132.89931
	28		06.12.2024	Rs. 170.05000
	29	Ltr. No.- 29	30.03.2025	Rs. 450.46690
Total Allotment --- ---			Rs. 15,269.58298	

2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-


116.73616

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.

3 Physical Progress achieved:

- Construction of Road Works.


Div. Acct Officer
RWD (Works Division), Banka-I


15.05.25
Executive Engineer
RWD (Works Division), Banka-I
Amun
10/05/2025

Circle : Bhagalpur

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Banka-1

Sl. Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allocated Amount (Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (in lac)	Remarks
				Length (in Km)	Amount (in Lac)	Initial Rectification with Surface Renewal	5 yrs Routine Maintenance										
1	RMBV/ BAN/ 24004 1059, Behar Jhanka T04 To kersjore (VRS9)	20703502183	1086 ----- 01-03-2024	1.600	77.93500	56.53890	12.20621	MBD-02/24 25 ----- 16-08-2024	15.05.2025	N/A	3133	25	5% (With Including Waste Plastic)	32.38286	32.38286	23.89377	Surface Complete
2	RMBV/ BAN/ 24003 Sahetpang Gachhva RCD Road to Chhitrasen	20703513017	1086 ----- 01-03-2024	2.080	113.49500	89.38625	13.60299	MBD-02/24 25 ----- 16-08-2024	15.05.2025	N/A	3127	25	5% (With Including Waste Plastic)	51.47974	51.47974	35.17211	Surface Complete
3	RMBV/ BAN/ 24003 1068 Samukhya more to Kadihara (TRAC K.68)	20703502190	1086 ----- 01-03-2024	1.900	131.67000	102.16071	13.46070	MBD-02/24 25 ----- 16-08-2024	15.05.2025	N/A	3129	25	5% (With Including Waste Plastic)	57.87927	57.87927	42.60971	Surface Complete
4	RMBV/ BAN/ 24003 1407 Parachak to Rajwara Khoji (V.R. 8)	N2070350020 57	1086 ----- 01-03-2024	2.000	101.66400	77.43587	14.18531	MBD-02/24 25 ----- 16-08-2024	15.05.2025	N/A	3127	25	5% (With Including Waste Plastic)	43.59167	43.59167	33.44962	Surface Complete
Grand Total -																135.12521	


15.5.25

Priyam
15.05.25
Executive Engineer
RWD Works Division
Banka-1
Shanon
10/05/2025


**Office of the Executive Engineer
Rural Works Department, Works Division, Banka-1**

Name of Road :- L027 Parachak to Rajwara khoji (VR 8)
Name of Scheme :- 3054 / MR (New maintenance Policy 2018)
Name of contractor/Agency:- M/S Balajee Construction
Length of Road :- 2.0 km
Project ID :- N207035002057
Package No. :- MR-N/23-24 BANKA-1/07
Batch No. :- RM/BA/BAN/24/0003
Name of Block :- Phullidumar


Certified that
100% Measurement
has been checked by me


Junior Engineer RWD
Work section Phullidumar
Works Division : Banka-1

Certified that
50% Measurement
has been checked by me


Assitant Engineer RWD
Work Sub Division Phullidumar
Works Division : Banka-1

Certified that
10% Measurement
has been checked by me


Executive Engineer,
Rural Works Department,
Works Division : Banka-1

Name of Customer :

Name of Work/ Road :Parachak to Rajwara Khoji

Sr.no	Location of test(in km)	Corrected U.I value(mm/km)	Road catagory
2	0.1	3180	G
3	0.2	3367	G
4	0.3	3086	G
5	0.4	2992	G
6	0.5	3273	G
7	0.6	2805	G
8	0.7	2992	G
9	0.8	3180	G
10	0.9	3273	G
11	1	2899	G
12	1.1	3367	G
13	1.2	2992	G
14	1.3	3180	G
15	1.4	3460	G
16	1.5	3273	G
17	1.6	2803	G
18	1.7	3204	G
19	1.8	3123	G
20	1.9	2997	G
21	2	3103	G

20/04/25
SR

21/04/25
A.2

Priyam
06/02/25

Name of Customer : Balaji Construction
Name of Work/ Road : 1027 Parachak to Rajwara Khoji
Lab Job number : 72
Date : 2/4/2025
Section No. : 72

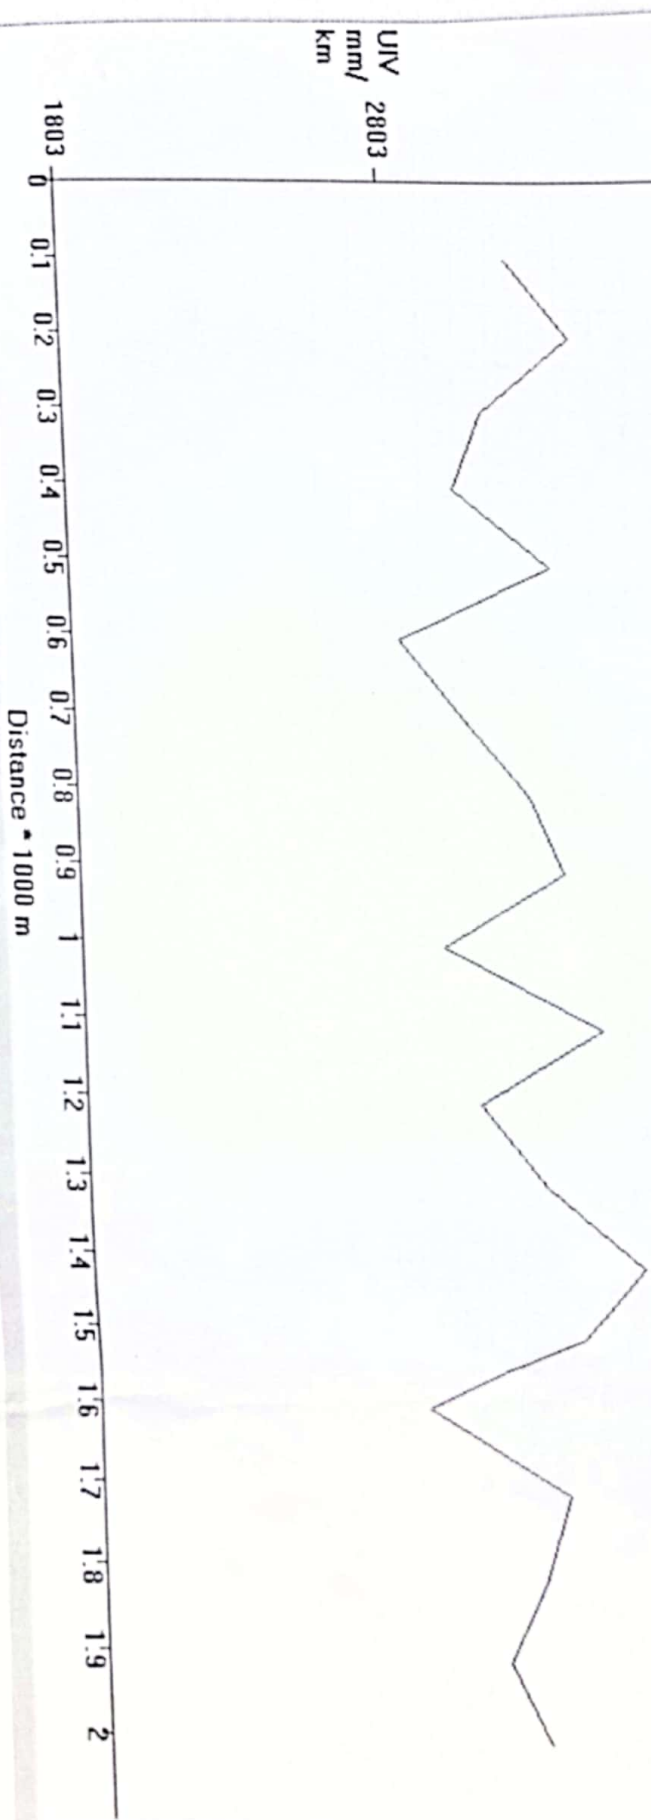
Test Date : 2/4/2025
Machine No. : 19612
Start S No. :
Start E No. :
Weather :
Start Location :
End Location :
Road Name :
Road Type : (A) ASPHALTIC
Side :
UIV Range : 1803 To 4000 Interval 1000 mm/km
Dist Range : 0 To 2.1 0.1 1000 m
Equation : test

Print
 Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\Welcome\Desktop\Parachak.Xls, Section No. : 72, Eqn : test
 Name of Customer : Balaji Construction, Name of Work/ Road : 1027 Parachak to Rajwara Khoji, Lab Job number



So 2/4/25

Pilgaw
20/02/25

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			$Y = 0 * X^2 + 0.866 * X + 501.6$			
04/02/25	13:17:02	72	0.1	310	30.3	3100	3180	G	24.988605	86.818574	Normal	X = 3500		
04/02/25	13:17:22	72	0.1	330	30.3	3300	3367	G	24.988821	86.818827	Normal	Y = 3532		
04/02/25	13:17:43	72	0.1	300	30.3	3000	3086	G	24.988208	86.818823	Normal			
04/02/25	13:18:03	72	0.1	290	30.3	2900	2992	G	24.987179	86.818752	Normal			
04/02/25	13:18:24	72	0.1	320	30.3	3200	3273	G	24.986949	86.817759	Normal	RURAL ROAD		
04/02/25	13:18:46	72	0.1	270	30.3	2700	2805	G	24.986072	86.817997	Normal	Good	Average	Poor
04/02/25	13:19:06	72	0.1	290	20.2	2900	2992	G	24.985365	86.818183	Curve	<4000	4001-5000	>5001
04/02/25	13:19:26	72	0.1	310	20.2	3100	3180	G	24.98447	86.818464	Curve			
04/02/25	13:19:47	72	0.1	320	30.3	3200	3273	G	24.983576	86.818936	Normal			
04/02/25	13:20:08	72	0.1	280	30.3	2800	2899	G	24.9827	86.818812	Normal			
04/02/25	13:20:28	72	0.1	330	30.3	3300	3367	G	24.982272	86.818744	Normal			
04/02/25	13:20:49	72	0.1	290	30.3	2900	2992	G	24.981145	86.818688	Normal			
04/02/25	13:21:09	72	0.1	310	30.3	3100	3180	G	24.980247	86.818888	Normal			
04/02/25	13:21:30	72	0.1	340	30.3	3400	3460	G	24.978936	86.818913	Normal			
04/02/25	13:21:51	72	0.1	320	30.3	3200	3273	G	24.97824	86.818917	Normal			
04/02/25	13:22:11	72	0.1	280	30.3	2800	2803	G	24.977518	86.818839	Normal			
04/02/25	13:22:33	72	0.1	290	30.3	2900	3204	G	24.976426	86.818953	Normal			
04/02/25	13:22:54	72	0.1	310	30.3	3100	3123	G	24.975718	86.818947	Normal			
04/02/25	13:23:14	72	0.1	320	30.3	3200	2997	G	24.974682	86.819121	Normal			
04/02/25	13:23:35	72	0.1	270	30.3	2700	3103	G	24.973808	86.819532	Normal			
					Average IRI Value= 3127									

6/2/25

IRI/km
6/2/25
