

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, हरनौत।

Email Id-rwdharnaut@gmail.com

Mobile No-8986915905

पत्रांक.....629...../हरनौत

/दिनांक.....23...../5/2025

प्रेषक,

ई0 हिमांशु राज,
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, हरनौत।

सेवामें,


नोडल पदाधिकारी,
एम0आर0 3054 नई अनुरक्षण नीति 2018,
विश्वेश्वरैया भवन,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय : शीर्ष एम0आर0 3054 नई अनुरक्षण नीति 2018 अन्तर्गत पथ में कराये गए कार्य के विरुद्ध अधियाचना भेजने के संबंध में।

महाशय,


उपर्युक्त विषय के संबंध में कहना है कि शीर्ष एम0आर0 3054 नई अनुरक्षण नीति 2018 अन्तर्गत पथ में कराये गए कार्य के विरुद्ध अधियाचना इस पत्र के साथ समर्पित की जा रही है।

विश्वासभाजन,



कार्यपालक अभियंता

ग्रामीण कार्य विभाग, कार्य प्रमंडल,
हरनौत।



Requisition Formate for Scheme Head- MR-3054 Under Bihar Rural Road Maintenance Policy 2018 (In Rectification and Surface Renewal)																		
Division Name:- Rural Works Department, Works Division, Harnaut																		
S.No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lacs)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In Km)	Thickness of Bitumen Layer (In mm)	Value of Bitumen Content in %	Previous Total Alloted Amount (In Lacs)	Upto date Expenditure as per MIS (In Lacs)	Requisition against Work Done (In Lacs)	Remarks
					Length (In Km.)	Amount (In Lacs)	Initial Rectification on with surface Renewal (In Lacs)	5 Years Routine Maintenance (In Lacs)										
1	RM/NA/HAR/23/0004	Noorsaray Nari road to Pariouna	10200716021	2722/28.02.2023	1.330	77.865	55.89400	13.87000	03/M BD/20 23-24 (14.07.23)	13.04.2024	-	3541	25.00	5.00	32.29913	32.29913	22.51354	Work Completed
																	22.51354	

Divisional Accounts Officer
R.W.D, Works Division, Harnaut

Executive Engineer
R.W.D, Works Division, Harnaut

- 3 Physical Progress achieved:
(i) Construction of Road Works.

FORM GFR 19-A
(See Government of India's Decision (I) below Rule-150)
Form of Utilization Certificate of MR-New Maintenance Policy 2018
As on Dated - 22.05.2025

PIU-	Harnaut	F.Y.--	2025-26	Rs. In Lakhs
Name of Scheme	Sl. No.	Sanction No. & Date	Amount Received (in Rs. Lakhs)	Particulars
Construction of Rural Roads under New Maintenance Policy 2018		Opening Balance 01.04.25	₹ 7,793.72330	Certified that out of ₹ 7,985.54284 Lakhs
	33	10.05.25	₹ 191.81954	received & balance of grants-in-aid sanctioned during the Financial Yr. 2025-26 in favour of Executive Engg. R.W.D. Works Division Harnaut, Nalanda, a sum of ₹ 7,650.82910 Lakhs has been utilized for the purpose of MR-3054 New Policy 2018 scheme as given in the margin for which it was sanctioned and that the balance of ₹ 334.71374 Lakhs remaining unutilized at the end of the period under 22 May 2025
Total Allotment --- ---			₹ 7,985.54284	


- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-


- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.

3 Physical Progress achieved:

- Construction of Road Works.


23/05/25
Asst. LT Manager
RWD (Works Division), Harnaut

Sr. Div. Acct. Officer
RWD (Works Division), Harnaut


22.05.25
Executive Engineer
RWD (Works Division), Harnaut

Office of Executive Engineer
Rural Works Department, Works Division -Harnaut


Name of Road : Noorsaray Nari Road to Parlouna
Name Of Scheme : MR-3054 (New Maint.Policy-2018)
Name of Contractor / Agency : Narendra Kr Nirala
Length of Road : 1.33 KM
Project Id : 10200716021
Batch No. : RM/NA/HAR/23/0004
Name of Block : Noorsarai


Certified that 100%
Measurement have been
Checked by Me

Certified that 50% Measurement
have been Checked by Me

Certified that 10%
Measurement have been
Checked by Me

Junior Engineer RWD
Works Section Noorsarai
Works Division - Harnaut


Assitant Engineer RWD
Works Sub Division Noorsarai
Works Division -Harnaut

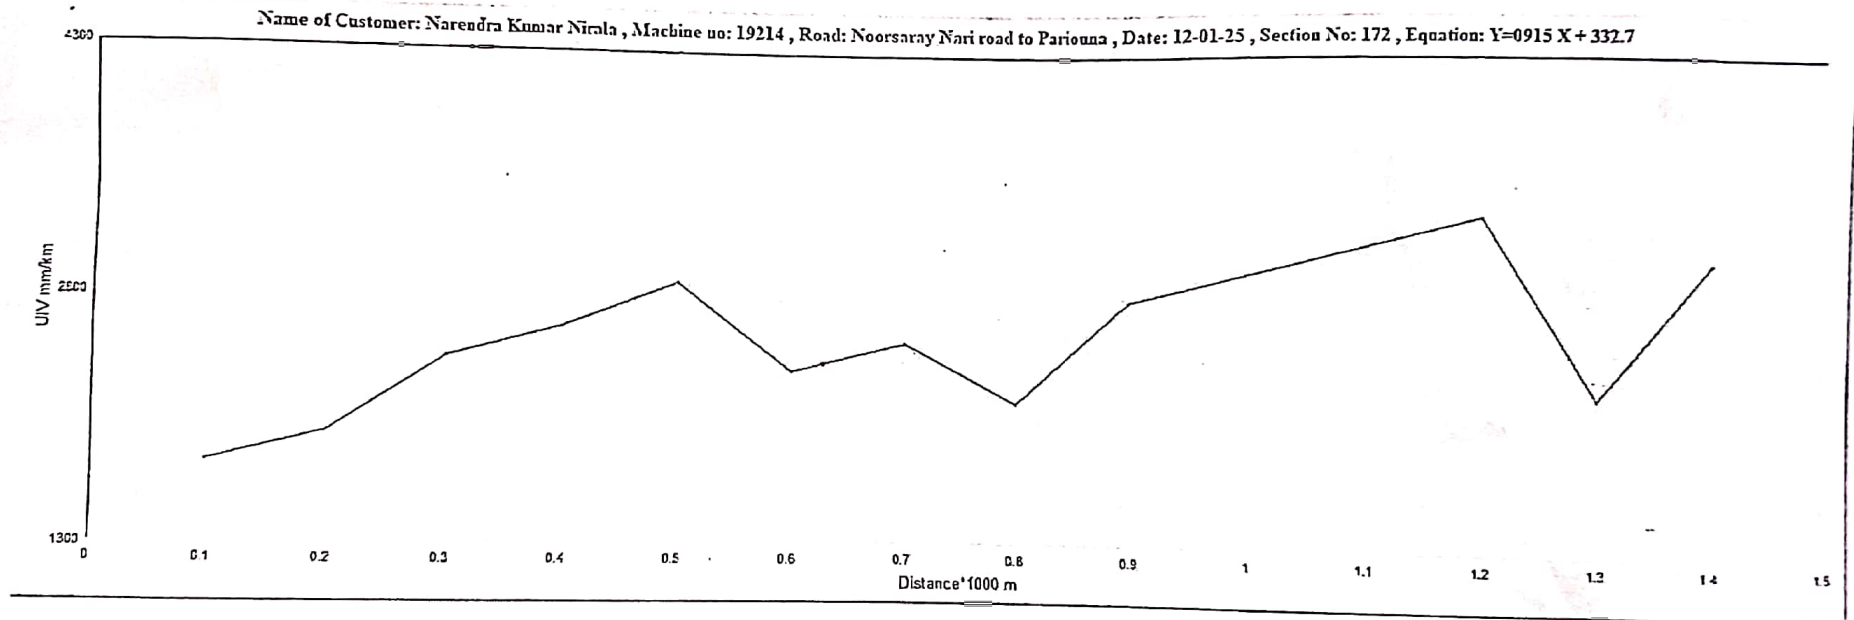

Executive Engineer
Rural works Department
Works Division - Harnaut

Name of work : Noorsaray Nari road to Pariouna		
Name of customer : Narendra Kumar Nirala		
(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
12/01/25	11:41:06	172	100	100	16.0 cm	17.0 Km/Hr	1600.0 mm/Km	1797	2.55	Good	25.2522250	N	85.4712710	E	Normal
12/01/25	11:41:23	172	100	200	18.0 cm	20.1 Km/Hr	1800.0 mm/Km	1980	2.78	Good	25.2508360	N	85.4713430	E	Normal
12/01/25	11:41:52	172	100	300	23.0 cm	18.2 Km/Hr	2300.0 mm/Km	2437	3.35	Good	25.2497930	N	85.4718190	E	Normal
12/01/25	11:42:09	172	100	400	25.0 cm	17.3 Km/Hr	2500.0 mm/Km	2620	3.57	Good	25.2486410	N	85.4719510	E	Normal
12/01/25	11:42:28	172	100	500	28.0 cm	11.7 Km/Hr	2800.0 mm/Km	2895	3.9	Good	25.2489880	N	85.4725940	E	Curve
12/01/25	11:42:56	172	100	600	22.0 cm	22.2 Km/Hr	2200.0 mm/Km	2346	3.23	Good	25.2485840	N	85.4735220	E	Normal
12/01/25	11:43:20	172	100	700	24.0 cm	19.3 Km/Hr	2400.0 mm/Km	2529	3.46	Good	25.2485430	N	85.4735610	E	Normal
12/01/25	11:43:48	172	100	800	20.0 cm	18.2 Km/Hr	2000.0 mm/Km	2163	3.01	Good	25.2477340	N	85.4735000	E	Normal
12/01/25	11:44:16	172	100	900	27.0 cm	14.0 Km/Hr	2700.0 mm/Km	2803	3.78	Good	25.2469650	N	85.4736120	E	Curve
12/01/25	11:44:40	172	100	1000	29.0 cm	13.4 Km/Hr	2900.0 mm/Km	2986	4.01	Good	25.2462290	N	85.4735820	E	Normal
12/01/25	11:45:05	172	100	1100	31.0 cm	12.7 Km/Hr	3100.0 mm/Km	3169	4.23	Good	25.2462700	N	85.4735970	E	Normal
12/01/25	11:45:27	172	100	1200	33.0 cm	21.1 Km/Hr	3300.0 mm/Km	3352	4.45	Good	25.2452830	N	85.4734100	E	Breaker
12/01/25	11:45:59	172	100	1300	21.0 cm	15.2 Km/Hr	2100.0 mm/Km	2254	3.12	Good	25.2445970	N	85.4728390	E	Normal
12/01/25	11:46:24	172	100	1400	30.0 cm	22.4 Km/Hr	3000.0 mm/Km	3078	4.12	Good	25.2437170	N	85.4725650	E	Normal

Wf
13/01/25
AB/ Noor Sarai

Wf
13-01/25
EE



wf
13/01/25
AR/Noorsaray

Hyg
13-01-25
EE

16

1

[illegible]

		2.00 hrs	2.00 hrs
③ for RCC M-15	2000 M Stone		
	6.00 hrs.		6.00 hrs.
④ for fixing 600mm Triangle sign			
	6.00 hrs.		6.00 hrs.
⑤ for fixing 600mm Circular sign			
	2.00 hrs.		2.00 hrs.
⑥ for fixing 600mm X 600mm Rectangular			
	4.00 hrs.		4.00 hrs.

Continuation

Scanned with OKEN Scanner
