

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, औरंगाबाद
Email ID:-eerwdaurangabad1@gmail.com Mob:- 8986915333

पत्रांक. 2377 (315)..... औरंगाबाद / दिनांक. 24/8/21.....

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अध्याचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वास भाजन
21/8/21
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल औरंगाबाद
21/08/21

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Aurangabad

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Aurangabad

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/AU/AUR/20/0005	TANDAWA MAHARAJGANJ ROAD TO ITAWA	16281032332	5979/30.10.2019	2	71.198	45.37	21.43	81MBD-2019-20 15.09.2020	14.06.2021	21.08.2021	3120	25MM	5.067%	0.00000	0.00000	45.37	Comp.
TOTAL																	45.37	

[Signature]
21/08/21
Divisional Accounts Officer
Rural Works Department, works Division,
Aurangabad

[Signature]
21/08/21
Executive Engineer
Rural Works Department
Works Division, Aurangabad

Seco Analyzer


Name of Customer : M/S JAIMAA VAISHNAW CON
Name of Work/Road : TANDAWA MAHARAJGANJ R
Lab Job number : 36
Date : 21-09-2021
Section No. : 36

Test Date : 21-09-2021 Road Name : TANDAWA MAHARAJGANJ F
Machine No : 377 Road Type : (R) RURAL ROAD
Start S No : 205 Side : Nabinagar Interval
Start E No : 225
Weather : Normal UV Range : 1518 To 5000 1000 mm/km
Start Location : 24628827.84 Dist Range : 0 To 2.1 0.1 * 1000 m
End Location : 24628867.84 Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print Generate Report and Graph

Redraw Graph

Map View

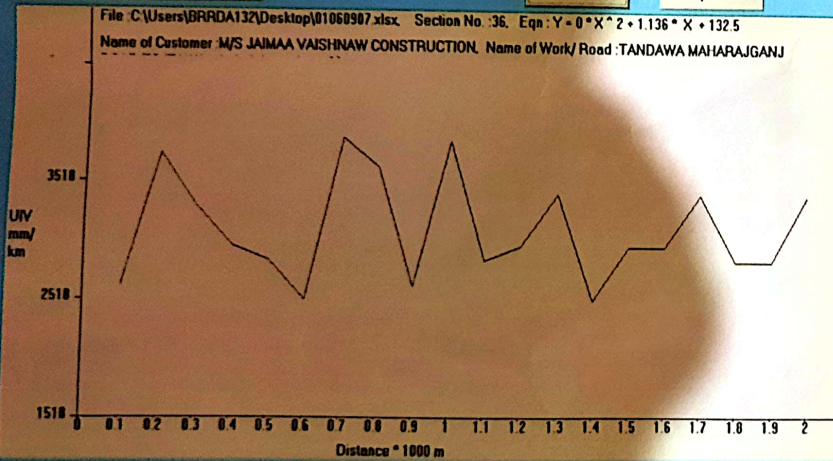

Name Of Road :- TANDAWA MAHARAJGANJ ROAD TO ITAWA

Date	Time	Section	Length	Bumps	Speed	OR		CATEGORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	UIV	ROAD				
21/8/21	6:53:5	36	0.1	220	30.3	2200	2631	G	3.58	24.626827	84.138219	Normal
21/8/21	6:54:40	36	0.1	320	20.2	3200	3767	G	4.93	24.625874	84.138192	Speed Breaker
21/8/21	6:54:46	36	0.1	280	20.2	2800	3313	G	3.4	24.626221	84.140538	Normal
21/8/21	6:54:6	36	0.1	250	30.3	2500	2972	G	3.99	24.627944	84.138986	Normal
21/8/21	6:55:9	36	0.1	240	20.2	2400	2858	G	3.85	24.626827	84.140274	Normal
21/8/21	6:53:14	36	0.1	210	30.3	2100	2518	G	3.44	24.628337	84.138981	Normal
21/8/21	6:53:18	36	0.1	350	20.2	3400	3908	G	5.33	24.626803	84.140116	Speed Breaker
21/8/21	6:53:20	36	0.1	310	20.2	3100	3654	G	4.8	24.629909	84.142676	Speed Breaker
21/8/21	6:53:23	36	0.1	220	30.3	2200	2631	G	3.58	24.627733	84.141303	Normal
21/8/21	6:53:26	36	0.1	330	10.1	3300	3881	G	5.06	24.624799	84.137703	Speed Breaker
21/8/21	6:53:29	36	0.1	240	30.3	2400	2858	G	3.85	24.626567	84.137515	Normal
21/8/21	6:53:32	36	0.1	250	30.3	2500	2972	G	3.99	24.624196	84.14099	Normal
21/8/21	6:53:36	36	0.1	290	10.1	2900	3426	G	3.53	24.626183	84.140216	Normal
21/8/21	6:53:36	36	0.1	210	30.3	2100	2518	G	3.44	24.627652	84.144354	Normal
21/8/21	6:53:42	36	0.1	250	30.3	2500	2972	G	3.99	24.627705	84.14353	Normal
21/8/21	6:53:44	36	0.1	250	30.3	2500	2972	G	3.99	24.627041	84.144562	Normal
21/8/21	6:53:44	36	0.1	290	20.2	2900	3426	G	4.53	24.628248	84.144554	Speed Breaker
21/8/21	6:53:46	36	0.1	240	20.2	2400	2858	G	3.85	24.628806	84.143218	Normal
21/8/21	6:53:48	36	0.1	240	30.3	2400	2858	G	3.85	24.628848	84.142203	Normal
21/8/21	6:53:48	36	0.1	290	10.1	2900	3426	G	3.53	24.628067	84.142892	Normal
Total Length			2									

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 2635$$

$$Y = 3120$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

21/8/21
J.E

21/8/21
A.E

21/8/21
E.E

OM SAI TESTING AND RESEARCH LABORATORY

2nd floor maheswari complex fraser road patna

PIN CODE 800001

Ref.....

Date

BITUMEN CONTENT TEST OF SEMI-DENSE BITUMINOUS CONCRETE

Name of Road REPAIR OF ROAD FROM TANDWA MAHARAJGANJ
ROAD TO ITWA UNDER SCHEME
MR 3054

Type Of Material :SEMI-DENSE BITUMINOUS
CONCRETE

DATE OF COLLECTION

8-Jun-21

DATE OF TESTING

10-Jun-21

SAMPLE NO.

A1

A2

A3

Chainage & Section:		0+540 KM	1+210 KM	1+925 KM
S.NO.	Observations	1	2	3
1	Wt. of Mix taken before extration	500	500	500
2	Wt. of filter paper before extration	6.02	6.02	6.01
3	Wt. of Mix after extration	471.91	472.48	471.88
4	Wt. of filter paper after extration	6.93	6.35	7.05
5	Wt. of filler collected from extract after allowing for seting	1.81	1.83	1.80
6	Wt. of filler collected in filter paper	0.91	0.33	1.04
7	Wt. of Aggregate + Filler collected after extration	474.63	474.64	474.7
8	Percentage of Bitumen (in the Mix) $\frac{(A-G) \times 100}{A}$	5.07	5.072	5.06
Layer		Value		
SDBC		Avg. Value	5.067%	
	Checked By			

