

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक:- 111(अनु०)

पालीगंज/दिनांक:- 01/2/21

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी
सह- सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- MR (3054) under Bihar Rural Road Maintenance Policy -2018 अन्तर्गत
कार्यन्वित की जा रही योजना का आवंटन हेतु अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि निम्नलिखित योजना का कुल राशि रुपये
66,81,393.00 मात्र का आवंटन हेतु अधियाचना विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई
समर्पित किया जाता है।

अनु० :- (1) अधियाचना विहित प्रपत्र में

विश्वासभाजन

01-02-21
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

02-02-21 01/2/21

Requisition format for Scheme Head - MR (3054) under Bihar Rural Road Maintenance Policy -2018 (Initial Rectification and Surface Renewal)

Name of Work Division:- Paliganj

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (A.A) Letter No. & Date	Administrative Approval (A.A)		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	MIR-N/19-20 Paliganj/08	Sahar Rampur to Mahajpura via Anchauli	NEA2200 01592	Li no. 6459 dt. 13.12.2019	2.83	117.58600	77.10000	29.80626	05/MBD 20 20-21 dt. 18.06.20	17.03.2021	-	Details Attached	20	5.11.1%	NIL	NIL	66.81393	
Total																	66.81393	

Executive Engineer
RWD Works Division Paliganj

01.02.21
01.02.21
01/2/21

PACKAGE NO. : MP-N/19-20/BALKEA-1/09

CONTRACTOR : SANTOSH KUMAR

Scanned with CamScanner

Name of Customer :	SANTOSH KR
Name of Work/Road :	SAHAR RAMPUR TO MAHAJ
Lab Job number	
Date :	10-01-2021
Section No.	43


Test Date :	10-01-2021	Road Name :	MAHAJ PURA VIA ANCHAU
Machine No :		Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval	
Weather :		UV Range :	1992 To 5000 mm/km
Start Location :		Dist Range :	0 To 28 0.1 1000 m
End Location :		Equation :	

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\SHAZN\Desktop\13 DEC 2020\10 JAN 2021\13.xls, Section No. : 43, Eqn :
 Name of Customer : SANTOSH KR, Name of Work/Road : SAHAR RAMPUR TO MAHAJ PURA VIA ANCHAU, Lab

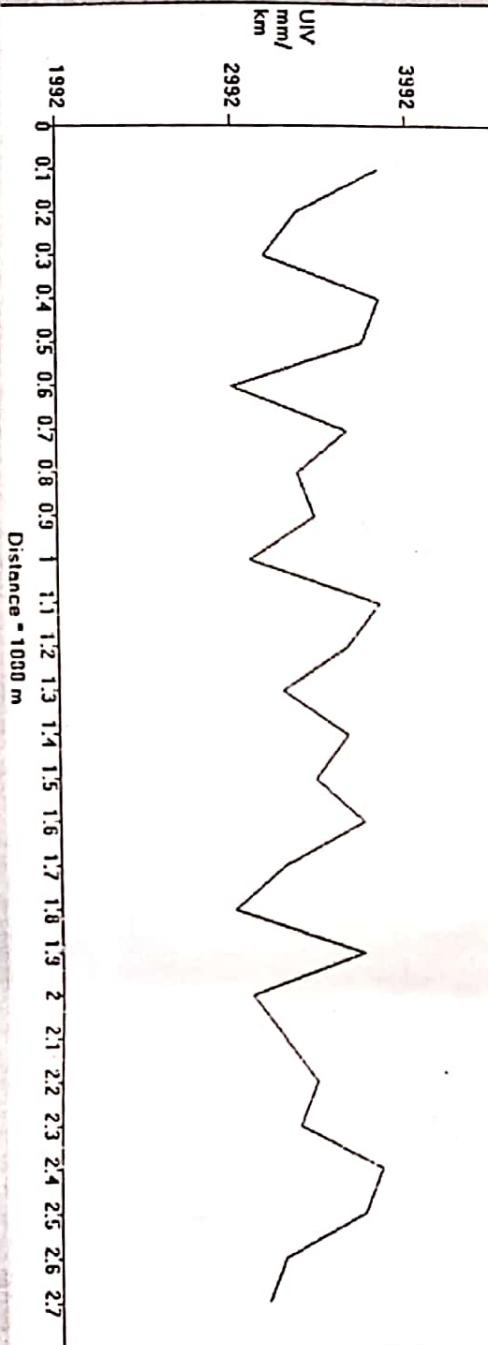

R. T. 2004
 10/01/21
 J.E.

S. S. Rany
 10/01/21
 Executive Engineer
 A.E.

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना-800007

पत्रांक - १४/म.प्र.

पटना/दिनांक- १५.१.२०२१

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना - 7

सेवा में,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, साह्यारम्पुर।

विषय :- जाँचफल प्रतिवेदन के संबंध में।

प्रसंग :- AE, Nawabpur vide letter no - 38 dt 5.1.2021

महाशय,

उपर्युक्त विषयक के संबंध में जाँचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

Sahar Rampur to Mahaupura via Adaula

MSS - Type B

SDR

Bitumen Grit/Gravel for SDR

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R.W.D. GULJARIBAGH, PATNA - 7
38 PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

15/01/2021

Name of Project/Road : Sahar Rampur to Mahulpura via Achanli

Name of Scheme : M.R. 3834

Name of Agency : Sri Sanjiv Kumar

Nature of sample : Mix seal (13.2 mm to 0.075 mm)

Date of Collection/Received : 7.1.2021

Location : 1375 m

Date of Test : 12.1.2021

Ref : Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division - Neubabpur

vide letter No. 38 Dt. 5.1.2021

Agreement No / Package No. : 05 / M 20 / 2020 - 21

Sl. No	A.I.V.
Average Test Value	Required Value(Max)
1	40%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs 15.280				Required Value		Remarks
		Weight Retd.	% of Wt. Retained	% of Cum. Retained	% of Passing	Type A	Type B	
1	13.2	0.00	0.00	0.00	100	-----	100	
2	11.2	0.359	2.35	2.35	97.65	100	88-100	
3	5.6	2.847	57.90	60.25	39.75	52-88	31-52	
4	2.8	2.529	16.55	76.80	23.20	14-38	5-25	
5	0.09	3.247	21.25	98.05	1.95	0-5	0-5	

[Signature]
A.D.
12/1/2021

[Signature]
A.E.
12/1/2021

[Signature]
E.E.
12/1/2021

Regional Laboratory
R.W.D. Guljaribagh patna - 7

Regional Laboratory
R.W.D. Guljaribagh patna - 7

Regional Laboratory
R.W.D. Guljaribagh patna - 7

Regional Laboratory
R.W.D. Guljaribagh patna - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D. GULZARBAGH, PATNA - 7

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road :- Sahar Rampur to Mahaupura via Achanli

Name of Scheme :- MR-354

Name of Agency :- Sri Sanjash Kumar

Nature of sample : Semi Dense Bituminous Concrete Date of Collection/Received :- 7.1.2021

Location :- 1375M

Date of Test :- 12.1.2021

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division - Nambalpur

vide letter No. 38 Dt. 5.1.2021

Agreement No / Package No. : 05 / MR0 / 2020-21

A.I.V.		Remarks
Average Test Value	Required Value max (%)	
—	30 %	

Sl. No	Sieve Size in (mm)	Weight of Sample Taken (kg)				Required Value	Remarks
		Weight Retd.	% of Wt. Retained	% of Cum. Retained	% of Passing		
1	13.2	0.00	0.00	0.00	100	100	
2	9.5	0.620	3.80	3.80	96.20	90-100	
3	4.75	8.320	47.50	51.30	48.70	35-51	
4	2.36	3.251	18.45	69.75	30.25	24-33	
5	1.18	1.947	11.05	80.80	19.20	15-30	
6	0.300	1.313	7.45	88.25	11.75	9-19	
7	.075	1.436	8.15	96.40	3.60	3-8	

Lab
12/1/2021

Regional Laboratory

Gulzarbagh Patna - 7

AD
12/1/2021

Regional Laboratory

R.W.D. Gulzarbagh Patna - 7

A.E.
12/1/2021

Regional Laboratory

R.W.D. Gulzarbagh Patna - 7

E.E.
12/1/2021

Regional Laboratory

R.W.D. Gulzarbagh Patna - 7

OFFICE OF THE EXECUTIVE ENGINEER
REGIONAL LABORATORY R W 2

THE EXECUTIVE ENGINEERING
REGIONAL LABORATORY, R. W. D. GULZARBEACH, PATENT
ILLUMINOUS MIX

NAME OF PROJECT/ROAD :- Satara
 NAME OF SCHEME :- MR-3054
 NAME OF AGENCY :- SSI
 NATURE OF SAMPLE :- Bituminous
 LOCATION :- 1320

Ref. Material cont.

Ref. Material sent by E.E./A.E.R.W.D. WORKS Division / Sub Division Nalanda Dist. No. 1275 M Date of Collection/Received 31-2021
Agreement No / Package No.: 65/mar/2021 Date of Test 16-12-21

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	515.00	506.00		
2	Wt. of Dry chips after extraction (b)	488.46	488.00		
3	Percentage of bitumen (in the mix) $[(a-b) \div 100] \times 100$ / a	515	50		
4	Average % bitumen		511		

Date: 10/10/2020
 By: [Signature]
 Checked: [Signature]
 Approved: [Signature]

Regional Laboratory
RWD Gulbarga, IndiaRegional Laboratory
R W Le Gault/Albany Institute

Regional Laboratory
R. W. D. O'Brien, Jr., Director

Name of Project/Road :- Sahar Road Raopur to Mahabubnagar via Achauli
Name of Scheme :- MR-3054 Bituminous mix
Name of Agency :- Sri Sankesh Kumar
Nature of sample :- Bitumens Content for SDOs
Location :- 1375 M
Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division. Nandaula P.S. vide letter No. 38 Dt. 01/02/21
Agreement No / Package No. :- 05/mab/2020-21
Date of Collection/Received :- 01.1.2021
Date of Test :- 15.1.2021

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	515.00	506.00	509.00	
2	Wt. of Dry chips after extraction (b)	488.46	480.70	482.70	
3	Percentage of bitumen (in the mix) [(a-b)*100]/a (%)	5.15	5.0	5.17	
4	Average % bitumen	5.11			

Rajendra
A.D.
Regional Laboratory
R.W.D. Guljaribagh patna - 7

Rajendra
A.D.
Regional Laboratory
R.W.D. Guljaribagh patna - 7

Rajendra
A.D.
Regional Laboratory
R.W.D. Guljaribagh patna - 7

Rajendra
A.E.
Regional Laboratory
R.W.D. Guljaribagh patna - 7
