

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, औरंगाबाद

Email ID:-eerwdaurangabad1@gmail.com

Mob:- 8986915333

पत्रांक...437 अड...

औरंगाबाद / दिनांक...12/02/21...

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वास भाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Aurangabad

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Aurangabad

Sl.no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/AU/AUR/19/0024	Amba nabinagar Road - Chakua	10602802022	3140/22.07.2019	6.5	203.08	122.37	12.05	74MBD-2019-20 20.02.2020	19.11.2020	17.12.2020	3401	25MM	5.041%	61.18500	61.18500	61.18500	Comp.
2	RM/AU/AUR/19/0030	Deo - Bahola	10602802105	3140/22.07.2019	6.52	211.88	130.92	59.68	58MBD-2019-20 04.02.2020	03.11.2020	21.12.2020	3340	25MM	5.012%	65.46000	65.46000	65.46000	Comp.
3	RM/AU/AUR/19/0030	GT Rd Deo More - Rasulpur	10602802115	3140/22.07.2019	2.62	92.14	57.95	24.22	58MBD-2019-20 04.02.2020	03.11.2020	17.12.2020	2875	25MM	5.063%	34.77000	34.77000	23.18000	Comp.
4	RM/AU/AUR/19/0031	Khairawan - Bariawan	10602802121	3140/22.07.2019	2.07	76.02	48.85	18.91	61MBD-2019-20 05.02.2020	04.11.2020	17.12.2020	3335	25MM	5.000%	29.31000	29.31000	19.54000	Comp.
5	RM/AU/AUR/19/0015	Deo Jeetabigha - Eroura	10602902011	3140/22.07.2019	1.56	59.49	39.87	13.60	78MBD-2019-20 20.02.2020	19.11.2020	17.12.2020	3199	25MM	5.014%	23.92200	23.92200	15.94800	Comp.
6	RM/AU/AUR/19/0033	AURANGABAD NABINAGAR ROAD - SORI	NEA22000214	3140/22.07.2019	2.2	71.85	44.54	20.04	80MBD-2019-20 20.02.2020	19.11.2020	18.12.2020	2961	25MM	5.000%	26.72600	26.72600	17.81400	Comp.
7	RM/AU/AUR/19/0033	Aurangabad Nabinagar - Sonbarsa Khairi	10602802096	3140/22.07.2019	1.49	53.57	37.15	15.96	80MBD-2019-20 20.02.2020	19.11.2020	28.11.2020	2988	25MM	5.000%	20.26800	20.26800	19.54000	Comp.
8	RM/AU/AUR/19/0034	Aurangabad Nabinagar Rd. Charan Vajrapur Rajpur	10602802097	3140/22.07.2019	4.84	157.38	95.33	9.23	64MBD-2019-20 05.02.2020	04.11.2020	18.12.2020	2404	25MM	5.000%	57.19800	57.19800	38.13200	Comp.
9	RM/AU/AUR/19/0034	Charan Mali Road - Sanoura Khamba	10602802103	3140/22.07.2019	2.57	89.38	55.76	24.65	64MBD-2019-20 05.02.2020	04.11.2020	18.12.2020	3012	25MM	5.000%	33.45600	33.45600	22.30400	Comp.
10	RM/AU/AUR/19/0010	Khairi to Gram Sonahi Road	10602901035	3140/22.07.2019	2.05	78.8	50.88	19.97	84MBD-2019-20 25.02.2020	24.11.2020	13.11.2020	3540	25MM	5.011%	0.00000	0.00000	50.88000	Comp.
11	RM/AU/AUR/19/0027	Basudev Kenal to Tamsih village	10602901031	3140/22.07.2019	2.3	76.08	47.32	20.92	62MBD-2019-20 05.02.2020	04.11.2020	18.12.2020	2934	25MM	5.017%	28.39200	28.39200	18.92800	Comp.
12	RM/AU/AUR/19/0027	Amba Jiwa Bigha Road to Choraha	10602901012	3140/22.07.2019	5.5	175.66	109.15	48.86	62MBD-2019-20 05.02.2020	04.11.2020	24.12.2020	3830	25MM	5.093%	54.57500	54.57500	54.57500	Comp.
13	RM/AU/AUR/19/0036	AURANGABAD NABINAGAR ROAD SATTAR	NEA22000221	3140/22.07.2019	1.6	56.81	35.7	15.35	68MBD-2019-20 08.02.2020	07.02.2020	28.11.2020	2655	25MM	5.195%	21.42000	21.42000	14.28000	Comp.
14	RM/AU/AUR/19/0032	Modernisation & Const of NH-2 Dadpi to deojara Rd via Mahuwan art Rd	10602803009	3140/22.07.2019	6.8	258.417	153.52	63.19	69MBD-2019-20 10.02.2020	09.11.2020	08.12.2020	2770	25MM	5.000%	76.76000	76.76000	76.76000	Comp.

15	RM/AU/AUR/ 19/0028	G.T. Road to Narkappi	10602802400	3140/22.07.2019	4.1	165.66	110.98	42.81	80MBD-2019-20 20.02.2020	19.11.2020	17.12.2020	3016	25MM	5.000%	55.49000	55.49000	55.49000	Comp.
16	RM/AU/AUR/ 19/0009	Nabinagar Road - Kunrwa	10602902029	3140/22.07.2019	3.32	118.96	76.06	30.93	82MBD-2019-20 20.02.2020	19.11.2020	18.12.2020	2986	25MM	5.042%	45.63600	45.63600	30.42400	Comp.
17	RM/AU/AUR/ 19/0028	Const of Rd from Madanpur NH-2 Ghorghat more to Ghorghat thawai Rd	10602801016	3140/22.07.2019	5	246.1	174.29	47.12	65MBD-2019-20 05.02.2020	04.11.2020	17.12.2020	2276	25MM	5.000%	87.14500	87.14500	87.14500	Comp.
18	RM/AU/AUR/ 19/0034	AURANGABAD NABINAGAR ROAD - GHAMHARIA	NEA22000211	3140/22.07.2019	1.6	50.44	31.92	13.36	64MBD-2019-20 05.02.2020	04.11.2020	18.12.20	3103	25MM	5.000%	19.15200	19.15200	12.76800	Comp.
19	RM/AU/AUR/ 19/0024	Const of Rd from Amba Nabinagar to persawan	10602801003	3140/22.07.2019	2.5	88.42	55.36	24.09	74MBD-2019-20 20.02.2020	19.11.2020	24.12.2020	2449	25MM	5.012%	33.21600	33.21600	22.14400	Comp.
20	RM/AU/AUR/ 19/0006	Const of Inda bigha pokhar to sokhya talab via western portion of naugrah	10602803011	3140/22.07.2019	3.8	148.32	97.33	36.07	05.02.2020 66MBD-2019-20	04.11.2020	03.11.2020	2125	25.00MM	5.009%	68.24400	65.24400	32.08600	Comp.
21	RM/AU/AUR/ 19/0012	L029 - T01 G.T.ROAD TO KUSA (TRACK29)	10602802064	3140/22.07.2019	5.76	203.59	130.86	52.30	20.02.2020 76MBD-2019-20	19.11.2020	19.12.2020	3021 2271	25.00MM	5.020%	0.00000	0.00000	130.86000	Comp.
22	RM/AU/AUR/ 19/0036	Manjhiyawa Jsoiya Via Ankorha Railway Station raad	10602901065	3140/22.07.2019	7.4	274.03	175.78	70.63	08.02.2020 68MBD-2019-20	07.11.2020	20.11.2020	2574	25.00MM	5.077%	123.04600	123.04600	52.73400	Comp.
23	RM/AU/AUR/ 19/0032	GT Road - Narkappi	10602902016	3140/22.07.2019	3.85	139.12	88.96	36.22	10.02.2020 69MBD-2019-20	09.11.2020	17.11.2020	3225	25.00MM	5.096%	71.16800	71.16800	17.79200	Comp.
24	RM/AU/AUR/ 19/0031	khiriyawanpirthu - chei nawada	NEA22000208	3140/22.07.2019	6	314.39	223.55	56.35	05.02.2020 61MBD-2019-20	04.11.2020	26.11.2020	2556	25.00MM	5.002%	156.48500	156.48500	67.06500	Comp.
TOTAL																	1009.916	

Divisional Accounts Officer
Rural Works Department, works Division,
Aurangabad

Executive Engineer
Rural Works Department
Works Division, Aurangabad

Name Of Road Aurangabad Navinagar - Sonbarsa Khaira

Date	Time	Section	Length	Bumps	Speed	OR		CATEGORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	UIV	ROAD				
28/ 11/ 20	13: 31: 0	3	0.1	300	10.1	3000	3540	G	3.66	24.669595	84.177222	Normal
28/ 11/ 20	13: 31: 35	3	0.1	270	20.2	2700	3199	G	3.26	24.668898	84.177	Normal
28/ 11/ 20	13: 32: 0	3	0.1	250	20.2	2500	2972	G	3.99	24.66824	84.175958	Normal
28/ 11/ 20	13: 32: 11	3	0.1	230	30.3	2300	2745	G	3.72	24.667647	84.175202	Normal
28/ 11/ 20	13: 32: 11	3	0.1	240	20.2	2400	2858	G	3.85	24.666887	84.175302	Normal
28/ 11/ 20	13: 32: 11	3	0.1	210	30.3	2100	2518	G	3.44	24.665968	84.175268	Normal
28/ 11/ 20	13: 32: 46	3	0.1	190	30.3	1900	2290	G	3.16	24.665113	84.175202	Normal
28/ 11/ 20	13: 33: 0	3	0.1	190	30.3	1900	2290	G	3.16	24.664138	84.17515	Normal
28/ 11/ 20	13: 33: 0	3	0.1	200	30.3	2000	2404	G	3.3	24.663265	84.175168	Normal
28/ 11/ 20	13: 33: 21	3	0.1	270	30.3	2700	3199	G	3.26	24.662288	84.17507	Normal
28/ 11/ 20	13: 33: 21	3	0.1	320	20.2	3200	3767	G	3.93	24.661903	84.175707	Normal
28/ 11/ 20	13: 33: 21	3	0.1	290	30.3	2900	3426	G	3.53	24.661852	84.17677	Normal
28/ 11/ 20	13: 34: 0	3	0.1	310	30.3	3100	3654	G	3.8	24.661405	84.17771	Normal
28/ 11/ 20	13: 34: 0	3	0.1	250	30.3	2500	2972	G	3.99	24.6607	84.1784	Normal
Total Length			1.4									

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 2514$$

$$Y = 2988$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

[Signature]
28/11/2020
J.E

[Signature]
28/11/20
A.E

[Signature]
21/12/20
E'E

Name of Customer : HARI OM CONSTRUCTION
Name of Work/ Road : ad Navinagar - Sonbarsa Khaira
Lab Job number : 3
Date : 02-05-2009
Section No. : 3


Test Date : 28-04-2010 Road Name : d Navinagar - Sonbarsa Khaira
Machine No : 377 Road Type : (R) RURAL ROAD
Start S No : 3 Side : Nabinegar Interval
Start E No : 16
Weather : Normal UIV Range : 1290 To 5000 1000 mm/km
Start Location : 24.669595 84 Dist Range : 0 To 1.5 0.1 * 1000 m
End Location : 24.660784 176 Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

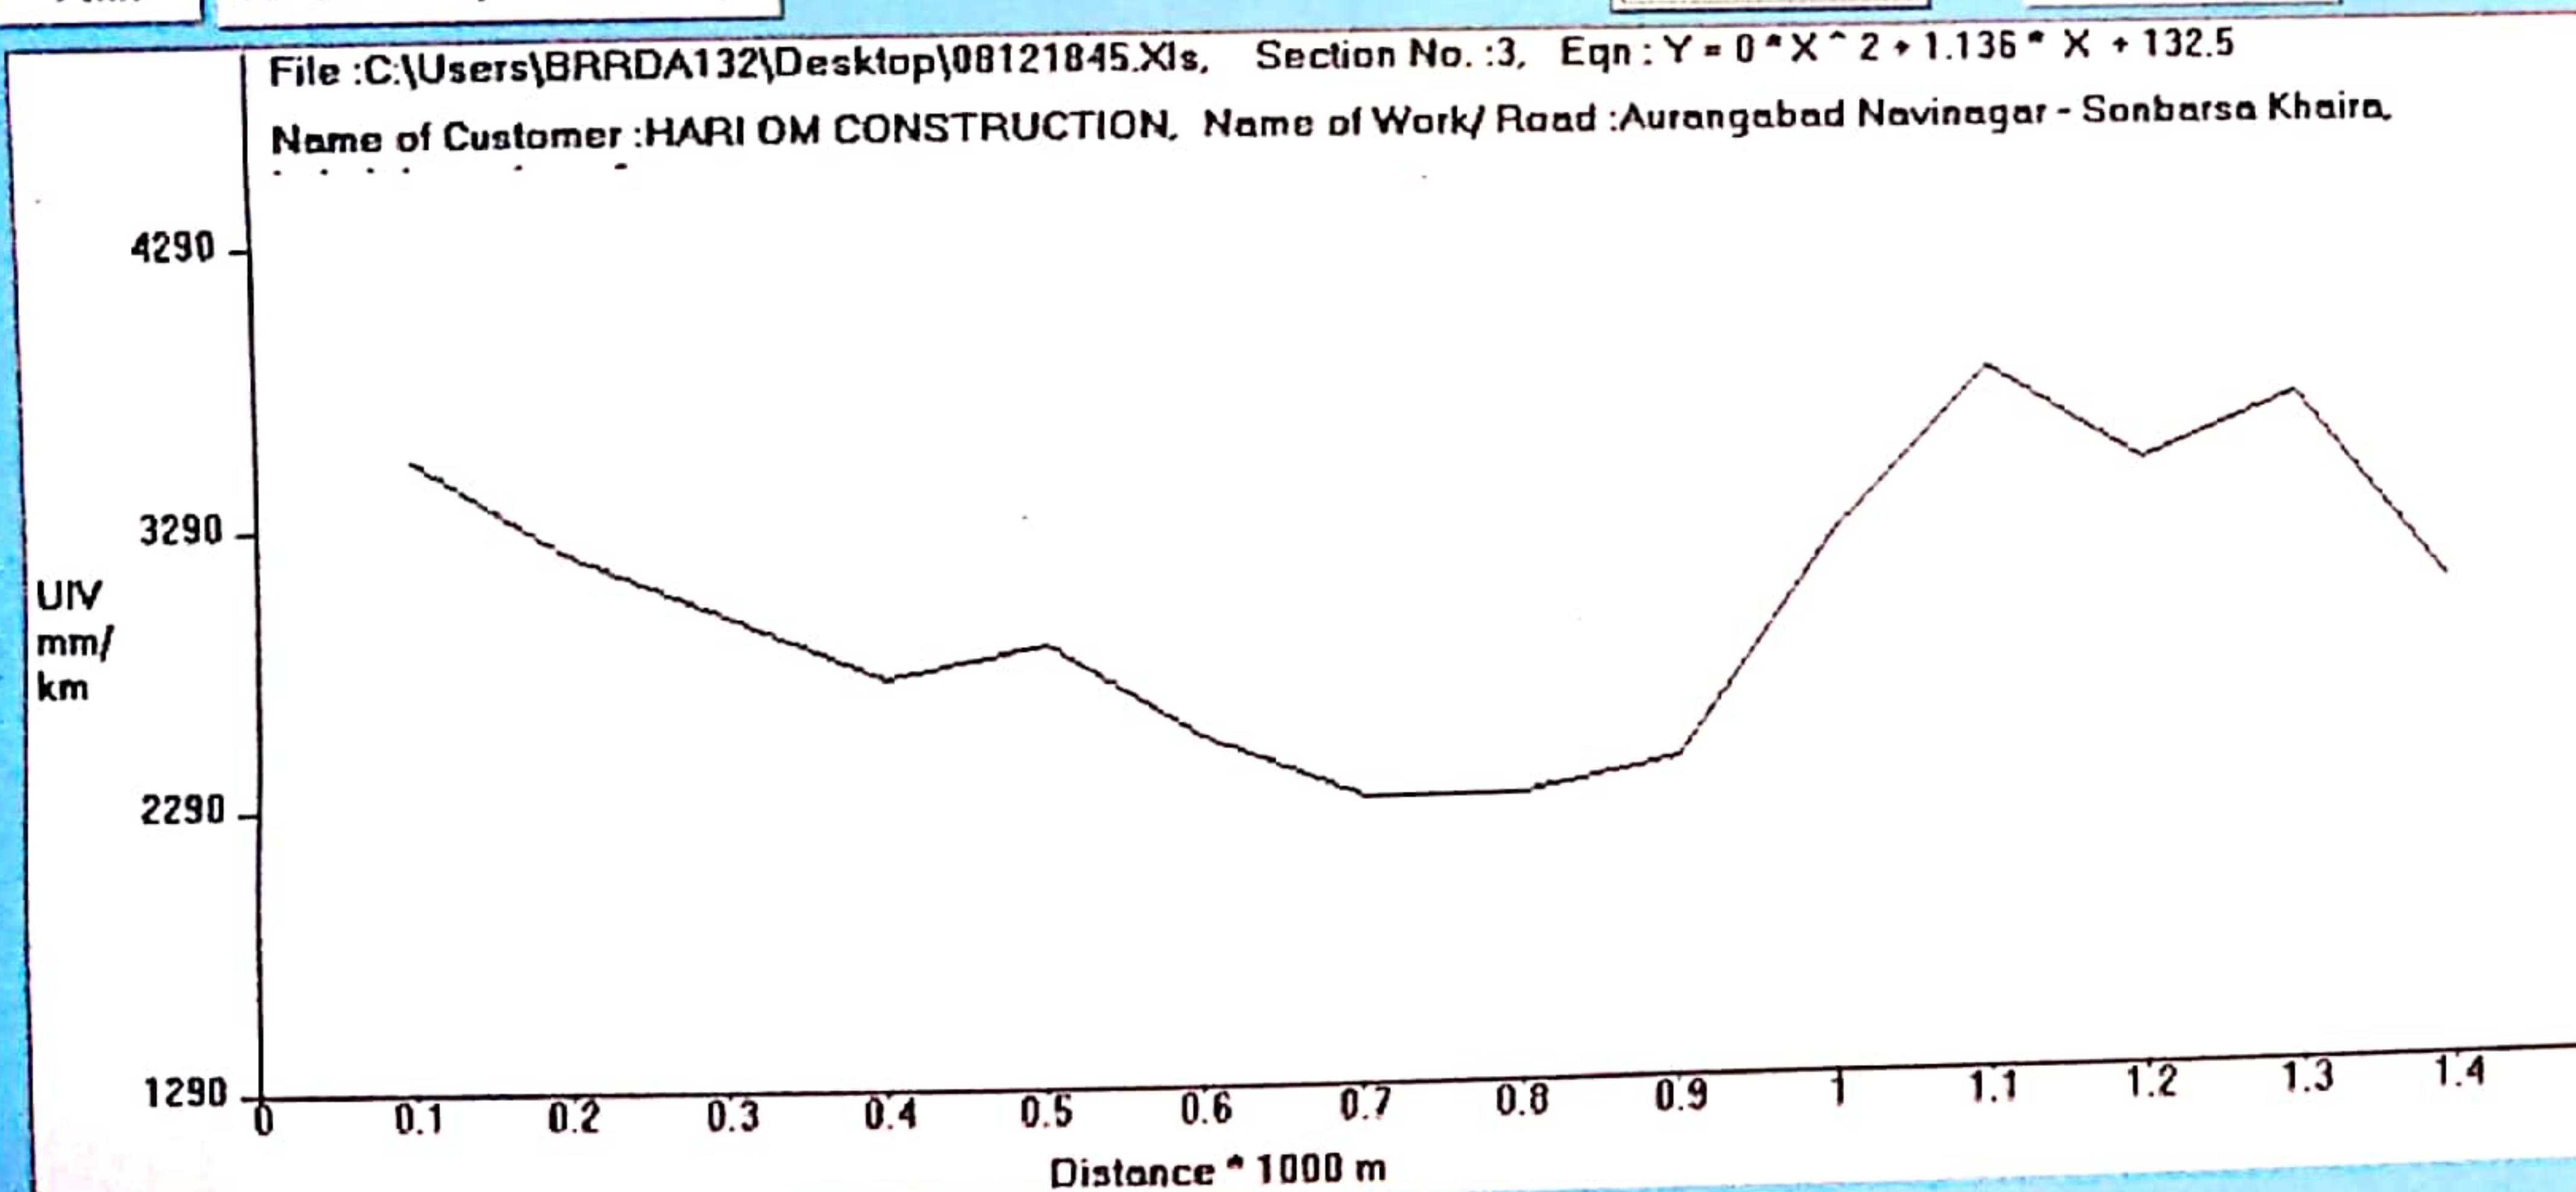

[Signature]
28/11/2020
I.E

[Signature]
28/11/20

[Signature]
21/12/20

OM SAI TESTING AND RESEARCH LABORATORY

2nd floor mahaveer complex framer road pune

PIN CODE 411001

BITUMEN CONTENT TEST OF SEMI-DENSE BITUMINOUS CONCRETE

Ref. of Road : AURANGABAD NABINAGAR ROAD TO SONBARSA
RET..... KHAIJA ROAD UNDER SCHEME MH 3054

Type Of Material : SEMI-DENSE BITUMINOUS CONCRETE

DATE OF COLLECTION 12-Dec-20

DATE OF TESTING 15-Dec-20

SAMPLE NO.

Chainage & Section				
S NO.	Observations	1	2	3
1	Wt. of Mix taken before extration	500	500	500
2	Wt. of filter paper before extration	6.00	6.00	6.00
3	Wt. of Mix after extration	472.5	471.0	472.4
4	Wt. of filter paper after extration	6.78	7.05	6.88
5	Wt. of filter collected from extract after allowing for seting	1.55	1.05	1.015
6	Wt. of filter collected in filter paper	0.78	1.05	0.88
7	Wt. of Aggregate + Filler collected after extration	474.83	474.0	475.2
8	Percentage of Bitumen (in the Mix) $\frac{(A-G) \times 100}{A}$	5.03	5.02	4.96
Layer		Value		
SEMI-DENSE BITUMINOUS CONCRETE		Avg Value	5.005%	

Checked By

Tested By

