

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, जहानाबाद।

पत्रांक: 05 /

जहानाबाद, दिनांक: 02.01.2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।

सेवा में,

नोडल पदाधिकारी=3054,
बिहार पथ नई अनुरक्षण नीति 2018
ग्रामीण कार्य विभाग, बिहार, पटना।


विषय :- बिहार राज्य पथ अनुरक्षण नीति 2018 अंतर्गत किये गये पथ के निर्माण कार्य में भुगतान करने हेतु निधि के आवंटन उपलब्ध कराने के संबंध में।


महाशय

उपर्युक्त विषय के संबंध में कहना है कि बिहार राज्य पथ अनुरक्षण नीति 2018 अंतर्गत कराये गए कार्य के भुगतान हेतु वित्तीय वर्ष 2020-21 में राशि आवंटित करने की कृपा की जाय।

अनु० - विहित प्रपत्र, Bump Integrator Testing Report.

विश्वासभाजन


2.1.21

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।

2.1.21

Requisition Format for Scheme Head- MR (3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Division- Rural Work Department, Works Division, Jehanabad.

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion As per Agreement	Actual Date of Completion	Value of IRU (in MM/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content percentage	Previous Total Amount Allocated (in Lakh)	Up to Date Expenditure as per MIS (in Lakh)	Requisition Against Work Done (in Lakh)	Remarks
					Length	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	Maintenance Amount of (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1		Katauli Rustampur Road	10603002274	5157/ 25.09.2019	2.00	78.2458	53.86942	17.02625	6MBD/ 2020-21	15.02.21	15.02.21	2660	25 MM	5%	43.17554	43.17554	10.78388	Complete
2		Mokimpur Mirzapur Bishunpur road	16301036090	5157/ 25.09.2019	1.90	70.8800	47.85100	16.66735	6MBD/ 2020-21	15.02.21	15.02.21	2429	25 MM	5%	0.00000	0.00000	47.85100	Complete
3	RM/E/JAH/ 19/0006	Jehanabad Arwal road/H. 110 to Yadubigha.	10603004031	5157/ 25.09.2019	0.86	33.26	19.14500	8.7033	6MBD/ 2020-21	15.02.21	15.02.21	2813	25 MM	5%	0.00000	0.00000	19.14500	Complete
4		Kako Main road to Domtoli Katurba School)	10603001052	5157/ 25.09.2019	0.50	19.0900	12.25600	5.37550	6MBD/ 2020-21	15.02.21	15.02.21	2222	25 MM	5%	0.00000	0.00000	12.25600	Complete
Total					5.260	201.476	133.221	47.772							43.176	43.176	90.046	


 Executive Engineer
 Rural Work Division
 Works Division, Jehanabad
 25/11/21

ROAD NAME:- KATAULI TO RUSTAMPUR

CONT. NAME:- MAGADH ENGINEERING WORK

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
29/11/20	12:56:17	22	0.05	140	0	2800	3265 G		25.150525	85.157727	Normal
29/11/20	12:56:52	22	0.05	160	10.1	1400	1888 G		25.150078	85.15781	Normal
29/11/20	12:57:0	22	0.05	150	10.1	3000	3462 G		25.149655	85.157945	Normal
29/11/20	12:57:0	22	0.05	140	10.1	2800	3265 G		25.149242	85.158113	Normal
29/11/20	12:57:26	22	0.05	170	10.1	3400	3856 G		25.14879	85.158282	Normal
29/11/20	12:57:26	22	0.05	120	10.1	2400	2872 G		25.148377	85.15842	Normal
29/11/20	12:58:0	22	0.05	120	10.1	2400	2872 G		25.147942	85.158585	Normal
29/11/20	12:58:2	22	0.05	110	10.1	2200	2675 G		25.14752	85.158737	Normal
29/11/20	12:58:2	22	0.05	90	10.1	1800	2281 G		25.147107	85.158888	Normal
29/11/20	12:58:2	22	0.05	100	10.1	2000	2478 G		25.14667	85.159057	Normal
29/11/20	12:58:37	22	0.05	160	10.1	2400	2872 G		25.146215	85.159242	Normal
29/11/20	12:59:0	22	0.05	130	10.1	2600	3069 G		25.145792	85.159427	Normal
29/11/20	12:59:12	22	0.05	100	10.1	2000	2478 G		25.145397	85.159612	Normal
29/11/20	12:59:12	22	0.05	90	10.1	1800	2281 G		25.144957	85.159813	Normal
29/11/20	12:59:12	22	0.05	110	10.1	2200	2675 G		25.144545	85.16	Normal
29/11/20	12:59:47	22	0.05	70	10.1	1400	1888 G		25.144115	85.160168	Normal
29/11/20	13:0:0	22	0.05	110	10.1	2200	2675 G		25.143657	85.16015	Normal
29/11/20	13:0:23	22	0.05	100	10.1	2000	2478 G		25.14319	85.16007	Normal
29/11/20	13:0:23	22	0.05	100	10.1	2000	2478 G		25.142753	85.159998	Normal
29/11/20	13:0:23	22	0.05	90	10.1	1800	2281 G		25.142308	85.159915	Normal
29/11/20	13:1:0	22	0.05	100	10.1	2000	2478 G		25.141873	85.15983	Normal
29/11/20	13:1:0	22	0.05	120	10.1	2400	2872 G		25.141418	85.159747	Normal
29/11/20	13:1:0	22	0.05	100	10.1	2000	2478 G		25.140975	85.159662	Normal
29/11/20	13:1:33	22	0.05	110	10.1	2200	2675 G		25.140515	85.159545	Normal
29/11/20	13:1:33	22	0.05	100	10.1	2000	2478 G		25.140082	85.15936	Normal
29/11/20	13:2:0	22	0.05	110	10.1	2200	2675 G		25.139703	85.15909	Normal
29/11/20	13:2:9	22	0.05	90	10.1	1800	2281 G		25.139342	85.158803	Normal
29/11/20	13:2:9	22	0.05	110	10.1	2200	2675 G		25.138912	85.158568	Normal
29/11/20	13:2:44	22	0.05	100	10.1	2000	2478 G		25.138507	85.15842	Normal

29/11/20	13:3:0	22	0.05	100	10.1	2000	2478 G	25.138072	85.158282	Normal
29/11/20	13:3:0	22	0.05	110	10.1	2200	2675 G	25.137613	85.158163	Normal
29/11/20	13:3:19	22	0.05	110	10.1	2200	2675 G	25.137163	85.158047	Normal
29/11/20	13:3:19	22	0.05	110	10.1	2200	2675 G	25.136722	85.157945	Normal
29/11/20	13:3:54	22	0.05	80	10.1	1600	2085 G	25.136277	85.157845	Normal
29/11/20	13:4:0	22	0.05	120	10.1	2400	2872 G	25.135853	85.157727	Normal
29/11/20	13:4:0	22	0.05	80	10.1	1600	2085 G	25.135418	85.157558	Normal
29/11/20	13:4:30	22	0.05	120	10.1	2400	2872 G	25.134995	85.157357	Normal
29/11/20	13:4:30	22	0.05	100	10.1	2000	2478 G	25.134553	85.157172	Normal
29/11/20	13:5:0	22	0.05	100	10.1	2000	2478 G	25.134128	85.156968	Normal
29/11/20	13:5:5	22	0.05	60	20.2	3400	3856 G	25.134028	85.156935	Speed Breaker

AVERAGE IRI VALUE:-2660

CA
02/01/2021

C.E (Hudayan)


3 on 01.2021

A.E

6
2
12/11/2021
E.E

File : G:\29111328.Xls, Section No. : 22, Egn : test

Name of Customer : MAGADH ENGINEERING WORK, Name of Work/ Road : KATAULI TO RUSTAMPUR, Lab Job

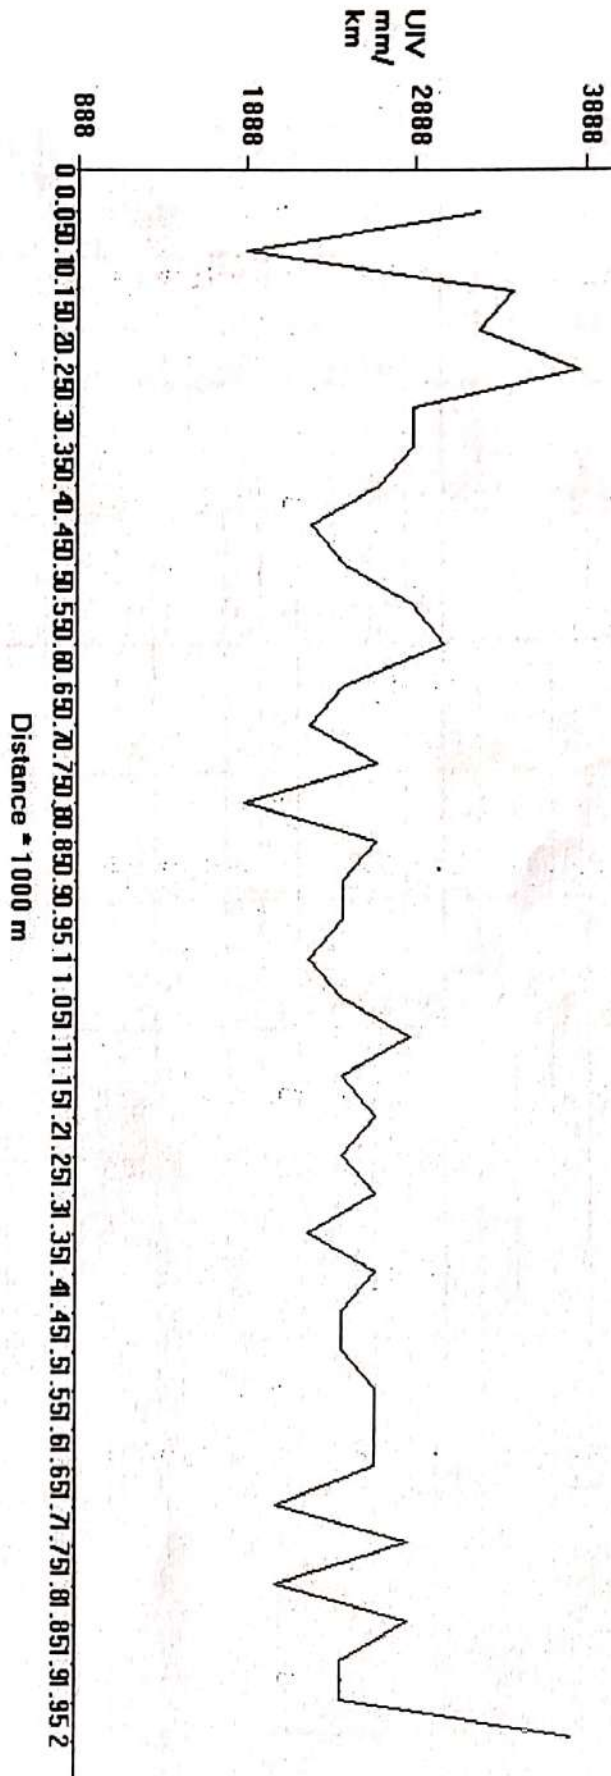

Q2/01/2021

2.5 (average)

Q2/01/2021

AE

Q2/01/2021

E.E

CONT. NAME:- MAGADH ENGINEERING WORKS

ROAD NAME:-MOKIMPUR TO MIRAPUR BISHUNPUR ROAD

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
1/1/21	12:50:3	26	0.1	0	0	0	510	G	25.101568	85.132003	Normal
1/1/21	12:51:14	26	0.1	220	0	2200	2675	G	25.102448	85.131902	Speed
1/1/21	12:52:0	26	0.1	220	10.1	2200	2675	G	25.103322	85.13178	Breaker
1/1/21	12:52:24	26	0.1	300	10.1	3000	3462	G	25.10421	85.1317	Normal
1/1/21	12:53:0	26	0.1	120	10.1	1200	1691	G	25.105103	85.131665	Normal
1/1/21	12:53:35	26	0.1	110	10.1	1100	1593	G	25.105992	85.13168	Normal
1/1/21	12:54:0	26	0.1	190	10.1	1900	2380	G	25.106932	85.13172	Normal
1/1/21	12:54:10	26	0.1	260	10.1	2600	3069	G	25.107838	85.132	Normal
1/1/21	12:54:45	26	0.1	170	10.1	1700	2183	G	25.108747	85.1317	Normal
1/1/21	12:55:0	26	0.1	150	10.1	1500	1986	G	25.10963	85.13177	Normal
1/1/21	12:56:0	26	0.1	120	0	1100	1593	G	25.11154	85.132508	Normal
1/1/21	12:56:31	26	0.1	240	10.1	2400	2872	G	25.112287	85.132845	Normal
1/1/21	12:57:6	26	0.1	300	0	3000	3462	G	25.112785	85.133535	Speed
1/1/21	12:57:42	26	0.1	280	10.1	2800	3265	G	25.11337	85.134175	Breaker
1/1/21	12:58:17	26	0.1	280	0	2800	3265	G	25.11384	85.134813	Speed
1/1/21	12:58:52	26	0.1	330	10.1	3300	3757	G	25.114752	85.134645	Breaker
1/1/21	12:59:0	26	0.1	140	10.1	1400	1888	G	25.11541	85.13502	Normal
1/1/21	12:59:27	26	0.1	160	10.1	1429	1916	G	25.115463	85.13513	Normal
1/1/21	12:60:27	26	0.09	160	10.1	1429	1916	G	25.11552	85.1342	Normal
AVERAGE							2429				

CA


02/01/2021

2.5 (Habyan)

3 on 01.2021
PE

6/11/21-1.1.2021
EE

File :D:\BUMP NEW DATA\01011533.Xls. Section No.:26. Egn :test
 Name of Customer :MAGADH ENGINEERING WORKS. Name of Work/ Road :MOKIMPUR TO MIRJAPUR

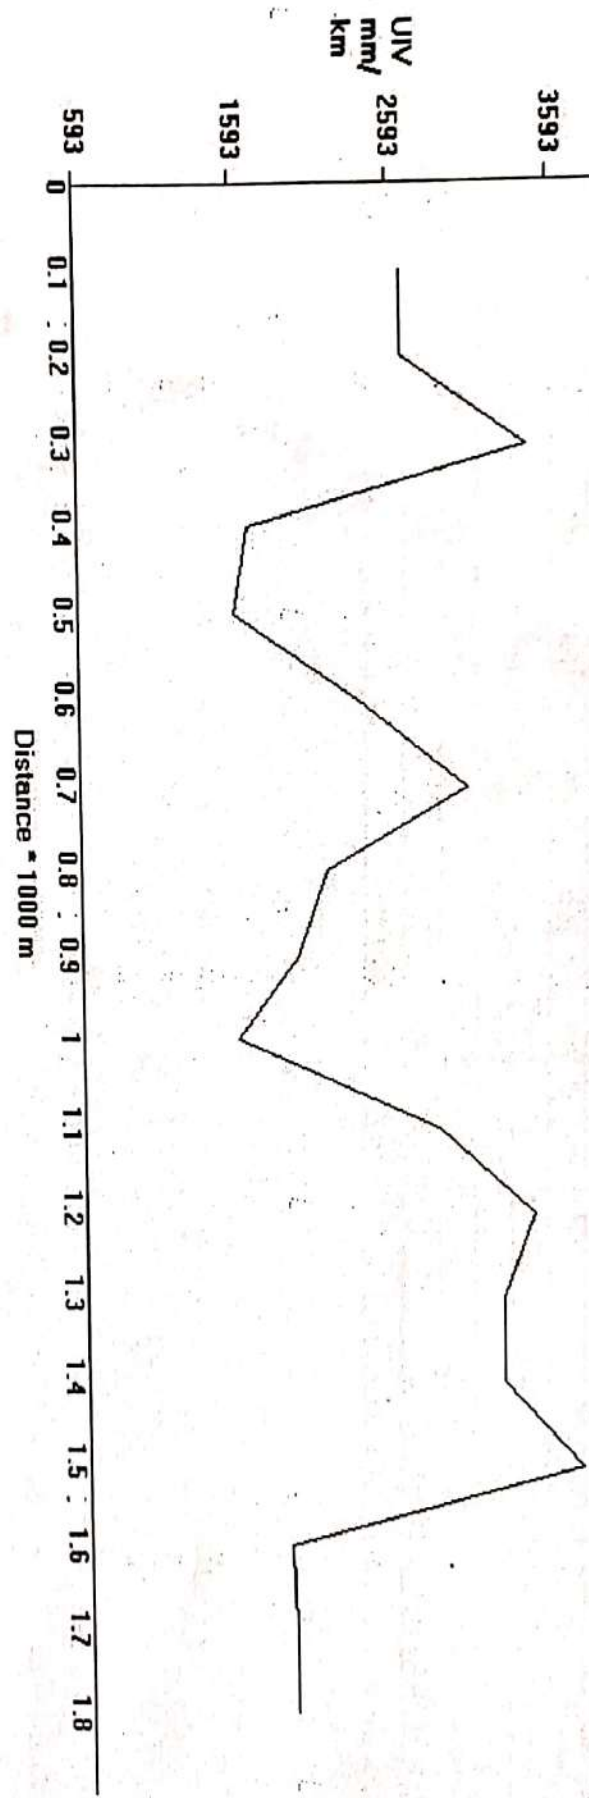

Q
 02/01/2021
 J.E

Q
 02.01.2021
 H.E

Q
 02.01.2021
 E.E

CONT. NAME:- MAGADH ENGINEERING WORKS

ROAD NAME:-JEHANABAD ARWAL ROAD TO YADU BIGHA

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
1/1/21	15:26:0	28	0.1	280	0	2800	3265 G		25.207593	84.895723	Normal
1/1/21	15:26:28	28	0.1	280	10.1	2800	3265 G		25.20692	84.895185	Normal
1/1/21	15:27:4	28	0.1	170	10.1	1700	2183 G		25.20628	84.89468	Normal
1/1/21	15:27:4	28	0.1	200	10.1	2000	2478 G		25.206193	84.893787	Normal
1/1/21	15:28:0	28	0.1	80	10.1	2286	2760 G		25.205932	84.893502	Normal
1/1/21	15:28:20	28	0.1	80	10.1	2286	2760 G		25.2061	84.89342	Normal
1/1/21	15:31:0	30	0.1	250	10.1	2500	2970 G		25.203793	84.892	Normal
1/1/21	15:31:30	30	0.1	250	10.1	2500	2970 G		25.203788	84.883	Normal
1/1/21	15:32:0	30	0.06	130	20.2	2800	3265 G		25.203668	84.89138	Normal
AVERAGE							2813				

02/10/21

30.01.2021


H.E

07/11/21

E.E

File : D:\BUMP NEW DATA\01011533.Xls, Section No. : 28, Egn : test

Name of Customer : MAGADH ENGINEERING WORKS, Name of Work/ Road : JEHANABAD ARWAL ROAD TO YADU

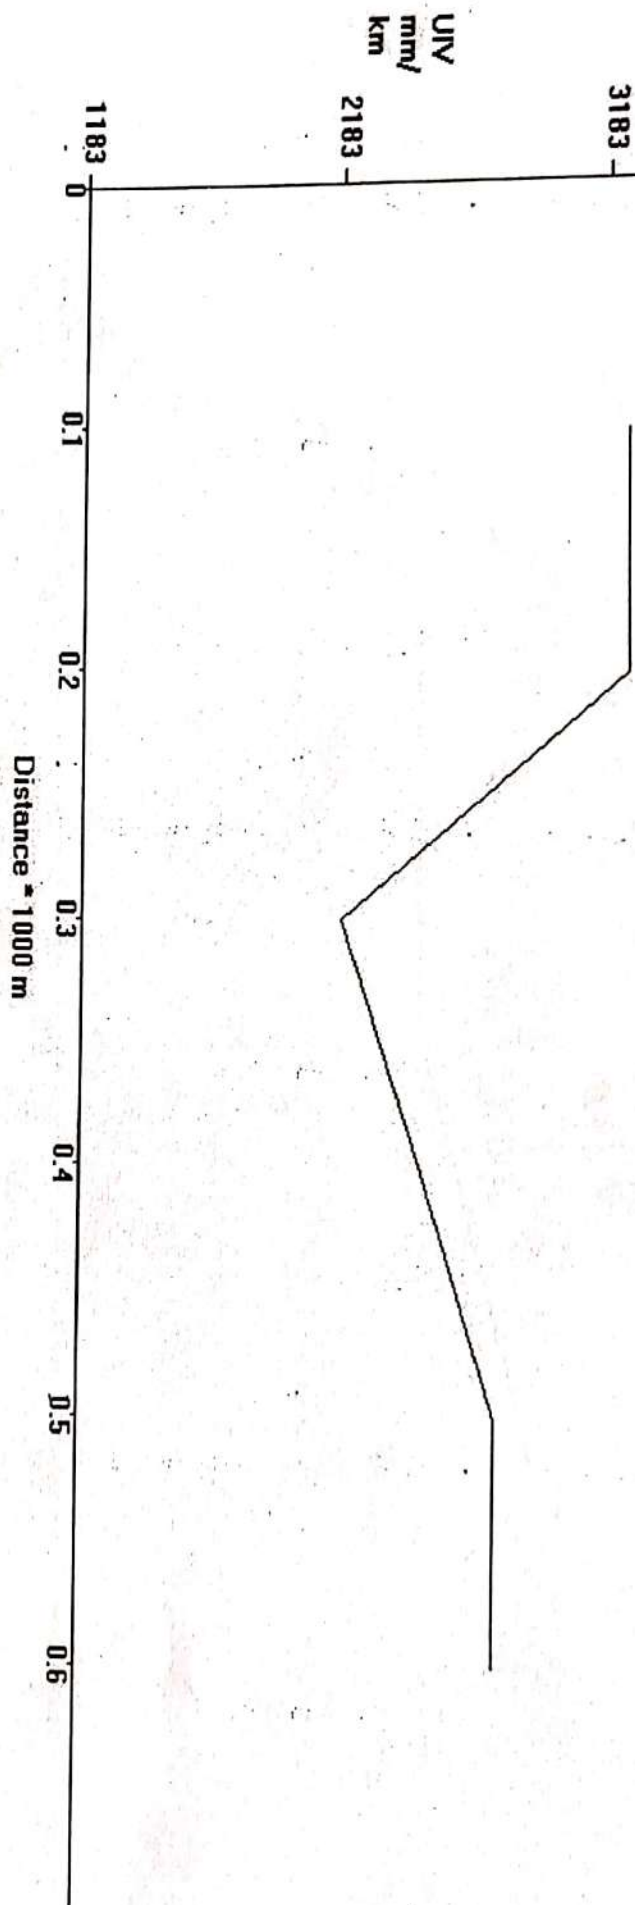


~~04/01/21~~

02.01.2021
A-E

02.11.2021
E-E

File : D:\BUMP NEW DATA\01011533.Xls. Section No. : 30. Egn : test

Name of Customer : MAGADH ENGINEERING WORKS. Name of Work/ Road : JEHANABAD ARWAL RD TO YADU

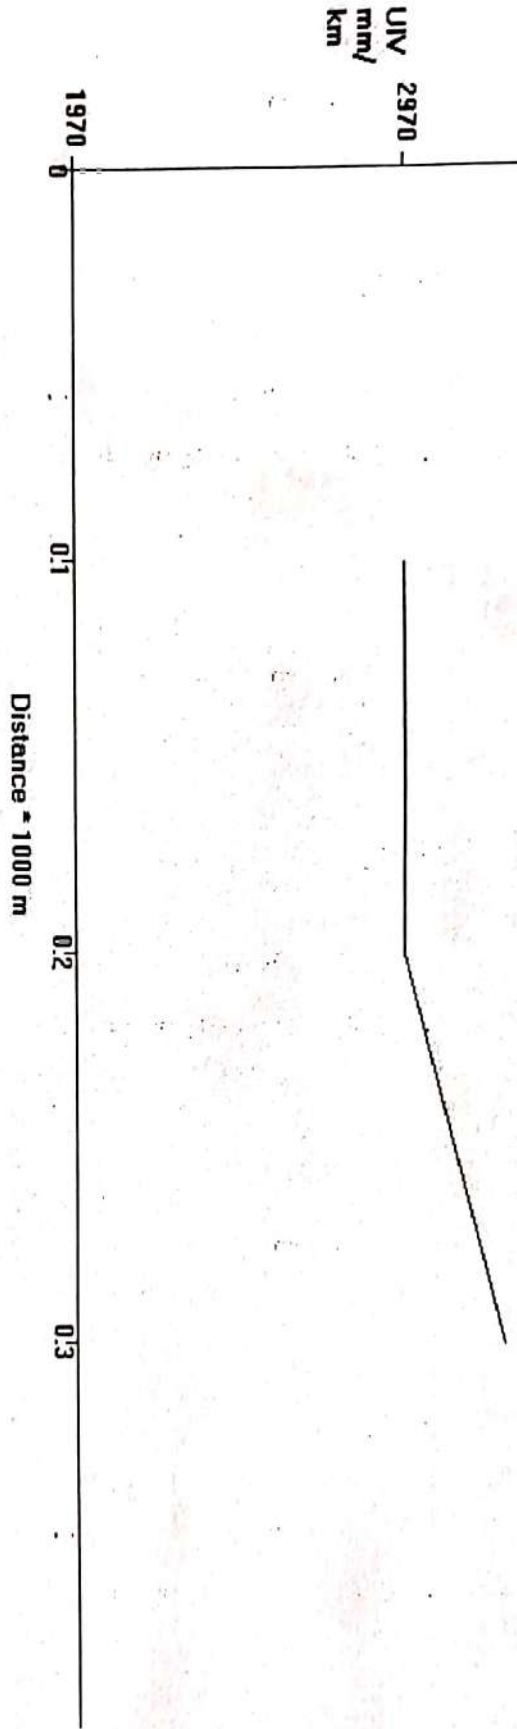

$\frac{d}{0.01/0.1}$
5.5

3
02.01.2021
A.E

$\frac{7}{2.1.2021}$
E.E

CONT. NAME:- MAGADH ENGINEERING WORKS											
ROAD NAME:-KAKO MAIN ROAD TO DOMTOLI KASTURBA SCHOOL											
Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
1/1/21	14:15:18	27	0.1	370	0	2600	3069 G		25.22794	85.62153	Normal
1/1/21	14:16:0	27	0.1	140	10.1	1400	1888 G		25.22699	85.62153	Speed Breaker
1/1/21	14:17:3	27	0.1	280	0	2800	3265 G		25.22621	85.62037	Normal
1/1/21	14:18:0	27	0.1	80	10.1	800	1297 G		25.22608	85.61077	Curve
1/1/21	14:18:14	27	0.1	120	10.1	1100	1593 G		25.22576	85.60925	Normal
AVERAGE							2222				


Dec 22/01/21
JE

Dec 22/10/21
JE

6/11/21
E.E

File :D:\BUMP NEW DATA\01011533.XIs, Section No.:27, Egn :test

Name of Customer :MAGADH ENGINEERING WORKS, Name of Work/ Road :KAKO MAIN ROAD TO DOMTOLI

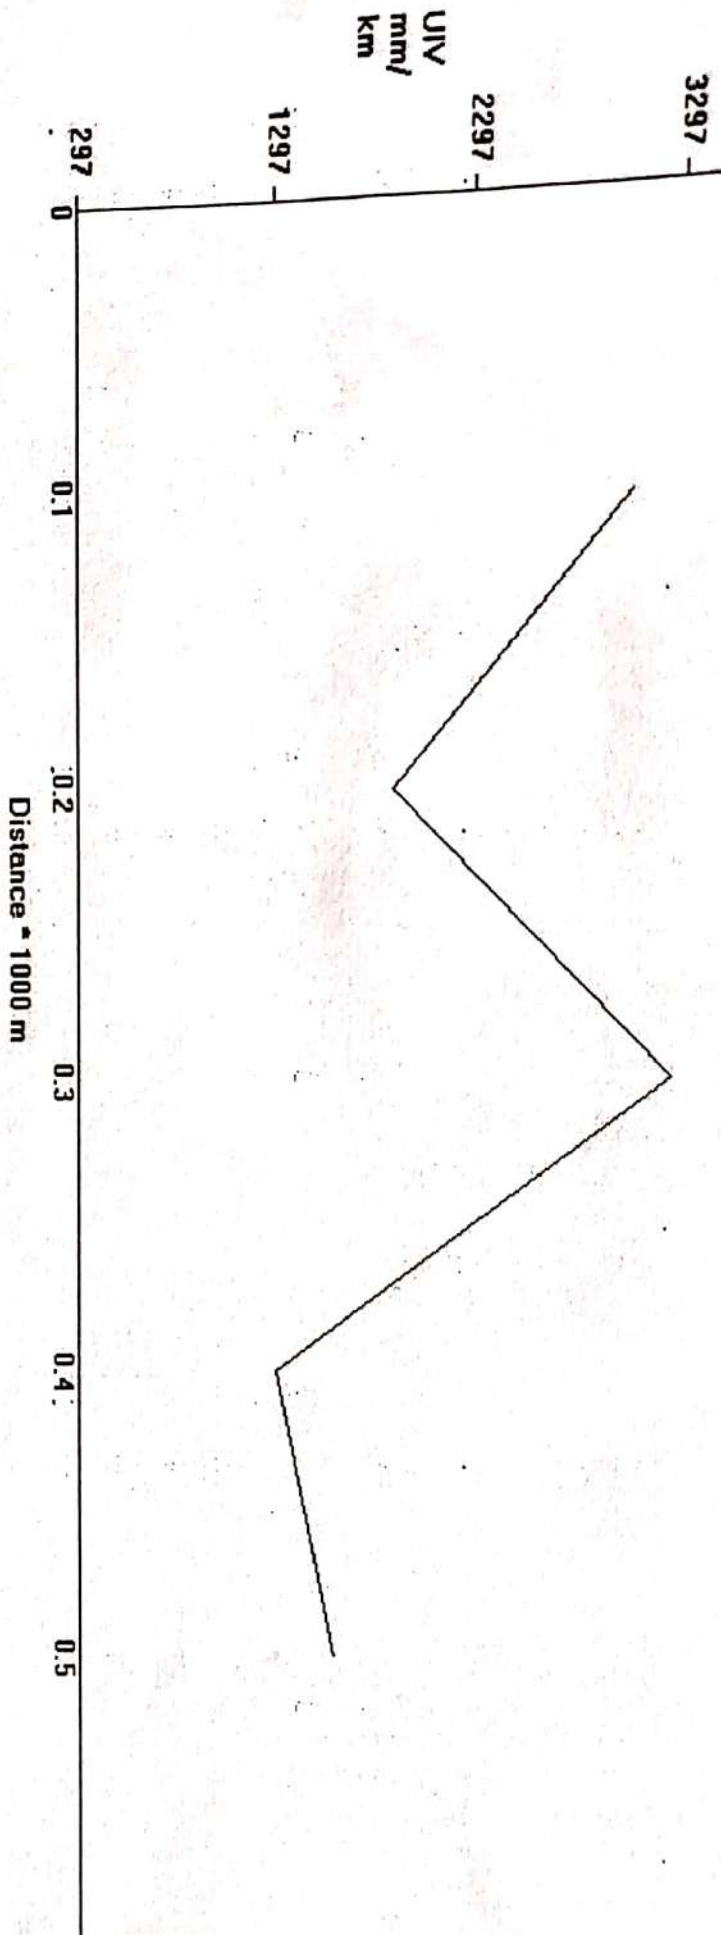

22/10/21
JE

22/10/21
JE

22/10/21
E.E
