

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, औरंगाबाद

Email ID:-eerwdaurangabad1@gmail.com

Mob:- 8986915333

पत्रांक.....146 अगस्त..... औरंगाबाद/दिनांक.....19/01/21.....

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद।

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054)योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वास भाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद

(HAPD)
19.01.21

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Aurangabad
Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Aurangabad

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/AU/AUR/19/0013	NABINAGAR BARUN ROAD - KHANDA	NEA2200060	3140/22.07.2019	2.3	86.66	60.07	17.90	70MBD-2019-20 15.02.2020	14.11.2020	16.01.2021	2440	25.00MM	5.069%	0.00000	0.00000	60.07	Comp.
2	RM/AU/AUR/19/0025	rishiapmaharajganj - haneya	NEA22000176	3140/22.07.2019	2.8	89.68	55.71	24.95	72MBD-2019-20 15.02.2020	14.11.2020	16.01.2021	3009	25.00MM	5.0620%	0.00000	0.00000	55.71	Comp.
3	RM/AU/AUR/19/0017	KACHANPUR - BARA PATH	10602902019	3140/22.07.2019	3.3	119.90	77.21	30.56	82MBD-2019-20 16.09.2020	15.06.2021	16.01.2021	2492	25.00MM	5.0440%	0.00000	0.00000	77.21	Comp.
															TOTAL		192.99	

[Signature]
 Divisional Accounts Officer
 Rural Works Department, works
 Division, Aurangabad

[Signature]
 Executive Engineer
 Rural Works Department
 Works Division, Aurangabad

[Signature]
 19/01/21

Name Of Road rishiamaharajanj - haneya

Date	Time	Section	Length	Bumps	Speed	OR	CATEGORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	ROAD				
16/1/21	15:21:4	68	0.1	300	20.2	3000	G	3.66	24.552045	84.247373	Normal
16/1/21	15:21:40	68	0.1	180	30.3	1800	G	3.02	24.550597	84.247978	Normal
16/1/21	15:21:40	68	0.1	200	30.3	2000	G	3.3	24.549638	84.248265	Normal
16/1/21	15:22:0	68	0.1	180	40.4	1800	G	3.02	24.548747	84.248502	Normal
16/1/21	15:22:0	68	0.1	250	20.2	2500	G	3.99	24.547772	84.248568	Normal
16/1/21	15:22:15	68	0.1	250	30.3	2500	G	3.99	24.546903	84.248535	Normal
16/1/21	15:22:15	68	0.1	200	30.3	2000	G	3.3	24.546002	84.248248	Normal
16/1/21	15:22:15	68	0.1	240	20.2	2400	G	3.85	24.545247	84.248618	Normal
16/1/21	15:22:50	68	0.1	230	30.3	2300	G	3.72	24.544493	84.249023	Normal
16/1/21	15:23:0	68	0.1	150	30.3	1500	G	2.6	24.542623	84.249225	Normal
16/1/21	15:23:25	68	0.1	230	20.2	2300	G	3.72	24.541438	84.249343	Normal
16/1/21	15:24:0	68	0.1	260	20.2	2600	G	3.13	24.540663	84.249763	Normal
16/1/21	15:24:0	68	0.1	310	10.1	3100	G	3.8	24.539927	84.250437	Normal
16/1/21	15:24:35	68	0.1	300	10.1	3000	G	4.66	24.539055	84.25069	Speed Breaker
16/1/21	15:25:0	68	0.1	230	20.2	2300	G	3.72	24.541438	84.249343	Normal
16/1/21	15:25:10	68	0.1	330	10.1	3300	G	5.06	24.538222	84.251027	Speed Breaker
16/1/21	15:25:10	68	0.1	270	20.2	2700	G	3.26	24.53714	84.251195	Normal
16/1/21	15:25:10	68	0.1	240	20.2	2400	G	3.85	24.536248	84.25116	Normal
16/1/21	15:25:46	68	0.1	220	30.3	2200	G	3.58	24.535372	84.250908	Normal
16/1/21	15:26:0	68	0.1	290	20.2	2900	G	3.53	24.53454	84.251228	Normal
16/1/21	15:26:21	68	0.1	290	10.1	2900	G	3.53	24.53369	84.251175	Normal
16/1/21	15:26:21	68	0.1	310	10.1	3100	G	4.8	24.532868	84.252188	Speed Breaker
16/1/21	15:27:0	68	0.1	330	20.2	3300	G	3.06	24.531965	84.252542	Normal
16/1/21	15:27:0	68	0.1	260	20.2	2600	G	3.13	24.53108	84.252862	Normal
16/1/21	15:27:31	68	0.1	280	30.3	2800	G	3.4	24.530193	84.252995	Normal
16/1/21	15:27:31	68	0.1	260	30.3	2600	G	4.13	24.529268	84.253113	Speed Breaker
16/1/21	15:28:7	68	0.1	250	30.3	2500	G	3.99	24.528343	84.252978	Normal
16/1/21	15:28:42	68	0.1	250	30.3	2500	G	3.99	24.528343	84.252978	Normal
Total Length			2.7								

16/1/21

16/1/21

19/11/21

Y = 0 * X ^ 2 + 1.136 * X + 132.5
X = 2533
Y = 3009

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

Name of Customer: PRIYA RANJAN KUMAR SINGH
 Name of Work: trishipmaharajganj - haneyra
 Road: 69
 Lab Job number: 69
 Date: 16.01.2021
 Section No. 69


Test Date: 16-01-2021
 Machine No: 377
 Start S No: 944
 Start E No: 970
 Weather: Normal
 Start Location: 24552045 84:
 End Location: 24528343 84:
 Road Name: trishipmaharajganj - haneyra
 Road Type: (R) RURAL ROAD
 Side: Left
 UV Range: 836 To 5000
 Dist Range: 0 To 20
 Equation: Y = 0 * X^2 + 1.136 * X + 132.5

Print Generate Report and Graph

Redraw Graph

Map View

File: C:\Users\BPRDA132\Desktop\16011730.Xls. Section No. 69. Eqn: $Y = 0 * X^2 + 1.136 * X + 132.5$
 Name of Customer: PRIYA RANJAN KUMAR SINGH. Name of Work/ Road: trishipmaharajganj - haneyra. Lab Job

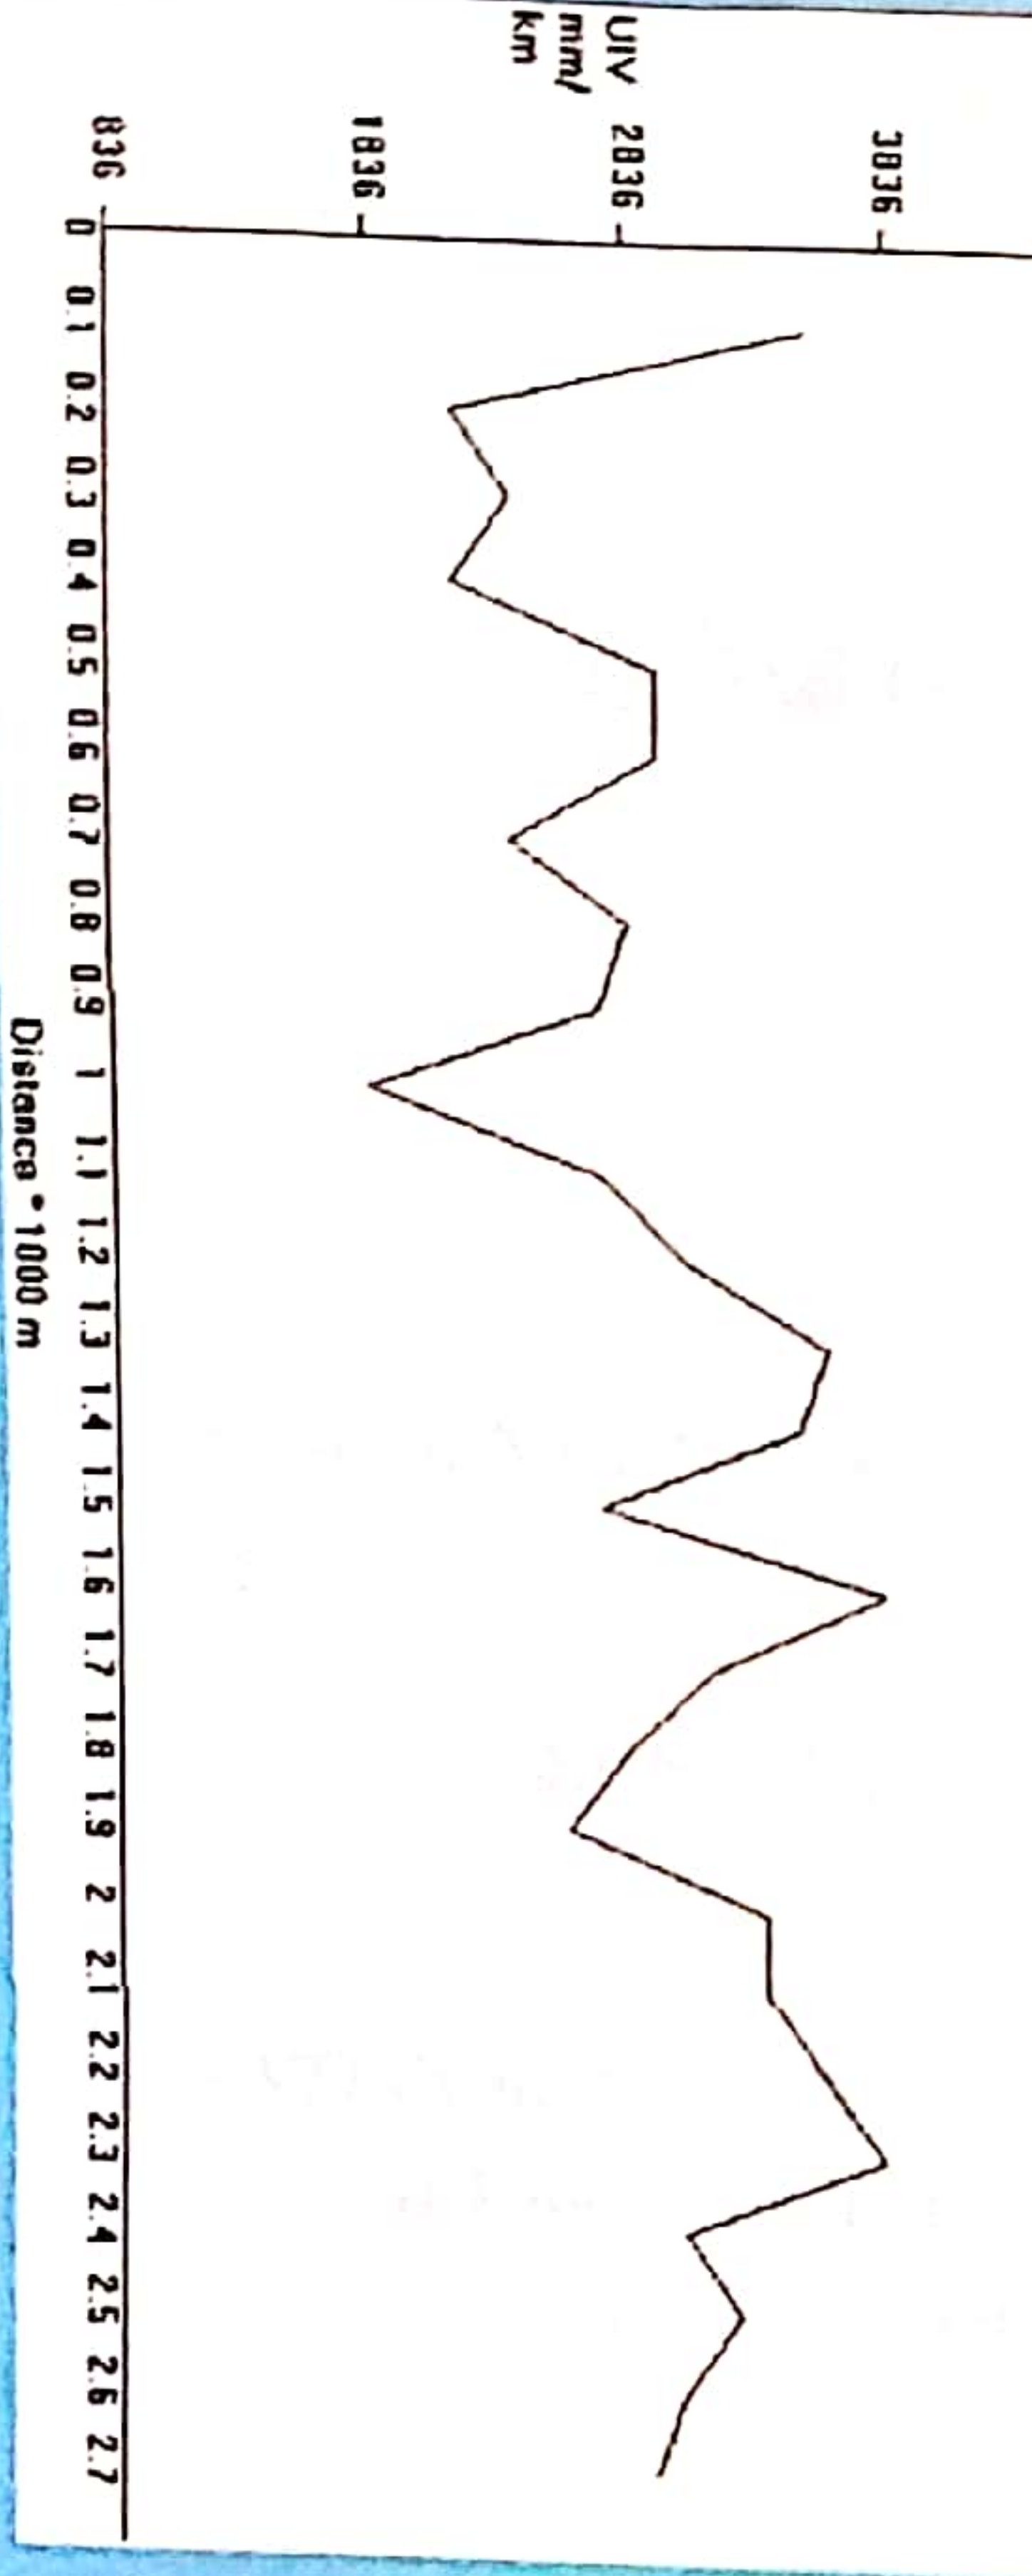

PANOLH
16.1.21

16.01.21
Asa

28.11.21
1911121

**REPORT ON
BITUMEN CONTENT TEST
FOR THE PROPOSED
C/O**

**RISIUP MAHARAJGANJ TO HANEYA ROAD
UNDER SCHEME MR 3054
AGREEMENT NO -72 MBD/2019-20**

**SUBMITTED TO:
EXECUTIVE ENGINEER
RWD. WORKS DIVISION, AURANGABAD**

**AGENCY NAME :
PRIYARANJAN KUMAR SINGH
VILL-SARSA P.O RISIUP AURANGABAD**

**TESTING BY :
*OM SAI TESTING AND RESEARCH
LABORATORY***

*2nd Floor Mahaveer Complex Fraser Road Patna
PIN CODE 800001*

OM SAI TESTING AND RESEARCH LABORATORY

2nd floor makeswari complex fraser road patna

PIN CODE 800001

Ref.....

Date

BITUMEN CONTENT TEST OF SEMI-DENSE BITUMINOUS CONCRETE

Name of RISIUP MAHARAJGANJ TO HANEYA ROAD UNDER SCHEME
Road : 3054

Type Of Material : SEMI-DENSE
BITUMINOUS CONCRETE

DATE OF COLLECTION 26-Dec-20

DATE OF TESTING 30-Dec-20

SAMPLE
NO.

A1 A2 A3

Chainage & Section:				
S.NO.	Observations	1	2	3
1	Wt. of Mix taken before extration	500	500	500
2	Wt. of filter paper before extration	6.00	6.00	6.00
3	Wt. of Mix after extration	472.1	471.89	472.13
4	Wt. of filter paper after extration	7.21	7.35	7.17
5	Wt. of filler collected from extract after allowing for seting	1.39	1.41	1.420
6	Wt. of filler collected in filter paper	1.21	1.35	1.17
7	Wt. of Aggregate + Filler collected after extration	474.7	474.65	474.7
8	Percentage of Bitumen (in the Mix) $\frac{(A-G) \times 100}{A}$	5.06	5.07	5.06
Layer		Value		
SEMI-DENSE BITUMINOUS CONCRETE		Avg. Value	5.0620%	

Checked By

