

ABSTRACT

Road Name- Temporary Restoration of Road from NH-57 Bela To shankarpur
Navtoliya

Block-DARBHANGA


RWD (W) DIVISION DARBHANGA -1

Road Actual Length - 2.70 KM


Effect Road Length - 433.00 M.

S.No.		UNIT	QUANTITY	RATE	AMOUNT (Rs)
1	Providing and filling bricks bats in ditches including cost of bricks bats and labour all complete job as per specification and direction of E/I .	CUM	180.778	1867.76	337650
	Add G.S.T. 12 %				40518
	Add 1 % Labor cess				3376
	Seigniorage Fee @1063.00/cum x0.10				19217
					400761


Rs - 4,00,761 =


J.E.

Work Section Darbhanga-2

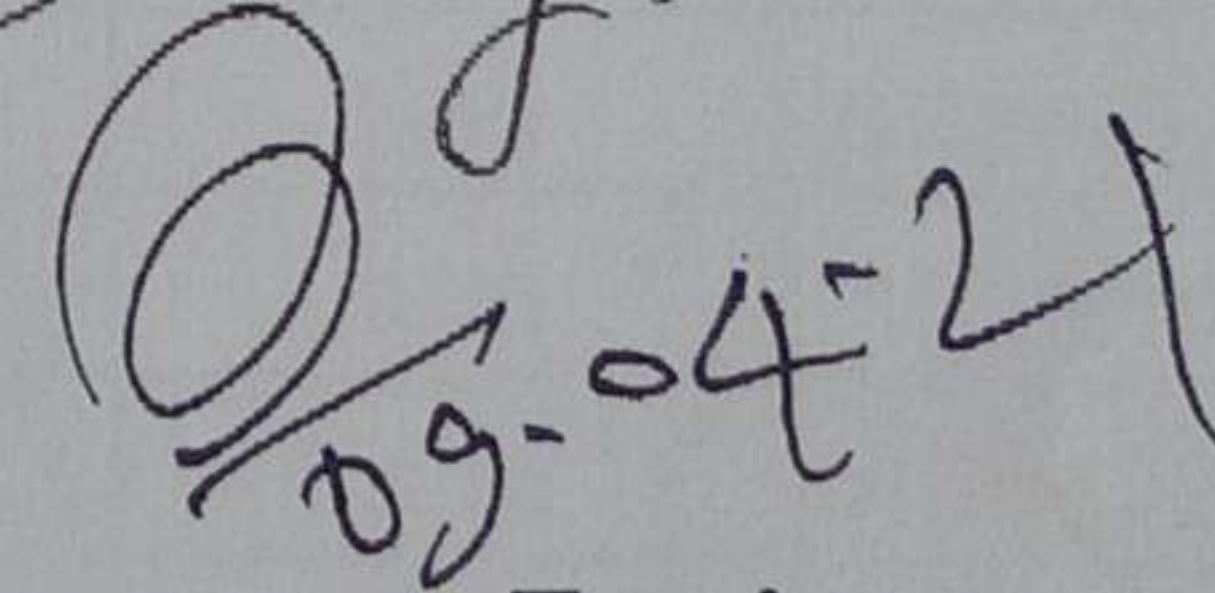

A.E.

Work Sub-Division
Darbhanga


E.E.

RWD Darbhanga -1

कार्यपालक अभियंता द्वारा कार विर काम प्रमंडल - फुलपारा के पत्रांक 542 अंकु
दिनांक 07/04/2021 के द्वारा समर्पित जाँच प्रविवेदन के आधार पर।
Post - Fecto T/A for Rs- 4,00,761 = (Rupees Four Lacs
Seven hundred Sixty one) only.


09-04-21

Superintending Engineer

RWD, Works Circle, Darbhanga

09/04/2021

Detailed Estimate for Temporary Restoration of NH-57 Bela To Shankarpur Navtoliya road for the year 2020 -21.

Block -Darbhanga

Total Restoration Length -433.00 M

R.W.D.[W] Division -Darbhanga -1

S.N.	item	No.	Length (M)	Width(M)	Depth (M)(AV)	Quantity (cum)
1	Providing and filling bricks bats in ditches including cost of bricks bats and labour all complete job as per specification and direction of E/I .					
	Chainage in M					
	10	1	2.00	0.90	0.150	0.270
	15	1	4.50	0.70	0.150	0.473
		1	9.90	2.40	0.200	4.752
	34	1	2.50	1.50	0.250	0.938
		1	1.10	1.20	0.200	0.264
	41	1	1.25	1.50	0.225	0.422
	47	1	25.00	4.00	0.250	25.000
	72	1	58.00	3.70	0.250	53.650
	134	1	15.00	2.25	0.250	8.438
		1	10.00	1.10	0.200	2.200
	172	1	2.20	2.50	0.200	1.100
	196	1	12.00	1.60	0.225	4.320
	210	1	19.00	2.10	0.250	9.975
	259	1	32.00	1.70	0.250	13.600
	260	1	5.10	1.00	0.150	0.765
	306	1	5.00	1.00	0.225	1.125
		1	1.40	1.00	0.150	0.210
		1	2.50	2.00	0.150	0.750
	355	1	43.00	3.80	(0.225+0.350)/2	46.978
	419	1	6.00	3.70	0.250	5.550
		1	11.70	2.70	0.225	7.108
		1	2.90	1.10	0.200	0.638
	441	1	17.00	2.70	0.250	11.475
		1	3.25	1.50	0.225	1.097
	532	1	2.50	1.50	0.150	0.563
	538	1	13.00	0.70	0.225	2.048
	551	1	20.00	2.60	0.250	13.000
	571	1	9.00	3.80	0.250	8.550
	583	1	8.00	1.70	0.225	3.060

12/12/20

R

02/02

597	1	4.20	1.10	0.150	0.693
603	1	3.50	1.60	0.225	1.260
	1	5.50	2.25	0.250	3.094
Branch road at 67 M	1	37.00	3.50	0.225	29.138
147	1	23.00	4.25	1.400	136.850
171	1	15.00	2.20	0.300	9.900
Total Qty.					180.778

JE

AE

EE

RWD(W) Division Darbhanga -1
