

Requisition Form for scheme Head : MR 3054 Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD. WORKS DIVISION, ROSERA

Sl No	Package No	Project ID as Per MIS	Name of Road	Adminstrative Approval (AA) Letter No and Date	Length (In Km)	Amount (In Lakh)	Agreement Amount		Agreement No and Date	Date of Completion as per Agreement	Actual Date of Completion	1st Year			
							Initial Rectification with Surface Renewal	5 Year Routine Maintenance				1st Quarter	2nd Quarter	3rd Quarter	4th Quarter
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
1	RM/S.A/ROS/19/0002	32010302032	T03 - Pithadobhi	1856, 24-06-2019	3.2	103.604	59.93327	27.34381	07(MBD)2019-20/18-03-2020	17-03-21	29-05-21	1.36719	1.36719		
2	RM/S.A/ROS/19/0002	NEA22000624	BHARBARI - BHATANDI	1856, 24-06-2020	5.2	191.143	110.08328	50.36004	07(MBD)2019-20/18-03-2020	17-03-21	30-06-21	2.51800	2.51800		
3	RM/S.A/ROS/19/0002	NEA22000626	NOTIPIR - PILHADOBHI	1856, 24-06-2021	4.8	172.589	99.38067	45.33192	07(MBD)2019-20/18-03-2021	17-03-21	29-05-21	2.26659	2.26659		
4	RM/S.A/ROS/19/0002	NEA22000627	MDR T05 NURADPUR TO - JAHANGIRPUR LALPUR	1856, 24-06-2022	2.2	82.57	49.33191	19.16835	07(MBD)2019-20/18-03-2022	17-03-21	29-05-21	0.95841	0.95841		
Total						549.906	318.72913	142.20412	0	0	0	7.11019	7.11019		

Sr. DAO
RWD (W) Division Rosera

Executive Engineer
RWD (W) Division Rosera

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रोसड़ा।**

पत्रांक :- 1607/अभ/ रोसड़ा, दिनांक :- 08 / 07 / 2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रोसड़ा।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- नई अनुरक्षण नीति 2018 शीर्ष MR-3054 योजना अंतर्गत (अनुरक्षण मद) राशि की अधियाचना के संबंध में।

महाशय,
उपर्युक्त विषयक नई अनुरक्षण नीति 2018 शीर्ष MR-3054 योजना मद अंतर्गत (अनुरक्षण मद) व्यय हेतु विहित प्रपत्र में अधियाचना पत्र संलग्न कर भेजी जा रही है।


अतः अनुरोध है कि संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा करें, ताकि किये गये कार्यों का भुगतान किया जा सके।

अनु०-यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रोसड़ा।

File : C:\Users\BRRdA38\Desktop\BUMP REPORT\25-05-2022\03051931.xls. Section No. : 96, Eqn : $Y = 0 \cdot X^2 +$
Name of Customer : M/S Brothers Builders, Name of Work / Road : Bharbari - Bhatandi, Lab Job number :

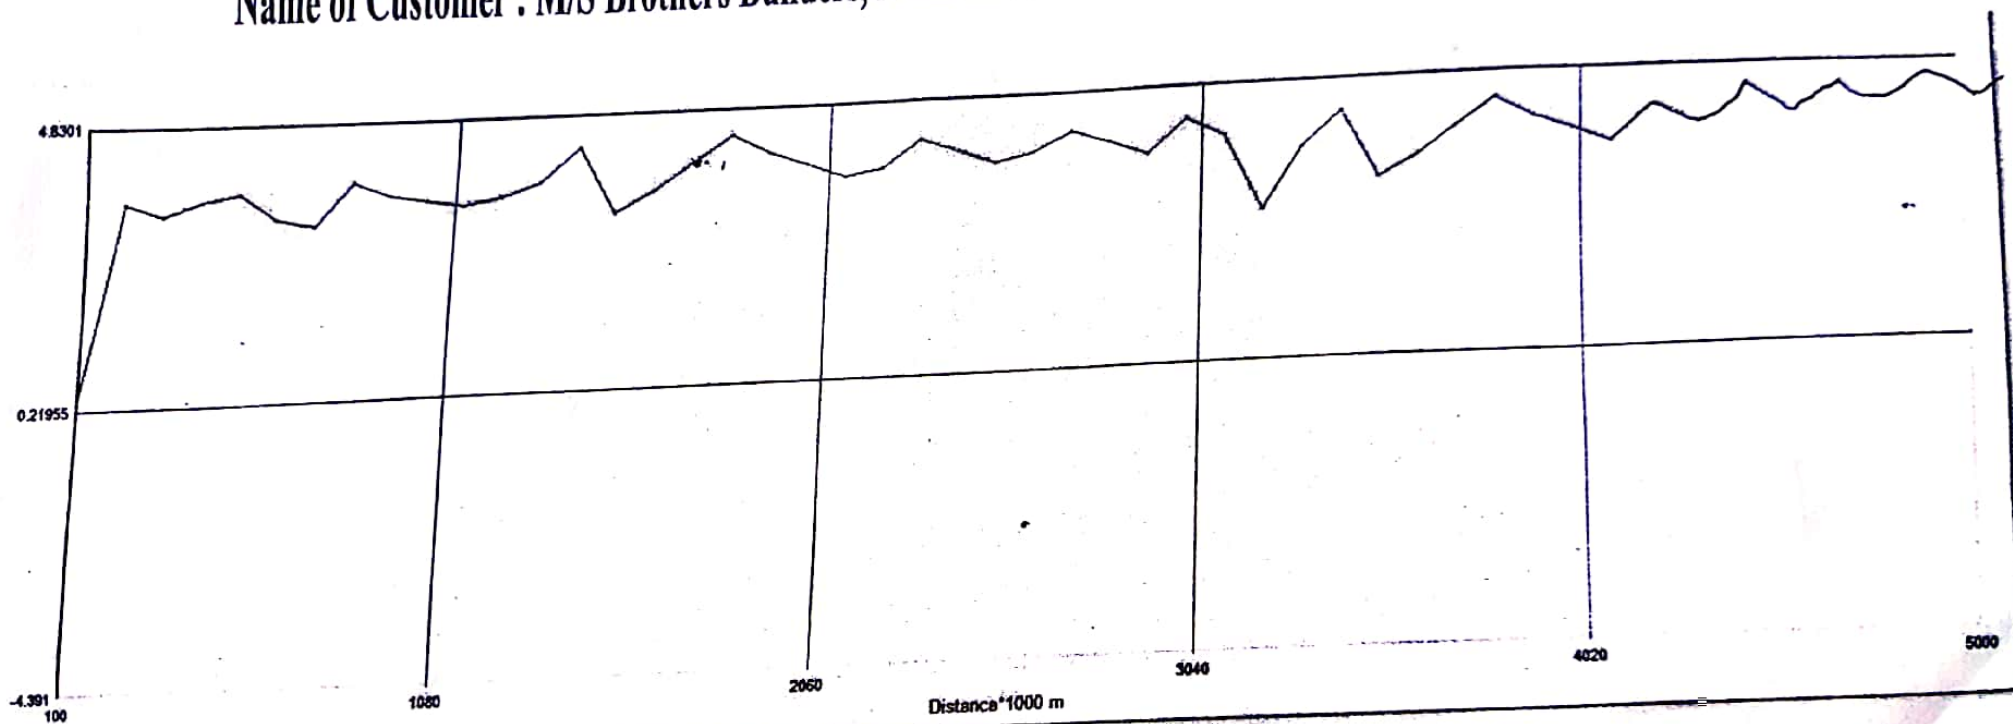

01/07/2022
J-E

01/7/22
A-E

01/07/22
GE

कार्यपालक अभियंता
ग्राम का. विभाग
सूर्य प्रमंडल, रोमहा

Dat	Time	Section	Length	Bumps	Speed	OR	IRI	TEGORY	Latitude	ongitude	Event		
No.			in km	in mm	Rate	mm/A/m	mm/A/m	ROAD					
05-05-22	20:11:0	SS	0.1	570	0	3800	4449 A		25.81608	86.13298	Curve	$y = 0 \cdot x + 2 \cdot 1.136 \cdot x + 132.5$	
05-05-22	20:11:25	SS	0.1	330	10.1	3300	3881 G		25.8161	86.14242	Normal	$x = 5200$	
05-05-22	20:12:0	SS	0.1	290	10.1	2900	3426 G		25.81662	86.15	Normal	$y = 6039$	
05-05-22	20:12:36	SS	0.1	480	10.1	4800	5585 P		25.81751	86.15302	Speed Breaker		
05-05-22	20:13:11	SS	0.1	330	10.1	3300	3881 G		25.81825	86.1560	Normal	(R) RURAL ROAD	
05-05-22	20:13:11	SS	0.1	420	10.1	4200	4903 A		25.81954	86.16278	Curve	Good	Average
05-05-22	20:14:0	SS	0.1	330	10.1	3300	3881 G		25.81954	86.16918	Normal	<4000	>5001
05-05-22	20:14:21	SS	0.1	430	10.1	4300	5017 P		25.82008	86.17743	Speed Breaker		
05-05-22	20:14:57	SS	0.1	300	10.1	3000	3540 G		25.82012	86.18618	Normal		
05-05-22	20:15:0	SS	0.1	390	10.1	3900	4449 A		25.82092	86.19628	Curve		
05-05-22	20:15:32	SS	0.1	330	10.1	3300	3881 G		25.82183	86.19948	Curve		
05-05-22	20:16:0	SS	0.1	300	10.1	3000	3540 G		25.82264	86.20185	Normal		
05-05-22	20:16:7	SS	0.1	520	10.1	5200	4449 A		25.82347	86.20992	Normal		
05-05-22	20:17:0	SS	0.1	330	10.1	3300	3881 G		25.82429	86.21363	Curve		
05-05-22	20:17:18	SS	0.1	370	20.2	3700	4335 A		25.82507	86.21835	Normal		
05-05-22	20:17:18	SS	0.1	320	20.2	3200	3767 G		25.82589	86.22322	Normal		
05-05-22	20:17:18	SS	0.1	210	20.2	2100	2518 G		25.82676	86.2244	Normal		
05-05-22	20:18:0	SS	0.1	250	20.2	2500	2972 G		25.82762	86.22542	Normal		
05-05-22	20:18:0	SS	0.1	250	20.2	2500	2972 G		25.82849	86.22793	Curve		
05-05-22	20:18:28	SS	0.1	300	20.2	3000	3540 G		25.82899	86.2348	Curve		
05-05-22	20:18:28	SS	0.1	300	20.2	3000	3540 G		25.8291	86.24493	Normal		
05-05-22	20:19:4	SS	0.1	380	10.1	3800	4449 A		25.82916	86.25487	Curve		
05-05-22	20:19:4	SS	0.1	480	10.1	4800	5585 P		25.82927	86.2648	Speed Breaker		
05-05-22	20:20:0	SS	0.1	380	10.1	3800	4449 A		25.8299	86.27103	Curve		
05-05-22	20:20:14	SS	0.1	380	10.1	3800	4449 A		25.83048	86.27945	Speed Breaker		
05-05-22	20:20:50	SS	0.1	500	10.1	5000	5812 P		25.83107	86.28652	Normal		
05-05-22	20:21:0	SS	0.1	330	10.1	3300	3881 G		25.83095	86.29612	Curve		
05-05-22	20:21:25	SS	0.1	380	20.2	3800	4449 A		25.83053	86.3042	Curve		
05-05-22	20:21:25	SS	0.1	360	20.2	3600	4222 A		25.83023	86.31397	Normal		
05-05-22	20:22:0	SS	0.1	250	20.2	2500	2972 G		25.8301	86.3239	Normal		
05-05-22	20:22:0	SS	0.1	210	20.2	2100	2518 G		25.82975	86.3308	Normal		
05-05-22	20:22:0	SS	0.1	210	20.2	2100	2518 G		25.82881	86.33215	Curve		
05-05-22	20:22:35	SS	0.1	360	20.2	3600	4222 A		25.82798	86.33618	Normal		
05-05-22	20:22:35	SS	0.1	340	20.2	3400	3994 G		25.82719	86.33972	Normal		
05-05-22	20:23:11	SS	0.1	250	20.2	2500	2972 G		25.82663	86.34578	Normal		
05-05-22	20:23:11	SS	0.1	300	20.2	3000	3540 G		25.82646	86.35605	Normal		
05-05-22	20:23:46	SS	0.1	210	20.2	2100	2518 G		25.8261	86.36532	Normal		
05-05-22	20:47:0	SS	0.1	250	20.2	2500	2972 G		25.827	86.21532	Curve		
05-05-22	20:47:17	SS	0.1	360	0	3600	4222 A		25.82727	86.20605	Curve		
05-05-22	20:47:17	SS	0.1	380	20.2	3800	4449 A		25.82772	86.19813	Normal		

Name of the work: Bharbari - Bhatandi

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUNIP (cm)	Speed (Km/Hr)	U/I (mm/Km)	Corrected U/I (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction I	Remarks
25-05-2022	15 09 06	96	100	100	0.0 cm	8.9 Km/Hr	0.0 mm/Km	237.9	0.419	Good	25.804435	N	86.089084	E	Normal
25-05-2022	15 09 48	96	100	200	26.0 cm	11.6 Km/Hr	2600.0 mm/Km	2653.3	3.61	Good	25.804515	N	86.089087	E	Curve
25-05-2022	15 10 11	96	100	300	24.0 cm	19.0 Km/Hr	2400.0 mm/Km	2467.5	3.384	Good	25.804436	N	86.089094	E	Normal
25-05-2022	15 10 30	96	100	400	26.0 cm	13.6 Km/Hr	2600.0 mm/Km	2653.3	3.61	Good	25.804517	N	86.089086	E	Normal
25-05-2022	15 11 04	96	100	500	27.0 cm	17.8 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.804136	N	86.089090	E	Curve
25-05-2022	15 11 33	96	100	600	23.0 cm	17.6 Km/Hr	2300.0 mm/Km	2374.6	3.27	Good	25.805035	N	86.089085	E	Normal
25-05-2022	15 11 50	96	100	700	22.0 cm	17.8 Km/Hr	2200.0 mm/Km	2281.7	3.155	Good	25.805136	N	86.089088	E	Normal
25-05-2022	15 12 20	96	100	800	28.0 cm	18.0 Km/Hr	2800.0 mm/Km	2839.1	3.835	Good	25.805137	N	86.089091	E	Normal
25-05-2022	15 12 58	96	100	900	26.0 cm	17.3 Km/Hr	2600.0 mm/Km	2653.3	3.61	Good	25.805138	N	86.089093	E	Normal
25-05-2022	15 13 21	96	100	1000	25.0 cm	17.0 Km/Hr	2500.0 mm/Km	2560.4	3.497	Good	25.805125	N	86.089092	E	Normal
25-05-2022	15 13 46	96	100	1100	24.0 cm	17.3 Km/Hr	2400.0 mm/Km	2467.5	3.384	Good	25.805123	N	86.089101	E	Normal
25-05-2022	15 14 08	96	100	1200	25.0 cm	18.2 Km/Hr	2500.0 mm/Km	2560.4	3.497	Good	25.805120	N	86.089100	E	Normal
25-05-2022	15 14 31	96	100	1300	27.0 cm	18.4 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.804512	N	86.089102	E	Normal
25-05-2022	15 14 55	96	100	1400	32.0 cm	19.7 Km/Hr	3200.0 mm/Km	3210.7	4.28	Good	25.804515	N	86.089103	E	Normal
25-05-2022	15 15 22	96	100	1500	22.0 cm	19.2 Km/Hr	2200.0 mm/Km	2281.7	3.155	Good	25.804525	N	86.089106	E	Normal
25-05-2022	15 15 47	96	100	1600	25.0 cm	19.7 Km/Hr	2500.0 mm/Km	2560.4	3.497	Good	25.804530	N	86.089109	E	Normal
25-05-2022	15 16 11	96	100	1700	29.0 cm	21.4 Km/Hr	2900.0 mm/Km	2932	3.947	Good	25.804531	N	86.089111	E	Normal
25-05-2022	15 16 44	96	100	1800	33.0 cm	17.5 Km/Hr	3300.0 mm/Km	3303.6	4.391	Good	25.804532	N	86.089115	E	Normal
25-05-2022	15 17 10	96	100	1900	30.0 cm	18.4 Km/Hr	3000.0 mm/Km	3024.9	4.059	Good	25.804533	N	86.089113	E	Normal
25-05-2022	15 17 32	96	100	2000	28.0 cm	18.8 Km/Hr	2800.0 mm/Km	2839.1	3.835	Good	25.804538	N	86.089116	E	Normal
25-05-2022	15 17 57	96	100	2100	26.0 cm	18.1 Km/Hr	2600.0 mm/Km	2653.3	3.61	Good	25.804540	N	86.089118	E	Normal
25-05-2022	15 18 20	96	100	2200	27.0 cm	18.8 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.804542	N	86.089120	E	Normal
25-05-2022	15 18 42	96	100	2300	31.0 cm	18.8 Km/Hr	3100.0 mm/Km	3117.8	4.17	Good	25.804544	N	86.089108	E	Normal
25-05-2022	15 19 03	96	100	2400	29.0 cm	19.6 Km/Hr	2900.0 mm/Km	2932	3.947	Good	25.804550	N	86.089107	E	Normal
25-05-2022	15 19 26	96	100	2500	27.0 cm	19.6 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.804552	N	86.089105	E	Normal
25-05-2022	15 19 49	96	100	2600	28.0 cm	19.2 Km/Hr	2800.0 mm/Km	2839.1	3.835	Good	25.804560	N	86.089114	E	Normal
25-05-2022	15 20 13	96	100	2700	31.0 cm	18.9 Km/Hr	3100.0 mm/Km	3117.8	4.17	Good	25.804562	N	86.089116	E	Normal
25-05-2022	15 20 37	96	100	2800	29.0 cm	18.8 Km/Hr	2900.0 mm/Km	2932	3.947	Good	25.804564	N	86.089119	E	Curve
25-05-2022	15 20 59	96	100	2900	27.0 cm	18.9 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.804566	N	86.089121	E	Normal
25-05-2022	15 21 19	96	100	3000	32.0 cm	19.9 Km/Hr	3200.0 mm/Km	3210.7	4.28	Good	25.804568	N	86.089124	E	Normal
25-05-2022	15 21 39	96	100	3100	29.0 cm	19.8 Km/Hr	2900.0 mm/Km	2932	3.947	Good	25.804569	N	86.089126	E	Curve
25-05-2022	15 22 01	96	100	3200	18.0 cm	19.2 Km/Hr	1800.0 mm/Km	1910.1	2.692	Good	25.804572	N	86.089125	E	Normal
25-05-2022	15 22 25	96	100	3300	27.0 cm	18.4 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.804575	N	86.089127	E	Normal
25-05-2022	15 22 51	96	100	3400	32.0 cm	19.7 Km/Hr	3200.0 mm/Km	3210.7	4.28	Good	25.804578	N	86.089129	E	Curve
25-05-2022	15 23 12	96	100	3500	22.0 cm	19.2 Km/Hr	2200.0 mm/Km	2281.7	3.155	Good	25.804579	N	86.089130	E	Normal
25-05-2022	15 23 35	96	100	3600	25.0 cm	19.7 Km/Hr	2500.0 mm/Km	2560.4	3.497	Good	25.804580	N	86.089132	E	Curve

25/05/2022
J-E

AS
α 17/22
A.G

अ. नाना
ए. ए.
कार्यपालक अभियंता
ग्राम का. विभाग
कार्य प्रमंडल, रोम्बर

25-05-2022	15 23 57	96	100	3700	29 0 cm	21.3 Km/Hr	2900 0 mm/Km	2932	3.947	Good	25 804583	N	86 089135	E	Normal
25-05-2022	15 24 21	96	100	3800	33 0 cm	17.4 Km/Hr	3300 0 mm/Km	3303 6	4.391	Good	25 804593	N	86 089136	E	Normal
25-05-2022	15 24 43	96	100	3900	30 0 cm	18.3 Km/Hr	3000 0 mm/Km	3024 9	4.059	Good	25 804594	N	86 089138	E	Normal
25-05-2022	15 25 05	96	100	4000	28 0 cm	18.7 Km/Hr	2800 0 mm/Km	2819 1	3.835	Good	25 804592	N	86 089139	E	Normal
25-05-2022	15 25 29	96	100	4100	26 0 cm	18.2 Km/Hr	2600 0 mm/Km	2653 3	3.61	Good	25 804595	N	86 089141	E	Curve
25-05-2022	15 25 52	96	100	4200	31 0 cm	18.7 Km/Hr	3100 0 mm/Km	3117 8	4.17	Good	25 804597	N	86 089145	E	Normal
25-05-2022	15 26 02	96	100	4300	24 0 cm	19.0 Km/Hr	2400 0 mm/Km	2467 5	3.384	Good	25 804599	N	86 089144	E	Normal
25-05-2022	15 33 51	96	100	4400	26 0 cm	17.6 Km/Hr	2600 0 mm/Km	2653 3	3.61	Good	25 804601	N	86 089143	E	Normal
25-05-2022	15 34 14	96	100	4500	27 0 cm	17.8 Km/Hr	2700 0 mm/Km	2746 2	3.723	Good	25 804605	N	86 089142	E	Curve
25-05-2022	15 34 59	96	100	4600	27 0 cm	18.9 Km/Hr	2700 0 mm/Km	2746 2	3.723	Good	25 804609	N	86 089146	E	Normal
25-05-2022	15 35 10	96	100	4700	32 0 cm	19.9 Km/Hr	3200 0 mm/Km	3210 7	4.28	Good	25 804611	N	86 089148	E	Normal
25-05-2022	15 35 55	96	100	4800	29 0 cm	19.8 Km/Hr	2900 0 mm/Km	2932	3.947	Good	25 804615	N	86 089150	E	Curve
25-05-2022	15 36 15	96	100	4900	18 0 cm	19.2 Km/Hr	1800 0 mm/Km	1910.1	2.692	Good	25 804620	N	86 089152	E	Normal
25-05-2022	15 36 45	96	100	5000	22 0 cm	19.2 Km/Hr	2200 0 mm/Km	2281.7	3.155	Good	25 804622	N	86 089154	E	Normal
25-05-2022	15 36 59	96	100	5100	25 0 cm	19.7 Km/Hr	2500 0 mm/Km	2560.4	3.497	Good	25 804623	N	86 089156	E	Curve
25-05-2022	15 37 09	96	100	5200	29 0 cm	21.3 Km/Hr	2900 0 mm/Km	2932	3.947	Good	25 804625	N	86 089157	E	Normal

01/07/2022
J-E

AS
01/07/22
A-E

EXECUTIVE ENGINEER
RURAL WORKS ROSERA
कार्यपालक अभियंता
ग्रा० का० विभाग
कार्य प्रमंडल, रोमडा

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- R.W.D Works Division Rosera

1	Name of the Road	Bharbari - Bhatandi		
2	Batch No.	RM/SA/Ros/19/0002		
3	Project Id	NEA22000624		
4	Total Length of Road (in Km)	5.2 km		
5	Length of Road to Meet Required Service Level [Completed length] (in Km)	5.2 k.m		
6	No. of Total Quarter (ie3 Months as a unit in 5 years)	1st Quarter		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount ofr Maintenance] (in Lakh)	50.36004		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)	2.518		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]= [3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGATAION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh [6])				2.51800

Date of inpection by E/I or his agent

Prepared by Contractor's Self Control Unit

Name and Designation of person inspection road

01/07/2022
J-E

AS
01/7/22

(Signature)

कार्यपालक अभियंता
क्रा० का० विभाग
काब प्रमंडल, रोमहा

Date

Signature of person inspecting Road

Certify by E/I [signature] Date:-

Government of Bihar OM01 Rural Works Department			1st Quarter of 1st Year										
Road From :Bharbari To Bhatandi Length of Road :- 5.200 KM Period:- From 01/05/21 To 31/08/2021 Inspector :- J.E. , RWD Sub-Division Rosera , Works Section Rosera			ORDINARY MAINTENANCE INSPECTION REPORT Form OM01 To :- .. Excutive Engineer RWD, Works Division Rosera (Samastipur) Position :- .. E.E.										
Standard Work Item			Unit of Work required in each Kilometre										
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	Comments
OM101	Pothole Patching	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No pothole found
OM 102	Surface Depression and Rut Patching	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Surface Depression and Rut Patching found
OM 103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Crack Sealing found
OM 104	Surface Treatment												
	(a) Loss of Agreegate (Surface Ravelling)	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Loss of Agreegate (Surface Ravelling) found.
	(b) Bleeding / Flushing	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Bleeding / Flushing required.
	(c) Crocodile Cracking	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Crocodile Cracking found.
OM 105	Edge Repair	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Edge Repair Required.
OM 106	Digouts	M ²	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	
OM 107	Concrete Pavement	M ³	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	
	Other activities												
OM 200 Shoulder													
OM 201	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Edge Drop-off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Roughness, Scouring or Potholes Required.
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Holding water found.
OM 202	Embankment Repair	M ³	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Embankment Repair Required.
	Other activities		N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	
OM 302	Culvert Cleaning	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM 303	Culvert and Pit Repair	M ³	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	Other activities (White Washing)	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required

M/s BROTHERS BUILDERS
Bidder
PARTNER

Appendix

J.E. RWD(w) Rosera

A.E. RWD Rosera

Excutive Engineer, Works Division
Rosera (Samastipur)

कार्यपालक अभियंता
ग्रा० का० विभाग
कार्य प्रमंडल, रोसड़ा

Standard Work Item		Work	Unit of Work required in each Kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM 400 Vegetation													
OM 401	Grass Control												
	(a) Roadside- General Tidy	Ha	NII	NII	NII	NII	NII	NII					Not Required
	(b) Clear near Safety signs, Kilometre posts and Roadside furniture	Ha	NII	NII	NII	NII	NII	NII					Not Required
OM402	Tree and Shrub Managenent	No	NII	NII	NII	NII	NII	NII					Not Required
	(Cutting Trees)	No	NII	NII	NII	NII	NII	NII					Not Required
	(Cutting shrubs)	No	NII	NII	NII	NII	NII	NII					Not Required
	Other activlites (Trimming of Grass)	M ²	NII	NII	NII	NII	NII	NII					Not Required
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No	NII	NII	NII	NII	NII	NII					Not Required
OM502	Guard Stones	Lm	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.					Not Required
OM503	Distance Stones	No	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.					Not Required
OM504	Road Marking	M ²	NII	NII	NII	NII	NII	NII	NII	NII	NII		Not Required
	Other activities												

(Signature of Contractor/Authorized Representative)

Date

Time

Place

Note:- Enclose photographs with the report.

[Signature]
29/8/24
J.E. RWD(W) Rosera

[Signature]
01/7/22
A.E. RWD Rosera

[Signature]
Excutive Engineer, Works Division
Rosera (Samastipur)

कार्यपालक अधिकारी
! प्रा० का० विभाग
कार्य प्रमंडल, रोसरा
